

Town of Warwick
Orange County, New York

Town Hall
132 Kings Highway
Warwick, NY 10990

Project Manual

Town of Warwick

Ball Road Culvert Replacement

February 2025

Prepared by:

**Henningson, Durham & Richardson
Architecture and Engineering, P.C.**

50 Tice Boulevard, Suite 210
Woodcliff Lake, New Jersey 07677

This page intentionally left blank.

Table of Contents

<u>Item</u>	<u>Page</u>
Advertisement for Bid.....	1 of 323
Instructions to Bidder.....	4 of 323

Bid Package

Bid Form.....	17 of 323
Information to Bidders.....	22 of 323
Bid Tabulation Spreadsheet.....	23 of 323
Bidder Qualification Statement.....	25 of 323
Agreement.....	37 of 323
Bid Bond.....	45 of 323
Certification of Federal Aid Contracts.....	47 of 323
Disclosure of Lobbying Activities.....	49 of 323
Statement of Non-Collusion.....	51 of 323
Disadvantaged Business Enterprise Utilization Requirements.....	53 of 323
Certification of Non-Segregated Facilities.....	55 of 323
Certification of Limited Foreign Involvement.....	57 of 323
General Conditions.....	59 of 323
Supplementary Conditions.....	134 of 323
Prevailing Wage Rates (New York State).....	143 of 323
Prevailing Wage Rates (Federal).....	194 of 323
Performance Bond.....	224 of 323
Payment Bond.....	229 of 323

Attachments

Attachment 1: Subsurface Soil Logs and Geotechnical Report.....	233 of 323
Attachment 2: NYS OPRHP Letter	266 of 323
NYSDEC Permit.....	267 of 323
USACE Permit.....	279 of 323

This page is intentionally blank.

ADVERTISEMENT FOR BIDS

Town of Warwick
Warwick, NY
Ball Road Culvert Replacement

General Notice

TOWN OF WARWICK (Owner) is requesting Bids for the construction of the following Project:

Sealed Bids for the construction of the Ball Road Culvert Replacement will be received by **The Town of Warwick**, at the office of the Warwick Town Hall, 132 Kings Highway, Warwick, New York until 10 A.M. local time on March 25, 2025, at which time the Bids received will be publicly opened and read. The Project consists of constructing replacing a culvert that was damaged during Hurricane Ida and associated stream work to restore fish passage to the stream.

Obtaining the Bidding Documents

Copies of the Bidding Documents may be obtained from the Town of Warwick webpage, www.TownofWarwick.org. Neither Owner nor Engineer will be responsible for full or partial sets of Bidding Documents, including Addenda if any, obtained from sources other than the Issuing Office.

Each bid shall be accompanied by an acceptable form of Bid Guarantee in an amount equal to at least five percent (5%) of the amount of the Bid payable to the Town of Warwick as a guarantee that if the Bid is accepted, the Bidder will execute the Contract and file acceptable Performance and Labor, Material Payment Bonds, and Certificate(s) of Insurance within five (5) days after the award of the Contract.

Each successful Bidder shall be required to furnish and pay for satisfactory Performance and Labor & Material Payment Bonds, each in the amount at least equal to the Contract Amount as security for the faithful performance and payment of all Contractor's obligations under the Contract Documents.

Bids may be held by the Town of Warwick for a period not to exceed thirty (30) calendar days from the date of the Bid Opening for the purpose of reviewing the Bids and investigating the qualifications of Bidders prior to awarding the Contract. This project has high priority, and all documents will be reviewed as soon as practicable to minimize this review period.

SITE INSPECTION:

A pre-bid site inspection will not be held but the Contractor is encouraged to visit the site as needed.

OWNERS RIGHTS RESERVED:

The Town of Warwick hereinafter called the Owner, reserves the right to reject any and all Bids and to waive any formality or technicality in any bid in the interest of the Owner.

STATEMENT OF NON-COLLUSION:

Bidders on the Contracts are required to execute a non-collusion bidding certificates pursuant to Section 103d of the General Municipal Law of the State of New York.

Attention of bidders is particularly called to the requirement as to conditions of employment to be observed and minimum wage rates to be paid under the contract, Section 3, Segregated Facilities, Section

109, and Executive Order 11246. The requirements for Bidders and Contractors under this order, which concerns non-discrimination in employment, are explained in the Contract Documents. Bidders are also required to comply with the provisions of Section 291-299 of the Executive Law of the State of New York.

The Town of Warwick hereby notifies all Bidders that it will affirmatively insure that in regard to any Contract entered into pursuant to this advertisement, minority business enterprises will be afforded full opportunity to submit bids in response to this invitation and will not be discriminated against on the grounds of race, color, or national origin in consideration for an award.

PREVAILING WAGES:

The labor on the contract awarded as a result of this advertisement shall be performed in accordance with Article 8 (Section 220-223) of the New York State Labor Law. Certified payroll must be included with each invoice submitted to the Town of Warwick for payment.

Owner: Town of Warwick

By: Eileen Astorino

Title: Town Clerk

Date: February 19, 2025

INSTRUCTIONS TO BIDDERS

FOR CONSTRUCTION CONTRACT

TABLE OF CONTENTS

	Page
Article 1— Defined Terms	1
Article 2— Bidding Documents.....	1
Article 3— Qualifications of Bidders.....	2
Article 4— Site and Other Areas; Existing Site Conditions; Examination of Site; Owner’s Safety Program; Other Work at the Site	3
Article 5— Bidder’s Representations and Certifications	5
Article 6— Interpretations and Addenda	6
Article 7— Bid Security	7
Article 8— Contract Times.....	8
Article 9— Substitute and “Or Equal” Items.....	8
Article 10— Subcontractors, Suppliers, and Others	8
Article 11— Preparation of Bid.....	9
Article 12— Basis of Bid.....	10
Article 13— Submittal of Bid	10
Article 14— Modification and Withdrawal of Bid	11
Article 15— Opening of Bids.....	11
Article 16— Bids to Remain Subject to Acceptance	11
Article 17— Evaluation of Bids and Award of Contract	11
Article 18— Bonds and Insurance	12
Article 19— Signing of Agreement	12
Article 20— Sales and Use Taxes	12

ARTICLE 1—DEFINED TERMS

- 1.01 Terms used in these Instructions to Bidders have the meanings indicated in the General Conditions and Supplementary Conditions. Additional terms used in these Instructions to Bidders have the meanings indicated below:
- A. *Issuing Office*—The office from which the Bidding Documents are to be issued, and which registers plan holders.
 - B. *Bidder*—One who submits a Bid directly to Owner as distinct from a sub-bidder, who submits a Bid to a Bidder.
 - C. *Successful Bidder*—The lowest, responsible and responsive Bidder to whom Owner (on the basis of owner's evaluation as hereinafter provided) makes an award.

ARTICLE 2—BIDDING DOCUMENTS

- 2.01 Bidder shall obtain a complete set of Bidding Requirements and proposed Contract Documents (together, the Bidding Documents). See the Agreement for a list of the Contract Documents. It is Bidder's responsibility to determine that it is using a complete set of documents in the preparation of a Bid. Bidder assumes sole responsibility for errors or misinterpretations resulting from the use of incomplete documents, by Bidder itself or by its prospective Subcontractors and Suppliers.
- 2.02 Bidding Documents are made available for the sole purpose of obtaining Bids for completion of the Project and permission to download or distribution of the Bidding Documents does not confer a license or grant permission or authorization for any other use, nor does it grant or confer ownership or any property interest in the Bidding Documents and other documents distributed for the Project. Authorization to download documents, or other distribution, includes the right for Bidding Documents holders to print documents solely for their use, and the use of their prospective Subcontractors and Suppliers, provided the Bidding Documents holder pays all costs associated with printing or reproduction. Paper or other types of printed documents may not be re-sold under any circumstances.
- 2.03 Owner has established a Bidding Documents Website as indicated in the Advertisement or invitation to bid. Owner recommends that Bidder register as a Bidding Documents holder with the Issuing Office at such website, and obtain a complete set of the Bidding Documents from such website. Bidders may rely that sets of Bidding Documents obtained from the Bidding Documents Website are complete, unless an omission is blatant. Registered Bidding Documents holders will receive Addenda issued by Owner or Issuing Office.
- 2.04 Bidder may register as a Bidding Documents holder and obtain complete sets of Bidding Documents, in the format stated in the Advertisement or invitation to bid, from the Issuing Office. Bidders may rely that sets of Bidding Documents obtained from the Issuing Office are complete, unless an omission is blatant. Registered Bidding Documents holders will receive Addenda issued by Owner or Issuing Office.
- 2.05 *Electronic Documents*
- A. When the Bidding Requirements indicate that electronic (digital) copies of the Bidding Documents are available, such documents will be made available to prospective Bidders as Electronic Documents in the manner specified.

1. Bidding Documents will be provided in Adobe PDF (Portable Document Format) (.pdf) that is readable by Adobe Acrobat Reader Version [insert version number] or later. It is the intent of the Engineer and Owner that such Electronic Documents are to be exactly representative of the paper copies of the documents. However, because the Owner and Engineer cannot totally control the transmission and receipt of Electronic Documents nor any bidder's or the Contractor's means of reproduction of such documents, the Owner and Engineer cannot and do not guarantee that Electronic Documents and reproductions prepared from those versions are identical in every manner to the paper copies.
- B. Unless otherwise stated in the Bidding Documents, the Bidder may use and rely upon complete sets of Electronic Documents of the Bidding Documents, described in Paragraph 2.06.A above. However, Bidder assumes all risks associated with differences arising from transmission/receipt of Electronic Documents versions of Bidding Documents and reproductions prepared from those versions and, further, assumes all risks, costs, and responsibility associated with use of the Electronic Documents versions to derive information that is not explicitly contained in paper versions of the documents, and for Bidder's reliance upon such derived information.
- 1.

ARTICLE 3—QUALIFICATIONS OF BIDDERS

- 3.01 To demonstrate Bidder's qualifications to perform the Work, after submitting its Bid and within 5 days of Owner's or Engineer's request, Bidder must submit the following information:
 - A. Written evidence establishing its qualifications such as financial data, previous experience, and present commitments.
 - B. A written statement that Bidder is authorized to do business in the state where the Project is located, or a written certification that Bidder will obtain such authority prior to the Effective Date of the Contract. Such statement or certification, as applicable, shall be signed by the same officer of Bidder's company that signed the Bid.
 - C. Bidder's state (or other issuing entity) contractor license number, if applicable.
 - D. Subcontractor and Supplier qualification information.
 - E. Other required information regarding qualifications.
- 3.02 A Bidder's failure to submit required qualification information within the times indicated may disqualify Bidder from receiving an award of the Contract.
- 3.03 No requirement in this Article 3 to submit information will prejudice the right of Owner to seek additional pertinent information regarding Bidder's qualifications.
- 3.04 Bidders shall be experienced in the kind of Work to be performed, shall have the or be able to obtain construction equipment necessary for the Work, and shall possess sufficient capital to properly perform the Work within the time allowed. Bids received from Bidders who have previously failed to complete work within the time required, or who have previously performed similar work in an unsatisfactory manner, may be rejected. A Bid may be rejected if Bidder cannot show and document to Owner's satisfaction that Bidder has the necessary ability, facilities, equipment, and resources to commence the Work at the time prescribed and thereafter to

prosecute and complete the Work at the rate or within the times specified. A Bid may be rejected if Bidder is already obligated for the performance of other work which would delay the commencement, prosecution or completion of the Work.

ARTICLE 4—SITE AND OTHER AREAS; EXISTING SITE CONDITIONS; EXAMINATION OF SITE; OWNER'S SAFETY PROGRAM; OTHER WORK AT THE SITE

4.01 *Site and Other Areas*

- A. The Site is identified in the Bidding Documents, including in Specifications Section 01 11 00 – Summary of Work. By definition, the Site includes rights-of-way, easements, and other lands furnished by Owner for the use of the Contractor. Any additional lands required for temporary construction facilities, construction equipment, or storage of materials and equipment, and any access needed for such additional lands, are to be obtained and paid for by Contractor.

4.02 *Existing Site Conditions*

A. *Subsurface and Physical Conditions; Hazardous Environmental Conditions*

1. The Supplementary Conditions identify the following regarding existing conditions at or adjacent to the Site:
 - a. Those reports of explorations and tests of subsurface conditions at or adjacent to the Site that contain Technical Data.
 - b. Those drawings known to Owner of existing physical conditions at or adjacent to the Site, including those drawings depicting existing surface or subsurface structures at or adjacent to the Site (except Underground Facilities), that contain Technical Data.
 - c. Reports and drawings known to Owner relating to Hazardous Environmental Conditions that have been identified at or adjacent to the Site.
 - d. Technical Data contained in such reports and drawings.
2. Owner will make copies of reports and drawings referenced above available to any prospective Bidder on request. These reports and drawings are not part of the Contract Documents, but the Technical Data contained therein upon whose accuracy Bidder is entitled to rely, as provided in the General Conditions, has been identified and established in the Supplementary Conditions. Bidder is responsible for any interpretation or conclusion Bidder draws from any Technical Data or any other data, interpretations, opinions, or information contained in such reports or shown or indicated in such drawings.
3. If the Supplementary Conditions do not identify Technical Data, the default definition of Technical Data set forth in Article 1 of the General Conditions will apply.
4. *Geotechnical Baseline Report and Geotechnical Data Report:* The Bidding Documents contain a Geotechnical Baseline Report (GBR) and Geotechnical Data Report (GDR).
 - a. As set forth in Specifications Section 02 06 13 – Geotechnical Baseline Report, the GBR describes certain select subsurface conditions that are anticipated to be encountered by Contractor during construction in specified locations (“Baseline

Conditions”). Because it is an attachment to a Specifications section, the GBR is a Contract Document.

- b. The Baseline Conditions in the GBR are intended to reduce uncertainty and the degree of contingency in submitted Bids. However, Bidders cannot rely solely on the Baseline Conditions. Bids should be based on a comprehensive approach that includes an independent review and analysis of the GBR, all other Contract Documents, Technical Data, other available information, and observable surface conditions. Not all potential subsurface conditions are baselined.
 - c. Nothing in the GBR is intended to relieve Bidders of the responsibility to make their own determinations regarding construction costs, bidding strategies, and Bid prices, nor of the responsibility to select and be responsible for the means, methods, techniques, sequences, and procedures of construction, and for safety precautions and programs incident thereto.
 - d. As set forth in Specifications section 02 06 13 – Geotechnical Baseline Report, the GDR is a Contract Document containing data prepared by or for the Owner in support of the GBR.
- A. *Underground Facilities:* Underground Facilities are shown or indicated on the Drawings, pursuant to Paragraph 5.05 of the General Conditions, and not in the drawings referred to in Paragraph 5.02.A of these Instructions to Bidders. Information and data regarding the presence or location of Underground Facilities are not intended to be categorized, identified, or defined as Technical Data.
- B. *Adequacy of Data:* Provisions concerning responsibilities for the adequacy of data furnished to prospective Bidders with respect to subsurface conditions, other physical conditions, and Underground Facilities, and possible changes in the Bidding Documents due to differing or unanticipated subsurface or physical conditions appear in Paragraphs 5.03, 5.04, and 5.05 of the General Conditions. Provisions concerning responsibilities for the adequacy of data furnished to prospective Bidders with respect to a Hazardous Environmental Condition at the Site, if any, and possible changes in the Contract Documents due to any Hazardous Environmental Condition uncovered or revealed at the Site which was not shown or indicated in the Drawings or Specifications or identified in the Contract Documents to be within the scope of the Work, appear in Paragraph 5.06 of the General Conditions.

4.03 *Site Visit and Testing by Bidders*

- A. Bidder shall visit the Site and conduct a thorough visual examination of the Site and adjacent areas. During the visit the Bidder must not disturb any ongoing operations at the Site. The Site visit shall be conducted during normal working hours.
- B. Bidder is not required to conduct any subsurface testing, or exhaustive investigations of Site conditions.
- C. On request, and to the extent Owner has control over the Site, and schedule permitting, the Owner will provide Bidder general access to the Site to conduct such additional examinations, investigations, explorations, tests, and studies as Bidder deems necessary for preparing and submitting a successful Bid. Owner will not have any obligation to grant such access if doing so is not practical because of existing operations, security or safety concerns, or restraints on Owner’s authority regarding the Site.

- D. Bidder must comply with Laws and Regulations regarding excavation and location of utilities, obtain necessary permits, and comply with all terms and conditions established by Owner or by property owners or other entities controlling the Site with respect to schedule, access, existing operations, security, liability insurance, and applicable safety programs.
- E. Bidder must fill all holes and clean up and restore the Site to its former condition upon completion of such explorations, investigations, tests, and studies.

4.04 *Owner's Safety Program*

- A. Site visits and work at the Site may be governed by an Owner safety program. If an Owner safety program exists, it will be indicated in the Supplementary Conditions.

4.05 *Other Work at the Site*

- A. Reference is made to Article 8 of the Supplementary Conditions for the identification of the general nature of other work of which Owner is aware (if any) that is to be performed at the Site by Owner or others (such as utilities and other prime contractors) and relates to the Work contemplated by these Bidding Documents. If Owner is party to a written contract for such other work, then on request, Owner will provide to each Bidder access to examine such contracts (other than portions thereof related to price and other potentially confidential matters), if any.

ARTICLE 5—BIDDER'S REPRESENTATIONS AND CERTIFICATIONS

5.01 *It is the responsibility of each Bidder before submitting a Bid to:*

- A. examine and carefully study the Bidding Documents, and any data and reference items identified in the Bidding Documents;
- B. visit the Site, conduct a thorough, alert visual examination of the Site and adjacent areas, and become familiar with and satisfy itself as to the general, local, and Site conditions that may affect cost, progress, and performance of the Work;
- C. become familiar with and satisfy itself as to all Laws and Regulations that may affect cost, progress, and performance of the Work;
- D. carefully study all: (1) reports of explorations and tests of subsurface conditions at or adjacent to the Site and all drawings of physical conditions relating to existing surface or subsurface structures at the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings, and (2) reports and drawings relating to Hazardous Environmental Conditions, if any, at or adjacent to the Site that have been identified in the Supplementary Conditions, especially with respect to Technical Data in such reports and drawings;
- E. consider the information known to Bidder itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Bidding Documents; and the Site-related reports and drawings identified in the Bidding Documents, with respect to the effect of such information, observations, and documents on (1) the cost, progress, and performance of the Work; (2) the means, methods, techniques, sequences, and procedures of construction to be employed by Bidder; and (3) Bidder's safety precautions and programs;

- F. agree, based on the information and observations referred to in the preceding paragraph, that at the time of submitting its Bid no further examinations, investigations, explorations, tests, studies, or data are necessary for the determination of its Bid for performance of the Work at the price bid and within the times required, and in accordance with the other terms and conditions of the Bidding Documents;
- G. become aware of the general nature of the work to be performed by Owner and others at the Site that relates to the Work as indicated in the Bidding Documents;
- H. promptly give Engineer written notice of all conflicts, errors, ambiguities, or discrepancies that Bidder discovers in the Bidding Documents and confirm that the written resolution thereof by Engineer is acceptable to Bidder;
- I. determine that the Bidding Documents are generally sufficient to indicate and convey understanding of all terms and conditions for the performance and furnishing of the Work; and
- J. agree that the submission of a Bid will constitute an incontrovertible representation by Bidder that Bidder has complied with every requirement of this Article, that without exception the Bid and all prices in the Bid are premised upon performing and furnishing the Work required by the Bidding Documents.

ARTICLE 6—INTERPRETATIONS AND ADDENDA

- 6.01 Owner on its own initiative may issue Addenda to clarify, correct, supplement, or change the Bidding Documents.
- 6.02 Bidder shall submit all questions about the meaning or intent of the Bidding Documents to Engineer in writing. Contact information and submittal procedures for such questions are as follows:
 - HDR Engineering, Inc.
 - 50 Tice Blvd, Suite 210*
 - Woodcliff Lake, New Jersey 07677*
 - LAURA BARCA, PE
 - LAURA.BARCA@HDRINC.COM
- 6.03 Interpretations or clarifications considered necessary by Engineer in response to such questions will be issued by Addenda delivered to all Bidding Documents holders registered with the Issuing Office. Questions received less than seven days prior to the date for opening of Bids may not be answered.
- 6.04 Only responses set forth in an Addendum will be binding. Oral and other interpretations or clarifications will be without legal effect. Responses to questions are not part of the Contract

Documents unless set forth in an Addendum that expressly modifies or supplements the Bidding Documents.

- A. Questions received less than seven days prior to the date for opening of Bids may not be answered; questions must be received by Tuesday, March 18, 2025

ARTICLE 7—BID SECURITY

7.01 *Required Form and Amount of Bid Security*

- A. A Bid must be accompanied by bid security made payable to Owner in an amount of 5 percent of Bidder's maximum Bid price (determined by adding the base bid and all alternates) and in the form of a bid bond issued by a surety meeting the requirements of Paragraph 6.01 of the General Conditions.
- B. Such bid bond will be issued in the form included in the Bidding Documents.

7.02 *Bid Security of Successful Bidder*

- A. The Bid security of the apparent Successful Bidder will be retained until Owner awards the Contract to such Bidder, and such Bidder has signed the Contract, furnished the required Contract security, and met the other conditions of the Notice of Award, whereupon the Successful Bidder's bid security will be released.
- B. If the Successful Bidder fails to sign and deliver the Contract and furnish the required Contract security within the number of days, indicated in Paragraph 20.01 of these Instructions to Bidders, after the Notice of Award, Owner may consider Bidder to be in default, annul the Notice of Award, and the bid security of that Bidder will be forfeited.
- C. Upon Successful Bidder's default:
 - 1. When the bid security is a penal sum bid bond, the entire penal sum amount of the bid bond will be forfeit and due Owner.
 - 2. When the bid security is a damages form of bid bond, to the extent of Owner's damages will be forfeit and due Owner.
 - 3. If a type of bid security other than a bid bond is allowed and is furnished, the amount that will be forfeit and due Owner will be the same as for the form of bid bond included in the Bidding Documents. Owner will so notify the defaulting Bidder in writing of the annulment and the amount of the forfeiture, with documentation of the amount forfeited.
- D. Such forfeiture will be Owner's exclusive remedy if Bidder defaults.

7.03 *Bid Security of Bidders other than the Successful Bidder*

- A. The bid security of other Bidders that Owner believes to have a reasonable chance of receiving the award may be retained by Owner until the earlier of seven days after the Effective Date of the Contract or 61 days after the Bid opening, whereupon bid security furnished by such Bidders will be released.
- B. Bid security of other Bidders that Owner believes do not have a reasonable chance of receiving the award will be released within seven days after the bid opening.

- C. Release of Bid Security: Owner may release any Bidder's bid security by returning such bid security to the associated Bidder. When bid security is in the form of a bid bond, Owner may dispose of or destroy the bid bond and so advise the associated Bidder in writing that the bid bond has been released.

ARTICLE 8—CONTRACT TIMES

- 8.01 The number of days within which, or the dates by which, the Work is to be (a) substantially completed and (b) ready for final payment, and (c) Milestones (if any), are to be achieved are set forth in the Agreement.
- 8.02 Provisions for liquidated and special damages, if any, for failure to timely attain a Milestone, Substantial Completion, or completion of the Work in readiness for final payment, are set forth in the Agreement.

ARTICLE 9—SUBSTITUTE AND “OR EQUAL” ITEMS

- 9.01 The Contract for the Work, as awarded, will be on the basis of materials, equipment, and procedures specified or described in the Bidding Documents without consideration during the bidding and Contract award process of possible substitute or “or-equal” items or procedures. In cases in which the Contract allows the Contractor to request that Engineer authorize the use of a substitute or “or-equal” item of material or equipment or procedure, application for such acceptance may not be made to and will not be considered by Engineer until after the Effective Date of the Contract.
- 9.02 All prices that Bidder sets forth in its Bid will be based on the presumption that the Contractor will furnish the materials and equipment specified or described in the Bidding Documents, and will perform the Work in accordance with procedures indicated in the Bidding Documents, as supplemented by Addenda, if any. Assumptions regarding the possibility of post-bid approvals of “or-equal” or substitution requests are made at Bidder's sole risk.

ARTICLE 10—SUBCONTRACTORS, SUPPLIERS, AND OTHERS

- 10.01 A Bidder must be prepared to retain specific Subcontractors and Suppliers for the performance of the Work if required to do so in the Specifications or elsewhere in the Bidding Documents. If a prospective Bidder objects to retaining any such Subcontractor or Supplier and the concern is not relieved by an Addendum, then the prospective Bidder should not submit a Bid.
- 10.02 The apparent Successful Bidder, and any other Bidder so requested by Owner or Engineer, must submit to Owner (with a copy to Engineer) a list of the Subcontractors and Suppliers proposed for the following portions of the Work within five days after the bid opening:
- 10.03 If requested by Owner or Engineer, such list must be accompanied by an experience statement with pertinent information regarding similar projects and other evidence of qualification for each such Subcontractor or Supplier. If Owner or Engineer, after due investigation, has reasonable objection to any proposed Subcontractor or Supplier, Owner may, before the Notice of Award is given, request apparent Successful Bidder to submit an acceptable substitute, in which case apparent Successful Bidder will submit a substitute, Bidder's Bid price will be increased (or

decreased) by the difference in cost occasioned by such substitution, and Owner may consider such price adjustment in evaluating Bids and awarding the Contract.

- 10.04 If apparent Successful Bidder declines to make a requested substitution, Owner may award the Contract to another Bidder, consistent with the basis for evaluating the Bids for award as set forth in these Instructions to Bidders, that proposes to use acceptable Subcontractors and Suppliers. Declining to make requested substitutions will constitute grounds for forfeiture of the bid security of any Bidder. Any Subcontractor or Supplier, so listed and against which Owner or Engineer makes no written objection prior to issuance of the Notice of Award will be deemed acceptable to Owner and Engineer subject to subsequent revocation of such acceptance as provided in Paragraph 7.07 of the General Conditions.

ARTICLE 11—PREPARATION OF BID

- 11.01 The Bid Form is included with the Bidding Documents.
- A. All blanks on the Bid Form must be completed in ink and the Bid Form signed in ink. Erasures or alterations must be initialed in ink by the person signing the Bid Form. A Bid price must be indicated for each section, Bid item, alternate, adjustment unit price item, and unit price item listed therein.
 - B. If the Bid Form expressly indicates that submitting pricing on a specific alternate item is optional, and Bidder elects to not furnish pricing for such optional alternate item, then Bidder may enter the words “No Bid” or “Not Applicable.”
- 11.02 If Bidder has obtained the Bidding Documents as Electronic Documents, then Bidder shall prepare its Bid on a paper copy of the Bid Form printed from the Electronic Documents version of the Bidding Documents. The printed copy of the Bid Form must be clearly legible, printed on 8.5inch by 11-inch paper and as closely identical in appearance to the Electronic Document version of the Bid Form as may be practical. The Owner reserves the right to accept Bid Forms which nominally vary in appearance from the original paper version of the Bid Form, providing that all required information and submittals are included with the Bid.
- 11.03 A Bid by a corporation must be signed in the corporate name by a corporate officer (whose title must appear under the signature), accompanied by evidence of authority to sign. The corporate address and state of incorporation must be shown.
- 11.04 A Bid by a partnership must be executed in the partnership name and signed by a partner (whose title must appear under the signature), accompanied by evidence of authority to sign. The official address of the partnership must be shown.
- 11.05 A Bid by a limited liability company must be signed in the name of the firm by a member or other authorized person and accompanied by evidence of authority to sign. The state of formation of the firm and the official address of the firm must be shown.
- 11.06 A Bid by an individual must show the Bidder’s name and official address.
- 11.07 A Bid by a joint venture must be signed by an authorized representative of each joint venturer in the manner indicated on the Bid Form. The joint venture must have been formally established prior to submittal of a Bid, and the official address of the joint venture must be shown.
- 11.08 All names must be printed in ink below the signatures.

- 11.09 The Bid must contain an acknowledgment of receipt of all Addenda, the numbers of which must be filled in on the Bid Form.
- 11.10 Postal and e-mail addresses and telephone number for communications regarding the Bid must be indicated on the Bid Form.
- 11.11 The Bid must contain evidence of Bidder's authority to do business in the state where the Project is located, or Bidder must certify in writing that it will obtain such authority within the time for acceptance of Bids and attach such certification to the Bid.
- 11.12 If Bidder is required to be licensed to submit a Bid or perform the Work in the state where the Project is located, the Bid must contain evidence of Bidder's licensure, or Bidder must certify in writing that it will obtain such licensure within the time for acceptance of Bids and attach such certification to the Bid. Bidder's state contractor license number, if any, must also be shown on the Bid Form.

ARTICLE 12—BASIS OF BID

12.01 *Unit Price*

- A. Bidders must submit a Bid on a unit price basis for each item of Work listed in the unit price section of the Bid Form.
- B. The "Bid Price" (sometimes referred to as the extended price) for each item of Unit Price Work will be the product of the "Estimated Quantity", which Owner or its representative has set forth in the Bid Form, for the item and the corresponding "Bid Unit Price" offered by the Bidder. The total of all unit price bid items will be the sum of these "Bid Prices"; such total will be used by Owner for Bid comparison purposes. The final quantities and final Contract Price will be determined in accordance with Paragraph 13.03 of the General Conditions.
- C. Discrepancies between the multiplication of units of Work and unit prices will be resolved in favor of the unit prices. Discrepancies between the indicated sum of any column of figures and the correct sum thereof will be resolved in favor of the correct sum.

12.02 *Cash Allowances*

- A. For cash allowances the bid price (for items other than cash allowances) must include such amounts as Bidder deems proper for Contractor's overhead, handling and installation costs, profit, and other expenses on account of cash allowances, if any, named in the Contract Documents, in accordance with Paragraph 13.02.B of the General Conditions.

ARTICLE 13—SUBMITTAL OF BID

- 13.01 The Bidding Documents include one separate, unbound copy of the Bid Form, and, where required, the Bid Bond Form and other supplements to the Bid Form. The unbound copy of the Bid Form and supplements (if any) is to be completed and submitted with the Bid security and the other documents required with the Bid by Article 2 of the Bid Form.
- 13.02 A Bid must be received no later than the date and time prescribed and at the place indicated in the Advertisement or invitation to bid and must be enclosed in a plainly marked package with the Project title, and, if applicable, the designated portion of the Project for which the Bid is submitted, and the name and address of Bidder, and must be accompanied by the Bid security and other required documents. If a Bid is sent by mail or other delivery method, the sealed

envelope containing the Bid must be enclosed in a separate package plainly marked on the outside with the notation "BID ENCLOSED." A mailed Bid shall be addressed to Eileen Astorino, Town of Warwick Town Clerk, 132 Kings Highway, Warwick, New York 10990.

- 13.03 Bids received after the date and time prescribed for the opening of Bids, or not submitted at the correct location or in the designated manner, will not be accepted and will be returned to the Bidder unopened. Owner accepts no responsibility for delays in returning Bids submitted or delivered to the incorrect location.

ARTICLE 14—MODIFICATION AND WITHDRAWAL OF BID

- 14.01 An unopened Bid may be withdrawn by an appropriate document duly signed in the same manner that a Bid must be signed and delivered to the place where Bids are to be submitted, prior to the date and time established in the Bidding Documents for the receipt of Bids. Upon receipt of such notice, the unopened Bid will be returned to the Bidder.
- 14.02 If a Bidder wishes to modify its Bid prior to Bid opening, Bidder must withdraw its initial Bid in the manner specified in Paragraph 15.01 of this Article and submit a new Bid prior to the date and time for established in the Bidding Documents the receipt of Bids.
- 14.03 If, within [24] hours after Bids are opened, any Bidder files a duly signed, written notice with Owner and promptly thereafter demonstrates to the reasonable satisfaction of Owner that there was a material and substantial mistake in the preparation of its Bid, the Bidder may withdraw its Bid, and the bid security will be returned. Thereafter, if the Work is rebid, the Bidder will be disqualified from further bidding on the Work.

ARTICLE 15—OPENING OF BIDS

- 15.01 Bids will be opened at the time and place indicated in the Advertisement or invitation to bid and, unless obviously non-responsive, will be read aloud publicly. An abstract of the amounts of the base Bids and major alternates, if any, will be made available to Bidders after the opening of Bids.

ARTICLE 16—BIDS TO REMAIN SUBJECT TO ACCEPTANCE

- 16.01 All Bids will remain subject to acceptance for the period of time stated in the Bid Form, but Owner may, in its sole discretion, release any Bid and return the Bid security prior to the end of this period.

ARTICLE 17—EVALUATION OF BIDS AND AWARD OF CONTRACT

- 17.01 Owner reserves the right to reject any or all Bids, including without limitation, nonconforming, nonresponsive, unbalanced, or conditional Bids. Owner also reserves the right to waive all minor Bid informalities not involving price, time, or changes in the Work.
- 17.02 Owner will reject the Bid of any Bidder that Owner finds, after reasonable inquiry and evaluation, to not be responsible. Owner may reject the Bid of any Bidder that fails to demonstrate appropriate qualifications, experience, and resources for the Work, in accordance with Article 3 of these Instructions to Bidders.
- 17.03 If Bidder purports to add terms or conditions to its Bid, takes exception to any provision of the Bidding Documents, or attempts to alter the contents of the Contract Documents for purposes of

the Bid, whether in the Bid itself or in a separate communication to Owner or Engineer, then Owner will reject the Bid as nonresponsive.

17.04 *Basis for Award of Contract*

- A. If Owner awards the contract for the Work, such award will be to the responsible Bidder submitting the lowest-priced, responsive Bid that has not otherwise been disqualified.

17.05 *Evaluation of Bids*

- A. In evaluating Bids, Owner will consider whether the Bids comply with the prescribed requirements, and such alternates, unit prices, and other data, as may be requested in the Bid Form or elsewhere in the Bidding Documents, or prior to the Notice of Award.
 - B. *Unit Price Work*: For the determination of the apparent low-price Bid when unit price bids are submitted, Bids will be compared on the basis of the total of the products of the estimated quantity of each item and unit price bid for that item, together with amount(s) of lump sum items (if any).
- 17.06** In evaluating whether a Bidder is responsible, Owner will consider the qualifications, experience, and resources of the Bidder and may consider the qualifications, experience, and resources of Subcontractors and Suppliers proposed for those portions of the Work for which the identity of Subcontractors and Suppliers must be submitted as provided in the Bidding Documents.
- 17.07** Owner, with or without Engineer's assistance, may conduct such investigations as Owner deems necessary to establish the responsibility, qualifications, and financial ability of Bidders and any proposed Subcontractors or Suppliers.

ARTICLE 18—BONDS AND INSURANCE

- 18.01** Paragraph 2.01 and Article 6 of the General Conditions, as may be modified by the Supplementary Conditions, set forth Owner's requirements as to performance and payment bonds, other required bonds (if any), and insurance. When the Successful Bidder delivers the signed Agreement to Owner (or Owner's representative), it must be accompanied by required bonds and insurance documentation.

ARTICLE 19—SIGNING OF AGREEMENT

- 19.01** When Owner issues a Notice of Award to the Successful Bidder, it will be accompanied by the unsigned counterparts of the Agreement, along with the other Contract Documents as identified in the Agreement. Within 15 days thereafter, Successful Bidder must execute and deliver the required number of counterparts of the Agreement and required bonds and insurance documentation (as required by the Contract Documents) to Owner. Within 10 days thereafter, Owner will deliver one fully signed counterpart of the Agreement to Successful Bidder, together with printed and electronic copies of the Contract Documents as stated in Paragraph 2.02 of the General Conditions.

ARTICLE 20—SALES AND USE TAXES

- 20.01** Owner is exempt from New York state sales and use taxes on materials and equipment to be incorporated in the Work. Said taxes must not be included in the Bid. Refer to Paragraph SC-7.10 of the Supplementary Conditions for additional information.

BID FORM

FOR CONSTRUCTION CONTRACT

The terms used in this Bid with initial capital letters have the meanings stated in the Instructions to Bidders, the General Conditions, and the Supplementary Conditions.

ARTICLE 1—OWNER AND BIDDER

- 1.01 This Bid is submitted to: **Town of Warwick Town Hall, Clerks Office, 132 Kings Highway, Warwick, New York 10990**, herein referred to as the Owner.
- 1.02 The undersigned Bidder proposes and agrees, if this Bid is accepted, to enter into an Agreement with Owner in the form included in the Bidding Documents to perform all Work as specified or indicated in the Bidding Documents for the prices and within the times indicated in this Bid and in accordance with the other terms and conditions of the Bidding Documents.

ARTICLE 2—ATTACHMENTS TO THIS BID

- 2.01 The following documents are submitted with and made a condition of this Bid:
 - A. Advertisement;
 - B. Instructions to Bidders;
 - C. Bid Form;
 - D. Information to Bidders;
 - E. Bid Tabulation Spreadsheet;
 - F. Qualification Statement with supporting data;
 - G. Agreement;
 - H. Bid Bond;
 - I. Certification of Federal Aid Contracts;
 - J. Disclosure of Lobby Activities;
 - K. Statement of Non-Collusion;
 - L. DBE Utilization Requirements;
 - M. Certificate of Non-Segregated Facilities;
 - N. Certification of Limited Foreign Involvement;
 - O. General Conditions,
 - P. Supplementary Conditions;
 - Q. Special Specifications;
 - R. Prevailing Wage Rate Information;
 - S. Performance Bond;
 - T. Payment Bond; and
 - U. Drawings for the General Work consisting of Contract.

ARTICLE 3—TIME OF COMPLETION

- 3.01 Bidder agrees that the Work will be substantially complete and will be completed and ready for final payment in accordance with Paragraph 15.06 of the General Conditions on or before the dates or within the number of days indicated in the Agreement.
- 3.02 Bidder accepts the provisions of the Agreement as to liquidated damages.

ARTICLE 4—BIDDER’S ACKNOWLEDGEMENTS: ACCEPTANCE PERIOD, INSTRUCTIONS, AND RECEIPT OF ADDENDA

4.01 *Bid Acceptance Period*

- A. This Bid will remain subject to acceptance for 60 days after the Bid opening, or for such longer period of time that Bidder may agree to in writing upon request of Owner.
- B. Bidder will sign and deliver the required number of counterparts of the Agreement with the Bonds and other documents required by the Bidding Requirements within 15 days after the date of Owner’s Notice of Award.

4.02 *Instructions to Bidders*

- A. Bidder accepts all of the terms and conditions of the Instructions to Bidders, including without limitation those dealing with the disposition of Bid security.

4.03 *Receipt of Addenda*

- A. Bidder hereby acknowledges receipt of the following Addenda:

Addendum Number	Addendum Date

ARTICLE 5—BASIS OF BID

5.01 Bidder will complete the Work in accordance with the Contract Documents for the following prices as shown on the Bid Tabulation Spreadsheet.

5.02 Communication concerning this bid shall be addressed to:

HDR Engineering, Inc.
50 Tice Blvd, Suite 210
Woodcliff Lake, New Jersey 07677
Attn: Laura Barca, PE
Laura.Barca@hdrinc.com

ARTICLE 6—BIDDER'S REPRESENTATIONS AND CERTIFICATIONS

6.01 *Bidder's Representations*

A. In submitting this Bid, Bidder represents the following:

1. Bidder has examined and carefully studied the Bidding Documents, including Addenda.
2. Bidder has visited the Site, conducted a thorough visual examination of the Site and adjacent areas, and become familiar with the general, local, and Site conditions that may affect cost, progress, and performance of the Work.
3. Bidder is familiar with all Laws and Regulations that may affect cost, progress, and performance of the Work.
4. Bidder has carefully studied the reports of explorations and tests of subsurface conditions at or adjacent to the Site and the drawings of physical conditions relating to existing surface or subsurface structures at the Site that have been identified in the Supplementary Conditions, with respect to the Technical Data in such reports and drawings.
5. Bidder has carefully studied the reports and drawings relating to Hazardous Environmental Conditions, if any, at or adjacent to the Site that have been identified in the Supplementary Conditions, with respect to Technical Data in such reports and drawings.
6. Bidder has considered the information known to Bidder itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Bidding Documents; and the Technical Data identified in the Supplementary Conditions or by definition, with respect to the effect of such information, observations, and Technical Data on (a) the cost, progress, and performance of the Work; (b) the means, methods, techniques, sequences, and procedures of construction to be employed by Bidder, if selected as Contractor; and (c) Bidder's (Contractor's) safety precautions and programs.
7. Based on the information and observations referred to in the preceding paragraph, Bidder agrees that no further examinations, investigations, explorations, tests, studies, or data are necessary for the performance of the Work at the Contract Price, within the Contract Times, and in accordance with the other terms and conditions of the Contract.

8. Bidder is aware of the general nature of work to be performed by Owner and others at the Site that relates to the Work as indicated in the Bidding Documents.
9. Bidder has given Engineer written notice of all conflicts, errors, ambiguities, or discrepancies that Bidder has discovered in the Bidding Documents, and of discrepancies between Site conditions and the Contract Documents, and the written resolution thereof by Engineer is acceptable to Contractor.
10. The Bidding Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance and furnishing of the Work.
11. The submission of this Bid constitutes an incontrovertible representation by Bidder that without exception the Bid and all prices in the Bid are premised upon performing and furnishing the Work required by the Bidding Documents.

6.02 *Bidder's Certifications*

A. The Bidder certifies the following:

1. This Bid is genuine and not made in the interest of or on behalf of any undisclosed individual or entity and is not submitted in conformity with any collusive agreement or rules of any group, association, organization, or corporation.
2. Bidder has not directly or indirectly induced or solicited any other Bidder to submit a false or sham Bid.
3. Bidder has not solicited or induced any individual or entity to refrain from bidding.
4. Bidder has not engaged in corrupt, fraudulent, collusive, or coercive practices in competing for the Contract. For the purposes of this Paragraph 8.02.A:
 - a. Corrupt practice means the offering, giving, receiving, or soliciting of anything of value likely to influence the action of a public official in the bidding process.
 - b. Fraudulent practice means an intentional misrepresentation of facts made (a) to influence the bidding process to the detriment of Owner, (b) to establish bid prices at artificial non-competitive levels, or (c) to deprive Owner of the benefits of free and open competition.
 - c. Collusive practice means a scheme or arrangement between two or more Bidders, with or without the knowledge of Owner, a purpose of which is to establish bid prices at artificial, non-competitive levels.
 - d. Coercive practice means harming or threatening to harm, directly or indirectly, persons or their property to influence their participation in the bidding process or affect the execution of the Contract.

BIDDER hereby submits this Bid as set forth above:

Bidder:

(typed or printed name of organization)

By:

(individual's signature)

Name:

(typed or printed)

Title:

(typed or printed)

Date:

(typed or printed)

If Bidder is a corporation, a partnership, or a joint venture, attach evidence of authority to sign.

Attest:

(individual's signature)

Name:

(typed or printed)

Title:

(typed or printed)

Date:

(typed or printed)

Bidder's Address for giving notices:

Bidder's Contact Person:

Name:

(typed or printed)

Title:

(typed or printed)

Phone:

Email:

Address:

Bidder's Contractor License No.: (if applicable)

INFORMATION TO BIDDERS

FOR

BALL ROAD CULVERT REPLACEMENT

BIDDERS SHALL NOTE:

The item numbers listed in the Contract Documents and Bid Tabulation form refer to New York State Department of Transportation Standard Specifications Book dated January 1, 2025. The contractor shall become familiar with the NYSDOT Specifications and the NYSDOT Standard sheets prior to preparing a bid for this project. The New York State DOT specifications are available for viewing on the NYSDOT website or for purchase from the NYSDOT Plan Sales Office.

The cost of all work, labor, materials, plant and equipment noted in the said items shall be deemed to be included in the prices bid for the respective scheduled items.

The Standard Specification's Measurement and Payment Sections for contract items below shall be as provided in their respective Standard Specification unless otherwise noted in the Bid Tabulation for the item to be deemed included under other scheduled contract bid items.

Town of Warwick, Orange County, New York
Ball Road Culvert Replacement
BID TABULATION

Contractor Name:

No.	ITEM NUMBER	ITEM	UNIT	UNIT PRICE	ESTIMATED QUANTITY	BID AMOUNT
1	201.06	CLEARING AND GRUBBING	LS		1	
2	202.19	REMOVAL OF SUBSTRUCTURES	CY		45	
3	203.02	UNCLASSIFIED EXCAVATION AND DISPOSAL	CY		180	
4	203.03	EMBANKMENT IN PLACE (CULVERT)	CY		1310	
5	203.07	SELECT GRANULAR FILL	CY		40	
6	207.21	GEOTEXTILE SEPARATION	SY		175	
7	209.1003	SEED AND MULCH - TEMPORARY	SY		100	
8	209.13	SILT FENCE-TEMPORARY	LF		410	
9	209.1901	ROLLED EROSION CONTROL PRODUCT, CLASS II TYPE A, INTERMEDIATE	SY		100	
10	201.3001	REMOVAL AND DISPOSAL OF CONCRETE-ENCASED PIPE ACM	LF		5	
11	304.12	SUBBASE COURSE, TYPE 2 (12" DEPTH)	CY		100	
12	404.0683	6.3 F3 TOP COURSE ASPHALT, 80 SERIES COMPACTION (1" DEPTH)	TON		25	
13	404.1279	12.5 F9 BINDER COURSE ASPHALT, 70 SERIES COMPACTION (2" DEPTH)	TON		45	
14	404.3779	37.5 F9 BASE COURSE ASPHALT, 70 SERIES COMPACTION (4" DEPTH)	TON		75	
15	407.0102	DILUTED TACK CACT	GAL		350	
16	552.17	SHIELDS AND SHORING (SOE)	SF		1320	
17	553.030001	TEMPORARY WATERWAY DIVERSION STRUCTURE	EACH		1	
18	556.0202	EPOXY-COATED BAR REINFORCEMENT FOR STRUCTURES (REBAR IN CLOSURE POUR #5 BARS)	LB		321	
19	556.0202	EPOXY-COATED BAR REINFORCEMENT FOR STRUCTURES (WINGWALL UNIT REINFORCEMENT #4 BARS)	LB		1123	
20	562.0101	PRECAST THREE SIDE STRUCTURE	SY		65	
21	562.03	WINGWALL WITH FOOTING (CONCRETE)	SY		46	
22	595.98200018	SPRAY-APPLIED WATERPROOF MEMBRANE	SF		585	
23	606.10	BOX BEAM GUIDE RAILING	LF		685	
24	606.100002	BOX BEAM GUIDE RAILING (SHOP BENT)	LF		140	
25	606.100003	BOX BEAM GUIDE RAILING (SHOP MITERED)	LF		45	
26	606.120101	BOX BEAM END PIECE	EA		1	
27	606.120201	BOX BEAM GUIDE RAILING , END ASSEMBLY, TYPE IIA	EA		3	
28	606.71000015	REMOVE AND DISPOSE OF BOX BEAM GUIDE RAIL AND STORE POSTS	LF		780	
29	606.22	ANCHORAGE UNITS FOR CORRUGATED BEAM GUIDE RAILING	EA		11	
30	608.020102	ASPHALT SIDEWALKS, DRIVEWAYS AND BICYCLE PATHS,AND VEGETATION CONTROL STRIPS	TON		80	
31	610.1402	4" TOPSOIL ROADSIDE	CY		30	

Town of Warwick, Orange County, New York
Ball Road Culvert Replacement
BID TABULATION

Contractor Name: _____

No.	ITEM NUMBER	ITEM	UNIT	UNIT PRICE	ESTIMATED QUANTITY	BID AMOUNT
32	610.1601	TURF ESTABLISHMENT - ROADSIDE	SY		270	
33	615.01010108	MATERIAL FOR STREAM BED ESTABLISHMENT	CY		50	
34	619.01	BASIC WORK ZONE TRAFFIC CONTROL INCLUDING FLAGGER	LS		1	
35	619.04	TYPE III CONSTRUCTION BARRICADES	EA		5	
36	619.1701	TEMPORARY CONCRETE BARRIER	LF		100	
37	620.04	STONE FILL - MEDIUM (GENERALLY 100 LB MIN., 6")	CY		10	
38	620.0801	BEDDING MATERIAL, TYPE 1	CY		10	
39	623.12	CRUSHED BEDDING MATERIAL	CY		25	
40	625.01	SURVEY OPERATIONS	LS		1	
41	627.5014001	CUTTING PAVEMENT	LF		130	
42	645.13080010	REINSTALL SIGN PANELS ASSEMBLIES	SF		2	
43	645.81	TYPE A SIGN POSTS	EA		1	
44	699.040001	MOBILIZATION/DEMOBILIZATION	LS		1	
45		Dewatering 24/7 including pump and generator rent	Mos		4	

TOTAL AMOUNT OF BID:

(value in numerals)

_____ Dollars
 (value in words)

and _____ Cents.
 (value in words cont.)

Signed: _____

Company: _____

Title: _____

Date: _____

QUALIFICATIONS STATEMENT

ARTICLE 1—GENERAL INFORMATION

1.01 Provide contact information for the Business:

Legal Name of Business:			
Corporate Office			
Name:		Phone number:	
Title:		Email address:	
Business address of corporate office:			
Local Office			
Name:		Phone number:	
Title:		Email address:	
Business address of local office:			

1.02 Provide information on the Business's organizational structure:

Form of Business:	☐ Sole Proprietorship ☐ Partnership ☐ Corporation		
☐ Limited Liability Company ☐ Joint Venture comprised of the following companies:			
1.			
2.			
3.			
Provide a separate Qualification Statement for each Joint Venturer.			
Date Business was formed:		State in which Business was formed:	
Is this Business authorized to operate in the Project location?		☐ Yes ☐ No ☐ Pending	

1.03 Identify all businesses that own Business in whole or in part (25% or greater), or that are wholly or partly (25% or greater) owned by Business:

Name of business:		Affiliation:	
Address:			
Name of business:		Affiliation:	
Address:			

Name of business:		Affiliation:	
Address:			

1.04 Provide information regarding the Business's officers, partners, and limits of authority.

Name:		Title:	
Authorized to sign contracts:	☐ Yes ☐ No	Limit of Authority:	\$
Name:		Title:	
Authorized to sign contracts:	☐ Yes ☐ No	Limit of Authority:	\$
Name:		Title:	
Authorized to sign contracts:	☐ Yes ☐ No	Limit of Authority:	\$
Name:		Title:	

ARTICLE 2—LICENSING

2.01 Provide information regarding licensure for Business:

Name of License:			
Licensing Agency:			
License No:		Expiration Date:	
Name of License:			
Licensing Agency:			
License No:		Expiration Date:	

ARTICLE 3—DIVERSE BUSINESS CERTIFICATIONS

3.01 Provide information regarding Business's Diverse Business Certification, if any. Provide evidence of current certification.

Certification	Certifying Agency	Certification Date
☐ Disadvantaged Business Enterprise		
☐ Minority Business Enterprise		
☐ Woman-Owned Business Enterprise		
☐ Small Business Enterprise		
☐ Disabled Business Enterprise		
☐ Veteran-Owned Business Enterprise		
☐ Service-Disabled Veteran-Owned Business		
☐ HUBZone Business (Historically Underutilized) Business		

☐ Other			
☐ None			

ARTICLE 4—SAFETY

4.01 Provide information regarding Business's safety organization and safety performance.

Name of Business's Safety Officer:		
Safety Certifications		
Certification Name	Issuing Agency	Expiration

4.02 Provide Worker's Compensation Insurance Experience Modification Rate (EMR), Total Recordable Frequency Rate (TRFR) for incidents, and Total Number of Recorded Manhours (MH) for the last 3 years and the EMR, TRFR, and MH history for the last 3 years of any proposed Subcontractor(s) that will provide Work valued at 10% or more of the Contract Price. Provide documentation of the EMR history for Business and Subcontractor(s).

Year									
Company	EMR	TRFR	MH	EMR	TRFR	MH	EMR	TRFR	MH

ARTICLE 5—FINANCIAL

5.01 Provide information regarding the Business's financial stability. Provide the most recent audited financial statement, and if such audited financial statement is not current, also provide the most current financial statement.

Financial Institution:			
Business address:			
Date of Business's most recent financial statement:		☐ Attached	
Date of Business's most recent audited financial statement:		☐ Attached	
Financial indicators from the most recent financial statement			
Contractor's Current Ratio (Current Assets ÷ Current Liabilities)			
Contractor's Quick Ratio ((Cash and Cash Equivalents + Accounts Receivable + Short Term Investments) ÷ Current Liabilities)			

ARTICLE 6—SURETY INFORMATION

- 6.01 Provide information regarding the surety company that will issue required bonds on behalf of the Business, including but not limited to performance and payment bonds.

Surety Name:			
Surety is a corporation organized and existing under the laws of the state of:			
Is surety authorized to provide surety bonds in the Project location?	☐ Yes ☐ No		
Is surety listed in “Companies Holding Certificates of Authority as Acceptable Sureties on Federal Bonds and as Acceptable Reinsuring Companies” published in Department Circular 570 (as amended) by the Bureau of the Fiscal Service, U.S. Department of the Treasury?			
☐ Yes ☐ No			
Mailing Address (principal place of business):			
Physical Address (principal place of business):			
Phone (main):		Phone (claims):	

ARTICLE 7—INSURANCE

- 7.01 Provide information regarding Business’s insurance company(s), including but not limited to its Commercial General Liability carrier. Provide information for each provider.

Name of insurance provider, and type of policy (CLE, auto, etc.):			
Insurance Provider	Type of Policy (Coverage Provided)		
Are providers licensed or authorized to issue policies in the Project location?		☐ Yes ☐ No	
Does provider have an A.M. Best Rating of A-VII or better?		☐ Yes ☐ No	
Mailing Address (principal place of business):			
Physical Address (principal place of business):			

Phone (main):		Phone (claims):	
---------------	--	-----------------	--

ARTICLE 8—CONSTRUCTION EXPERIENCE

8.01 Provide information that will identify the overall size and capacity of the Business.

Average number of current full-time employees:	
Estimate of revenue for the current year:	
Estimate of revenue for the previous year:	

8.02 Provide information regarding the Business's previous contracting experience.

Years of experience with projects like the proposed project:				
As a general contractor:		As a joint venturer:		
Has Business, or a predecessor in interest, or an affiliate identified in Paragraph 1.03:				
Been disqualified as a bidder by any local, state, or federal agency within the last 5 years? ☐ Yes ☐ No				
Been barred from contracting by any local, state, or federal agency within the last 5 years? ☐ Yes ☐ No				
Been released from a bid in the past 5 years? ☐ Yes ☐ No				
Defaulted on a project or failed to complete any contract awarded to it? ☐ Yes ☐ No				
Refused to construct or refused to provide materials defined in the contract documents or in a change order? ☐ Yes ☐ No				
Been a party to any currently pending litigation or arbitration? ☐ Yes ☐ No				
Provide full details in a separate attachment if the response to any of these questions is Yes.				

8.03 List all projects currently under contract in Schedule A and provide indicated information.

8.04 List a minimum of three and a maximum of six projects completed in the last 5 years in Schedule B and provide indicated information to demonstrate the Business's experience with projects similar in type and cost of construction.

8.05 In Schedule C, provide information on key individuals whom Business intends to assign to the Project. Provide resumes for those individuals included in Schedule C. Key individuals include the Project Manager, Project Superintendent, Quality Manager, and Safety Manager. Resumes may be provided for Business's key leaders as well.

ARTICLE 9—REQUIRED ATTACHMENTS

9.01 Provide the following information with the Statement of Qualifications:

- A. If Business is a Joint Venture, separate Qualifications Statements for each Joint Venturer, as required in Paragraph 1.02.
- B. Diverse Business Certifications if required by Paragraph 3.01.
- C. Certification of Business's safety performance if required by Paragraph 4.02.

- D. Financial statements as required by Paragraph 5.01.
- E. Attachments providing additional information as required by Paragraph 8.02.
- F. Schedule A (Current Projects) as required by Paragraph 8.03.
- G. Schedule B (Previous Experience with Similar Projects) as required by Paragraph 8.04.
- H. Schedule C (Key Individuals) and resumes for the key individuals listed, as required by Paragraph 8.05.
- I. Additional items as pertinent.

This Statement of Qualifications is offered by:

Business:

(typed or printed name of organization)

By:

(individual's signature)

Name:

(typed or printed)

Title:

(typed or printed)

Date:

(date signed)

(If Business is a corporation, a partnership, or a joint venture, attach evidence of authority to sign.)

Attest:

(individual's signature)

Name:

(typed or printed)

Title:

(typed or printed)

Address for giving notices:

Designated Representative:

Name:

(typed or printed)

Title:

(typed or printed)

Address:

Phone:

Email:

Schedule A—Current Projects

Name of Organization					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					

Schedule B—Previous Experience with Similar Projects

Name of Organization					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					

Schedule B—Previous Experience with Similar Projects

Name of Organization					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					
Project Owner			Project Name		
General Description of Project					
Project Cost			Date Project Completed		
Key Project Personnel	Project Manager	Project Superintendent	Safety Manager	Quality Control Manager	
Name					
Reference Contact Information (listing names indicates approval to contacting the names individuals as a reference)					
	Name	Title/Position	Organization	Telephone	Email
Owner					
Designer					
Construction Manager					

Schedule C—Key Individuals

Project Manager			
Name of individual			
Years of experience as project manager			
Years of experience with this organization			
Number of similar projects as project manager			
Number of similar projects in other positions			
Current Project Assignments			
Name of assignment		Percent of time used for this project	Estimated project completion date
Reference Contact Information (listing names indicates approval to contact named individuals as a reference)			
Name		Name	
Title/Position		Title/Position	
Organization		Organization	
Telephone		Telephone	
Email		Email	
Project		Project	
Candidate's role on project		Candidate's role on project	
Project Superintendent			
Name of individual			
Years of experience as project superintendent			
Years of experience with this organization			
Number of similar projects as project superintendent			
Number of similar projects in other positions			
Current Project Assignments			
Name of assignment		Percent of time used for this project	Estimated project completion date
Reference Contact Information (listing names indicates approval to contact named individuals as a reference)			
Name		Name	
Title/Position		Title/Position	
Organization		Organization	
Telephone		Telephone	
Email		Email	
Project		Project	
Candidate's role on project		Candidate's role on project	

Safety Manager			
Name of individual			
Years of experience as project manager			
Years of experience with this organization			
Number of similar projects as project manager			
Number of similar projects in other positions			
Current Project Assignments			
Name of assignment		Percent of time used for this project	Estimated project completion date
Reference Contact Information (listing names indicates approval to contact named individuals as a reference)			
Name		Name	
Title/Position		Title/Position	
Organization		Organization	
Telephone		Telephone	
Email		Email	
Project		Project	
Candidate's role on project		Candidate's role on project	
Quality Control Manager			
Name of individual			
Years of experience as project superintendent			
Years of experience with this organization			
Number of similar projects as project superintendent			
Number of similar projects in other positions			
Current Project Assignments			
Name of assignment		Percent of time used for this project	Estimated project completion date
Reference Contact Information (listing names indicates approval to contact named individuals as a reference)			
Name		Name	
Title/Position		Title/Position	
Organization		Organization	
Telephone		Telephone	
Email		Email	
Project		Project	
Candidate's role on project		Candidate's role on project	

AGREEMENT

BETWEEN OWNER AND CONTRACTOR
FOR CONSTRUCTION CONTRACT (STIPULATED PRICE)

This Agreement is by and between _____ (“Owner”) and
_____ (“Contractor”).

Terms used in this Agreement have the meanings stated in the General Conditions and the Supplementary Conditions.

Owner and Contractor hereby agree as follows:

ARTICLE 1—WORK

1.01 Contractor shall complete all Work as specified or indicated in the Contract Documents. The Work is generally described as follows:

ARTICLE 2—THE PROJECT

2.01 The Project, of which the Work under the Contract Documents is a part, is generally described as follows: Ball Road Culvert Replacement

ARTICLE 3—ENGINEER

3.01 Not used.

ARTICLE 4—CONTRACT TIMES

4.01 *Time is of the Essence*

A. All time limits for Milestones, if any, Substantial Completion, and completion and readiness for final payment as stated in the Contract Documents are of the essence of the Contract.

4.02 *Contract Times: Dates*

A. A. The Work will be substantially completed on or before September 05, 2025. Any in-steam work is prohibited by NYSDEC permit between October 01st and April 30th of any year.

B. All time limits for Milestones, if any, Substantial Completion, and completion and readiness for final payment as stated in the Contract Documents are of the essence of the Contract.

C. The Work will be substantially completed by September 05, 2025 as provided in Paragraph 4.01 of the General Conditions, and completed and ready for final payment in accordance with Paragraph 15.06 of the General Conditions.

4.03 *Liquidated Damages*

i. Contractor and Owner recognize that time is of the essence as stated in Paragraph 4.01 above and that Owner will suffer financial and other losses if the Work is not completed and Milestones not achieved within the times specified in Paragraph 4.02 above, plus any extensions thereof allowed in accordance with the Contract.

The parties also recognize the delays, expense, and difficulties involved in proving, in a legal or arbitration proceeding, the actual loss suffered by Owner if the Work is not completed on time. Accordingly, instead of requiring any such proof, Owner and Contractor agree that as liquidated damages for delay (but not as a penalty):

1. Substantial Completion: Contractor shall pay Owner \$1,500 for each day that expires after the time (as duly adjusted pursuant to the Contract) specified in Paragraph 4.02.A above for Substantial Completion until the Work is substantially complete.
2. Completion of Remaining Work: After Substantial Completion, if Contractor shall neglect, refuse, or fail to complete the remaining Work within the Contract Times (as duly adjusted pursuant to the Contract) for completion and readiness for final payment, Contractor shall pay Owner \$1,500 for each day that expires after such time until the Work is completed and ready for final payment.
3. Liquidated damages for failing to timely attain Substantial Completion and final completion are not additive and will not be imposed concurrently.
4. Milestones: Contractor shall pay Owner \$1,500 for each day that expires after the time (as duly adjusted pursuant to the Contract) specified above for achievement of Milestone 1, until Milestone 1 is achieved.

4.04 Special Damages

- A. In addition to the amount provided for liquidated damages, Contractor shall reimburse Owner (1) for any fines or penalties imposed on Owner as a direct result of the Contractor's failure to attain Substantial Completion according to the Contract Times, and (2) for the actual costs reasonably incurred by Owner for engineering, construction observation, inspection, and administrative services needed after the time specified in Paragraph 4.02 for Substantial Completion (as duly adjusted pursuant to the Contract), until the Work is substantially complete.
- B. After Contractor achieves Substantial Completion, if Contractor shall neglect, refuse, or fail to complete the remaining Work within the Contract Times, Contractor shall reimburse Owner for the actual costs reasonably incurred by Owner for engineering, construction observation, inspection, and administrative services needed after the time specified in Paragraph 4.02 for Work to be completed and ready for final payment (as duly adjusted pursuant to the Contract), until the Work is completed and ready for final payment.

ARTICLE 5—CONTRACT PRICE

- 5.01 Owner shall pay Contractor for completion of the Work in accordance with the Contract Documents, the amounts that follow, subject to adjustment under the Contract:
- A. For all Unit Price Work, an amount equal to the sum of the extended prices (established for each separately identified item of Unit Price Work by multiplying the unit price times the actual quantity of that item).

The extended prices for Unit Price Work set forth as of the Effective Date of the Contract are based on estimated quantities. As provided in Paragraph 13.03 of the General Conditions, estimated quantities are not guaranteed, and determinations of actual quantities and classifications are to be made by Engineer.

- B. For all Work, at the prices stated in Contractor's Bid, attached hereto as an exhibit.

ARTICLE 6—PAYMENT PROCEDURES

6.01 *Submittal and Processing of Payments*

- A. Contractor shall submit Applications for Payment in accordance with Article 15 of the General Conditions. Applications for Payment will be processed by Engineer as provided in the General Conditions.

6.02 *Progress Payments; Retainage*

- A. Owner shall make monthly progress payments to the Contractor as requested and only for work deemed satisfactory by the Engineer.

1.03 *Final Payment*

- A. Upon final completion and acceptance of the Work in accordance with Paragraph 15.06 of the General Conditions, Owner shall pay the remainder of the Contract Price as recommended by Engineer as provided in said Paragraph 15.06.

ARTICLE 7—CONTRACT DOCUMENTS

7.01 *Contents*

- A. The Contract Documents consist of all of the following:
 - 1. This Agreement.
 - 2. Bonds:
 - a. Performance bond (together with power of attorney).
 - b. Payment bond (together with power of attorney).
 - 3. General Conditions.
 - 4. Supplementary Conditions.
 - 5. Wage Determination Schedule.
 - 6. Statutory and Funding-Financing Entity Requirements.
 - 7. Specifications as listed in the table of contents of the project manual (copy of list attached).
 - 8. Drawings listed on the attached sheet index.
 - 10. Addenda (if any).
 - 11. Exhibits to this Agreement (if any).
 - 12. The following which may be delivered or issued on or after the Effective Date of the Contract and are not attached hereto:

- a. Notice to Proceed.
 - b. Work Change Directives.
 - c. Change Orders.
 - d. Field Orders.
 - e. Warranty Bond, if any.
- B. The Contract Documents listed in Paragraph 7.01.A are attached to this Agreement (except as expressly noted otherwise above).
- C. There are no Contract Documents other than those listed above in this Article 7.
- D. The Contract Documents may only be amended, modified, or supplemented as provided in the Contract.

ARTICLE 8—REPRESENTATIONS, CERTIFICATIONS, AND STIPULATIONS

8.01 Contractor's Representations

- A. In order to induce Owner to enter into this Contract, Contractor makes the following representations:
- 1. Contractor has examined and carefully studied the Contract Documents, including Addenda.
 - 2. Contractor has visited the Site, conducted a thorough visual examination of the Site and adjacent areas, and become familiar with the general, local, and Site conditions that may affect cost, progress, and performance of the Work.
 - 3. Contractor is familiar with all Laws and Regulations that may affect cost, progress, and performance of the Work.
 - 4. Contractor has carefully studied the reports of explorations and tests of subsurface conditions at or adjacent to the Site and the drawings of physical conditions relating to existing surface or subsurface structures at the Site that have been identified in the Supplementary Conditions, with respect to the Technical Data in such reports and drawings.
 - 5. Contractor has carefully studied the reports and drawings relating to Hazardous Environmental Conditions, if any, at or adjacent to the Site that have been identified in the Supplementary Conditions, with respect to Technical Data in such reports and drawings.
 - 6. Contractor has considered the information known to Contractor itself; information commonly known to contractors doing business in the locality of the Site; information and observations obtained from visits to the Site; the Contract Documents; and the Technical Data identified in the Supplementary Conditions or by definition, with respect to the effect of such information, observations, and Technical Data on (a) the cost, progress, and performance of the Work; (b) the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor; and (c) Contractor's safety precautions and programs.

7. Based on the information and observations referred to in the preceding paragraph, Contractor agrees that no further examinations, investigations, explorations, tests, studies, or data are necessary for the performance of the Work at the Contract Price, within the Contract Times, and in accordance with the other terms and conditions of the Contract.
8. Contractor is aware of the general nature of work to be performed by Owner and others at the Site that relates to the Work as indicated in the Contract Documents.
9. Contractor has given Engineer written notice of all conflicts, errors, ambiguities, or discrepancies that Contractor has discovered in the Contract Documents, and of discrepancies between Site conditions and the Contract Documents, and the written resolution thereof by Engineer is acceptable to Contractor.
10. The Contract Documents are generally sufficient to indicate and convey understanding of all terms and conditions for performance and furnishing of the Work.
11. Contractor's entry into this Contract constitutes an incontrovertible representation by Contractor that without exception all prices in the Agreement are premised upon performing and furnishing the Work required by the Contract Documents.

8.02 *Contractor's Certifications*

- A. Contractor certifies that it has not engaged in corrupt, fraudulent, collusive, or coercive practices in competing for or in executing the Contract. For the purposes of this Paragraph 8.02:
 1. "corrupt practice" means the offering, giving, receiving, or soliciting of anything of value likely to influence the action of a public official in the bidding process or in the Contract execution;
 2. "fraudulent practice" means an intentional misrepresentation of facts made (a) to influence the bidding process or the execution of the Contract to the detriment of Owner, (b) to establish Bid or Contract prices at artificial non-competitive levels, or (c) to deprive Owner of the benefits of free and open competition;
 3. "collusive practice" means a scheme or arrangement between two or more Bidders, with or without the knowledge of Owner, a purpose of which is to establish Bid prices at artificial, non-competitive levels; and
 4. "coercive practice" means harming or threatening to harm, directly or indirectly, persons or their property to influence their participation in the bidding process or affect the execution of the Contract.

8.03 *Standard General Conditions*

- A. Owner stipulates that if the General Conditions that are made a part of this Contract are EJCDC® C-700, Standard General Conditions for the Construction Contract (2018), published by the Engineers Joint Contract Documents Committee, and if Owner is the party that has furnished said General Conditions, then Owner has plainly shown all modifications to the standard wording of such published document to the Contractor, through a process such as highlighting or "track changes" (redline/strikeout), or in the Supplementary Conditions.

ARTICLE 9 – MISCELLANEOUS

9.01 *Terms*

- A. Terms used in this Agreement will have the meanings stated in the General Conditions and the Supplementary Conditions.

9.02 *Assignment of Contract*

- A. Unless expressly agreed to elsewhere in the Contract, no assignment by a party hereto of any rights under or interests in the Contract will be binding on another party hereto without the written consent of the party sought to be bound; and, specifically but without limitation, money that may become due and money that is due may not be assigned without such consent (except to the extent that the effect of this restriction may be limited by law), and unless specifically stated to the contrary in any written consent to an assignment, no assignment will release or discharge the assignor from any duty or responsibility under the Contract Documents.

9.03 *Successors and Assigns*

- A. Owner and Contractor each binds itself, its successors, assigns, and legal representatives to the other party hereto, its successors, assigns, and legal representatives in respect to all covenants, agreements, and obligations contained in the Contract Documents.

9.04 *Severability*

- A. Any provision or part of the Contract Documents held to be void or unenforceable under any Law or Regulation shall be deemed stricken, and all remaining provisions shall continue to be valid and binding upon Owner and Contractor, who agree that the Contract Documents shall be reformed to replace such stricken provision or part thereof with a valid and enforceable provision that comes as close as possible to expressing the intention of the stricken provision.

9.05 *Contractor's Certifications*

- A. Contractor certifies that it has not engaged in corrupt, fraudulent, collusive, or coercive practices in competing for or in executing the Contract. For the purposes of this Paragraph 10.05:
 - 1. "corrupt practice" means the offering, giving, receiving, or soliciting of any thing of value likely to influence the action of a public official in the bidding process or in the Contract execution;
 - 2. "fraudulent practice" means an intentional misrepresentation of facts made (a) to influence the bidding process or the execution of the Contract to the detriment of Owner, (b) to establish Bid or Contract prices at artificial non-competitive levels, or (c) to deprive Owner of the benefits of free and open competition;
 - 3. "collusive practice" means a scheme or arrangement between two or more Bidders, with or without the knowledge of Owner, a purpose of which is to establish Bid prices at artificial, non-competitive levels; and
 - 4. "coercive practice" means harming or threatening to harm, directly or indirectly, persons or their property to influence their participation in the bidding process or affect the execution of the Contract.

9.06 *Other Provisions*

- A. Owner stipulates that if the General Conditions that are made a part of this Contract are based on EJCDC® C-700, Standard General Conditions for the Construction Contract, published by the Engineers Joint Contract Documents Committee®, and if Owner is the party that has furnished said General Conditions, then Owner has plainly shown all modifications to the standard wording of such published document to the Contractor, through a process such as highlighting or “track changes” (redline/strikeout), or in the Supplementary Conditions.

IN WITNESS WHEREOF, Owner and Contractor have signed this Agreement.

This Agreement will be effective on
Contract).

(which is the Effective Date of the

Contractor:

(typed or printed name of organization)

By: _____
(individual's signature)

Date: _____
(date signed)

Name: _____
(typed or printed)

Title: _____
(typed or printed)

Attest: _____
(individual's signature)

Title: _____
(typed or printed)

Address for giving notices:

Designated Representative:

Name: _____
(typed or printed)

Title: _____
(typed or printed)

Address:

Phone: _____

Email: _____

(If [Type of Entity] is a corporation, attach evidence of authority to sign. If [Type of Entity] is a public body, attach evidence of authority to sign and resolution or other documents authorizing execution of this Agreement.)

(typed or printed name of organization)

By: _____
(individual's signature)

Date: _____
(date signed)

Name: _____
(typed or printed)

Title: _____
(typed or printed)

(If [Type of Entity] is a corporation, a partnership, or a joint venture, attach evidence of authority to sign.)

Attest: _____
(individual's signature)

Title: _____
(typed or printed)

Address for giving notices:

Designated Representative:

Name: _____
(typed or printed)

Title: _____
(typed or printed)

Address:

Phone: _____

Email: _____

License No.: _____
(where applicable)

State: _____

BID BOND (PENAL SUM FORM)

Bidder Name: Address <i>(principal place of business)</i> :	Surety Name: Address <i>(principal place of business)</i> :
Owner Name: Town of Warwick Address <i>(principal place of business)</i> : 132 Kings Highway Warwick, New York 10990	Bid Project <i>(name and location)</i> : Town of Warwick, Ball Road Culvert Replacement Bid Due Date: March 25 th , 2025
Bond Penal Sum: Date of Bond:	
Surety and Bidder, intending to be legally bound hereby, subject to the terms set forth in this Bid Bond, do each cause this Bid Bond to be duly executed by an authorized officer, agent, or representative.	
Bidder	Surety
_____ <i>(Full formal name of Bidder)</i>	_____ <i>(Full formal name of Surety) (corporate seal)</i>
By: _____ <i>(Signature)</i>	By: _____ <i>(Signature) (Attach Power of Attorney)</i>
Name: _____ <i>(Printed or typed)</i>	Name: _____ <i>(Printed or typed)</i>
Title: _____	Title: _____
Attest: _____ <i>(Signature)</i>	Attest: _____ <i>(Signature)</i>
Name: _____ <i>(Printed or typed)</i>	Name: _____ <i>(Printed or typed)</i>
Title: _____	Title: _____
<i>Notes: (1) Note: Addresses are to be used for giving any required notice. (2) Provide execution by any additional parties, such as joint venturers, if necessary.</i>	

1. Bidder and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to pay to Owner upon default of Bidder the penal sum set forth on the face of this Bond. Payment of the penal sum is the extent of Bidder's and Surety's liability. Recovery of such penal sum under the terms of this Bond will be Owner's sole and exclusive remedy upon default of Bidder.
2. Default of Bidder occurs upon the failure of Bidder to deliver within the time required by the Bidding Documents (or any extension thereof agreed to in writing by Owner) the executed Agreement required by the Bidding Documents and any performance and payment bonds required by the Bidding Documents.
3. This obligation will be null and void if:
 - 3.1. Owner accepts Bidder's Bid and Bidder delivers within the time required by the Bidding Documents (or any extension thereof agreed to in writing by Owner) the executed Agreement required by the Bidding Documents and any performance and payment bonds required by the Bidding Documents, or
 - 3.2. All Bids are rejected by Owner, or
 - 3.3. Owner fails to issue a Notice of Award to Bidder within the time specified in the Bidding Documents (or any extension thereof agreed to in writing by Bidder and, if applicable, consented to by Surety when required by Paragraph 5 hereof).
4. Payment under this Bond will be due and payable upon default of Bidder and within 30 calendar days after receipt by Bidder and Surety of written notice of default from Owner, which notice will be given with reasonable promptness, identifying this Bond and the Project and including a statement of the amount due.
5. Surety waives notice of any and all defenses based on or arising out of any time extension to issue Notice of Award agreed to in writing by Owner and Bidder, provided that the total time for issuing Notice of Award including extensions does not in the aggregate exceed 120 days from the Bid due date without Surety's written consent.
6. No suit or action will be commenced under this Bond prior to 30 calendar days after the notice of default required in Paragraph 4 above is received by Bidder and Surety, and in no case later than one year after the Bid due date.
7. Any suit or action under this Bond will be commenced only in a court of competent jurisdiction located in the state in which the Project is located.
8. Notices required hereunder must be in writing and sent to Bidder and Surety at their respective addresses shown on the face of this Bond. Such notices may be sent by personal delivery, commercial courier, or by United States Postal Service registered or certified mail, return receipt requested, postage pre-paid, and will be deemed to be effective upon receipt by the party concerned.
9. Surety shall cause to be attached to this Bond a current and effective Power of Attorney evidencing the authority of the officer, agent, or representative who executed this Bond on behalf of Surety to execute, seal, and deliver such Bond and bind the Surety thereby.
10. This Bond is intended to conform to all applicable statutory requirements. Any applicable requirement of any applicable statute that has been omitted from this Bond will be deemed to be included herein as if set forth at length. If any provision of this Bond conflicts with any applicable statute, then the provision of said statute governs and the remainder of this Bond that is not in conflict therewith continues in full force and effect.
11. The term "Bid" as used herein includes a Bid, offer, or proposal as applicable.

BIDDER'S CERTIFICATION FOR FEDERAL AID CONTRACTS

The prospective participant certifies, by signing and submitting this bid or proposal, to the best of his/her knowledge and belief, that:

1. No Federal appropriate funds have been paid or will be paid, by or on behalf of the undersigned, to any person for influencing or attempting to influence an officer or employee of any Federal agency a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress, in connection with the awarding of any Federal contract, the making of any Federal grant, the making of any Federal loan, the entering into of any cooperative agreement, and the extension, continuation, renewal, amendment, or modification of any Federal contract, grant, loan, or cooperative agreement.
2. If any funds other than Federal appropriate funds have been paid or will be paid to any person for influencing or attempting to influence an officer or employee of any Federal agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress, in connection with this Federal contract, grant, loan, or cooperative agreement, the undersigned shall complete and submit Standard Form-LLL, "Disclosure Form to Report Lobbying", in accordance its instructions.

This certification is a material representation of fact upon which reliance was placed when this transaction was made or entered into. Submission of this certification is a prerequisite for making or entering into this transaction imposed by Section 1352, Title 31, U.S. Code. Any person who fails to file the required certification shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.

The prospective participant also agrees by submitting his/her bid or proposal that he/she shall require that the language of this certification be included in all lower tier subcontracts which exceed \$100,000 and that such subrecipients shall certify and disclose accordingly.

THESE MUST BE INCLUDED IN ALL FEDERAL AID CONTRACTS, AND MUST BE INCLUDED IN EACH BID PROPOSAL WHETHER NYSDOT SPECIFICATIONS OR LOCAL SPECIFICATIONS ARE USED.

This page intentionally left blank.

DISCLOSURE OF LOBBYING ACTIVITIES

Complete this form to disclose lobbying activities pursuant to 31 U.S.C. 1352

Approved by OMB

0348-0046

(See reverse for public burden disclosure.)

1. Type of Federal Action: ☐ a. contract ☐ b. grant ☐ c. cooperative agreement ☐ d. loan ☐ e. loan guarantee ☐ f. loan insurance		2. Status of Federal Action: ☐ a. bid/offer/application ☐ b. initial award ☐ c. post-award		3. Report Type: ☐ a. initial filing ☐ b. material change For Material Change Only: year _____ quarter _____ date of last report _____	
4. Name and Address of Reporting Entity: ☐ Prime ☐ Subawardee Tier _____, if known: Congressional District, if known: 4c			5. If Reporting Entity in No. 4 is a Subawardee, Enter Name and Address of Prime: Congressional District, if known:		
6. Federal Department/Agency:			7. Federal Program Name/Description: CFDA Number, if applicable: _____		
8. Federal Action Number, if known:			9. Award Amount, if known: \$		
10. a. Name and Address of Lobbying Registrant (if individual, last name, first name, MI):			b. Individuals Performing Services (including address if different from No. 10a) (last name, first name, MI):		
11. Information requested through this form is authorized by title 31 U.S.C. section 1352. This disclosure of lobbying activities is a material representation of fact upon which reliance was placed by the tier above when this transaction was made or entered into. This disclosure is required pursuant to 31 U.S.C. 1352. This information will be available for public inspection. Any person who fails to file the required disclosure shall be subject to a civil penalty of not less than \$10,000 and not more than \$100,000 for each such failure.			Signature: _____ Print Name: _____ Title: _____ Telephone No.: _____ Date: _____		
Federal Use Only:					Authorized for Local Reproduction Standard Form LLL (Rev. 7-97)

INSTRUCTIONS FOR COMPLETION OF SF-LLL, DISCLOSURE OF LOBBYING ACTIVITIES

This disclosure form shall be completed by the reporting entity, whether subawardee or prime Federal recipient, at the initiation or receipt of a covered Federal action, or a material change to a previous filing, pursuant to title 31 U.S.C. section 1352. The filing of a form is required for each payment or agreement to make payment to any lobbying entity for influencing or attempting to influence an officer or employee of any agency, a Member of Congress, an officer or employee of Congress, or an employee of a Member of Congress in connection with a covered Federal action. Complete all items that apply for both the initial filing and material change report. Refer to the implementing guidance published by the Office of Management and Budget for additional information.

1. Identify the type of covered Federal action for which lobbying activity is and/or has been secured to influence the outcome of a covered Federal action.
2. Identify the status of the covered Federal action.
3. Identify the appropriate classification of this report. If this is a followup report caused by a material change to the information previously reported, enter the year and quarter in which the change occurred. Enter the date of the last previously submitted report by this reporting entity for this covered Federal action.
4. Enter the full name, address, city, State and zip code of the reporting entity. Include Congressional District, if known. Check the appropriate classification of the reporting entity that designates if it is, or expects to be, a prime or subaward recipient. Identify the tier of the subawardee, e.g., the first subawardee of the prime is the 1st tier. Subawards include but are not limited to subcontracts, subgrants and contract awards under grants.
5. If the organization filing the report in item 4 checks "Subawardee," then enter the full name, address, city, State and zip code of the prime Federal recipient. Include Congressional District, if known.
6. Enter the name of the Federal agency making the award or loan commitment. Include at least one organizational level below agency name, if known. For example, Department of Transportation, United States Coast Guard.
7. Enter the Federal program name or description for the covered Federal action (item 1). If known, enter the full Catalog of Federal Domestic Assistance (CFDA) number for grants, cooperative agreements, loans, and loan commitments.
8. Enter the most appropriate Federal identifying number available for the Federal action identified in item 1 (e.g., Request for Proposal (RFP) number; Invitation for Bid (IFB) number; grant announcement number; the contract, grant, or loan award number; the application/proposal control number assigned by the Federal agency). Include prefixes, e.g., "RFP-DE-90-001."
9. For a covered Federal action where there has been an award or loan commitment by the Federal agency, enter the Federal amount of the award/loan commitment for the prime entity identified in item 4 or 5.
10. (a) Enter the full name, address, city, State and zip code of the lobbying registrant under the Lobbying Disclosure Act of 1995 engaged by the reporting entity identified in item 4 to influence the covered Federal action.

(b) Enter the full names of the individual(s) performing services, and include full address if different from 10 (a). Enter Last Name, First Name, and Middle Initial (MI).
11. The certifying official shall sign and date the form, print his/her name, title, and telephone number.

According to the Paperwork Reduction Act, as amended, no persons are required to respond to a collection of information unless it displays a valid OMB Control Number. The valid OMB control number for this information collection is OMB No. 0348-0046. Public reporting burden for this collection of information is estimated to average 10 minutes per response, including time for reviewing instructions, searching existing data sources, gathering and maintaining the data needed, and completing and reviewing the collection of information. Send comments regarding the burden estimate or any other aspect of this collection of information, including suggestions for reducing this burden, to the Office of Management and Budget, Paperwork Reduction Project (0348-0046), Washington, DC 20503.

**STATEMENT OF NON-COLLUSION BY BIDDER
PURSUANT TO SECTION 103-D
GENERAL MUNICIPAL LAW**

PROJECT TITLE:

STATE OF NEW YORK)

) SS:

COUNTY OF)

I, _____ of the (Town, Village, City) of _____ in the County of _____ and the State of _____ of full age, being duly sworn according to law on my oath depose and say that:

I am _____, an officer of the firm of _____ the bidder making the Proposal for the above named work, and that I executed the said Proposal with full authority to do so; that said bidder has not, directly or indirectly, entered into any agreement, participated in any collusion, or otherwise in connection with the above named work; and that all statements contained in said Proposal and in this affidavit are true and correct, and made with the full knowledge that Town of Warwick as Owner relies upon the truth of the statements contained in said Proposal and in the statements contained in this affidavit in awarding the contract for said work.

The prices in this bid have been arrived at independently without collusion, consultation, communication, or agreement for the purpose of restricting competition, as to any matter relating to such prices with any bidder, with any competitor;

Unless otherwise require by law, the prices which have been quoted in this bid have not been knowingly disclosed by the bidder, and will not knowingly be disclosed by the bidder prior to opening, directly or indirectly, to any other bidder or to any competitor;

No attempt has been made or will be made by the bidder to induce any other person, partnership or corporation to submit or not to submit a bid for the purpose of restricting competition;

I further warrant that no person or selling agency has been employed or retained to solicit or secure such contract upon an agreement or understanding for a commission, percentage, brokerage or contingent fee, except bonafide employees or bonafide established commercial or selling agencies maintained by _____.

(Name of Contractor)

Subscribed and sworn to

(Also type or print name and title of affiant under signature)

before me this _____ day of _____ 20____

Notary Public of

My commission expires _____,

Town of Warwick, New York
Ball Road Culvert Replacement

February 2025

This page intentionally left blank.

NEW YORK STATE DEPARTMENT OF TRANSPORTATION

DISADVANTAGED BUSINESS ENTERPRISE

UTILIZATION REQUIREMENTS

The Department has established the following Disadvantaged Business Enterprise (DBE) utilization goals for this contract in accordance with §102-12 of the Standard Specifications.

Disadvantaged Business Enterprise Utilization Goal: 7%

For clarification of Utilization Requirements refer to §102-12

Information related to the current certification status of Disadvantaged Business Enterprises can be obtained by contacting the:

NYS Department of Transportation
Office of Equal Opportunity Development & Compliance
1220 Washington Avenue
Building 4, Room G-16
Albany, New York 1232
(518) 457 – 1127 or (518) 457 – 1129

Disadvantaged Business Enterprise Officer

The Bidder must designate and enter below the name of a Disadvantaged Business Enterprise Officer who will have the responsibility for and must be capable of effectively administering and promoting an active Disadvantaged Business Enterprise Program and who must be assigned adequate authority and responsibility to do so.

Bidder Designated DBE Officer: _____
(Name) (Title) .

Telephone Number: _____

(THIS PAGE MUST BE RETURNED WITH BID)

This page intentionally left blank.

CERTIFICATE OF NON-SEGREGATED FACILITIES

We, _____ (Contractor)
Certify that we do not and will not maintain or provide for our employees any segregated facilities at any of our establishments, and that we do not and will not permit our employees to perform their services at any location, under our control, where segregated facilities are maintained. We understand and agree that breach of this certification is a violation of Equal Opportunity clause required by Executive Order 11246, amended.

As used in this certification, the term "segregated facilities" means any waiting rooms, work areas, rest rooms and wash rooms, restaurants and other eating areas, time clocks, locker rooms and other storage or dressing areas, parking lots, drinking fountains, recreation or entertainment areas, transportation and housing facilities provided for employees which are segregated by explicit directive or are in fact segregated on the basis of race, creed, color, or national origin, because of habit, local custom or otherwise.

We further agree that (except where we have obtained identical certifications from proposed Subcontractors for specific time periods) we will obtain identical certifications from proposed Subcontractors prior to the award of subcontracts exceeding \$10,000 which are not exempt from the provisions of the Equal Opportunity clause; that we will retain such certification in our files; and that we will forward the following notice to such proposed Subcontractors (except where the proposed Subcontractors have submitted identical certifications for specific time periods).

NOTICE TO PROSPECTIVE SUBBUILDERS OF REQUIREMENT FOR CERTIFICATION OF NON-SEGREGATED FACILITIES. A certification of Non-segregated facilities as required by the 9 May 1967 order on Elimination of Segregated Facilities, by the Secretary of Labor (32 Fed. Reg. 7439, 19 May 1967), must be submitted from the provisions either for each subcontract or for all subcontracts during a period (i.e. quarterly, semi-annually, or annually).

NOTE: Whoever knowingly and willfully makes any false, fictitious or fraudulent representation may be liable to criminal prosecution under 18 U.S.C. 1001.

(Name of Contractor)

By: _____

Date: _____

Title: _____

This page intentionally left blank.

**BIDDER'S CERTIFICATION OF
LIMITED FOREIGN INVOLVEMENT**

(Completion of this statement is required in advance of consideration for award of this contract.)

SUBMITTED TO:

SUBMITTED FOR:

SUBMITTED BY:

Name:

(print or type name of bidder)

A Corporation / A Partnership / An Individual / A Joint Venture

Address:

Gentlemen:

The undersigned certifies under oath the truth and correctness of all statements made hereinafter.

1. The Offeror is not a contractor of a foreign country included on the list of countries that discriminate against U.S. firms as published by the U.S. Trade Representative (USTR).
2. The Offeror has not or will not enter into any subcontract with a subcontractor or a foreign country included on the USTR list.
3. The Offeror will not provide any product of a country included on the USTR list.

(print or type name of bidder)

(Seal, if Corporation)

By: _____

Title: _____

This page intentionally left blank.

STANDARD GENERAL CONDITIONS

OF THE CONSTRUCTION CONTRACT

TABLE OF CONTENTS

	Page
Article 1—Definitions and Terminology.....	1
1.01 Defined Terms.....	1
1.02 Terminology	6
Article 2—Preliminary Matters	7
2.01 Delivery of Performance and Payment Bonds; Evidence of Insurance.....	7
2.02 Copies of Documents	7
2.03 Before Starting Construction	7
2.04 Preconstruction Conference; Designation of Authorized Representatives	8
2.05 Acceptance of Schedules	8
2.06 Electronic Transmittals	8
Article 3—Contract Documents: Intent, Requirements, Reuse	9
3.01 Intent.....	9
3.02 Reference Standards	9
3.03 Reporting and Resolving Discrepancies	10
3.04 Requirements of the Contract Documents	10
3.05 Reuse of Documents	11
Article 4—Commencement and Progress of the Work	11
4.01 Commencement of Contract Times; Notice to Proceed.....	11
4.02 Starting the Work.....	11
4.03 Reference Points	11
4.04 Progress Schedule	12
4.05 Delays in Contractor’s Progress	12
Article 5—Site; Subsurface and Physical Conditions; Hazardous Environmental Conditions	13
5.01 Availability of Lands	13
5.02 Use of Site and Other Areas.....	14
5.03 Subsurface and Physical Conditions.....	15
5.04 Differing Subsurface or Physical Conditions	16
5.05 Underground Facilities	17

5.06	Hazardous Environmental Conditions at Site	19
Article 6—Bonds and Insurance.....		21
6.01	Performance, Payment, and Other Bonds	21
6.02	Insurance—General Provisions	22
6.03	Contractor’s Insurance	24
6.04	Builder’s Risk and Other Property Insurance	25
6.05	Property Losses; Subrogation	25
6.06	Receipt and Application of Property Insurance Proceeds	27
Article 7—Contractor’s Responsibilities		27
7.01	Contractor’s Means and Methods of Construction	27
7.02	Supervision and Superintendence	27
7.03	Labor; Working Hours	27
7.04	Services, Materials, and Equipment	28
7.05	“Or Equals”	28
7.06	Substitutes	29
7.07	Concerning Subcontractors and Suppliers.....	31
7.08	Patent Fees and Royalties.....	32
7.09	Permits	33
7.10	Taxes	33
7.11	Laws and Regulations.....	33
7.12	Record Documents.....	33
7.13	Safety and Protection.....	34
7.14	Hazard Communication Programs	35
7.15	Emergencies	35
7.16	Submittals	35
7.17	Contractor’s General Warranty and Guarantee	38
7.18	Indemnification	39
7.19	Delegation of Professional Design Services	39
Article 8—Other Work at the Site.....		40
8.01	Other Work	40
8.02	Coordination	41
8.03	Legal Relationships.....	41
Article 9—Owner’s Responsibilities		42

9.01	Communications to Contractor	42
9.02	Replacement of Engineer	42
9.03	Furnish Data	42
9.04	Pay When Due	42
9.05	Lands and Easements; Reports, Tests, and Drawings	43
9.06	Insurance	43
9.07	Change Orders	43
9.08	Inspections, Tests, and Approvals	43
9.09	Limitations on Owner's Responsibilities	43
9.10	Undisclosed Hazardous Environmental Condition	43
9.11	Evidence of Financial Arrangements	43
9.12	Safety Programs	43
Article 10—Engineer's Status During Construction		44
10.01	Owner's Representative	44
10.02	Visits to Site	44
10.03	Resident Project Representative	44
10.04	Engineer's Authority	44
10.05	Determinations for Unit Price Work	45
10.06	Decisions on Requirements of Contract Documents and Acceptability of Work	45
10.07	Limitations on Engineer's Authority and Responsibilities	45
10.08	Compliance with Safety Program	45
Article 11—Changes to the Contract		46
11.01	Amending and Supplementing the Contract	46
11.02	Change Orders	46
11.03	Work Change Directives	46
11.04	Field Orders	47
11.05	Owner-Authorized Changes in the Work	47
11.06	Unauthorized Changes in the Work	47
11.07	Change of Contract Price	47
11.08	Change of Contract Times	49
11.09	Change Proposals	49
11.10	Notification to Surety	50
Article 12—Claims		50

12.01	Claims	50
Article 13—Cost of the Work; Allowances; Unit Price Work		51
13.01	Cost of the Work	51
13.02	Allowances	55
13.03	Unit Price Work	55
Article 14—Tests and Inspections; Correction, Removal, or Acceptance of Defective Work		56
14.01	Access to Work.....	56
14.02	Tests, Inspections, and Approvals.....	56
14.03	Defective Work	57
14.04	Acceptance of Defective Work.....	58
14.05	Uncovering Work	58
14.06	Owner May Stop the Work	58
14.07	Owner May Correct Defective Work.....	59
Article 15—Payments to Contractor; Set-Offs; Completion; Correction Period		59
15.01	Progress Payments.....	59
15.02	Contractor’s Warranty of Title	62
15.03	Substantial Completion.....	62
15.04	Partial Use or Occupancy	63
15.05	Final Inspection	64
15.06	Final Payment.....	64
15.07	Waiver of Claims	65
15.08	Correction Period	66
Article 16—Suspension of Work and Termination		67
16.01	Owner May Suspend Work	67
16.02	Owner May Terminate for Cause.....	67
16.03	Owner May Terminate for Convenience.....	68
16.04	Contractor May Stop Work or Terminate	68
Article 17—Final Resolution of Disputes		69
17.01	Methods and Procedures.....	69
Article 18—Miscellaneous		69
18.01	Giving Notice	69
18.02	Computation of Times	69
18.03	Cumulative Remedies	70

18.04	Limitation of Damages	70
18.05	No Waiver	70
18.06	Survival of Obligations	70
18.07	Controlling Law	70
18.08	Assignment of Contract	70
18.09	Successors and Assigns	70
18.10	Headings.....	70

STANDARD GENERAL CONDITIONS

OF THE CONSTRUCTION CONTRACT

ARTICLE 1—DEFINITIONS AND TERMINOLOGY

1.01 *Defined Terms*

- A. Wherever used in the Bidding Requirements or Contract Documents, a term printed with initial capital letters, including the term's singular and plural forms, will have the meaning indicated in the definitions below. In addition to terms specifically defined, terms with initial capital letters in the Contract Documents include references to identified articles and paragraphs, and the titles of other documents or forms.
1. *Addenda*—Written or graphic instruments issued prior to the opening of Bids which clarify, correct, or change the Bidding Requirements or the proposed Contract Documents.
 2. *Agreement*—The written instrument, executed by Owner and Contractor, that sets forth the Contract Price and Contract Times, identifies the parties and the Engineer, and designates the specific items that are Contract Documents.
 3. *Application for Payment*—The document prepared by Contractor, in a form acceptable to Engineer, to request progress or final payments, and which is to be accompanied by such supporting documentation as is required by the Contract Documents.
 4. *Bid*—The offer of a Bidder submitted on the prescribed form setting forth the prices for the Work to be performed.
 5. *Bidder*—An individual or entity that submits a Bid to Owner.
 6. *Bidding Documents*—The Bidding Requirements, the proposed Contract Documents, and all Addenda.
 7. *Bidding Requirements*—The Advertisement or invitation to bid, Instructions to Bidders, Bid Bond or other Bid security, if any, the Bid Form, and the Bid with any attachments.
 8. *Change Order*—A document which is signed by Contractor and Owner and authorizes an addition, deletion, or revision in the Work or an adjustment in the Contract Price or the Contract Times, or other revision to the Contract, issued on or after the Effective Date of the Contract.
 9. *Change Proposal*—A written request by Contractor, duly submitted in compliance with the procedural requirements set forth herein, seeking an adjustment in Contract Price or Contract Times; contesting an initial decision by Engineer concerning the requirements of the Contract Documents or the acceptability of Work under the Contract Documents; challenging a set-off against payments due; or seeking other relief with respect to the terms of the Contract.
 10. *Claim*
 - a. A demand or assertion by Owner directly to Contractor, duly submitted in compliance with the procedural requirements set forth herein, seeking an adjustment of Contract Price or Contract Times; contesting an initial decision by Engineer concerning the

requirements of the Contract Documents or the acceptability of Work under the Contract Documents; contesting Engineer's decision regarding a Change Proposal; seeking resolution of a contractual issue that Engineer has declined to address; or seeking other relief with respect to the terms of the Contract.

- b. A demand or assertion by Contractor directly to Owner, duly submitted in compliance with the procedural requirements set forth herein, contesting Engineer's decision regarding a Change Proposal, or seeking resolution of a contractual issue that Engineer has declined to address.
 - c. A demand or assertion by Owner or Contractor, duly submitted in compliance with the procedural requirements set forth herein, made pursuant to Paragraph 12.01.A.4, concerning disputes arising after Engineer has issued a recommendation of final payment.
 - d. A demand for money or services by a third party is not a Claim.
- 11. *Constituent of Concern*—Asbestos, petroleum, radioactive materials, polychlorinated biphenyls (PCBs), lead-based paint (as defined by the HUD/EPA standard), hazardous waste, and any substance, product, waste, or other material of any nature whatsoever that is or becomes listed, regulated, or addressed pursuant to Laws and Regulations regulating, relating to, or imposing liability or standards of conduct concerning, any hazardous, toxic, or dangerous waste, substance, or material.
 - 12. *Contract*—The entire and integrated written contract between Owner and Contractor concerning the Work.
 - 13. *Contract Documents*—Those items so designated in the Agreement, and which together comprise the Contract.
 - 14. *Contract Price*—The money that Owner has agreed to pay Contractor for completion of the Work in accordance with the Contract Documents.
 - 15. *Contract Times*—The number of days or the dates by which Contractor shall: (a) achieve Milestones, if any; (b) achieve Substantial Completion; and (c) complete the Work.
 - 16. *Contractor*—The individual or entity with which Owner has contracted for performance of the Work.
 - 17. *Cost of the Work*—See Paragraph 13.01 for definition.
 - 18. *Drawings*—The part of the Contract that graphically shows the scope, extent, and character of the Work to be performed by Contractor.
 - 19. *Effective Date of the Contract*—The date, indicated in the Agreement, on which the Contract becomes effective.
 - 20. *Electronic Document*—Any Project-related correspondence, attachments to correspondence, data, documents, drawings, information, or graphics, including but not limited to Shop Drawings and other Submittals, that are in an electronic or digital format.
 - 21. *Electronic Means*—Electronic mail (email), upload/download from a secure Project website, or other communications methods that allow: (a) the transmission or communication of Electronic Documents; (b) the documentation of transmissions, including sending and receipt; (c) printing of the transmitted Electronic Document by the

recipient; (d) the storage and archiving of the Electronic Document by sender and recipient; and (e) the use by recipient of the Electronic Document for purposes permitted by this Contract. Electronic Means does not include the use of text messaging, or of Facebook, Twitter, Instagram, or similar social media services for transmission of Electronic Documents.

22. *Engineer*—The individual or entity named as such in the Agreement.
23. *Field Order*—A written order issued by Engineer which requires minor changes in the Work but does not change the Contract Price or the Contract Times.
24. *Hazardous Environmental Condition*—The presence at the Site of Constituents of Concern in such quantities or circumstances that may present a danger to persons or property exposed thereto.
 - a. The presence at the Site of materials that are necessary for the execution of the Work, or that are to be incorporated into the Work, and that are controlled and contained pursuant to industry practices, Laws and Regulations, and the requirements of the Contract, is not a Hazardous Environmental Condition.
 - b. The presence of Constituents of Concern that are to be removed or remediated as part of the Work is not a Hazardous Environmental Condition.
 - c. The presence of Constituents of Concern as part of the routine, anticipated, and obvious working conditions at the Site, is not a Hazardous Environmental Condition.
25. *Laws and Regulations; Laws or Regulations*—Any and all applicable laws, statutes, rules, regulations, ordinances, codes, and binding decrees, resolutions, and orders of any and all governmental bodies, agencies, authorities, and courts having jurisdiction.
26. *Liens*—Charges, security interests, or encumbrances upon Contract-related funds, real property, or personal property.
27. *Milestone*—A principal event in the performance of the Work that the Contract requires Contractor to achieve by an intermediate completion date, or by a time prior to Substantial Completion of all the Work.
28. *Notice of Award*—The written notice by Owner to a Bidder of Owner's acceptance of the Bid.
29. *Notice to Proceed*—A written notice by Owner to Contractor fixing the date on which the Contract Times will commence to run and on which Contractor shall start to perform the Work.
30. *Owner*—The individual or entity with which Contractor has contracted regarding the Work, and which has agreed to pay Contractor for the performance of the Work, pursuant to the terms of the Contract.
31. *Progress Schedule*—A schedule, prepared and maintained by Contractor, describing the sequence and duration of the activities comprising Contractor's plan to accomplish the Work within the Contract Times.
32. *Project*—The total undertaking to be accomplished for Owner by engineers, contractors, and others, including planning, study, design, construction, testing, commissioning, and start-up, and of which the Work to be performed under the Contract Documents is a part.

33. *Resident Project Representative*—The authorized representative of Engineer assigned to assist Engineer at the Site. As used herein, the term Resident Project Representative (RPR) includes any assistants or field staff of Resident Project Representative.
34. *Samples*—Physical examples of materials, equipment, or workmanship that are representative of some portion of the Work and that establish the standards by which such portion of the Work will be judged.
35. *Schedule of Submittals*—A schedule, prepared and maintained by Contractor, of required submittals and the time requirements for Engineer’s review of the submittals.
36. *Schedule of Values*—A schedule, prepared and maintained by Contractor, allocating portions of the Contract Price to various portions of the Work and used as the basis for reviewing Contractor’s Applications for Payment.
37. *Shop Drawings*—All drawings, diagrams, illustrations, schedules, and other data or information that are specifically prepared or assembled by or for Contractor and submitted by Contractor to illustrate some portion of the Work. Shop Drawings, whether approved or not, are not Drawings and are not Contract Documents.
38. *Site*—Lands or areas indicated in the Contract Documents as being furnished by Owner upon which the Work is to be performed, including rights-of-way and easements, and such other lands or areas furnished by Owner which are designated for the use of Contractor.
39. *Specifications*—The part of the Contract that consists of written requirements for materials, equipment, systems, standards, and workmanship as applied to the Work, and certain administrative requirements and procedural matters applicable to the Work.
40. *Subcontractor*—An individual or entity having a direct contract with Contractor or with any other Subcontractor for the performance of a part of the Work.
41. *Submittal*—A written or graphic document, prepared by or for Contractor, which the Contract Documents require Contractor to submit to Engineer, or that is indicated as a Submittal in the Schedule of Submittals accepted by Engineer. Submittals may include Shop Drawings and Samples; schedules; product data; Owner-delegated designs; sustainable design information; information on special procedures; testing plans; results of tests and evaluations, source quality-control testing and inspections, and field or Site quality-control testing and inspections; warranties and certifications; Suppliers’ instructions and reports; records of delivery of spare parts and tools; operations and maintenance data; Project photographic documentation; record documents; and other such documents required by the Contract Documents. Submittals, whether or not approved or accepted by Engineer, are not Contract Documents. Change Proposals, Change Orders, Claims, notices, Applications for Payment, and requests for interpretation or clarification are not Submittals.
42. *Substantial Completion*—The time at which the Work (or a specified part thereof) has progressed to the point where, in the opinion of Engineer, the Work (or a specified part thereof) is sufficiently complete, in accordance with the Contract Documents, so that the Work (or a specified part thereof) can be utilized for the purposes for which it is intended. The terms “substantially complete” and “substantially completed” as applied to all or part of the Work refer to Substantial Completion of such Work.

43. *Successful Bidder*—The Bidder to which the Owner makes an award of contract.
44. *Supplementary Conditions*—The part of the Contract that amends or supplements these General Conditions.
45. *Supplier*—A manufacturer, fabricator, supplier, distributor, or vendor having a direct contract with Contractor or with any Subcontractor to furnish materials or equipment to be incorporated in the Work by Contractor or a Subcontractor.
46. *Technical Data*
- a. Those items expressly identified as Technical Data in the Supplementary Conditions, with respect to either (1) existing subsurface conditions at or adjacent to the Site, or existing physical conditions at or adjacent to the Site including existing surface or subsurface structures (except Underground Facilities) or (2) Hazardous Environmental Conditions at the Site.
 - b. If no such express identifications of Technical Data have been made with respect to conditions at the Site, then Technical Data is defined, with respect to conditions at the Site under Paragraphs 5.03, 5.04, and 5.06, as the data contained in boring logs, recorded measurements of subsurface water levels, assessments of the condition of subsurface facilities, laboratory test results, and other factual, objective information regarding conditions at the Site that are set forth in any geotechnical, environmental, or other Site or facilities conditions report prepared for the Project and made available to Contractor.
 - c. Information and data regarding the presence or location of Underground Facilities are not intended to be categorized, identified, or defined as Technical Data, and instead Underground Facilities are shown or indicated on the Drawings.
47. *Underground Facilities*—All active or not-in-service underground lines, pipelines, conduits, ducts, encasements, cables, wires, manholes, vaults, tanks, tunnels, or other such facilities or systems at the Site, including but not limited to those facilities or systems that produce, transmit, distribute, or convey telephone or other communications, cable television, fiber optic transmissions, power, electricity, light, heat, gases, oil, crude oil products, liquid petroleum products, water, steam, waste, wastewater, storm water, other liquids or chemicals, or traffic or other control systems. An abandoned facility or system is not an Underground Facility.
48. *Unit Price Work*—Work to be paid for on the basis of unit prices.
49. *Work*—The entire construction or the various separately identifiable parts thereof required to be provided under the Contract Documents. Work includes and is the result of performing or providing all labor, services, and documentation necessary to produce such construction; furnishing, installing, and incorporating all materials and equipment into such construction; and may include related services such as testing, start-up, and commissioning, all as required by the Contract Documents.
50. *Work Change Directive*—A written directive to Contractor issued on or after the Effective Date of the Contract, signed by Owner and recommended by Engineer, ordering an addition, deletion, or revision in the Work.

1.02 Terminology

- A. The words and terms discussed in Paragraphs 1.02.B, C, D, and E are not defined terms that require initial capital letters, but, when used in the Bidding Requirements or Contract Documents, have the indicated meaning.
- B. *Intent of Certain Terms or Adjectives:* The Contract Documents include the terms “as allowed,” “as approved,” “as ordered,” “as directed” or terms of like effect or import to authorize an exercise of professional judgment by Engineer. In addition, the adjectives “reasonable,” “suitable,” “acceptable,” “proper,” “satisfactory,” or adjectives of like effect or import are used to describe an action or determination of Engineer as to the Work. It is intended that such exercise of professional judgment, action, or determination will be solely to evaluate, in general, the Work for compliance with the information in the Contract Documents and with the design concept of the Project as a functioning whole as shown or indicated in the Contract Documents (unless there is a specific statement indicating otherwise). The use of any such term or adjective is not intended to and shall not be effective to assign to Engineer any duty or authority to supervise or direct the performance of the Work, or any duty or authority to undertake responsibility contrary to the provisions of Article 10 or any other provision of the Contract Documents.
- C. *Day:* The word “day” means a calendar day of 24 hours measured from midnight to the next midnight.
- D. *Defective:* The word “defective,” when modifying the word “Work,” refers to Work that is unsatisfactory, faulty, or deficient in that it:
 - 1. does not conform to the Contract Documents;
 - 2. does not meet the requirements of any applicable inspection, reference standard, test, or approval referred to in the Contract Documents; or
 - 3. has been damaged prior to Engineer’s recommendation of final payment (unless responsibility for the protection thereof has been assumed by Owner at Substantial Completion in accordance with Paragraph 15.03 or Paragraph 15.04).
- E. *Furnish, Install, Perform, Provide*
 - 1. The word “furnish,” when used in connection with services, materials, or equipment, means to supply and deliver said services, materials, or equipment to the Site (or some other specified location) ready for use or installation and in usable or operable condition.
 - 2. The word “install,” when used in connection with services, materials, or equipment, means to put into use or place in final position said services, materials, or equipment complete and ready for intended use.
 - 3. The words “perform” or “provide,” when used in connection with services, materials, or equipment, means to furnish and install said services, materials, or equipment complete and ready for intended use.
 - 4. If the Contract Documents establish an obligation of Contractor with respect to specific services, materials, or equipment, but do not expressly use any of the four words “furnish,” “install,” “perform,” or “provide,” then Contractor shall furnish and install said services, materials, or equipment complete and ready for intended use.

- F. *Contract Price or Contract Times*: References to a change in “Contract Price or Contract Times” or “Contract Times or Contract Price” or similar, indicate that such change applies to (1) Contract Price, (2) Contract Times, or (3) both Contract Price and Contract Times, as warranted, even if the term “or both” is not expressed.
- G. Unless stated otherwise in the Contract Documents, words or phrases that have a well-known technical or construction industry or trade meaning are used in the Contract Documents in accordance with such recognized meaning.

ARTICLE 2—PRELIMINARY MATTERS

2.01 *Delivery of Performance and Payment Bonds; Evidence of Insurance*

- A. *Performance and Payment Bonds*: When Contractor delivers the signed counterparts of the Agreement to Owner, Contractor shall also deliver to Owner the performance bond and payment bond (if the Contract requires Contractor to furnish such bonds).
- B. *Evidence of Contractor’s Insurance*: When Contractor delivers the signed counterparts of the Agreement to Owner, Contractor shall also deliver to Owner, with copies to each additional insured (as identified in the Contract), the certificates, endorsements, and other evidence of insurance required to be provided by Contractor in accordance with Article 6, except to the extent the Supplementary Conditions expressly establish other dates for delivery of specific insurance policies.
- C. *Evidence of Owner’s Insurance*: After receipt of the signed counterparts of the Agreement and all required bonds and insurance documentation, Owner shall promptly deliver to Contractor, with copies to each additional insured (as identified in the Contract), the certificates and other evidence of insurance required to be provided by Owner under Article 6.

2.02 *Copies of Documents*

- A. Owner shall furnish to Contractor four printed copies of the Contract (including one fully signed counterpart of the Agreement), and one copy in electronic portable document format (PDF). Additional printed copies will be furnished upon request at the cost of reproduction.
- B. Owner shall maintain and safeguard at least one original printed record version of the Contract, including Drawings and Specifications signed and sealed by Engineer and other design professionals. Owner shall make such original printed record version of the Contract available to Contractor for review. Owner may delegate the responsibilities under this provision to Engineer.

2.03 *Before Starting Construction*

- A. *Preliminary Schedules*: Within 10 days after the Effective Date of the Contract (or as otherwise required by the Contract Documents), Contractor shall submit to Engineer for timely review:
 - 1. a preliminary Progress Schedule indicating the times (numbers of days or dates) for starting and completing the various stages of the Work, including any Milestones specified in the Contract;
 - 2. a preliminary Schedule of Submittals; and
 - 3. a preliminary Schedule of Values for all of the Work which includes quantities and prices of items which when added together equal the Contract Price and subdivides the Work

into component parts in sufficient detail to serve as the basis for progress payments during performance of the Work. Such prices will include an appropriate amount of overhead and profit applicable to each item of Work.

2.04 *Preconstruction Conference; Designation of Authorized Representatives*

- A. Before any Work at the Site is started, a conference attended by Owner, Contractor, Engineer, and others as appropriate will be held to establish a working understanding among the parties as to the Work, and to discuss the schedules referred to in Paragraph 2.03.A, procedures for handling Shop Drawings, Samples, and other Submittals, processing Applications for Payment, electronic or digital transmittals, and maintaining required records.
- B. At this conference Owner and Contractor each shall designate, in writing, a specific individual to act as its authorized representative with respect to the services and responsibilities under the Contract. Such individuals shall have the authority to transmit and receive information, render decisions relative to the Contract, and otherwise act on behalf of each respective party.

2.05 *Acceptance of Schedules*

- A. At least 10 days before submission of the first Application for Payment a conference, attended by Contractor, Engineer, and others as appropriate, will be held to review the schedules submitted in accordance with Paragraph 2.03.A. No progress payment will be made to Contractor until acceptable schedules are submitted to Engineer.
 - 1. The Progress Schedule will be acceptable to Engineer if it provides an orderly progression of the Work to completion within the Contract Times. Such acceptance will not impose on Engineer responsibility for the Progress Schedule, for sequencing, scheduling, or progress of the Work, nor interfere with or relieve Contractor from Contractor's full responsibility therefor.
 - 2. Contractor's Schedule of Submittals will be acceptable to Engineer if it provides a workable arrangement for reviewing and processing the required submittals.
 - 3. Contractor's Schedule of Values will be acceptable to Engineer as to form and substance if it provides a reasonable allocation of the Contract Price to the component parts of the Work.
 - 4. If a schedule is not acceptable, Contractor will have an additional 10 days to revise and resubmit the schedule.

2.06 *Electronic Transmittals*

- A. Except as otherwise stated elsewhere in the Contract, the Owner, Engineer, and Contractor may send, and shall accept, Electronic Documents transmitted by Electronic Means.
- B. If the Contract does not establish protocols for Electronic Means, then Owner, Engineer, and Contractor shall jointly develop such protocols.
- C. Subject to any governing protocols for Electronic Means, when transmitting Electronic Documents by Electronic Means, the transmitting party makes no representations as to long-term compatibility, usability, or readability of the Electronic Documents resulting from the recipient's use of software application packages, operating systems, or computer hardware differing from those used in the drafting or transmittal of the Electronic Documents.

ARTICLE 3—CONTRACT DOCUMENTS: INTENT, REQUIREMENTS, REUSE

3.01 *Intent*

- A. The Contract Documents are complementary; what is required by one Contract Document is as binding as if required by all.
- B. It is the intent of the Contract Documents to describe a functionally complete Project (or part thereof) to be constructed in accordance with the Contract Documents.
- C. Unless otherwise stated in the Contract Documents, if there is a discrepancy between the electronic versions of the Contract Documents (including any printed copies derived from such electronic versions) and the printed record version, the printed record version will govern.
- D. The Contract supersedes prior negotiations, representations, and agreements, whether written or oral.
- E. Engineer will issue clarifications and interpretations of the Contract Documents as provided herein.
- F. Any provision or part of the Contract Documents held to be void or unenforceable under any Law or Regulation will be deemed stricken, and all remaining provisions will continue to be valid and binding upon Owner and Contractor, which agree that the Contract Documents will be reformed to replace such stricken provision or part thereof with a valid and enforceable provision that comes as close as possible to expressing the intention of the stricken provision.
- G. Nothing in the Contract Documents creates:
 - 1. any contractual relationship between Owner or Engineer and any Subcontractor, Supplier, or other individual or entity performing or furnishing any of the Work, for the benefit of such Subcontractor, Supplier, or other individual or entity; or
 - 2. any obligation on the part of Owner or Engineer to pay or to see to the payment of any money due any such Subcontractor, Supplier, or other individual or entity, except as may otherwise be required by Laws and Regulations.

3.02 *Reference Standards*

- A. *Standards Specifications, Codes, Laws and Regulations*
 - 1. Reference in the Contract Documents to standard specifications, manuals, reference standards, or codes of any technical society, organization, or association, or to Laws or Regulations, whether such reference be specific or by implication, means the standard specification, manual, reference standard, code, or Laws or Regulations in effect at the time of opening of Bids (or on the Effective Date of the Contract if there were no Bids), except as may be otherwise specifically stated in the Contract Documents.
 - 2. No provision of any such standard specification, manual, reference standard, or code, and no instruction of a Supplier, will be effective to change the duties or responsibilities of Owner, Contractor, or Engineer from those set forth in the part of the Contract Documents prepared by or for Engineer. No such provision or instruction shall be effective to assign to Owner or Engineer any duty or authority to supervise or direct the performance of the Work, or any duty or authority to undertake responsibility

inconsistent with the provisions of the part of the Contract Documents prepared by or for Engineer.

3.03 *Reporting and Resolving Discrepancies*

A. *Reporting Discrepancies*

1. *Contractor's Verification of Figures and Field Measurements:* Before undertaking each part of the Work, Contractor shall carefully study the Contract Documents, and check and verify pertinent figures and dimensions therein, particularly with respect to applicable field measurements. Contractor shall promptly report in writing to Engineer any conflict, error, ambiguity, or discrepancy that Contractor discovers, or has actual knowledge of, and shall not proceed with any Work affected thereby until the conflict, error, ambiguity, or discrepancy is resolved by a clarification or interpretation by Engineer, or by an amendment or supplement to the Contract issued pursuant to Paragraph 11.01.
2. *Contractor's Review of Contract Documents:* If, before or during the performance of the Work, Contractor discovers any conflict, error, ambiguity, or discrepancy within the Contract Documents, or between the Contract Documents and (a) any applicable Law or Regulation, (b) actual field conditions, (c) any standard specification, manual, reference standard, or code, or (d) any instruction of any Supplier, then Contractor shall promptly report it to Engineer in writing. Contractor shall not proceed with the Work affected thereby (except in an emergency as required by Paragraph 7.15) until the conflict, error, ambiguity, or discrepancy is resolved, by a clarification or interpretation by Engineer, or by an amendment or supplement to the Contract issued pursuant to Paragraph 11.01.
3. Contractor shall not be liable to Owner or Engineer for failure to report any conflict, error, ambiguity, or discrepancy in the Contract Documents unless Contractor had actual knowledge thereof.

B. *Resolving Discrepancies*

1. Except as may be otherwise specifically stated in the Contract Documents, the provisions of the part of the Contract Documents prepared by or for Engineer take precedence in resolving any conflict, error, ambiguity, or discrepancy between such provisions of the Contract Documents and:
 - a. the provisions of any standard specification, manual, reference standard, or code, or the instruction of any Supplier (whether or not specifically incorporated by reference as a Contract Document); or
 - b. the provisions of any Laws or Regulations applicable to the performance of the Work (unless such an interpretation of the provisions of the Contract Documents would result in violation of such Law or Regulation).

3.04 *Requirements of the Contract Documents*

- A. During the performance of the Work and until final payment, Contractor and Owner shall submit to the Engineer in writing all matters in question concerning the requirements of the Contract Documents (sometimes referred to as requests for information or interpretation—RFIs), or relating to the acceptability of the Work under the Contract Documents, as soon as possible after such matters arise. Engineer will be the initial interpreter of the requirements of the Contract Documents, and judge of the acceptability of the Work.

- B. Engineer will, with reasonable promptness, render a written clarification, interpretation, or decision on the issue submitted, or initiate an amendment or supplement to the Contract Documents. Engineer's written clarification, interpretation, or decision will be final and binding on Contractor, unless it appeals by submitting a Change Proposal, and on Owner, unless it appeals by filing a Claim.
- C. If a submitted matter in question concerns terms and conditions of the Contract Documents that do not involve (1) the performance or acceptability of the Work under the Contract Documents, (2) the design (as set forth in the Drawings, Specifications, or otherwise), or (3) other engineering or technical matters, then Engineer will promptly notify Owner and Contractor in writing that Engineer is unable to provide a decision or interpretation. If Owner and Contractor are unable to agree on resolution of such a matter in question, either party may pursue resolution as provided in Article 12.

3.05 *Reuse of Documents*

- A. Contractor and its Subcontractors and Suppliers shall not:
 - 1. have or acquire any title to or ownership rights in any of the Drawings, Specifications, or other documents (or copies of any thereof) prepared by or bearing the seal of Engineer or its consultants, including electronic media versions, or reuse any such Drawings, Specifications, other documents, or copies thereof on extensions of the Project or any other project without written consent of Owner and Engineer and specific written verification or adaptation by Engineer; or
 - 2. have or acquire any title or ownership rights in any other Contract Documents, reuse any such Contract Documents for any purpose without Owner's express written consent, or violate any copyrights pertaining to such Contract Documents.
- B. The prohibitions of this Paragraph 3.05 will survive final payment, or termination of the Contract. Nothing herein precludes Contractor from retaining copies of the Contract Documents for record purposes.

ARTICLE 4—COMMENCEMENT AND PROGRESS OF THE WORK

4.01 *Commencement of Contract Times; Notice to Proceed*

- A. The Contract Times will commence to run on the 30th day after the Effective Date of the Contract or, if a Notice to Proceed is given, on the day indicated in the Notice to Proceed. A Notice to Proceed may be given at any time within 30 days after the Effective Date of the Contract. In no event will the Contract Times commence to run later than the 60th day after the day of Bid opening or the 30th day after the Effective Date of the Contract, whichever date is earlier.

4.02 *Starting the Work*

- A. Contractor shall start to perform the Work on the date when the Contract Times commence to run. No Work may be done at the Site prior to such date.

4.03 *Reference Points*

- A. Owner shall provide engineering surveys to establish reference points for construction which in Engineer's judgment are necessary to enable Contractor to proceed with the Work. Contractor shall be responsible for laying out the Work, shall protect and preserve the

established reference points and property monuments, and shall make no changes or relocations without the prior written approval of Owner. Contractor shall report to Engineer whenever any reference point or property monument is lost or destroyed or requires relocation because of necessary changes in grades or locations, and shall be responsible for the accurate replacement or relocation of such reference points or property monuments by professionally qualified personnel.

4.04 *Progress Schedule*

- A. Contractor shall adhere to the Progress Schedule established in accordance with Paragraph 2.05 as it may be adjusted from time to time as provided below.
 - 1. Contractor shall submit to Engineer for acceptance (to the extent indicated in Paragraph 2.05) proposed adjustments in the Progress Schedule that will not result in changing the Contract Times.
 - 2. Proposed adjustments in the Progress Schedule that will change the Contract Times must be submitted in accordance with the requirements of Article 11.
- B. Contractor shall carry on the Work and adhere to the Progress Schedule during all disputes or disagreements with Owner. No Work will be delayed or postponed pending resolution of any disputes or disagreements, or during any appeal process, except as permitted by Paragraph 16.04, or as Owner and Contractor may otherwise agree in writing.

4.05 *Delays in Contractor's Progress*

- A. If Owner, Engineer, or anyone for whom Owner is responsible, delays, disrupts, or interferes with the performance or progress of the Work, then Contractor shall be entitled to an equitable adjustment in Contract Price or Contract Times.
- B. Contractor shall not be entitled to an adjustment in Contract Price or Contract Times for delay, disruption, or interference caused by or within the control of Contractor. Delay, disruption, and interference attributable to and within the control of a Subcontractor or Supplier shall be deemed to be within the control of Contractor.
- C. If Contractor's performance or progress is delayed, disrupted, or interfered with by unanticipated causes not the fault of and beyond the control of Owner, Contractor, and those for which they are responsible, then Contractor shall be entitled to an equitable adjustment in Contract Times. Such an adjustment will be Contractor's sole and exclusive remedy for the delays, disruption, and interference described in this paragraph. Causes of delay, disruption, or interference that may give rise to an adjustment in Contract Times under this paragraph include but are not limited to the following:
 - 1. Severe and unavoidable natural catastrophes such as fires, floods, epidemics, and earthquakes;
 - 2. Abnormal weather conditions;
 - 3. Acts or failures to act of third-party utility owners or other third-party entities (other than those third-party utility owners or other third-party entities performing other work at or adjacent to the Site as arranged by or under contract with Owner, as contemplated in Article 8); and
 - 4. Acts of war or terrorism.

- D. Contractor's entitlement to an adjustment of Contract Times or Contract Price is limited as follows:
1. Contractor's entitlement to an adjustment of the Contract Times is conditioned on the delay, disruption, or interference adversely affecting an activity on the critical path to completion of the Work, as of the time of the delay, disruption, or interference.
 2. Contractor shall not be entitled to an adjustment in Contract Price for any delay, disruption, or interference if such delay is concurrent with a delay, disruption, or interference caused by or within the control of Contractor. Such a concurrent delay by Contractor shall not preclude an adjustment of Contract Times to which Contractor is otherwise entitled.
 3. Adjustments of Contract Times or Contract Price are subject to the provisions of Article 11.
- E. Each Contractor request or Change Proposal seeking an increase in Contract Times or Contract Price must be supplemented by supporting data that sets forth in detail the following:
1. The circumstances that form the basis for the requested adjustment;
 2. The date upon which each cause of delay, disruption, or interference began to affect the progress of the Work;
 3. The date upon which each cause of delay, disruption, or interference ceased to affect the progress of the Work;
 4. The number of days' increase in Contract Times claimed as a consequence of each such cause of delay, disruption, or interference; and
 5. The impact on Contract Price, in accordance with the provisions of Paragraph 11.07.
- Contractor shall also furnish such additional supporting documentation as Owner or Engineer may require including, where appropriate, a revised progress schedule indicating all the activities affected by the delay, disruption, or interference, and an explanation of the effect of the delay, disruption, or interference on the critical path to completion of the Work.
- F. Delays, disruption, and interference to the performance or progress of the Work resulting from the existence of a differing subsurface or physical condition, an Underground Facility that was not shown or indicated by the Contract Documents, or not shown or indicated with reasonable accuracy, and those resulting from Hazardous Environmental Conditions, are governed by Article 5, together with the provisions of Paragraphs 4.05.D and 4.05.E.
- G. Paragraph 8.03 addresses delays, disruption, and interference to the performance or progress of the Work resulting from the performance of certain other work at or adjacent to the Site.

ARTICLE 5—SITE; SUBSURFACE AND PHYSICAL CONDITIONS; HAZARDOUS ENVIRONMENTAL CONDITIONS

5.01 *Availability of Lands*

- A. Owner shall furnish the Site. Owner shall notify Contractor in writing of any encumbrances or restrictions not of general application but specifically related to use of the Site with which Contractor must comply in performing the Work.

- B. Upon reasonable written request, Owner shall furnish Contractor with a current statement of record legal title and legal description of the lands upon which permanent improvements are to be made and Owner's interest therein as necessary for giving notice of or filing a mechanic's or construction lien against such lands in accordance with applicable Laws and Regulations.
- C. Contractor shall provide for all additional lands and access thereto that may be required for temporary construction facilities or storage of materials and equipment.

5.02 *Use of Site and Other Areas*

A. *Limitation on Use of Site and Other Areas*

1. Contractor shall confine construction equipment, temporary construction facilities, the storage of materials and equipment, and the operations of workers to the Site, adjacent areas that Contractor has arranged to use through construction easements or otherwise, and other adjacent areas permitted by Laws and Regulations, and shall not unreasonably encumber the Site and such other adjacent areas with construction equipment or other materials or equipment. Contractor shall assume full responsibility for (a) damage to the Site; (b) damage to any such other adjacent areas used for Contractor's operations; (c) damage to any other adjacent land or areas, or to improvements, structures, utilities, or similar facilities located at such adjacent lands or areas; and (d) for injuries and losses sustained by the owners or occupants of any such land or areas; provided that such damage or injuries result from the performance of the Work or from other actions or conduct of the Contractor or those for which Contractor is responsible.
 2. If a damage or injury claim is made by the owner or occupant of any such land or area because of the performance of the Work, or because of other actions or conduct of the Contractor or those for which Contractor is responsible, Contractor shall (a) take immediate corrective or remedial action as required by Paragraph 7.13, or otherwise; (b) promptly attempt to settle the claim as to all parties through negotiations with such owner or occupant, or otherwise resolve the claim by arbitration or other dispute resolution proceeding, or in a court of competent jurisdiction; and (c) to the fullest extent permitted by Laws and Regulations, indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them, from and against any such claim, and against all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to any claim or action, legal or equitable, brought by any such owner or occupant against Owner, Engineer, or any other party indemnified hereunder to the extent caused directly or indirectly, in whole or in part by, or based upon, Contractor's performance of the Work, or because of other actions or conduct of the Contractor or those for which Contractor is responsible.
- B. *Removal of Debris During Performance of the Work:* During the progress of the Work the Contractor shall keep the Site and other adjacent areas free from accumulations of waste materials, rubbish, and other debris. Removal and disposal of such waste materials, rubbish, and other debris will conform to applicable Laws and Regulations.
 - C. *Cleaning:* Prior to Substantial Completion of the Work Contractor shall clean the Site and the Work and make it ready for utilization by Owner. At the completion of the Work Contractor shall remove from the Site and adjacent areas all tools, appliances, construction equipment

and machinery, and surplus materials and shall restore to original condition all property not designated for alteration by the Contract Documents.

- D. *Loading of Structures:* Contractor shall not load nor permit any part of any structure to be loaded in any manner that will endanger the structure, nor shall Contractor subject any part of the Work or adjacent structures or land to stresses or pressures that will endanger them.

5.03 *Subsurface and Physical Conditions*

- A. *Reports and Drawings:* The Supplementary Conditions identify:

1. Those reports of explorations and tests of subsurface conditions at or adjacent to the Site that contain Technical Data;
2. Those drawings of existing physical conditions at or adjacent to the Site, including those drawings depicting existing surface or subsurface structures at or adjacent to the Site (except Underground Facilities), that contain Technical Data; and
3. Technical Data contained in such reports and drawings.

- B. *Underground Facilities:* Underground Facilities are shown or indicated on the Drawings, pursuant to Paragraph 5.05, and not in the drawings referred to in Paragraph 5.03.A. Information and data regarding the presence or location of Underground Facilities are not intended to be categorized, identified, or defined as Technical Data.

- C. *Reliance by Contractor on Technical Data:* Contractor may rely upon the accuracy of the Technical Data expressly identified in the Supplementary Conditions with respect to such reports and drawings, but such reports and drawings are not Contract Documents. If no such express identification has been made, then Contractor may rely upon the accuracy of the Technical Data as defined in Paragraph 1.01.A.46.b.

- D. *Limitations of Other Data and Documents:* Except for such reliance on Technical Data, Contractor may not rely upon or make any claim against Owner or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, with respect to:
 1. the completeness of such reports and drawings for Contractor's purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences, and procedures of construction to be employed by Contractor, and safety precautions and programs incident thereto;
 2. other data, interpretations, opinions, and information contained in such reports or shown or indicated in such drawings;
 3. the contents of other Site-related documents made available to Contractor, such as record drawings from other projects at or adjacent to the Site, or Owner's archival documents concerning the Site; or
 4. any Contractor interpretation of or conclusion drawn from any Technical Data or any such other data, interpretations, opinions, or information.

5.04 *Differing Subsurface or Physical Conditions*

- A. *Notice by Contractor:* If Contractor believes that any subsurface or physical condition that is uncovered or revealed at the Site:
1. is of such a nature as to establish that any Technical Data on which Contractor is entitled to rely as provided in Paragraph 5.03 is materially inaccurate;
 2. is of such a nature as to require a change in the Drawings or Specifications;
 3. differs materially from that shown or indicated in the Contract Documents; or
 4. is of an unusual nature, and differs materially from conditions ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract Documents;

then Contractor shall, promptly after becoming aware thereof and before further disturbing the subsurface or physical conditions or performing any Work in connection therewith (except in an emergency as required by Paragraph 7.15), notify Owner and Engineer in writing about such condition. Contractor shall not further disturb such condition or perform any Work in connection therewith (except with respect to an emergency) until receipt of a written statement permitting Contractor to do so.

- B. *Engineer's Review:* After receipt of written notice as required by the preceding paragraph, Engineer will promptly review the subsurface or physical condition in question; determine whether it is necessary for Owner to obtain additional exploration or tests with respect to the condition; conclude whether the condition falls within any one or more of the differing site condition categories in Paragraph 5.04.A; obtain any pertinent cost or schedule information from Contractor; prepare recommendations to Owner regarding the Contractor's resumption of Work in connection with the subsurface or physical condition in question and the need for any change in the Drawings or Specifications; and advise Owner in writing of Engineer's findings, conclusions, and recommendations.
- C. *Owner's Statement to Contractor Regarding Site Condition:* After receipt of Engineer's written findings, conclusions, and recommendations, Owner shall issue a written statement to Contractor (with a copy to Engineer) regarding the subsurface or physical condition in question, addressing the resumption of Work in connection with such condition, indicating whether any change in the Drawings or Specifications will be made, and adopting or rejecting Engineer's written findings, conclusions, and recommendations, in whole or in part.
- D. *Early Resumption of Work:* If at any time Engineer determines that Work in connection with the subsurface or physical condition in question may resume prior to completion of Engineer's review or Owner's issuance of its statement to Contractor, because the condition in question has been adequately documented, and analyzed on a preliminary basis, then the Engineer may at its discretion instruct Contractor to resume such Work.
- E. *Possible Price and Times Adjustments*
1. Contractor shall be entitled to an equitable adjustment in Contract Price or Contract Times, to the extent that the existence of a differing subsurface or physical condition, or any related delay, disruption, or interference, causes an increase or decrease in

Contractor's cost of, or time required for, performance of the Work; subject, however, to the following:

- a. Such condition must fall within any one or more of the categories described in Paragraph 5.04.A;
 - b. With respect to Work that is paid for on a unit price basis, any adjustment in Contract Price will be subject to the provisions of Paragraph 13.03; and,
 - c. Contractor's entitlement to an adjustment of the Contract Times is subject to the provisions of Paragraphs 4.05.D and 4.05.E.
2. Contractor shall not be entitled to any adjustment in the Contract Price or Contract Times with respect to a subsurface or physical condition if:
 - a. Contractor knew of the existence of such condition at the time Contractor made a commitment to Owner with respect to Contract Price and Contract Times by the submission of a Bid or becoming bound under a negotiated contract, or otherwise;
 - b. The existence of such condition reasonably could have been discovered or revealed as a result of any examination, investigation, exploration, test, or study of the Site and contiguous areas expressly required by the Bidding Requirements or Contract Documents to be conducted by or for Contractor prior to Contractor's making such commitment; or
 - c. Contractor failed to give the written notice required by Paragraph 5.04.A.
 3. If Owner and Contractor agree regarding Contractor's entitlement to and the amount or extent of any adjustment in the Contract Price or Contract Times, then any such adjustment will be set forth in a Change Order.
 4. Contractor may submit a Change Proposal regarding its entitlement to or the amount or extent of any adjustment in the Contract Price or Contract Times, no later than 30 days after Owner's issuance of the Owner's written statement to Contractor regarding the subsurface or physical condition in question.
- F. *Underground Facilities; Hazardous Environmental Conditions:* Paragraph 5.05 governs rights and responsibilities regarding the presence or location of Underground Facilities. Paragraph 5.06 governs rights and responsibilities regarding Hazardous Environmental Conditions. The provisions of Paragraphs 5.03 and 5.04 are not applicable to the presence or location of Underground Facilities, or to Hazardous Environmental Conditions.

5.05 *Underground Facilities*

- A. *Contractor's Responsibilities:* Unless it is otherwise expressly provided in the Supplementary Conditions, the cost of all of the following are included in the Contract Price, and Contractor shall have full responsibility for:
1. reviewing and checking all information and data regarding existing Underground Facilities at the Site;
 2. complying with applicable state and local utility damage prevention Laws and Regulations;

3. verifying the actual location of those Underground Facilities shown or indicated in the Contract Documents as being within the area affected by the Work, by exposing such Underground Facilities during the course of construction;
 4. coordination of the Work with the owners (including Owner) of such Underground Facilities, during construction; and
 5. the safety and protection of all existing Underground Facilities at the Site, and repairing any damage thereto resulting from the Work.
- B. *Notice by Contractor:* If Contractor believes that an Underground Facility that is uncovered or revealed at the Site was not shown or indicated on the Drawings, or was not shown or indicated on the Drawings with reasonable accuracy, then Contractor shall, promptly after becoming aware thereof and before further disturbing conditions affected thereby or performing any Work in connection therewith (except in an emergency as required by Paragraph 7.15), notify Owner and Engineer in writing regarding such Underground Facility.
- C. *Engineer's Review:* Engineer will:
1. promptly review the Underground Facility and conclude whether such Underground Facility was not shown or indicated on the Drawings, or was not shown or indicated with reasonable accuracy;
 2. identify and communicate with the owner of the Underground Facility; prepare recommendations to Owner (and if necessary issue any preliminary instructions to Contractor) regarding the Contractor's resumption of Work in connection with the Underground Facility in question;
 3. obtain any pertinent cost or schedule information from Contractor; determine the extent, if any, to which a change is required in the Drawings or Specifications to reflect and document the consequences of the existence or location of the Underground Facility; and
 4. advise Owner in writing of Engineer's findings, conclusions, and recommendations.
- During such time, Contractor shall be responsible for the safety and protection of such Underground Facility.
- D. *Owner's Statement to Contractor Regarding Underground Facility:* After receipt of Engineer's written findings, conclusions, and recommendations, Owner shall issue a written statement to Contractor (with a copy to Engineer) regarding the Underground Facility in question addressing the resumption of Work in connection with such Underground Facility, indicating whether any change in the Drawings or Specifications will be made, and adopting or rejecting Engineer's written findings, conclusions, and recommendations in whole or in part.
- E. *Early Resumption of Work:* If at any time Engineer determines that Work in connection with the Underground Facility may resume prior to completion of Engineer's review or Owner's issuance of its statement to Contractor, because the Underground Facility in question and conditions affected by its presence have been adequately documented, and analyzed on a preliminary basis, then the Engineer may at its discretion instruct Contractor to resume such Work.
- F. *Possible Price and Times Adjustments*
1. Contractor shall be entitled to an equitable adjustment in the Contract Price or Contract Times, to the extent that any existing Underground Facility at the Site that was not shown

or indicated on the Drawings, or was not shown or indicated with reasonable accuracy, or any related delay, disruption, or interference, causes an increase or decrease in Contractor's cost of, or time required for, performance of the Work; subject, however, to the following:

- a. With respect to Work that is paid for on a unit price basis, any adjustment in Contract Price will be subject to the provisions of Paragraph 13.03;
 - b. Contractor's entitlement to an adjustment of the Contract Times is subject to the provisions of Paragraphs 4.05.D and 4.05.E; and
 - c. Contractor gave the notice required in Paragraph 5.05.B.
2. If Owner and Contractor agree regarding Contractor's entitlement to and the amount or extent of any adjustment in the Contract Price or Contract Times, then any such adjustment will be set forth in a Change Order.
 3. Contractor may submit a Change Proposal regarding its entitlement to or the amount or extent of any adjustment in the Contract Price or Contract Times, no later than 30 days after Owner's issuance of the Owner's written statement to Contractor regarding the Underground Facility in question.
 4. The information and data shown or indicated on the Drawings with respect to existing Underground Facilities at the Site is based on information and data (a) furnished by the owners of such Underground Facilities, or by others, (b) obtained from available records, or (c) gathered in an investigation conducted in accordance with the current edition of ASCE 38, Standard Guideline for the Collection and Depiction of Existing Subsurface Utility Data, by the American Society of Civil Engineers. If such information or data is incorrect or incomplete, Contractor's remedies are limited to those set forth in this Paragraph 5.05.F.

5.06 *Hazardous Environmental Conditions at Site*

A. *Reports and Drawings:* The Supplementary Conditions identify:

1. those reports known to Owner relating to Hazardous Environmental Conditions that have been identified at or adjacent to the Site;
2. drawings known to Owner relating to Hazardous Environmental Conditions that have been identified at or adjacent to the Site; and
3. Technical Data contained in such reports and drawings.

B. *Reliance by Contractor on Technical Data Authorized:* Contractor may rely upon the accuracy of the Technical Data expressly identified in the Supplementary Conditions with respect to such reports and drawings, but such reports and drawings are not Contract Documents. If no such express identification has been made, then Contractor may rely on the accuracy of the Technical Data as defined in Paragraph 1.01.A.46.b. Except for such reliance on Technical Data, Contractor may not rely upon or make any claim against Owner or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, with respect to:

1. the completeness of such reports and drawings for Contractor's purposes, including, but not limited to, any aspects of the means, methods, techniques, sequences and procedures

- of construction to be employed by Contractor, and safety precautions and programs incident thereto;
2. other data, interpretations, opinions, and information contained in such reports or shown or indicated in such drawings; or
 3. any Contractor interpretation of or conclusion drawn from any Technical Data or any such other data, interpretations, opinions or information.
- C. Contractor shall not be responsible for removing or remediating any Hazardous Environmental Condition encountered, uncovered, or revealed at the Site unless such removal or remediation is expressly identified in the Contract Documents to be within the scope of the Work.
- D. Contractor shall be responsible for controlling, containing, and duly removing all Constituents of Concern brought to the Site by Contractor, Subcontractors, Suppliers, or anyone else for whom Contractor is responsible, and for any associated costs; and for the costs of removing and remediating any Hazardous Environmental Condition created by the presence of any such Constituents of Concern.
- E. If Contractor encounters, uncovers, or reveals a Hazardous Environmental Condition whose removal or remediation is not expressly identified in the Contract Documents as being within the scope of the Work, or if Contractor or anyone for whom Contractor is responsible creates a Hazardous Environmental Condition, then Contractor shall immediately: (1) secure or otherwise isolate such condition; (2) stop all Work in connection with such condition and in any area affected thereby (except in an emergency as required by Paragraph 7.15); and (3) notify Owner and Engineer (and promptly thereafter confirm such notice in writing). Owner shall promptly consult with Engineer concerning the necessity for Owner to retain a qualified expert to evaluate such condition or take corrective action, if any. Promptly after consulting with Engineer, Owner shall take such actions as are necessary to permit Owner to timely obtain required permits and provide Contractor the written notice required by Paragraph 5.06.F. If Contractor or anyone for whom Contractor is responsible created the Hazardous Environmental Condition in question, then Owner may remove and remediate the Hazardous Environmental Condition, and impose a set-off against payments to account for the associated costs.
- F. Contractor shall not resume Work in connection with such Hazardous Environmental Condition or in any affected area until after Owner has obtained any required permits related thereto, and delivered written notice to Contractor either (1) specifying that such condition and any affected area is or has been rendered safe for the resumption of Work, or (2) specifying any special conditions under which such Work may be resumed safely.
- G. If Owner and Contractor cannot agree as to entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times, as a result of such Work stoppage, such special conditions under which Work is agreed to be resumed by Contractor, or any costs or expenses incurred in response to the Hazardous Environmental Condition, then within 30 days of Owner's written notice regarding the resumption of Work, Contractor may submit a Change Proposal, or Owner may impose a set-off. Entitlement to any such adjustment is subject to the provisions of Paragraphs 4.05.D, 4.05.E, 11.07, and 11.08.
- H. If, after receipt of such written notice, Contractor does not agree to resume such Work based on a reasonable belief it is unsafe, or does not agree to resume such Work under such special

conditions, then Owner may order the portion of the Work that is in the area affected by such condition to be deleted from the Work, following the contractual change procedures in Article 11. Owner may have such deleted portion of the Work performed by Owner's own forces or others in accordance with Article 8.

- I. To the fullest extent permitted by Laws and Regulations, Owner shall indemnify and hold harmless Contractor, Subcontractors, and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals, and all court, arbitration, or other dispute resolution costs) arising out of or relating to a Hazardous Environmental Condition, provided that such Hazardous Environmental Condition (1) was not shown or indicated in the Drawings, Specifications, or other Contract Documents, identified as Technical Data entitled to limited reliance pursuant to Paragraph 5.06.B, or identified in the Contract Documents to be included within the scope of the Work, and (2) was not created by Contractor or by anyone for whom Contractor is responsible. Nothing in this Paragraph 5.06.I obligates Owner to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.
- J. To the fullest extent permitted by Laws and Regulations, Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to the failure to control, contain, or remove a Constituent of Concern brought to the Site by Contractor or by anyone for whom Contractor is responsible, or to a Hazardous Environmental Condition created by Contractor or by anyone for whom Contractor is responsible. Nothing in this Paragraph 5.06.J obligates Contractor to indemnify any individual or entity from and against the consequences of that individual's or entity's own negligence.
- K. The provisions of Paragraphs 5.03, 5.04, and 5.05 do not apply to the presence of Constituents of Concern or to a Hazardous Environmental Condition uncovered or revealed at the Site.

ARTICLE 6—BONDS AND INSURANCE

6.01 *Performance, Payment, and Other Bonds*

- A. Contractor shall furnish a performance bond and a payment bond, each in an amount at least equal to the Contract Price, as security for the faithful performance and payment of Contractor's obligations under the Contract. These bonds must remain in effect until one year after the date when final payment becomes due or until completion of the correction period specified in Paragraph 15.08, whichever is later, except as provided otherwise by Laws or Regulations, the terms of a prescribed bond form, the Supplementary Conditions, or other provisions of the Contract.
- B. Contractor shall also furnish such other bonds (if any) as are required by the Supplementary Conditions or other provisions of the Contract.
- C. All bonds must be in the form included in the Bidding Documents or otherwise specified by Owner prior to execution of the Contract, except as provided otherwise by Laws or

Regulations, and must be issued and signed by a surety named in “Companies Holding Certificates of Authority as Acceptable Sureties on Federal Bonds and as Acceptable Reinsuring Companies” as published in Department Circular 570 (as amended and supplemented) by the Bureau of the Fiscal Service, U.S. Department of the Treasury. A bond signed by an agent or attorney-in-fact must be accompanied by a certified copy of that individual’s authority to bind the surety. The evidence of authority must show that it is effective on the date the agent or attorney-in-fact signed the accompanying bond.

- D. Contractor shall obtain the required bonds from surety companies that are duly licensed or authorized, in the state or jurisdiction in which the Project is located, to issue bonds in the required amounts.
- E. If the surety on a bond furnished by Contractor is declared bankrupt or becomes insolvent, or the surety ceases to meet the requirements above, then Contractor shall promptly notify Owner and Engineer in writing and shall, within 20 days after the event giving rise to such notification, provide another bond and surety, both of which must comply with the bond and surety requirements above.
- F. If Contractor has failed to obtain a required bond, Owner may exclude the Contractor from the Site and exercise Owner’s termination rights under Article 16.
- G. Upon request to Owner from any Subcontractor, Supplier, or other person or entity claiming to have furnished labor, services, materials, or equipment used in the performance of the Work, Owner shall provide a copy of the payment bond to such person or entity.
- H. Upon request to Contractor from any Subcontractor, Supplier, or other person or entity claiming to have furnished labor, services, materials, or equipment used in the performance of the Work, Contractor shall provide a copy of the payment bond to such person or entity.

6.02 *Insurance—General Provisions*

- A. Owner and Contractor shall obtain and maintain insurance as required in this article and in the Supplementary Conditions.
- B. All insurance required by the Contract to be purchased and maintained by Owner or Contractor shall be obtained from insurance companies that are duly licensed or authorized in the state or jurisdiction in which the Project is located to issue insurance policies for the required limits and coverages. Unless a different standard is indicated in the Supplementary Conditions, all companies that provide insurance policies required under this Contract shall have an A.M. Best rating of A-VII or better.
- C. Alternative forms of insurance coverage, including but not limited to self-insurance and “Occupational Accident and Excess Employer’s Indemnity Policies,” are not sufficient to meet the insurance requirements of this Contract, unless expressly allowed in the Supplementary Conditions.
- D. Contractor shall deliver to Owner, with copies to each additional insured identified in the Contract, certificates of insurance and endorsements establishing that Contractor has obtained and is maintaining the policies and coverages required by the Contract. Upon request by Owner or any other insured, Contractor shall also furnish other evidence of such required insurance, including but not limited to copies of policies, documentation of applicable self-insured retentions (if allowed) and deductibles, full disclosure of all relevant exclusions, and evidence of insurance required to be purchased and maintained by

Subcontractors or Suppliers. In any documentation furnished under this provision, Contractor, Subcontractors, and Suppliers may block out (redact) (1) any confidential premium or pricing information and (2) any wording specific to a project or jurisdiction other than those applicable to this Contract.

- E. Owner shall deliver to Contractor, with copies to each additional insured identified in the Contract, certificates of insurance and endorsements establishing that Owner has obtained and is maintaining the policies and coverages required of Owner by the Contract (if any). Upon request by Contractor or any other insured, Owner shall also provide other evidence of such required insurance (if any), including but not limited to copies of policies, documentation of applicable self-insured retentions (if allowed) and deductibles, and full disclosure of all relevant exclusions. In any documentation furnished under this provision, Owner may block out (redact) (1) any confidential premium or pricing information and (2) any wording specific to a project or jurisdiction other than those relevant to this Contract.
- F. Failure of Owner or Contractor to demand such certificates or other evidence of the other party's full compliance with these insurance requirements, or failure of Owner or Contractor to identify a deficiency in compliance from the evidence provided, will not be construed as a waiver of the other party's obligation to obtain and maintain such insurance.
- G. In addition to the liability insurance required to be provided by Contractor, the Owner, at Owner's option, may purchase and maintain Owner's own liability insurance. Owner's liability policies, if any, operate separately and independently from policies required to be provided by Contractor, and Contractor cannot rely upon Owner's liability policies for any of Contractor's obligations to the Owner, Engineer, or third parties.
- H. Contractor shall require:
 - 1. Subcontractors to purchase and maintain worker's compensation, commercial general liability, and other insurance that is appropriate for their participation in the Project, and to name as additional insureds Owner and Engineer (and any other individuals or entities identified in the Supplementary Conditions as additional insureds on Contractor's liability policies) on each Subcontractor's commercial general liability insurance policy; and
 - 2. Suppliers to purchase and maintain insurance that is appropriate for their participation in the Project.
- I. If either party does not purchase or maintain the insurance required of such party by the Contract, such party shall notify the other party in writing of such failure to purchase prior to the start of the Work, or of such failure to maintain prior to any change in the required coverage.
- J. If Contractor has failed to obtain and maintain required insurance, Contractor's entitlement to enter or remain at the Site will end immediately, and Owner may impose an appropriate set-off against payment for any associated costs (including but not limited to the cost of purchasing necessary insurance coverage), and exercise Owner's termination rights under Article 16.
- K. Without prejudice to any other right or remedy, if a party has failed to obtain required insurance, the other party may elect (but is in no way obligated) to obtain equivalent insurance to protect such other party's interests at the expense of the party who was required to provide such coverage, and the Contract Price will be adjusted accordingly.

- L. Owner does not represent that insurance coverage and limits established in this Contract necessarily will be adequate to protect Contractor or Contractor's interests. Contractor is responsible for determining whether such coverage and limits are adequate to protect its interests, and for obtaining and maintaining any additional insurance that Contractor deems necessary.
- M. The insurance and insurance limits required herein will not be deemed as a limitation on Contractor's liability, or that of its Subcontractors or Suppliers, under the indemnities granted to Owner and other individuals and entities in the Contract or otherwise.
- N. All the policies of insurance required to be purchased and maintained under this Contract will contain a provision or endorsement that the coverage afforded will not be canceled, or renewal refused, until at least 10 days prior written notice has been given to the purchasing policyholder. Within three days of receipt of any such written notice, the purchasing policyholder shall provide a copy of the notice to each other insured and Engineer.

6.03 *Contractor's Insurance*

- A. *Required Insurance:* Contractor shall purchase and maintain Worker's Compensation, Commercial General Liability, and other insurance pursuant to the specific requirements of the Supplementary Conditions.
- B. *General Provisions:* The policies of insurance required by this Paragraph 6.03 as supplemented must:
 - 1. include at least the specific coverages required;
 - 2. be written for not less than the limits provided, or those required by Laws or Regulations, whichever is greater;
 - 3. remain in effect at least until the Work is complete (as set forth in Paragraph 15.06.D), and longer if expressly required elsewhere in this Contract, and at all times thereafter when Contractor may be correcting, removing, or replacing defective Work as a warranty or correction obligation, or otherwise, or returning to the Site to conduct other tasks arising from the Contract;
 - 4. apply with respect to the performance of the Work, whether such performance is by Contractor, any Subcontractor or Supplier, or by anyone directly or indirectly employed by any of them to perform any of the Work, or by anyone for whose acts any of them may be liable; and
 - 5. include all necessary endorsements to support the stated requirements.
- C. *Additional Insureds:* The Contractor's commercial general liability, automobile liability, employer's liability, umbrella or excess, pollution liability, and unmanned aerial vehicle liability policies, if required by this Contract, must:
 - 1. include and list as additional insureds Owner and Engineer, and any individuals or entities identified as additional insureds in the Supplementary Conditions;
 - 2. include coverage for the respective officers, directors, members, partners, employees, and consultants of all such additional insureds;
 - 3. afford primary coverage to these additional insureds for all claims covered thereby (including as applicable those arising from both ongoing and completed operations);

4. not seek contribution from insurance maintained by the additional insured; and
5. as to commercial general liability insurance, apply to additional insureds with respect to liability caused in whole or in part by Contractor's acts or omissions, or the acts and omissions of those working on Contractor's behalf, in the performance of Contractor's operations.

6.04 *Builder's Risk and Other Property Insurance*

- A. *Builder's Risk*: Unless otherwise provided in the Supplementary Conditions, Contractor shall purchase and maintain builder's risk insurance upon the Work on a completed value basis, in the amount of the Work's full insurable replacement cost (subject to such deductible amounts as may be provided in the Supplementary Conditions or required by Laws and Regulations). The specific requirements applicable to the builder's risk insurance are set forth in the Supplementary Conditions.
- B. *Property Insurance for Facilities of Owner Where Work Will Occur*: Owner is responsible for obtaining and maintaining property insurance covering each existing structure, building, or facility in which any part of the Work will occur, or to which any part of the Work will attach or be adjoined. Such property insurance will be written on a special perils (all-risk) form, on a replacement cost basis, providing coverage consistent with that required for the builder's risk insurance, and will be maintained until the Work is complete, as set forth in Paragraph 15.06.D.
- C. *Property Insurance for Substantially Complete Facilities*: Promptly after Substantial Completion, and before actual occupancy or use of the substantially completed Work, Owner will obtain property insurance for such substantially completed Work, and maintain such property insurance at least until the Work is complete, as set forth in Paragraph 15.06.D. Such property insurance will be written on a special perils (all-risk) form, on a replacement cost basis, and provide coverage consistent with that required for the builder's risk insurance. The builder's risk insurance may terminate upon written confirmation of Owner's procurement of such property insurance.
- D. *Partial Occupancy or Use by Owner*: If Owner will occupy or use a portion or portions of the Work prior to Substantial Completion of all the Work, as provided in Paragraph 15.04, then Owner (directly, if it is the purchaser of the builder's risk policy, or through Contractor) will provide advance notice of such occupancy or use to the builder's risk insurer, and obtain an endorsement consenting to the continuation of coverage prior to commencing such partial occupancy or use.
- E. *Insurance of Other Property; Additional Insurance*: If the express insurance provisions of the Contract do not require or address the insurance of a property item or interest, then the entity or individual owning such property item will be responsible for insuring it. If Contractor elects to obtain other special insurance to be included in or supplement the builder's risk or property insurance policies provided under this Paragraph 6.04, it may do so at Contractor's expense.

6.05 *Property Losses; Subrogation*

- A. The builder's risk insurance policy purchased and maintained in accordance with Paragraph 6.04 (or an installation floater policy if authorized by the Supplementary Conditions), will contain provisions to the effect that in the event of payment of any loss or damage the insurer will have no rights of recovery against any insureds thereunder, or against

Engineer or its consultants, or their officers, directors, members, partners, employees, agents, consultants, or subcontractors.

1. Owner and Contractor waive all rights against each other and the respective officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, for all losses and damages caused by, arising out of, or resulting from any of the perils, risks, or causes of loss covered by such policies and any other property insurance applicable to the Work; and, in addition, waive all such rights against Engineer, its consultants, all individuals or entities identified in the Supplementary Conditions as builder's risk or installation floater insureds, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, under such policies for losses and damages so caused.
 2. None of the above waivers extends to the rights that any party making such waiver may have to the proceeds of insurance held by Owner or Contractor as trustee or fiduciary, or otherwise payable under any policy so issued.
- B. Any property insurance policy maintained by Owner covering any loss, damage, or consequential loss to Owner's existing structures, buildings, or facilities in which any part of the Work will occur, or to which any part of the Work will attach or adjoin; to adjacent structures, buildings, or facilities of Owner; or to part or all of the completed or substantially completed Work, during partial occupancy or use pursuant to Paragraph 15.04, after Substantial Completion pursuant to Paragraph 15.03, or after final payment pursuant to Paragraph 15.06, will contain provisions to the effect that in the event of payment of any loss or damage the insurer will have no rights of recovery against any insureds thereunder, or against Contractor, Subcontractors, or Engineer, or the officers, directors, members, partners, employees, agents, consultants, or subcontractors of each and any of them, and that the insured is allowed to waive the insurer's rights of subrogation in a written contract executed prior to the loss, damage, or consequential loss.
1. Owner waives all rights against Contractor, Subcontractors, and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them, for all losses and damages caused by, arising out of, or resulting from fire or any of the perils, risks, or causes of loss covered by such policies.
- C. The waivers in this Paragraph 6.05 include the waiver of rights due to business interruption, loss of use, or other consequential loss extending beyond direct physical loss or damage to Owner's property or the Work caused by, arising out of, or resulting from fire or other insured peril, risk, or cause of loss.
- D. Contractor shall be responsible for assuring that each Subcontract contains provisions whereby the Subcontractor waives all rights against Owner, Contractor, all individuals or entities identified in the Supplementary Conditions as insureds, the Engineer and its consultants, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, for all losses and damages caused by, arising out of, relating to, or resulting from fire or other peril, risk, or cause of loss covered by builder's risk insurance, installation floater, and any other property insurance applicable to the Work.

6.06 *Receipt and Application of Property Insurance Proceeds*

- A. Any insured loss under the builder's risk and other policies of property insurance required by Paragraph 6.04 will be adjusted and settled with the named insured that purchased the policy. Such named insured shall act as fiduciary for the other insureds, and give notice to such other insureds that adjustment and settlement of a claim is in progress. Any other insured may state its position regarding a claim for insured loss in writing within 15 days after notice of such claim.
- B. Proceeds for such insured losses may be made payable by the insurer either jointly to multiple insureds, or to the named insured that purchased the policy in its own right and as fiduciary for other insureds, subject to the requirements of any applicable mortgage clause. A named insured receiving insurance proceeds under the builder's risk and other policies of insurance required by Paragraph 6.04 shall maintain such proceeds in a segregated account, and distribute such proceeds in accordance with such agreement as the parties in interest may reach, or as otherwise required under the dispute resolution provisions of this Contract or applicable Laws and Regulations.
- C. If no other special agreement is reached, Contractor shall repair or replace the damaged Work, using allocated insurance proceeds.

ARTICLE 7—CONTRACTOR'S RESPONSIBILITIES

7.01 *Contractor's Means and Methods of Construction*

- A. Contractor shall be solely responsible for the means, methods, techniques, sequences, and procedures of construction.
- B. If the Contract Documents note, or Contractor determines, that professional engineering or other design services are needed to carry out Contractor's responsibilities for construction means, methods, techniques, sequences, and procedures, or for Site safety, then Contractor shall cause such services to be provided by a properly licensed design professional, at Contractor's expense. Such services are not Owner-delegated professional design services under this Contract, and neither Owner nor Engineer has any responsibility with respect to (1) Contractor's determination of the need for such services, (2) the qualifications or licensing of the design professionals retained or employed by Contractor, (3) the performance of such services, or (4) any errors, omissions, or defects in such services.

7.02 *Supervision and Superintendence*

- A. Contractor shall supervise, inspect, and direct the Work competently and efficiently, devoting such attention thereto and applying such skills and expertise as may be necessary to perform the Work in accordance with the Contract Documents.
- B. At all times during the progress of the Work, Contractor shall assign a competent resident superintendent who will not be replaced without written notice to Owner and Engineer except under extraordinary circumstances.

7.03 *Labor; Working Hours*

- A. Contractor shall provide competent, suitably qualified personnel to survey and lay out the Work and perform construction as required by the Contract Documents. Contractor shall maintain good discipline and order at the Site.

- B. Contractor shall be fully responsible to Owner and Engineer for all acts and omissions of Contractor's employees; of Suppliers and Subcontractors, and their employees; and of any other individuals or entities performing or furnishing any of the Work, just as Contractor is responsible for Contractor's own acts and omissions.
- C. Except as otherwise required for the safety or protection of persons or the Work or property at the Site or adjacent thereto, and except as otherwise stated in the Contract Documents, all Work at the Site will be performed during regular working hours, Monday through Friday. Contractor will not perform Work on a Saturday, Sunday, or any legal holiday. Contractor may perform Work outside regular working hours or on Saturdays, Sundays, or legal holidays only with Owner's written consent, which will not be unreasonably withheld.

7.04 *Services, Materials, and Equipment*

- A. Unless otherwise specified in the Contract Documents, Contractor shall provide and assume full responsibility for all services, materials, equipment, labor, transportation, construction equipment and machinery, tools, appliances, fuel, power, light, heat, telephone, water, sanitary facilities, temporary facilities, and all other facilities and incidentals necessary for the performance, testing, start up, and completion of the Work, whether or not such items are specifically called for in the Contract Documents.
- B. All materials and equipment incorporated into the Work must be new and of good quality, except as otherwise provided in the Contract Documents. All special warranties and guarantees required by the Specifications will expressly run to the benefit of Owner. If required by Engineer, Contractor shall furnish satisfactory evidence (including reports of required tests) as to the source, kind, and quality of materials and equipment.
- C. All materials and equipment must be stored, applied, installed, connected, erected, protected, used, cleaned, and conditioned in accordance with instructions of the applicable Supplier, except as otherwise may be provided in the Contract Documents.

7.05 *"Or Equals"*

- A. *Contractor's Request; Governing Criteria:* Whenever an item of equipment or material is specified or described in the Contract Documents by using the names of one or more proprietary items or specific Suppliers, the Contract Price has been based upon Contractor furnishing such item as specified. The specification or description of such an item is intended to establish the type, function, appearance, and quality required. Unless the specification or description contains or is followed by words reading that no like, equivalent, or "or equal" item is permitted, Contractor may request that Engineer authorize the use of other items of equipment or material, or items from other proposed Suppliers, under the circumstances described below.
 - 1. If Engineer in its sole discretion determines that an item of equipment or material proposed by Contractor is functionally equal to that named and sufficiently similar so that no change in related Work will be required, Engineer will deem it an "or equal" item. For the purposes of this paragraph, a proposed item of equipment or material will be considered functionally equal to an item so named if:
 - a. in the exercise of reasonable judgment Engineer determines that the proposed item:
 - 1) is at least equal in materials of construction, quality, durability, appearance, strength, and design characteristics;

- 2) will reliably perform at least equally well the function and achieve the results imposed by the design concept of the completed Project as a functioning whole;
 - 3) has a proven record of performance and availability of responsive service; and
 - 4) is not objectionable to Owner.
- b. Contractor certifies that, if the proposed item is approved and incorporated into the Work:
- 1) there will be no increase in cost to the Owner or increase in Contract Times; and
 - 2) the item will conform substantially to the detailed requirements of the item named in the Contract Documents.
- B. *Contractor's Expense*: Contractor shall provide all data in support of any proposed "or equal" item at Contractor's expense.
- C. *Engineer's Evaluation and Determination*: Engineer will be allowed a reasonable time to evaluate each "or-equal" request. Engineer may require Contractor to furnish additional data about the proposed "or-equal" item. Engineer will be the sole judge of acceptability. No "or-equal" item will be ordered, furnished, installed, or utilized until Engineer's review is complete and Engineer determines that the proposed item is an "or-equal," which will be evidenced by an approved Shop Drawing or other written communication. Engineer will advise Contractor in writing of any negative determination.
- D. *Effect of Engineer's Determination*: Neither approval nor denial of an "or-equal" request will result in any change in Contract Price. The Engineer's denial of an "or-equal" request will be final and binding, and may not be reversed through an appeal under any provision of the Contract.
- E. *Treatment as a Substitution Request*: If Engineer determines that an item of equipment or material proposed by Contractor does not qualify as an "or-equal" item, Contractor may request that Engineer consider the item a proposed substitute pursuant to Paragraph 7.06.

7.06 Substitutes

- A. *Contractor's Request; Governing Criteria*: Unless the specification or description of an item of equipment or material required to be furnished under the Contract Documents contains or is followed by words reading that no substitution is permitted, Contractor may request that Engineer authorize the use of other items of equipment or material under the circumstances described below. To the extent possible such requests must be made before commencement of related construction at the Site.
1. Contractor shall submit sufficient information as provided below to allow Engineer to determine if the item of material or equipment proposed is functionally equivalent to that named and an acceptable substitute therefor. Engineer will not accept requests for review of proposed substitute items of equipment or material from anyone other than Contractor.
 2. The requirements for review by Engineer will be as set forth in Paragraph 7.06.B, as supplemented by the Specifications, and as Engineer may decide is appropriate under the circumstances.

3. Contractor shall make written application to Engineer for review of a proposed substitute item of equipment or material that Contractor seeks to furnish or use. The application:
 - a. will certify that the proposed substitute item will:
 - 1) perform adequately the functions and achieve the results called for by the general design;
 - 2) be similar in substance to the item specified; and
 - 3) be suited to the same use as the item specified.
 - b. will state:
 - 1) the extent, if any, to which the use of the proposed substitute item will necessitate a change in Contract Times;
 - 2) whether use of the proposed substitute item in the Work will require a change in any of the Contract Documents (or in the provisions of any other direct contract with Owner for other work on the Project) to adapt the design to the proposed substitute item; and
 - 3) whether incorporation or use of the proposed substitute item in connection with the Work is subject to payment of any license fee or royalty.
 - c. will identify:
 - 1) all variations of the proposed substitute item from the item specified; and
 - 2) available engineering, sales, maintenance, repair, and replacement services.
 - d. will contain an itemized estimate of all costs or credits that will result directly or indirectly from use of such substitute item, including but not limited to changes in Contract Price, shared savings, costs of redesign, and claims of other contractors affected by any resulting change.
- B. *Engineer's Evaluation and Determination*: Engineer will be allowed a reasonable time to evaluate each substitute request, and to obtain comments and direction from Owner. Engineer may require Contractor to furnish additional data about the proposed substitute item. Engineer will be the sole judge of acceptability. No substitute will be ordered, furnished, installed, or utilized until Engineer's review is complete and Engineer determines that the proposed item is an acceptable substitute. Engineer's determination will be evidenced by a Field Order or a proposed Change Order accounting for the substitution itself and all related impacts, including changes in Contract Price or Contract Times. Engineer will advise Contractor in writing of any negative determination.
- C. *Special Guarantee*: Owner may require Contractor to furnish at Contractor's expense a special performance guarantee or other surety with respect to any substitute.
- D. *Reimbursement of Engineer's Cost*: Engineer will record Engineer's costs in evaluating a substitute proposed or submitted by Contractor. Whether or not Engineer approves a substitute so proposed or submitted by Contractor, Contractor shall reimburse Owner for the reasonable charges of Engineer for evaluating each such proposed substitute. Contractor shall also reimburse Owner for the reasonable charges of Engineer for making changes in the Contract Documents (or in the provisions of any other direct contract with Owner) resulting from the acceptance of each proposed substitute.

- E. *Contractor's Expense*: Contractor shall provide all data in support of any proposed substitute at Contractor's expense.
- F. *Effect of Engineer's Determination*: If Engineer approves the substitution request, Contractor shall execute the proposed Change Order and proceed with the substitution. The Engineer's denial of a substitution request will be final and binding, and may not be reversed through an appeal under any provision of the Contract. Contractor may challenge the scope of reimbursement costs imposed under Paragraph 7.06.D, by timely submittal of a Change Proposal.

7.07 *Concerning Subcontractors and Suppliers*

- A. Contractor may retain Subcontractors and Suppliers for the performance of parts of the Work. Such Subcontractors and Suppliers must be acceptable to Owner. The Contractor's retention of a Subcontractor or Supplier for the performance of parts of the Work will not relieve Contractor's obligation to Owner to perform and complete the Work in accordance with the Contract Documents.
- B. Contractor shall retain specific Subcontractors and Suppliers for the performance of designated parts of the Work if required by the Contract to do so.
- C. Subsequent to the submittal of Contractor's Bid or final negotiation of the terms of the Contract, Owner may not require Contractor to retain any Subcontractor or Supplier to furnish or perform any of the Work against which Contractor has reasonable objection.
- D. Prior to entry into any binding subcontract or purchase order, Contractor shall submit to Owner the identity of the proposed Subcontractor or Supplier (unless Owner has already deemed such proposed Subcontractor or Supplier acceptable during the bidding process or otherwise). Such proposed Subcontractor or Supplier shall be deemed acceptable to Owner unless Owner raises a substantive, reasonable objection within 5 days.
- E. Owner may require the replacement of any Subcontractor or Supplier. Owner also may require Contractor to retain specific replacements; provided, however, that Owner may not require a replacement to which Contractor has a reasonable objection. If Contractor has submitted the identity of certain Subcontractors or Suppliers for acceptance by Owner, and Owner has accepted it (either in writing or by failing to make written objection thereto), then Owner may subsequently revoke the acceptance of any such Subcontractor or Supplier so identified solely on the basis of substantive, reasonable objection after due investigation. Contractor shall submit an acceptable replacement for the rejected Subcontractor or Supplier.
- F. If Owner requires the replacement of any Subcontractor or Supplier retained by Contractor to perform any part of the Work, then Contractor shall be entitled to an adjustment in Contract Price or Contract Times, with respect to the replacement; and Contractor shall initiate a Change Proposal for such adjustment within 30 days of Owner's requirement of replacement.
- G. No acceptance by Owner of any such Subcontractor or Supplier, whether initially or as a replacement, will constitute a waiver of the right of Owner to the completion of the Work in accordance with the Contract Documents.

- H. On a monthly basis, Contractor shall submit to Engineer a complete list of all Subcontractors and Suppliers having a direct contract with Contractor, and of all other Subcontractors and Suppliers known to Contractor at the time of submittal.
- I. Contractor shall be solely responsible for scheduling and coordinating the work of Subcontractors and Suppliers.
- J. The divisions and sections of the Specifications and the identifications of any Drawings do not control Contractor in dividing the Work among Subcontractors or Suppliers, or in delineating the Work to be performed by any specific trade.
- K. All Work performed for Contractor by a Subcontractor or Supplier must be pursuant to an appropriate contractual agreement that specifically binds the Subcontractor or Supplier to the applicable terms and conditions of the Contract for the benefit of Owner and Engineer.
- L. Owner may furnish to any Subcontractor or Supplier, to the extent practicable, information about amounts paid to Contractor for Work performed for Contractor by the Subcontractor or Supplier.
- M. Contractor shall restrict all Subcontractors and Suppliers from communicating with Engineer or Owner, except through Contractor or in case of an emergency, or as otherwise expressly allowed in this Contract.

7.08 *Patent Fees and Royalties*

- A. Contractor shall pay all license fees and royalties and assume all costs incident to the use in the performance of the Work or the incorporation in the Work of any invention, design, process, product, or device which is the subject of patent rights or copyrights held by others. If an invention, design, process, product, or device is specified in the Contract Documents for use in the performance of the Work and if, to the actual knowledge of Owner or Engineer, its use is subject to patent rights or copyrights calling for the payment of any license fee or royalty to others, the existence of such rights will be disclosed in the Contract Documents.
- B. To the fullest extent permitted by Laws and Regulations, Owner shall indemnify and hold harmless Contractor, and its officers, directors, members, partners, employees, agents, consultants, and subcontractors, from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals, and all court or arbitration or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device specified in the Contract Documents, but not identified as being subject to payment of any license fee or royalty to others required by patent rights or copyrights.
- C. To the fullest extent permitted by Laws and Regulations, Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them, from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to any infringement of patent rights or copyrights incident to the use in the performance of the Work or resulting from the incorporation in the Work of any invention, design, process, product, or device not specified in the Contract Documents.

7.09 *Permits*

- A. Unless otherwise provided in the Contract Documents, Contractor shall obtain and pay for all construction permits, licenses, and certificates of occupancy. Owner shall assist Contractor, when necessary, in obtaining such permits and licenses. Contractor shall pay all governmental charges and inspection fees necessary for the prosecution of the Work which are applicable at the time of the submission of Contractor's Bid (or when Contractor became bound under a negotiated contract). Owner shall pay all charges of utility owners for connections for providing permanent service to the Work.

7.10 *Taxes*

- A. Contractor shall pay all sales, consumer, use, and other similar taxes required to be paid by Contractor in accordance with the Laws and Regulations of the place of the Project which are applicable during the performance of the Work.

7.11 *Laws and Regulations*

- A. Contractor shall give all notices required by and shall comply with all Laws and Regulations applicable to the performance of the Work. Neither Owner nor Engineer shall be responsible for monitoring Contractor's compliance with any Laws or Regulations.
- B. If Contractor performs any Work or takes any other action knowing or having reason to know that it is contrary to Laws or Regulations, Contractor shall bear all resulting costs and losses, and shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants, and subcontractors of each and any of them, from and against all claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such Work or other action. It is not Contractor's responsibility to make certain that the Work described in the Contract Documents is in accordance with Laws and Regulations, but this does not relieve Contractor of its obligations under Paragraph 3.03.
- C. Owner or Contractor may give written notice to the other party of any changes after the submission of Contractor's Bid (or after the date when Contractor became bound under a negotiated contract) in Laws or Regulations having an effect on the cost or time of performance of the Work, including but not limited to changes in Laws or Regulations having an effect on procuring permits and on sales, use, value-added, consumption, and other similar taxes. If Owner and Contractor are unable to agree on entitlement to or on the amount or extent, if any, of any adjustment in Contract Price or Contract Times resulting from such changes, then within 30 days of such written notice Contractor may submit a Change Proposal, or Owner may initiate a Claim.

7.12 *Record Documents*

- A. Contractor shall maintain in a safe place at the Site one printed record copy of all Drawings, Specifications, Addenda, Change Orders, Work Change Directives, Field Orders, written interpretations and clarifications, and approved Shop Drawings. Contractor shall keep such record documents in good order and annotate them to show changes made during construction. These record documents, together with all approved Samples, will be available to Engineer for reference. Upon completion of the Work, Contractor shall deliver these record documents to Engineer.

7.13 *Safety and Protection*

- A. Contractor shall be solely responsible for initiating, maintaining, and supervising all safety precautions and programs in connection with the Work. Such responsibility does not relieve Subcontractors of their responsibility for the safety of persons or property in the performance of their work, nor for compliance with applicable safety Laws and Regulations.
- B. Contractor shall designate a qualified and experienced safety representative whose duties and responsibilities are the prevention of Work-related accidents and the maintenance and supervision of safety precautions and programs.
- C. Contractor shall take all necessary precautions for the safety of, and shall provide the necessary protection to prevent damage, injury, or loss to:
 - 1. all persons on the Site or who may be affected by the Work;
 - 2. all the Work and materials and equipment to be incorporated therein, whether in storage on or off the Site; and
 - 3. other property at the Site or adjacent thereto, including trees, shrubs, lawns, walks, pavements, roadways, structures, other work in progress, utilities, and Underground Facilities not designated for removal, relocation, or replacement in the course of construction.
- D. All damage, injury, or loss to any property referred to in Paragraph 7.13.C.2 or 7.13.C.3 caused, directly or indirectly, in whole or in part, by Contractor, any Subcontractor, Supplier, or any other individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, shall be remedied by Contractor at its expense (except damage or loss attributable to the fault of Drawings or Specifications or to the acts or omissions of Owner or Engineer or anyone employed by any of them, or anyone for whose acts any of them may be liable, and not attributable, directly or indirectly, in whole or in part, to the fault or negligence of Contractor or any Subcontractor, Supplier, or other individual or entity directly or indirectly employed by any of them).
- E. Contractor shall comply with all applicable Laws and Regulations relating to the safety of persons or property, or to the protection of persons or property from damage, injury, or loss; and shall erect and maintain all necessary safeguards for such safety and protection.
- F. Contractor shall notify Owner; the owners of adjacent property; the owners of Underground Facilities and other utilities (if the identity of such owners is known to Contractor); and other contractors and utility owners performing work at or adjacent to the Site, in writing, when Contractor knows that prosecution of the Work may affect them, and shall cooperate with them in the protection, removal, relocation, and replacement of their property or work in progress.
- G. Contractor shall comply with the applicable requirements of Owner's safety programs, if any. Any Owner's safety programs that are applicable to the Work are identified or included in the Supplementary Conditions or Specifications.
- H. Contractor shall inform Owner and Engineer of the specific requirements of Contractor's safety program with which Owner's and Engineer's employees and representatives must comply while at the Site.

- I. Contractor's duties and responsibilities for safety and protection will continue until all the Work is completed, Engineer has issued a written notice to Owner and Contractor in accordance with Paragraph 15.06.C that the Work is acceptable, and Contractor has left the Site (except as otherwise expressly provided in connection with Substantial Completion).
- J. Contractor's duties and responsibilities for safety and protection will resume whenever Contractor or any Subcontractor or Supplier returns to the Site to fulfill warranty or correction obligations, or to conduct other tasks arising from the Contract Documents.

7.14 *Hazard Communication Programs*

- A. Contractor shall be responsible for coordinating any exchange of safety data sheets (formerly known as material safety data sheets) or other hazard communication information required to be made available to or exchanged between or among employers at the Site in accordance with Laws or Regulations.

7.15 *Emergencies*

- A. In emergencies affecting the safety or protection of persons or the Work or property at the Site or adjacent thereto, Contractor is obligated to act to prevent damage, injury, or loss. Contractor shall give Engineer prompt written notice if Contractor believes that any significant changes in the Work or variations from the Contract Documents have been caused by an emergency, or are required as a result of Contractor's response to an emergency. If Engineer determines that a change in the Contract Documents is required because of an emergency or Contractor's response, a Work Change Directive or Change Order will be issued.

7.16 *Submittals*

A. *Shop Drawing and Sample Requirements*

- 1. Before submitting a Shop Drawing or Sample, Contractor shall:
 - a. review and coordinate the Shop Drawing or Sample with other Shop Drawings and Samples and with the requirements of the Work and the Contract Documents;
 - b. determine and verify:
 - 1) all field measurements, quantities, dimensions, specified performance and design criteria, installation requirements, materials, catalog numbers, and similar information with respect to the Submittal;
 - 2) the suitability of all materials and equipment offered with respect to the indicated application, fabrication, shipping, handling, storage, assembly, and installation pertaining to the performance of the Work; and
 - 3) all information relative to Contractor's responsibilities for means, methods, techniques, sequences, and procedures of construction, and safety precautions and programs incident thereto;
 - c. confirm that the Submittal is complete with respect to all related data included in the Submittal.
- 2. Each Shop Drawing or Sample must bear a stamp or specific written certification that Contractor has satisfied Contractor's obligations under the Contract Documents with respect to Contractor's review of that Submittal, and that Contractor approves the Submittal.

3. With each Shop Drawing or Sample, Contractor shall give Engineer specific written notice of any variations that the Submittal may have from the requirements of the Contract Documents. This notice must be set forth in a written communication separate from the Submittal; and, in addition, in the case of a Shop Drawing by a specific notation made on the Shop Drawing itself.
- B. *Submittal Procedures for Shop Drawings and Samples:* Contractor shall label and submit Shop Drawings and Samples to Engineer for review and approval in accordance with the accepted Schedule of Submittals.
1. *Shop Drawings*
 - a. Contractor shall submit the number of copies required in the Specifications.
 - b. Data shown on the Shop Drawings must be complete with respect to quantities, dimensions, specified performance and design criteria, materials, and similar data to show Engineer the services, materials, and equipment Contractor proposes to provide, and to enable Engineer to review the information for the limited purposes required by Paragraph 7.16.C.
 2. *Samples*
 - a. Contractor shall submit the number of Samples required in the Specifications.
 - b. Contractor shall clearly identify each Sample as to material, Supplier, pertinent data such as catalog numbers, the use for which intended and other data as Engineer may require to enable Engineer to review the Submittal for the limited purposes required by Paragraph 7.16.C.
 3. Where a Shop Drawing or Sample is required by the Contract Documents or the Schedule of Submittals, any related Work performed prior to Engineer's review and approval of the pertinent submittal will be at the sole expense and responsibility of Contractor.
- C. *Engineer's Review of Shop Drawings and Samples*
1. Engineer will provide timely review of Shop Drawings and Samples in accordance with the accepted Schedule of Submittals. Engineer's review and approval will be only to determine if the items covered by the Submittals will, after installation or incorporation in the Work, comply with the requirements of the Contract Documents, and be compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents.
 2. Engineer's review and approval will not extend to means, methods, techniques, sequences, or procedures of construction, or to safety precautions or programs incident thereto.
 3. Engineer's review and approval of a separate item as such will not indicate approval of the assembly in which the item functions.
 4. Engineer's review and approval of a Shop Drawing or Sample will not relieve Contractor from responsibility for any variation from the requirements of the Contract Documents unless Contractor has complied with the requirements of Paragraph 7.16.A.3 and Engineer has given written approval of each such variation by specific written notation thereof incorporated in or accompanying the Shop Drawing or Sample. Engineer will

document any such approved variation from the requirements of the Contract Documents in a Field Order or other appropriate Contract modification.

5. Engineer's review and approval of a Shop Drawing or Sample will not relieve Contractor from responsibility for complying with the requirements of Paragraphs 7.16.A and B.
6. Engineer's review and approval of a Shop Drawing or Sample, or of a variation from the requirements of the Contract Documents, will not, under any circumstances, change the Contract Times or Contract Price, unless such changes are included in a Change Order.
7. Neither Engineer's receipt, review, acceptance, or approval of a Shop Drawing or Sample will result in such item becoming a Contract Document.
8. Contractor shall perform the Work in compliance with the requirements and commitments set forth in approved Shop Drawings and Samples, subject to the provisions of Paragraph 7.16.C.4.

D. *Resubmittal Procedures for Shop Drawings and Samples*

1. Contractor shall make corrections required by Engineer and shall return the required number of corrected copies of Shop Drawings and submit, as required, new Samples for review and approval. Contractor shall direct specific attention in writing to revisions other than the corrections called for by Engineer on previous Submittals.
2. Contractor shall furnish required Shop Drawing and Sample submittals with sufficient information and accuracy to obtain required approval of an item with no more than two resubmittals. Engineer will record Engineer's time for reviewing a third or subsequent resubmittal of a Shop Drawing or Sample, and Contractor shall be responsible for Engineer's charges to Owner for such time. Owner may impose a set-off against payments due Contractor to secure reimbursement for such charges.
3. If Contractor requests a change of a previously approved Shop Drawing or Sample, Contractor shall be responsible for Engineer's charges to Owner for its review time, and Owner may impose a set-off against payments due Contractor to secure reimbursement for such charges, unless the need for such change is beyond the control of Contractor.

E. *Submittals Other than Shop Drawings, Samples, and Owner-Delegated Designs*

1. The following provisions apply to all Submittals other than Shop Drawings, Samples, and Owner-delegated designs:
 - a. Contractor shall submit all such Submittals to the Engineer in accordance with the Schedule of Submittals and pursuant to the applicable terms of the Contract Documents.
 - b. Engineer will provide timely review of all such Submittals in accordance with the Schedule of Submittals and return such Submittals with a notation of either Accepted or Not Accepted. Any such Submittal that is not returned within the time established in the Schedule of Submittals will be deemed accepted.
 - c. Engineer's review will be only to determine if the Submittal is acceptable under the requirements of the Contract Documents as to general form and content of the Submittal.

- d. If any such Submittal is not accepted, Contractor shall confer with Engineer regarding the reason for the non-acceptance, and resubmit an acceptable document.
- 2. Procedures for the submittal and acceptance of the Progress Schedule, the Schedule of Submittals, and the Schedule of Values are set forth in Paragraphs 2.03, 2.04, and 2.05.
- F. Owner-delegated Designs: Submittals pursuant to Owner-delegated designs are governed by the provisions of Paragraph 7.19.

7.17 Contractor's General Warranty and Guarantee

- A. Contractor warrants and guarantees to Owner that all Work will be in accordance with the Contract Documents and will not be defective. Engineer is entitled to rely on Contractor's warranty and guarantee.
- B. Owner's rights under this warranty and guarantee are in addition to, and are not limited by, Owner's rights under the correction period provisions of Paragraph 15.08. The time in which Owner may enforce its warranty and guarantee rights under this Paragraph 7.17 is limited only by applicable Laws and Regulations restricting actions to enforce such rights; provided, however, that after the end of the correction period under Paragraph 15.08:
 - 1. Owner shall give Contractor written notice of any defective Work within 60 days of the discovery that such Work is defective; and
 - 2. Such notice will be deemed the start of an event giving rise to a Claim under Paragraph 12.01.B, such that any related Claim must be brought within 30 days of the notice.
- C. Contractor's warranty and guarantee hereunder excludes defects or damage caused by:
 - 1. abuse, or improper modification, maintenance, or operation, by persons other than Contractor, Subcontractors, Suppliers, or any other individual or entity for whom Contractor is responsible; or
 - 2. normal wear and tear under normal usage.
- D. Contractor's obligation to perform and complete the Work in accordance with the Contract Documents is absolute. None of the following will constitute an acceptance of Work that is not in accordance with the Contract Documents, a release of Contractor's obligation to perform the Work in accordance with the Contract Documents, or a release of Owner's warranty and guarantee rights under this Paragraph 7.17:
 - 1. Observations by Engineer;
 - 2. Recommendation by Engineer or payment by Owner of any progress or final payment;
 - 3. The issuance of a certificate of Substantial Completion by Engineer or any payment related thereto by Owner;
 - 4. Use or occupancy of the Work or any part thereof by Owner;
 - 5. Any review and approval of a Shop Drawing or Sample submittal;
 - 6. The issuance of a notice of acceptability by Engineer;
 - 7. The end of the correction period established in Paragraph 15.08;
 - 8. Any inspection, test, or approval by others; or

9. Any correction of defective Work by Owner.
- E. If the Contract requires the Contractor to accept the assignment of a contract entered into by Owner, then the specific warranties, guarantees, and correction obligations contained in the assigned contract will govern with respect to Contractor's performance obligations to Owner for the Work described in the assigned contract.

7.18 Indemnification

- A. To the fullest extent permitted by Laws and Regulations, and in addition to any other obligations of Contractor under the Contract or otherwise, Contractor shall indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them, from losses, damages, costs, and judgments (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals, and all court or arbitration or other dispute resolution costs) arising from third-party claims or actions relating to or resulting from the performance or furnishing of the Work, provided that any such claim, action, loss, cost, judgment or damage is attributable to bodily injury, sickness, disease, or death, or to damage to or destruction of tangible property (other than the Work itself), including the loss of use resulting therefrom, but only to the extent caused by any negligent act or omission of Contractor, any Subcontractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable.
- B. In any and all claims against Owner or Engineer, or any of their officers, directors, members, partners, employees, agents, consultants, or subcontractors, by any employee (or the survivor or personal representative of such employee) of Contractor, any Subcontractor, any Supplier, or any individual or entity directly or indirectly employed by any of them to perform any of the Work, or anyone for whose acts any of them may be liable, the indemnification obligation under Paragraph 7.18.A will not be limited in any way by any limitation on the amount or type of damages, compensation, or benefits payable by or for Contractor or any such Subcontractor, Supplier, or other individual or entity under workers' compensation acts, disability benefit acts, or other employee benefit acts.

7.19 Delegation of Professional Design Services

- A. Owner may require Contractor to provide professional design services for a portion of the Work by express delegation in the Contract Documents. Such delegation will specify the performance and design criteria that such services must satisfy, and the Submittals that Contractor must furnish to Engineer with respect to the Owner-delegated design.
- B. Contractor shall cause such Owner-delegated professional design services to be provided pursuant to the professional standard of care by a properly licensed design professional, whose signature and seal must appear on all drawings, calculations, specifications, certifications, and Submittals prepared by such design professional. Such design professional must issue all certifications of design required by Laws and Regulations.
- C. If a Shop Drawing or other Submittal related to the Owner-delegated design is prepared by Contractor, a Subcontractor, or others for submittal to Engineer, then such Shop Drawing or other Submittal must bear the written approval of Contractor's design professional when submitted by Contractor to Engineer.

- D. Owner and Engineer shall be entitled to rely upon the adequacy, accuracy, and completeness of the services, certifications, and approvals performed or provided by the design professionals retained or employed by Contractor under an Owner-delegated design, subject to the professional standard of care and the performance and design criteria stated in the Contract Documents.
- E. Pursuant to this Paragraph 7.19, Engineer's review, approval, and other determinations regarding design drawings, calculations, specifications, certifications, and other Submittals furnished by Contractor pursuant to an Owner-delegated design will be only for the following limited purposes:
 - 1. Checking for conformance with the requirements of this Paragraph 7.19;
 - 2. Confirming that Contractor (through its design professionals) has used the performance and design criteria specified in the Contract Documents; and
 - 3. Establishing that the design furnished by Contractor is consistent with the design concept expressed in the Contract Documents.
- F. Contractor shall not be responsible for the adequacy of performance or design criteria specified by Owner or Engineer.
- G. Contractor is not required to provide professional services in violation of applicable Laws and Regulations.

ARTICLE 8—OTHER WORK AT THE SITE

8.01 *Other Work*

- A. In addition to and apart from the Work under the Contract Documents, the Owner may perform other work at or adjacent to the Site. Such other work may be performed by Owner's employees, or through contracts between the Owner and third parties. Owner may also arrange to have third-party utility owners perform work on their utilities and facilities at or adjacent to the Site.
- B. If Owner performs other work at or adjacent to the Site with Owner's employees, or through contracts for such other work, then Owner shall give Contractor written notice thereof prior to starting any such other work. If Owner has advance information regarding the start of any third-party utility work that Owner has arranged to take place at or adjacent to the Site, Owner shall provide such information to Contractor.
- C. Contractor shall afford proper and safe access to the Site to each contractor that performs such other work, each utility owner performing other work, and Owner, if Owner is performing other work with Owner's employees, and provide a reasonable opportunity for the introduction and storage of materials and equipment and the execution of such other work.
- D. Contractor shall do all cutting, fitting, and patching of the Work that may be required to properly connect or otherwise make its several parts come together and properly integrate with such other work. Contractor shall not endanger any work of others by cutting, excavating, or otherwise altering such work; provided, however, that Contractor may cut or alter others' work with the written consent of Engineer and the others whose work will be affected.

- E. If the proper execution or results of any part of Contractor's Work depends upon work performed by others, Contractor shall inspect such other work and promptly report to Engineer in writing any delays, defects, or deficiencies in such other work that render it unavailable or unsuitable for the proper execution and results of Contractor's Work. Contractor's failure to so report will constitute an acceptance of such other work as fit and proper for integration with Contractor's Work except for latent defects and deficiencies in such other work.
- F. The provisions of this article are not applicable to work that is performed by third-party utilities or other third-party entities without a contract with Owner, or that is performed without having been arranged by Owner. If such work occurs, then any related delay, disruption, or interference incurred by Contractor is governed by the provisions of Paragraph 4.05.C.3.

8.02 *Coordination*

- A. If Owner intends to contract with others for the performance of other work at or adjacent to the Site, to perform other work at or adjacent to the Site with Owner's employees, or to arrange to have utility owners perform work at or adjacent to the Site, the following will be set forth in the Supplementary Conditions or provided to Contractor prior to the start of any such other work:
 - 1. The identity of the individual or entity that will have authority and responsibility for coordination of the activities among the various contractors;
 - 2. An itemization of the specific matters to be covered by such authority and responsibility; and
 - 3. The extent of such authority and responsibilities.
- B. Unless otherwise provided in the Supplementary Conditions, Owner shall have sole authority and responsibility for such coordination.

8.03 *Legal Relationships*

- A. If, in the course of performing other work for Owner at or adjacent to the Site, the Owner's employees, any other contractor working for Owner, or any utility owner that Owner has arranged to perform work, causes damage to the Work or to the property of Contractor or its Subcontractors, or delays, disrupts, interferes with, or increases the scope or cost of the performance of the Work, through actions or inaction, then Contractor shall be entitled to an equitable adjustment in the Contract Price or the Contract Times. Contractor must submit any Change Proposal seeking an equitable adjustment in the Contract Price or the Contract Times under this paragraph within 30 days of the damaging, delaying, disrupting, or interfering event. The entitlement to, and extent of, any such equitable adjustment will take into account information (if any) regarding such other work that was provided to Contractor in the Contract Documents prior to the submittal of the Bid or the final negotiation of the terms of the Contract, and any remedies available to Contractor under Laws or Regulations concerning utility action or inaction. When applicable, any such equitable adjustment in Contract Price will be conditioned on Contractor assigning to Owner all Contractor's rights against such other contractor or utility owner with respect to the damage, delay, disruption, or interference that is the subject of the adjustment. Contractor's entitlement to an adjustment of the Contract Times or Contract Price is subject to the provisions of Paragraphs 4.05.D and 4.05.E.

- B. Contractor shall take reasonable and customary measures to avoid damaging, delaying, disrupting, or interfering with the work of Owner, any other contractor, or any utility owner performing other work at or adjacent to the Site.
 - 1. If Contractor fails to take such measures and as a result damages, delays, disrupts, or interferes with the work of any such other contractor or utility owner, then Owner may impose a set-off against payments due Contractor, and assign to such other contractor or utility owner the Owner's contractual rights against Contractor with respect to the breach of the obligations set forth in this Paragraph 8.03.B.
 - 2. When Owner is performing other work at or adjacent to the Site with Owner's employees, Contractor shall be liable to Owner for damage to such other work, and for the reasonable direct delay, disruption, and interference costs incurred by Owner as a result of Contractor's failure to take reasonable and customary measures with respect to Owner's other work. In response to such damage, delay, disruption, or interference, Owner may impose a set-off against payments due Contractor.
- C. If Contractor damages, delays, disrupts, or interferes with the work of any other contractor, or any utility owner performing other work at or adjacent to the Site, through Contractor's failure to take reasonable and customary measures to avoid such impacts, or if any claim arising out of Contractor's actions, inactions, or negligence in performance of the Work at or adjacent to the Site is made by any such other contractor or utility owner against Contractor, Owner, or Engineer, then Contractor shall (1) promptly attempt to settle the claim as to all parties through negotiations with such other contractor or utility owner, or otherwise resolve the claim by arbitration or other dispute resolution proceeding or at law, and (2) indemnify and hold harmless Owner and Engineer, and the officers, directors, members, partners, employees, agents, consultants and subcontractors of each and any of them from and against any such claims, and against all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such damage, delay, disruption, or interference.

ARTICLE 9—OWNER'S RESPONSIBILITIES

9.01 *Communications to Contractor*

- A. Except as otherwise provided in these General Conditions, Owner shall issue all communications to Contractor through Engineer.

9.02 *Replacement of Engineer*

- A. Owner may at its discretion appoint an engineer to replace Engineer, provided Contractor makes no reasonable objection to the replacement engineer. The replacement engineer's status under the Contract Documents will be that of the former Engineer.

9.03 *Furnish Data*

- A. Owner shall promptly furnish the data required of Owner under the Contract Documents.

9.04 *Pay When Due*

- A. Owner shall make payments to Contractor when they are due as provided in the Agreement.

9.05 *Lands and Easements; Reports, Tests, and Drawings*

- A. Owner's duties with respect to providing lands and easements are set forth in Paragraph 5.01.
- B. Owner's duties with respect to providing engineering surveys to establish reference points are set forth in Paragraph 4.03.
- C. Article 5 refers to Owner's identifying and making available to Contractor copies of reports of explorations and tests of conditions at the Site, and drawings of physical conditions relating to existing surface or subsurface structures at the Site.

9.06 *Insurance*

- A. Owner's responsibilities, if any, with respect to purchasing and maintaining liability and property insurance are set forth in Article 6.

9.07 *Change Orders*

- A. Owner's responsibilities with respect to Change Orders are set forth in Article 11.

9.08 *Inspections, Tests, and Approvals*

- A. Owner's responsibility with respect to certain inspections, tests, and approvals is set forth in Paragraph 14.02.B.

9.09 *Limitations on Owner's Responsibilities*

- A. The Owner shall not supervise, direct, or have control or authority over, nor be responsible for, Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work. Owner will not be responsible for Contractor's failure to perform the Work in accordance with the Contract Documents.

9.10 *Undisclosed Hazardous Environmental Condition*

- A. Owner's responsibility in respect to an undisclosed Hazardous Environmental Condition is set forth in Paragraph 5.06.

9.11 *Evidence of Financial Arrangements*

- A. Upon request of Contractor, Owner shall furnish Contractor reasonable evidence that financial arrangements have been made to satisfy Owner's obligations under the Contract (including obligations under proposed changes in the Work).

9.12 *Safety Programs*

- A. While at the Site, Owner's employees and representatives shall comply with the specific applicable requirements of Contractor's safety programs of which Owner has been informed.
- B. Owner shall furnish copies of any applicable Owner safety programs to Contractor.

ARTICLE 10—ENGINEER'S STATUS DURING CONSTRUCTION

10.01 *Owner's Representative*

- A. Engineer will be Owner's representative during the construction period. The duties and responsibilities and the limitations of authority of Engineer as Owner's representative during construction are set forth in the Contract.

10.02 *Visits to Site*

- A. Engineer will make visits to the Site at intervals appropriate to the various stages of construction as Engineer deems necessary in order to observe, as an experienced and qualified design professional, the progress that has been made and the quality of the various aspects of Contractor's executed Work. Based on information obtained during such visits and observations, Engineer, for the benefit of Owner, will determine, in general, if the Work is proceeding in accordance with the Contract Documents. Engineer will not be required to make exhaustive or continuous inspections on the Site to check the quality or quantity of the Work. Engineer's efforts will be directed toward providing for Owner a greater degree of confidence that the completed Work will conform generally to the Contract Documents. On the basis of such visits and observations, Engineer will keep Owner informed of the progress of the Work and will endeavor to guard Owner against defective Work.
- B. Engineer's visits and observations are subject to all the limitations on Engineer's authority and responsibility set forth in Paragraph 10.07. Particularly, but without limitation, during or as a result of Engineer's visits or observations of Contractor's Work, Engineer will not supervise, direct, control, or have authority over or be responsible for Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work.

10.03 *Resident Project Representative*

- A. If Owner and Engineer have agreed that Engineer will furnish a Resident Project Representative to represent Engineer at the Site and assist Engineer in observing the progress and quality of the Work, then the authority and responsibilities of any such Resident Project Representative will be as provided in the Supplementary Conditions, and limitations on the responsibilities thereof will be as provided in the Supplementary Conditions and in Paragraph 10.07.
- B. If Owner designates an individual or entity who is not Engineer's consultant, agent, or employee to represent Owner at the Site, then the responsibilities and authority of such individual or entity will be as provided in the Supplementary Conditions.

10.04 *Engineer's Authority*

- A. Engineer has the authority to reject Work in accordance with Article 14.
- B. Engineer's authority as to Submittals is set forth in Paragraph 7.16.
- C. Engineer's authority as to design drawings, calculations, specifications, certifications and other Submittals from Contractor in response to Owner's delegation (if any) to Contractor of professional design services, is set forth in Paragraph 7.19.
- D. Engineer's authority as to changes in the Work is set forth in Article 11.

E. Engineer's authority as to Applications for Payment is set forth in Article 15.

10.05 *Determinations for Unit Price Work*

A. Engineer will determine the actual quantities and classifications of Unit Price Work performed by Contractor as set forth in Paragraph 13.03.

10.06 *Decisions on Requirements of Contract Documents and Acceptability of Work*

A. Engineer will render decisions regarding the requirements of the Contract Documents, and judge the acceptability of the Work, pursuant to the specific procedures set forth herein for initial interpretations, Change Proposals, and acceptance of the Work. In rendering such decisions and judgments, Engineer will not show partiality to Owner or Contractor, and will not be liable to Owner, Contractor, or others in connection with any proceedings, interpretations, decisions, or judgments conducted or rendered in good faith.

10.07 *Limitations on Engineer's Authority and Responsibilities*

A. Neither Engineer's authority or responsibility under this Article 10 or under any other provision of the Contract, nor any decision made by Engineer in good faith either to exercise or not exercise such authority or responsibility or the undertaking, exercise, or performance of any authority or responsibility by Engineer, will create, impose, or give rise to any duty in contract, tort, or otherwise owed by Engineer to Contractor, any Subcontractor, any Supplier, any other individual or entity, or to any surety for or employee or agent of any of them.

B. Engineer will not supervise, direct, control, or have authority over or be responsible for Contractor's means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto, or for any failure of Contractor to comply with Laws and Regulations applicable to the performance of the Work. Engineer will not be responsible for Contractor's failure to perform the Work in accordance with the Contract Documents.

C. Engineer will not be responsible for the acts or omissions of Contractor or of any Subcontractor, any Supplier, or of any other individual or entity performing any of the Work.

D. Engineer's review of the final Application for Payment and accompanying documentation, and all maintenance and operating instructions, schedules, guarantees, bonds, certificates of inspection, tests and approvals, and other documentation required to be delivered by Contractor under Paragraph 15.06.A, will only be to determine generally that their content complies with the requirements of, and in the case of certificates of inspections, tests, and approvals, that the results certified indicate compliance with the Contract Documents.

E. The limitations upon authority and responsibility set forth in this Paragraph 10.07 also apply to the Resident Project Representative, if any.

10.08 *Compliance with Safety Program*

A. While at the Site, Engineer's employees and representatives will comply with the specific applicable requirements of Owner's and Contractor's safety programs of which Engineer has been informed.

ARTICLE 11—CHANGES TO THE CONTRACT

11.01 *Amending and Supplementing the Contract*

- A. The Contract may be amended or supplemented by a Change Order, a Work Change Directive, or a Field Order.
- B. If an amendment or supplement to the Contract includes a change in the Contract Price or the Contract Times, such amendment or supplement must be set forth in a Change Order.
- C. All changes to the Contract that involve (1) the performance or acceptability of the Work, (2) the design (as set forth in the Drawings, Specifications, or otherwise), or (3) other engineering or technical matters, must be supported by Engineer's recommendation. Owner and Contractor may amend other terms and conditions of the Contract without the recommendation of the Engineer.

11.02 *Change Orders*

- A. Owner and Contractor shall execute appropriate Change Orders covering:
 - 1. Changes in Contract Price or Contract Times which are agreed to by the parties, including any undisputed sum or amount of time for Work actually performed in accordance with a Work Change Directive;
 - 2. Changes in Contract Price resulting from an Owner set-off, unless Contractor has duly contested such set-off;
 - 3. Changes in the Work which are: (a) ordered by Owner pursuant to Paragraph 11.05, (b) required because of Owner's acceptance of defective Work under Paragraph 14.04 or Owner's correction of defective Work under Paragraph 14.07, or (c) agreed to by the parties, subject to the need for Engineer's recommendation if the change in the Work involves the design (as set forth in the Drawings, Specifications, or otherwise) or other engineering or technical matters; and
 - 4. Changes that embody the substance of any final and binding results under: Paragraph 11.03.B, resolving the impact of a Work Change Directive; Paragraph 11.09, concerning Change Proposals; Article 12, Claims; Paragraph 13.02.D, final adjustments resulting from allowances; Paragraph 13.03.D, final adjustments relating to determination of quantities for Unit Price Work; and similar provisions.
- B. If Owner or Contractor refuses to execute a Change Order that is required to be executed under the terms of Paragraph 11.02.A, it will be deemed to be of full force and effect, as if fully executed.

11.03 *Work Change Directives*

- A. A Work Change Directive will not change the Contract Price or the Contract Times but is evidence that the parties expect that the modification ordered or documented by a Work Change Directive will be incorporated in a subsequently issued Change Order, following negotiations by the parties as to the Work Change Directive's effect, if any, on the Contract Price and Contract Times; or, if negotiations are unsuccessful, by a determination under the terms of the Contract Documents governing adjustments, expressly including Paragraph 11.07 regarding change of Contract Price.

- B. If Owner has issued a Work Change Directive and:
 - 1. Contractor believes that an adjustment in Contract Times or Contract Price is necessary, then Contractor shall submit any Change Proposal seeking such an adjustment no later than 30 days after the completion of the Work set out in the Work Change Directive.
 - 2. Owner believes that an adjustment in Contract Times or Contract Price is necessary, then Owner shall submit any Claim seeking such an adjustment no later than 60 days after issuance of the Work Change Directive.

11.04 *Field Orders*

- A. Engineer may authorize minor changes in the Work if the changes do not involve an adjustment in the Contract Price or the Contract Times and are compatible with the design concept of the completed Project as a functioning whole as indicated by the Contract Documents. Such changes will be accomplished by a Field Order and will be binding on Owner and also on Contractor, which shall perform the Work involved promptly.
- B. If Contractor believes that a Field Order justifies an adjustment in the Contract Price or Contract Times, then before proceeding with the Work at issue, Contractor shall submit a Change Proposal as provided herein.

11.05 *Owner-Authorized Changes in the Work*

- A. Without invalidating the Contract and without notice to any surety, Owner may, at any time or from time to time, order additions, deletions, or revisions in the Work. Changes involving the design (as set forth in the Drawings, Specifications, or otherwise) or other engineering or technical matters will be supported by Engineer's recommendation.
- B. Such changes in the Work may be accomplished by a Change Order, if Owner and Contractor have agreed as to the effect, if any, of the changes on Contract Times or Contract Price; or by a Work Change Directive. Upon receipt of any such document, Contractor shall promptly proceed with the Work involved; or, in the case of a deletion in the Work, promptly cease construction activities with respect to such deleted Work. Added or revised Work must be performed under the applicable conditions of the Contract Documents.
- C. Nothing in this Paragraph 11.05 obligates Contractor to undertake work that Contractor reasonably concludes cannot be performed in a manner consistent with Contractor's safety obligations under the Contract Documents or Laws and Regulations.

11.06 *Unauthorized Changes in the Work*

- A. Contractor shall not be entitled to an increase in the Contract Price or an extension of the Contract Times with respect to any work performed that is not required by the Contract Documents, as amended, modified, or supplemented, except in the case of an emergency as provided in Paragraph 7.15 or in the case of uncovering Work as provided in Paragraph 14.05.C.2.

11.07 *Change of Contract Price*

- A. The Contract Price may only be changed by a Change Order. Any Change Proposal for an adjustment in the Contract Price must comply with the provisions of Paragraph 11.09. Any Claim for an adjustment of Contract Price must comply with the provisions of Article 12.
- B. An adjustment in the Contract Price will be determined as follows:

1. Where the Work involved is covered by unit prices contained in the Contract Documents, then by application of such unit prices to the quantities of the items involved (subject to the provisions of Paragraph 13.03);
 2. Where the Work involved is not covered by unit prices contained in the Contract Documents, then by a mutually agreed lump sum (which may include an allowance for overhead and profit not necessarily in accordance with Paragraph 11.07.C.2); or
 3. Where the Work involved is not covered by unit prices contained in the Contract Documents and the parties do not reach mutual agreement to a lump sum, then on the basis of the Cost of the Work (determined as provided in Paragraph 13.01) plus a Contractor's fee for overhead and profit (determined as provided in Paragraph 11.07.C).
- C. *Contractor's Fee:* When applicable, the Contractor's fee for overhead and profit will be determined as follows:
1. A mutually acceptable fixed fee; or
 2. If a fixed fee is not agreed upon, then a fee based on the following percentages of the various portions of the Cost of the Work:
 - a. For costs incurred under Paragraphs 13.01.B.1 and 13.01.B.2, the Contractor's fee will be 15 percent;
 - b. For costs incurred under Paragraph 13.01.B.3, the Contractor's fee will be 5 percent;
 - c. Where one or more tiers of subcontracts are on the basis of Cost of the Work plus a fee and no fixed fee is agreed upon, the intent of Paragraphs 11.07.C.2.a and 11.07.C.2.b is that the Contractor's fee will be based on: (1) a fee of 15 percent of the costs incurred under Paragraphs 13.01.B.1 and 13.01.B.2 by the Subcontractor that actually performs the Work, at whatever tier, and (2) with respect to Contractor itself and to any Subcontractors of a tier higher than that of the Subcontractor that actually performs the Work, a fee of 5 percent of the amount (fee plus underlying costs incurred) attributable to the next lower tier Subcontractor; provided, however, that for any such subcontracted Work the maximum total fee to be paid by Owner will be no greater than 27 percent of the costs incurred by the Subcontractor that actually performs the Work;
 - d. No fee will be payable on the basis of costs itemized under Paragraphs 13.01.B.4, 13.01.B.5, and 13.01.C;
 - e. The amount of credit to be allowed by Contractor to Owner for any change which results in a net decrease in Cost of the Work will be the amount of the actual net decrease in Cost of the Work and a deduction of an additional amount equal to 5 percent of such actual net decrease in Cost of the Work; and
 - f. When both additions and credits are involved in any one change or Change Proposal, the adjustment in Contractor's fee will be computed by determining the sum of the costs in each of the cost categories in Paragraph 13.01.B (specifically, payroll costs, Paragraph 13.01.B.1; incorporated materials and equipment costs, Paragraph 13.01.B.2; Subcontract costs, Paragraph 13.01.B.3; special consultants costs, Paragraph 13.01.B.4; and other costs, Paragraph 13.01.B.5) and applying to each such cost category sum the appropriate fee from Paragraphs 11.07.C.2.a through 11.07.C.2.e, inclusive.

11.08 *Change of Contract Times*

- A. The Contract Times may only be changed by a Change Order. Any Change Proposal for an adjustment in the Contract Times must comply with the provisions of Paragraph 11.09. Any Claim for an adjustment in the Contract Times must comply with the provisions of Article 12.
- B. Delay, disruption, and interference in the Work, and any related changes in Contract Times, are addressed in and governed by Paragraph 4.05.

11.09 *Change Proposals*

- A. *Purpose and Content:* Contractor shall submit a Change Proposal to Engineer to request an adjustment in the Contract Times or Contract Price; contest an initial decision by Engineer concerning the requirements of the Contract Documents or relating to the acceptability of the Work under the Contract Documents; challenge a set-off against payment due; or seek other relief under the Contract. The Change Proposal will specify any proposed change in Contract Times or Contract Price, or other proposed relief, and explain the reason for the proposed change, with citations to any governing or applicable provisions of the Contract Documents. Each Change Proposal will address only one issue, or a set of closely related issues.

- B. *Change Proposal Procedures*

- 1. *Submittal:* Contractor shall submit each Change Proposal to Engineer within 30 days after the start of the event giving rise thereto, or after such initial decision.
- 2. *Supporting Data:* The Contractor shall submit supporting data, including the proposed change in Contract Price or Contract Time (if any), to the Engineer and Owner within 15 days after the submittal of the Change Proposal.
 - a. Change Proposals based on or related to delay, interruption, or interference must comply with the provisions of Paragraphs 4.05.D and 4.05.E.
 - b. Change proposals related to a change of Contract Price must include full and detailed accounts of materials incorporated into the Work and labor and equipment used for the subject Work.

The supporting data must be accompanied by a written statement that the supporting data are accurate and complete, and that any requested time or price adjustment is the entire adjustment to which Contractor believes it is entitled as a result of said event.

- 3. *Engineer's Initial Review:* Engineer will advise Owner regarding the Change Proposal, and consider any comments or response from Owner regarding the Change Proposal. If in its discretion Engineer concludes that additional supporting data is needed before conducting a full review and making a decision regarding the Change Proposal, then Engineer may request that Contractor submit such additional supporting data by a date specified by Engineer, prior to Engineer beginning its full review of the Change Proposal.
- 4. *Engineer's Full Review and Action on the Change Proposal:* Upon receipt of Contractor's supporting data (including any additional data requested by Engineer), Engineer will conduct a full review of each Change Proposal and, within 30 days after such receipt of the Contractor's supporting data, either approve the Change Proposal in whole, deny it in whole, or approve it in part and deny it in part. Such actions must be in writing, with a copy provided to Owner and Contractor. If Engineer does not take action on the Change

Proposal within 30 days, then either Owner or Contractor may at any time thereafter submit a letter to the other party indicating that as a result of Engineer's inaction the Change Proposal is deemed denied, thereby commencing the time for appeal of the denial under Article 12.

5. *Binding Decision*: Engineer's decision is final and binding upon Owner and Contractor, unless Owner or Contractor appeals the decision by filing a Claim under Article 12.
- C. *Resolution of Certain Change Proposals*: If the Change Proposal does not involve the design (as set forth in the Drawings, Specifications, or otherwise), the acceptability of the Work, or other engineering or technical matters, then Engineer will notify the parties in writing that the Engineer is unable to resolve the Change Proposal. For purposes of further resolution of such a Change Proposal, such notice will be deemed a denial, and Contractor may choose to seek resolution under the terms of Article 12.
- D. *Post-Completion*: Contractor shall not submit any Change Proposals after Engineer issues a written recommendation of final payment pursuant to Paragraph 15.06.B.

11.10 *Notification to Surety*

- A. If the provisions of any bond require notice to be given to a surety of any change affecting the general scope of the Work or the provisions of the Contract Documents (including, but not limited to, Contract Price or Contract Times), the giving of any such notice will be Contractor's responsibility. The amount of each applicable bond will be adjusted to reflect the effect of any such change.

ARTICLE 12—CLAIMS

12.01 *Claims*

- A. *Claims Process*: The following disputes between Owner and Contractor are subject to the Claims process set forth in this article:
 1. Appeals by Owner or Contractor of Engineer's decisions regarding Change Proposals;
 2. Owner demands for adjustments in the Contract Price or Contract Times, or other relief under the Contract Documents;
 3. Disputes that Engineer has been unable to address because they do not involve the design (as set forth in the Drawings, Specifications, or otherwise), the acceptability of the Work, or other engineering or technical matters; and
 4. Subject to the waiver provisions of Paragraph 15.07, any dispute arising after Engineer has issued a written recommendation of final payment pursuant to Paragraph 15.06.B.
- B. *Submittal of Claim*: The party submitting a Claim shall deliver it directly to the other party to the Contract promptly (but in no event later than 30 days) after the start of the event giving rise thereto; in the case of appeals regarding Change Proposals within 30 days of the decision under appeal. The party submitting the Claim shall also furnish a copy to the Engineer, for its information only. The responsibility to substantiate a Claim rests with the party making the Claim. In the case of a Claim by Contractor seeking an increase in the Contract Times or Contract Price, Contractor shall certify that the Claim is made in good faith, that the supporting data are accurate and complete, and that to the best of Contractor's knowledge

and belief the amount of time or money requested accurately reflects the full amount to which Contractor is entitled.

- C. *Review and Resolution*: The party receiving a Claim shall review it thoroughly, giving full consideration to its merits. The two parties shall seek to resolve the Claim through the exchange of information and direct negotiations. The parties may extend the time for resolving the Claim by mutual agreement. All actions taken on a Claim will be stated in writing and submitted to the other party, with a copy to Engineer.
- D. *Mediation*
 - 1. At any time after initiation of a Claim, Owner and Contractor may mutually agree to mediation of the underlying dispute. The agreement to mediate will stay the Claim submittal and response process.
 - 2. If Owner and Contractor agree to mediation, then after 60 days from such agreement, either Owner or Contractor may unilaterally terminate the mediation process, and the Claim submittal and decision process will resume as of the date of the termination. If the mediation proceeds but is unsuccessful in resolving the dispute, the Claim submittal and decision process will resume as of the date of the conclusion of the mediation, as determined by the mediator.
 - 3. Owner and Contractor shall each pay one-half of the mediator's fees and costs.
- E. *Partial Approval*: If the party receiving a Claim approves the Claim in part and denies it in part, such action will be final and binding unless within 30 days of such action the other party invokes the procedure set forth in Article 17 for final resolution of disputes.
- F. *Denial of Claim*: If efforts to resolve a Claim are not successful, the party receiving the Claim may deny it by giving written notice of denial to the other party. If the receiving party does not take action on the Claim within 90 days, then either Owner or Contractor may at any time thereafter submit a letter to the other party indicating that as a result of the inaction, the Claim is deemed denied, thereby commencing the time for appeal of the denial. A denial of the Claim will be final and binding unless within 30 days of the denial the other party invokes the procedure set forth in Article 17 for the final resolution of disputes.
- G. *Final and Binding Results*: If the parties reach a mutual agreement regarding a Claim, whether through approval of the Claim, direct negotiations, mediation, or otherwise; or if a Claim is approved in part and denied in part, or denied in full, and such actions become final and binding; then the results of the agreement or action on the Claim will be incorporated in a Change Order or other written document to the extent they affect the Contract, including the Work, the Contract Times, or the Contract Price.

ARTICLE 13—COST OF THE WORK; ALLOWANCES; UNIT PRICE WORK

13.01 *Cost of the Work*

- A. *Purposes for Determination of Cost of the Work*: The term Cost of the Work means the sum of all costs necessary for the proper performance of the Work at issue, as further defined below. The provisions of this Paragraph 13.01 are used for two distinct purposes:
 - 1. To determine Cost of the Work when Cost of the Work is a component of the Contract Price, under cost-plus-fee, time-and-materials, or other cost-based terms; or

2. When needed to determine the value of a Change Order, Change Proposal, Claim, set-off, or other adjustment in Contract Price. When the value of any such adjustment is determined on the basis of Cost of the Work, Contractor is entitled only to those additional or incremental costs required because of the change in the Work or because of the event giving rise to the adjustment.
- B. *Costs Included:* Except as otherwise may be agreed to in writing by Owner, costs included in the Cost of the Work will be in amounts no higher than those commonly incurred in the locality of the Project, will not include any of the costs itemized in Paragraph 13.01.C, and will include only the following items:
1. Payroll costs for employees in the direct employ of Contractor in the performance of the Work under schedules of job classifications agreed upon by Owner and Contractor in advance of the subject Work. Such employees include, without limitation, superintendents, foremen, safety managers, safety representatives, and other personnel employed full time on the Work. Payroll costs for employees not employed full time on the Work will be apportioned on the basis of their time spent on the Work. Payroll costs include, but are not limited to, salaries and wages plus the cost of fringe benefits, which include social security contributions, unemployment, excise, and payroll taxes, workers' compensation, health and retirement benefits, sick leave, and vacation and holiday pay applicable thereto. The expenses of performing Work outside of regular working hours, on Saturday, Sunday, or legal holidays, will be included in the above to the extent authorized by Owner.
 2. Cost of all materials and equipment furnished and incorporated in the Work, including costs of transportation and storage thereof, and Suppliers' field services required in connection therewith. All cash discounts accrue to Contractor unless Owner deposits funds with Contractor with which to make payments, in which case the cash discounts will accrue to Owner. All trade discounts, rebates, and refunds and returns from sale of surplus materials and equipment will accrue to Owner, and Contractor shall make provisions so that they may be obtained.
 3. Payments made by Contractor to Subcontractors for Work performed by Subcontractors. If required by Owner, Contractor shall obtain competitive bids from subcontractors acceptable to Owner and Contractor and shall deliver such bids to Owner, which will then determine, with the advice of Engineer, which bids, if any, will be acceptable. If any subcontract provides that the Subcontractor is to be paid on the basis of Cost of the Work plus a fee, the Subcontractor's Cost of the Work and fee will be determined in the same manner as Contractor's Cost of the Work and fee as provided in this Paragraph 13.01.
 4. Costs of special consultants (including but not limited to engineers, architects, testing laboratories, surveyors, attorneys, and accountants) employed or retained for services specifically related to the Work.
 5. Other costs consisting of the following:
 - a. The proportion of necessary transportation, travel, and subsistence expenses of Contractor's employees incurred in discharge of duties connected with the Work.
 - b. Cost, including transportation and maintenance, of all materials, supplies, equipment, machinery, appliances, office, and temporary facilities at the Site, which are

consumed in the performance of the Work, and cost, less market value, of such items used but not consumed which remain the property of Contractor.

- 1) In establishing included costs for materials such as scaffolding, plating, or sheeting, consideration will be given to the actual or the estimated life of the material for use on other projects; or rental rates may be established on the basis of purchase or salvage value of such items, whichever is less. Contractor will not be eligible for compensation for such items in an amount that exceeds the purchase cost of such item.

c. *Construction Equipment Rental*

- 1) Rentals of all construction equipment and machinery, and the parts thereof, in accordance with rental agreements approved by Owner as to price (including any surcharge or special rates applicable to overtime use of the construction equipment or machinery), and the costs of transportation, loading, unloading, assembly, dismantling, and removal thereof. All such costs will be in accordance with the terms of said rental agreements. The rental of any such equipment, machinery, or parts must cease when the use thereof is no longer necessary for the Work.
 - 2) Costs for equipment and machinery owned by Contractor or a Contractor-related entity will be paid at a rate shown for such equipment in the equipment rental rate book specified in the Supplementary Conditions. An hourly rate will be computed by dividing the monthly rates by 176. These computed rates will include all operating costs.
 - 3) With respect to Work that is the result of a Change Order, Change Proposal, Claim, set-off, or other adjustment in Contract Price ("changed Work"), included costs will be based on the time the equipment or machinery is in use on the changed Work and the costs of transportation, loading, unloading, assembly, dismantling, and removal when directly attributable to the changed Work. The cost of any such equipment or machinery, or parts thereof, must cease to accrue when the use thereof is no longer necessary for the changed Work.
- d. Sales, consumer, use, and other similar taxes related to the Work, and for which Contractor is liable, as imposed by Laws and Regulations.
- e. Deposits lost for causes other than negligence of Contractor, any Subcontractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable, and royalty payments and fees for permits and licenses.
- f. Losses and damages (and related expenses) caused by damage to the Work, not compensated by insurance or otherwise, sustained by Contractor in connection with the performance of the Work (except losses and damages within the deductible amounts of builder's risk or other property insurance established in accordance with Paragraph 6.04), provided such losses and damages have resulted from causes other than the negligence of Contractor, any Subcontractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable. Such losses include settlements made with the written consent and approval of Owner. No such losses, damages, and expenses will be included in the Cost of the Work for the purpose of determining Contractor's fee.

- g. The cost of utilities, fuel, and sanitary facilities at the Site.
 - h. Minor expenses such as communication service at the Site, express and courier services, and similar petty cash items in connection with the Work.
 - i. The costs of premiums for all bonds and insurance that Contractor is required by the Contract Documents to purchase and maintain.
- C. *Costs Excluded:* The term Cost of the Work does not include any of the following items:
- 1. Payroll costs and other compensation of Contractor's officers, executives, principals, general managers, engineers, architects, estimators, attorneys, auditors, accountants, purchasing and contracting agents, expeditors, timekeepers, clerks, and other personnel employed by Contractor, whether at the Site or in Contractor's principal or branch office for general administration of the Work and not specifically included in the agreed upon schedule of job classifications referred to in Paragraph 13.01.B.1 or specifically covered by Paragraph 13.01.B.4. The payroll costs and other compensation excluded here are to be considered administrative costs covered by the Contractor's fee.
 - 2. The cost of purchasing, renting, or furnishing small tools and hand tools.
 - 3. Expenses of Contractor's principal and branch offices other than Contractor's office at the Site.
 - 4. Any part of Contractor's capital expenses, including interest on Contractor's capital employed for the Work and charges against Contractor for delinquent payments.
 - 5. Costs due to the negligence of Contractor, any Subcontractor, or anyone directly or indirectly employed by any of them or for whose acts any of them may be liable, including but not limited to, the correction of defective Work, disposal of materials or equipment wrongly supplied, and making good any damage to property.
 - 6. Expenses incurred in preparing and advancing Claims.
 - 7. Other overhead or general expense costs of any kind and the costs of any item not specifically and expressly included in Paragraph 13.01.B.
- D. *Contractor's Fee*
- 1. When the Work as a whole is performed on the basis of cost-plus-a-fee, then:
 - a. Contractor's fee for the Work set forth in the Contract Documents as of the Effective Date of the Contract will be determined as set forth in the Agreement.
 - b. for any Work covered by a Change Order, Change Proposal, Claim, set-off, or other adjustment in Contract Price on the basis of Cost of the Work, Contractor's fee will be determined as follows:
 - 1) When the fee for the Work as a whole is a percentage of the Cost of the Work, the fee will automatically adjust as the Cost of the Work changes.
 - 2) When the fee for the Work as a whole is a fixed fee, the fee for any additions or deletions will be determined in accordance with Paragraph 11.07.C.2.
 - 2. When the Work as a whole is performed on the basis of a stipulated sum, or any other basis other than cost-plus-a-fee, then Contractor's fee for any Work covered by a Change

Order, Change Proposal, Claim, set-off, or other adjustment in Contract Price on the basis of Cost of the Work will be determined in accordance with Paragraph 11.07.C.2.

- E. *Documentation and Audit:* Whenever the Cost of the Work for any purpose is to be determined pursuant to this Article 13, Contractor and pertinent Subcontractors will establish and maintain records of the costs in accordance with generally accepted accounting practices. Subject to prior written notice, Owner will be afforded reasonable access, during normal business hours, to all Contractor's accounts, records, books, correspondence, instructions, drawings, receipts, vouchers, memoranda, and similar data relating to the Cost of the Work and Contractor's fee. Contractor shall preserve all such documents for a period of three years after the final payment by Owner. Pertinent Subcontractors will afford such access to Owner, and preserve such documents, to the same extent required of Contractor.

13.02 Allowances

- A. It is understood that Contractor has included in the Contract Price all allowances so named in the Contract Documents and shall cause the Work so covered to be performed for such sums and by such persons or entities as may be acceptable to Owner and Engineer.
- B. *Cash Allowances:* Contractor agrees that:
1. the cash allowances include the cost to Contractor (less any applicable trade discounts) of materials and equipment required by the allowances to be delivered at the Site, and all applicable taxes; and
 2. Contractor's costs for unloading and handling on the Site, labor, installation, overhead, profit, and other expenses contemplated for the cash allowances have been included in the Contract Price and not in the allowances, and no demand for additional payment for any of the foregoing will be valid.
- C. *Owner's Contingency Allowance:* Contractor agrees that an Owner's contingency allowance, if any, is for the sole use of Owner to cover unanticipated costs.
- D. Prior to final payment, an appropriate Change Order will be issued as recommended by Engineer to reflect actual amounts due Contractor for Work covered by allowances, and the Contract Price will be correspondingly adjusted.

13.03 Unit Price Work

- A. Where the Contract Documents provide that all or part of the Work is to be Unit Price Work, initially the Contract Price will be deemed to include for all Unit Price Work an amount equal to the sum of the unit price for each separately identified item of Unit Price Work times the estimated quantity of each item as indicated in the Agreement.
- B. The estimated quantities of items of Unit Price Work are not guaranteed and are solely for the purpose of comparison of Bids and determining an initial Contract Price. Payments to Contractor for Unit Price Work will be based on actual quantities.
- C. Each unit price will be deemed to include an amount considered by Contractor to be adequate to cover Contractor's overhead and profit for each separately identified item.
- D. Engineer will determine the actual quantities and classifications of Unit Price Work performed by Contractor. Engineer will review with Contractor the Engineer's preliminary determinations on such matters before rendering a written decision thereon (by recommendation of an Application for Payment or otherwise). Engineer's written decision

thereon will be final and binding (except as modified by Engineer to reflect changed factual conditions or more accurate data) upon Owner and Contractor, and the final adjustment of Contract Price will be set forth in a Change Order, subject to the provisions of the following paragraph.

E. *Adjustments in Unit Price*

1. Contractor or Owner shall be entitled to an adjustment in the unit price with respect to an item of Unit Price Work if:
 - a. the quantity of the item of Unit Price Work performed by Contractor differs materially and significantly from the estimated quantity of such item indicated in the Agreement; and
 - b. Contractor's unit costs to perform the item of Unit Price Work have changed materially and significantly as a result of the quantity change.
2. The adjustment in unit price will account for and be coordinated with any related changes in quantities of other items of Work, and in Contractor's costs to perform such other Work, such that the resulting overall change in Contract Price is equitable to Owner and Contractor.
3. Adjusted unit prices will apply to all units of that item.

ARTICLE 14—TESTS AND INSPECTIONS; CORRECTION, REMOVAL, OR ACCEPTANCE OF DEFECTIVE WORK

14.01 *Access to Work*

- A. Owner, Engineer, their consultants and other representatives and personnel of Owner, independent testing laboratories, and authorities having jurisdiction have access to the Site and the Work at reasonable times for their observation, inspection, and testing. Contractor shall provide them proper and safe conditions for such access and advise them of Contractor's safety procedures and programs so that they may comply with such procedures and programs as applicable.

14.02 *Tests, Inspections, and Approvals*

- A. Contractor shall give Engineer timely notice of readiness of the Work (or specific parts thereof) for all required inspections and tests, and shall cooperate with inspection and testing personnel to facilitate required inspections and tests.
- B. Owner shall retain and pay for the services of an independent inspector, testing laboratory, or other qualified individual or entity to perform all inspections and tests expressly required by the Contract Documents to be furnished and paid for by Owner, except that costs incurred in connection with tests or inspections of covered Work will be governed by the provisions of Paragraph 14.05.
- C. If Laws or Regulations of any public body having jurisdiction require any Work (or part thereof) specifically to be inspected, tested, or approved by an employee or other representative of such public body, Contractor shall assume full responsibility for arranging and obtaining such inspections, tests, or approvals, pay all costs in connection therewith, and furnish Engineer the required certificates of inspection or approval.

- D. Contractor shall be responsible for arranging, obtaining, and paying for all inspections and tests required:
1. by the Contract Documents, unless the Contract Documents expressly allocate responsibility for a specific inspection or test to Owner;
 2. to attain Owner's and Engineer's acceptance of materials or equipment to be incorporated in the Work;
 3. by manufacturers of equipment furnished under the Contract Documents;
 4. for testing, adjusting, and balancing of mechanical, electrical, and other equipment to be incorporated into the Work; and
 5. for acceptance of materials, mix designs, or equipment submitted for approval prior to Contractor's purchase thereof for incorporation in the Work.

Such inspections and tests will be performed by independent inspectors, testing laboratories, or other qualified individuals or entities acceptable to Owner and Engineer.

- E. If the Contract Documents require the Work (or part thereof) to be approved by Owner, Engineer, or another designated individual or entity, then Contractor shall assume full responsibility for arranging and obtaining such approvals.
- F. If any Work (or the work of others) that is to be inspected, tested, or approved is covered by Contractor without written concurrence of Engineer, Contractor shall, if requested by Engineer, uncover such Work for observation. Such uncovering will be at Contractor's expense unless Contractor had given Engineer timely notice of Contractor's intention to cover the same and Engineer had not acted with reasonable promptness in response to such notice.

14.03 *Defective Work*

- A. *Contractor's Obligation:* It is Contractor's obligation to assure that the Work is not defective.
- B. *Engineer's Authority:* Engineer has the authority to determine whether Work is defective, and to reject defective Work.
- C. *Notice of Defects:* Prompt written notice of all defective Work of which Owner or Engineer has actual knowledge will be given to Contractor.
- D. *Correction, or Removal and Replacement:* Promptly after receipt of written notice of defective Work, Contractor shall correct all such defective Work, whether or not fabricated, installed, or completed, or, if Engineer has rejected the defective Work, remove it from the Project and replace it with Work that is not defective.
- E. *Preservation of Warranties:* When correcting defective Work, Contractor shall take no action that would void or otherwise impair Owner's special warranty and guarantee, if any, on said Work.
- F. *Costs and Damages:* In addition to its correction, removal, and replacement obligations with respect to defective Work, Contractor shall pay all claims, costs, losses, and damages arising out of or relating to defective Work, including but not limited to the cost of the inspection, testing, correction, removal, replacement, or reconstruction of such defective Work, fines levied against Owner by governmental authorities because the Work is defective, and the costs of repair or replacement of work of others resulting from defective Work. Prior to final payment, if Owner and Contractor are unable to agree as to the measure of such claims, costs,

losses, and damages resulting from defective Work, then Owner may impose a reasonable set-off against payments due under Article 15.

14.04 *Acceptance of Defective Work*

- A. If, instead of requiring correction or removal and replacement of defective Work, Owner prefers to accept it, Owner may do so (subject, if such acceptance occurs prior to final payment, to Engineer's confirmation that such acceptance is in general accord with the design intent and applicable engineering principles, and will not endanger public safety). Contractor shall pay all claims, costs, losses, and damages attributable to Owner's evaluation of and determination to accept such defective Work (such costs to be approved by Engineer as to reasonableness), and for the diminished value of the Work to the extent not otherwise paid by Contractor. If any such acceptance occurs prior to final payment, the necessary revisions in the Contract Documents with respect to the Work will be incorporated in a Change Order. If the parties are unable to agree as to the decrease in the Contract Price, reflecting the diminished value of Work so accepted, then Owner may impose a reasonable set-off against payments due under Article 15. If the acceptance of defective Work occurs after final payment, Contractor shall pay an appropriate amount to Owner.

14.05 *Uncovering Work*

- A. Engineer has the authority to require additional inspection or testing of the Work, whether or not the Work is fabricated, installed, or completed.
- B. If any Work is covered contrary to the written request of Engineer, then Contractor shall, if requested by Engineer, uncover such Work for Engineer's observation, and then replace the covering, all at Contractor's expense.
- C. If Engineer considers it necessary or advisable that covered Work be observed by Engineer or inspected or tested by others, then Contractor, at Engineer's request, shall uncover, expose, or otherwise make available for observation, inspection, or testing as Engineer may require, that portion of the Work in question, and provide all necessary labor, material, and equipment.
 - 1. If it is found that the uncovered Work is defective, Contractor shall be responsible for all claims, costs, losses, and damages arising out of or relating to such uncovering, exposure, observation, inspection, and testing, and of satisfactory replacement or reconstruction (including but not limited to all costs of repair or replacement of work of others); and pending Contractor's full discharge of this responsibility the Owner shall be entitled to impose a reasonable set-off against payments due under Article 15.
 - 2. If the uncovered Work is not found to be defective, Contractor shall be allowed an increase in the Contract Price or an extension of the Contract Times, directly attributable to such uncovering, exposure, observation, inspection, testing, replacement, and reconstruction. If the parties are unable to agree as to the amount or extent thereof, then Contractor may submit a Change Proposal within 30 days of the determination that the Work is not defective.

14.06 *Owner May Stop the Work*

- A. If the Work is defective, or Contractor fails to supply sufficient skilled workers or suitable materials or equipment, or fails to perform the Work in such a way that the completed Work will conform to the Contract Documents, then Owner may order Contractor to stop the Work,

or any portion thereof, until the cause for such order has been eliminated; however, this right of Owner to stop the Work will not give rise to any duty on the part of Owner to exercise this right for the benefit of Contractor, any Subcontractor, any Supplier, any other individual or entity, or any surety for, or employee or agent of any of them.

14.07 Owner May Correct Defective Work

- A. If Contractor fails within a reasonable time after written notice from Engineer to correct defective Work, or to remove and replace defective Work as required by Engineer, then Owner may, after 7 days' written notice to Contractor, correct or remedy any such deficiency.
- B. In exercising the rights and remedies under this Paragraph 14.07, Owner shall proceed expeditiously. In connection with such corrective or remedial action, Owner may exclude Contractor from all or part of the Site, take possession of all or part of the Work and suspend Contractor's services related thereto, and incorporate in the Work all materials and equipment stored at the Site or for which Owner has paid Contractor but which are stored elsewhere. Contractor shall allow Owner, Owner's representatives, agents and employees, Owner's other contractors, and Engineer and Engineer's consultants access to the Site to enable Owner to exercise the rights and remedies under this paragraph.
- C. All claims, costs, losses, and damages incurred or sustained by Owner in exercising the rights and remedies under this Paragraph 14.07 will be charged against Contractor as set-offs against payments due under Article 15. Such claims, costs, losses and damages will include but not be limited to all costs of repair, or replacement of work of others destroyed or damaged by correction, removal, or replacement of Contractor's defective Work.
- D. Contractor shall not be allowed an extension of the Contract Times because of any delay in the performance of the Work attributable to the exercise by Owner of Owner's rights and remedies under this Paragraph 14.07.

ARTICLE 15—PAYMENTS TO CONTRACTOR; SET-OFFS; COMPLETION; CORRECTION PERIOD

15.01 Progress Payments

- A. *Basis for Progress Payments:* The Schedule of Values established as provided in Article 2 will serve as the basis for progress payments and will be incorporated into a form of Application for Payment acceptable to Engineer. Progress payments for Unit Price Work will be based on the number of units completed during the pay period, as determined under the provisions of Paragraph 13.03. Progress payments for cost-based Work will be based on Cost of the Work completed by Contractor during the pay period.
- B. *Applications for Payments*
 - 1. At least 20 days before the date established in the Agreement for each progress payment (but not more often than once a month), Contractor shall submit to Engineer for review an Application for Payment filled out and signed by Contractor covering the Work completed as of the date of the Application and accompanied by such supporting documentation as is required by the Contract Documents.
 - 2. If payment is requested on the basis of materials and equipment not incorporated in the Work but delivered and suitably stored at the Site or at another location agreed to in writing, the Application for Payment must also be accompanied by: (a) a bill of sale, invoice, copies of subcontract or purchase order payments, or other documentation

establishing full payment by Contractor for the materials and equipment; (b) at Owner's request, documentation warranting that Owner has received the materials and equipment free and clear of all Liens; and (c) evidence that the materials and equipment are covered by appropriate property insurance, a warehouse bond, or other arrangements to protect Owner's interest therein, all of which must be satisfactory to Owner.

3. Beginning with the second Application for Payment, each Application must include an affidavit of Contractor stating that all previous progress payments received by Contractor have been applied to discharge Contractor's legitimate obligations associated with prior Applications for Payment.
4. The amount of retainage with respect to progress payments will be as stipulated in the Agreement.

C. Review of Applications

1. Engineer will, within 10 days after receipt of each Application for Payment, including each resubmittal, either indicate in writing a recommendation of payment and present the Application to Owner, or return the Application to Contractor indicating in writing Engineer's reasons for refusing to recommend payment. In the latter case, Contractor may make the necessary corrections and resubmit the Application.
2. Engineer's recommendation of any payment requested in an Application for Payment will constitute a representation by Engineer to Owner, based on Engineer's observations of the executed Work as an experienced and qualified design professional, and on Engineer's review of the Application for Payment and the accompanying data and schedules, that to the best of Engineer's knowledge, information and belief:
 - a. the Work has progressed to the point indicated;
 - b. the quality of the Work is generally in accordance with the Contract Documents (subject to an evaluation of the Work as a functioning whole prior to or upon Substantial Completion, the results of any subsequent tests called for in the Contract Documents, a final determination of quantities and classifications for Unit Price Work under Paragraph 13.03, and any other qualifications stated in the recommendation); and
 - c. the conditions precedent to Contractor's being entitled to such payment appear to have been fulfilled in so far as it is Engineer's responsibility to observe the Work.
3. By recommending any such payment Engineer will not thereby be deemed to have represented that:
 - a. inspections made to check the quality or the quantity of the Work as it has been performed have been exhaustive, extended to every aspect of the Work in progress, or involved detailed inspections of the Work beyond the responsibilities specifically assigned to Engineer in the Contract; or
 - b. there may not be other matters or issues between the parties that might entitle Contractor to be paid additionally by Owner or entitle Owner to withhold payment to Contractor.

4. Neither Engineer's review of Contractor's Work for the purposes of recommending payments nor Engineer's recommendation of any payment, including final payment, will impose responsibility on Engineer:
 - a. to supervise, direct, or control the Work;
 - b. for the means, methods, techniques, sequences, or procedures of construction, or the safety precautions and programs incident thereto;
 - c. for Contractor's failure to comply with Laws and Regulations applicable to Contractor's performance of the Work;
 - d. to make any examination to ascertain how or for what purposes Contractor has used the money paid by Owner; or
 - e. to determine that title to any of the Work, materials, or equipment has passed to Owner free and clear of any Liens.
5. Engineer may refuse to recommend the whole or any part of any payment if, in Engineer's opinion, it would be incorrect to make the representations to Owner stated in Paragraph 15.01.C.2.
6. Engineer will recommend reductions in payment (set-offs) necessary in Engineer's opinion to protect Owner from loss because:
 - a. the Work is defective, requiring correction or replacement;
 - b. the Contract Price has been reduced by Change Orders;
 - c. Owner has been required to correct defective Work in accordance with Paragraph 14.07, or has accepted defective Work pursuant to Paragraph 14.04;
 - d. Owner has been required to remove or remediate a Hazardous Environmental Condition for which Contractor is responsible; or
 - e. Engineer has actual knowledge of the occurrence of any of the events that would constitute a default by Contractor and therefore justify termination for cause under the Contract Documents.

D. *Payment Becomes Due*

1. Ten days after presentation of the Application for Payment to Owner with Engineer's recommendation, the amount recommended (subject to any Owner set-offs) will become due, and when due will be paid by Owner to Contractor.

E. *Reductions in Payment by Owner*

1. In addition to any reductions in payment (set-offs) recommended by Engineer, Owner is entitled to impose a set-off against payment based on any of the following:
 - a. Claims have been made against Owner based on Contractor's conduct in the performance or furnishing of the Work, or Owner has incurred costs, losses, or damages resulting from Contractor's conduct in the performance or furnishing of the Work, including but not limited to claims, costs, losses, or damages from workplace injuries, adjacent property damage, non-compliance with Laws and Regulations, and patent infringement;

- b. Contractor has failed to take reasonable and customary measures to avoid damage, delay, disruption, and interference with other work at or adjacent to the Site;
 - c. Contractor has failed to provide and maintain required bonds or insurance;
 - d. Owner has been required to remove or remediate a Hazardous Environmental Condition for which Contractor is responsible;
 - e. Owner has incurred extra charges or engineering costs related to submittal reviews, evaluations of proposed substitutes, tests and inspections, or return visits to manufacturing or assembly facilities;
 - f. The Work is defective, requiring correction or replacement;
 - g. Owner has been required to correct defective Work in accordance with Paragraph 14.07, or has accepted defective Work pursuant to Paragraph 14.04;
 - h. The Contract Price has been reduced by Change Orders;
 - i. An event has occurred that would constitute a default by Contractor and therefore justify a termination for cause;
 - j. Liquidated or other damages have accrued as a result of Contractor's failure to achieve Milestones, Substantial Completion, or final completion of the Work;
 - k. Liens have been filed in connection with the Work, except where Contractor has delivered a specific bond satisfactory to Owner to secure the satisfaction and discharge of such Liens; or
 - l. Other items entitle Owner to a set-off against the amount recommended.
2. If Owner imposes any set-off against payment, whether based on its own knowledge or on the written recommendations of Engineer, Owner will give Contractor immediate written notice (with a copy to Engineer) stating the reasons for such action and the specific amount of the reduction, and promptly pay Contractor any amount remaining after deduction of the amount so withheld. Owner shall promptly pay Contractor the amount so withheld, or any adjustment thereto agreed to by Owner and Contractor, if Contractor remedies the reasons for such action. The reduction imposed will be binding on Contractor unless it duly submits a Change Proposal contesting the reduction.
 3. Upon a subsequent determination that Owner's refusal of payment was not justified, the amount wrongfully withheld will be treated as an amount due as determined by Paragraph 15.01.D.1 and subject to interest as provided in the Agreement.

15.02 *Contractor's Warranty of Title*

- A. Contractor warrants and guarantees that title to all Work, materials, and equipment furnished under the Contract will pass to Owner free and clear of (1) all Liens and other title defects, and (2) all patent, licensing, copyright, or royalty obligations, no later than 7 days after the time of payment by Owner.

15.03 *Substantial Completion*

- A. When Contractor considers the entire Work ready for its intended use Contractor shall notify Owner and Engineer in writing that the entire Work is substantially complete and request that Engineer issue a certificate of Substantial Completion. Contractor shall at the same time

submit to Owner and Engineer an initial draft of punch list items to be completed or corrected before final payment.

- B. Promptly after Contractor™s notification, Owner, Contractor, and Engineer shall make an inspection of the Work to determine the status of completion. If Engineer does not consider the Work substantially complete, Engineer will notify Contractor in writing giving the reasons therefor.
- C. If Engineer considers the Work substantially complete, Engineer will deliver to Owner a preliminary certificate of Substantial Completion which will fix the date of Substantial Completion. Engineer shall attach to the certificate a punch list of items to be completed or corrected before final payment. Owner shall have 14 days after receipt of the preliminary certificate during which to make written objections to Engineer as to any provisions of the certificate or attached punch list. If, after considering the objections to the provisions of the preliminary certificate, Engineer concludes that the Work is not substantially complete, Engineer will, within 14 days after submission of the preliminary certificate to Owner, notify Contractor in writing that the Work is not substantially complete, stating the reasons therefor. If Owner does not object to the provisions of the certificate, or if despite consideration of Owner™s objections Engineer concludes that the Work is substantially complete, then Engineer will, within said 14 days, execute and deliver to Owner and Contractor a final certificate of Substantial Completion (with a revised punch list of items to be completed or corrected) reflecting such changes from the preliminary certificate as Engineer believes justified after consideration of any objections from Owner.
- D. At the time of receipt of the preliminary certificate of Substantial Completion, Owner and Contractor will confer regarding Owner™s use or occupancy of the Work following Substantial Completion, review the builder™s risk insurance policy with respect to the end of the builder™s risk coverage, and confirm the transition to coverage of the Work under a permanent property insurance policy held by Owner. Unless Owner and Contractor agree otherwise in writing, Owner shall bear responsibility for security, operation, protection of the Work, property insurance, maintenance, heat, and utilities upon Owner™s use or occupancy of the Work.
- E. After Substantial Completion the Contractor shall promptly begin work on the punch list of items to be completed or corrected prior to final payment. In appropriate cases Contractor may submit monthly Applications for Payment for completed punch list items, following the progress payment procedures set forth above.
- F. Owner shall have the right to exclude Contractor from the Site after the date of Substantial Completion subject to allowing Contractor reasonable access to its property and complete or correct items on the punch list.

15.04 Partial Use or Occupancy

- A. Prior to Substantial Completion of all the Work, Owner may use or occupy any substantially completed part of the Work which has specifically been identified in the Contract Documents, or which Owner, Engineer, and Contractor agree constitutes a separately functioning and usable part of the Work that can be used by Owner for its intended purpose without

significant interference with Contractor's performance of the remainder of the Work, subject to the following conditions:

1. At any time, Owner may request in writing that Contractor permit Owner to use or occupy any such part of the Work that Owner believes to be substantially complete. If and when Contractor agrees that such part of the Work is substantially complete, Contractor, Owner, and Engineer will follow the procedures of Paragraph 15.03.A through 15.03.E for that part of the Work.
2. At any time, Contractor may notify Owner and Engineer in writing that Contractor considers any such part of the Work substantially complete and request Engineer to issue a certificate of Substantial Completion for that part of the Work.
3. Within a reasonable time after either such request, Owner, Contractor, and Engineer shall make an inspection of that part of the Work to determine its status of completion. If Engineer does not consider that part of the Work to be substantially complete, Engineer will notify Owner and Contractor in writing giving the reasons therefor. If Engineer considers that part of the Work to be substantially complete, the provisions of Paragraph 15.03 will apply with respect to certification of Substantial Completion of that part of the Work and the division of responsibility in respect thereof and access thereto.
4. No use or occupancy or separate operation of part of the Work may occur prior to compliance with the requirements of Paragraph 6.04 regarding builder's risk or other property insurance.

15.05 *Final Inspection*

- A. Upon written notice from Contractor that the entire Work or an agreed portion thereof is complete, Engineer will promptly make a final inspection with Owner and Contractor and will notify Contractor in writing of all particulars in which this inspection reveals that the Work, or agreed portion thereof, is incomplete or defective. Contractor shall immediately take such measures as are necessary to complete such Work or remedy such deficiencies.

15.06 *Final Payment*

A. *Application for Payment*

1. After Contractor has, in the opinion of Engineer, satisfactorily completed all corrections identified during the final inspection and has delivered, in accordance with the Contract Documents, all maintenance and operating instructions, schedules, guarantees, bonds, certificates or other evidence of insurance, certificates of inspection, annotated record documents (as provided in Paragraph 7.12), and other documents, Contractor may make application for final payment.
2. The final Application for Payment must be accompanied (except as previously delivered) by:
 - a. all documentation called for in the Contract Documents;
 - b. consent of the surety, if any, to final payment;
 - c. satisfactory evidence that all title issues have been resolved such that title to all Work, materials, and equipment has passed to Owner free and clear of any Liens or other title defects, or will so pass upon final payment.

- d. a list of all duly pending Change Proposals and Claims; and
 - e. complete and legally effective releases or waivers (satisfactory to Owner) of all Lien rights arising out of the Work, and of Liens filed in connection with the Work.
- 3. In lieu of the releases or waivers of Liens specified in Paragraph 15.06.A.2 and as approved by Owner, Contractor may furnish receipts or releases in full and an affidavit of Contractor that: (a) the releases and receipts include all labor, services, material, and equipment for which a Lien could be filed; and (b) all payrolls, material and equipment bills, and other indebtedness connected with the Work for which Owner might in any way be responsible, or which might in any way result in liens or other burdens on Owner's property, have been paid or otherwise satisfied. If any Subcontractor or Supplier fails to furnish such a release or receipt in full, Contractor may furnish a bond or other collateral satisfactory to Owner to indemnify Owner against any Lien, or Owner at its option may issue joint checks payable to Contractor and specified Subcontractors and Suppliers.
- B. *Engineer's Review of Final Application and Recommendation of Payment:* If, on the basis of Engineer's observation of the Work during construction and final inspection, and Engineer's review of the final Application for Payment and accompanying documentation as required by the Contract Documents, Engineer is satisfied that the Work has been completed and Contractor's other obligations under the Contract have been fulfilled, Engineer will, within 10 days after receipt of the final Application for Payment, indicate in writing Engineer's recommendation of final payment and present the final Application for Payment to Owner for payment. Such recommendation will account for any set-offs against payment that are necessary in Engineer's opinion to protect Owner from loss for the reasons stated above with respect to progress payments. Otherwise, Engineer will return the Application for Payment to Contractor, indicating in writing the reasons for refusing to recommend final payment, in which case Contractor shall make the necessary corrections and resubmit the Application for Payment.
- C. *Notice of Acceptability:* In support of its recommendation of payment of the final Application for Payment, Engineer will also give written notice to Owner and Contractor that the Work is acceptable, subject to stated limitations in the notice and to the provisions of Paragraph 15.07.
- D. *Completion of Work:* The Work is complete (subject to surviving obligations) when it is ready for final payment as established by the Engineer's written recommendation of final payment and issuance of notice of the acceptability of the Work.
- E. *Final Payment Becomes Due:* Upon receipt from Engineer of the final Application for Payment and accompanying documentation, Owner shall set off against the amount recommended by Engineer for final payment any further sum to which Owner is entitled, including but not limited to set-offs for liquidated damages and set-offs allowed under the provisions of this Contract with respect to progress payments. Owner shall pay the resulting balance due to Contractor within 30 days of Owner's receipt of the final Application for Payment from Engineer.

15.07 *Waiver of Claims*

- A. By making final payment, Owner waives its claim or right to liquidated damages or other damages for late completion by Contractor, except as set forth in an outstanding Claim,

appeal under the provisions of Article 17, set-off, or express reservation of rights by Owner. Owner reserves all other claims or rights after final payment.

- B. The acceptance of final payment by Contractor will constitute a waiver by Contractor of all claims and rights against Owner other than those pending matters that have been duly submitted as a Claim, or appealed under the provisions of Article 17.

15.08 *Correction Period*

- A. If within one year after the date of Substantial Completion (or such longer period of time as may be prescribed by the Supplementary Conditions or the terms of any applicable special guarantee required by the Contract Documents), Owner gives Contractor written notice that any Work has been found to be defective, or that Contractor's repair of any damages to the Site or adjacent areas has been found to be defective, then after receipt of such notice of defect Contractor shall promptly, without cost to Owner and in accordance with Owner's written instructions:
 - 1. correct the defective repairs to the Site or such adjacent areas;
 - 2. correct such defective Work;
 - 3. remove the defective Work from the Project and replace it with Work that is not defective, if the defective Work has been rejected by Owner, and
 - 4. satisfactorily correct or repair or remove and replace any damage to other Work, to the work of others, or to other land or areas resulting from the corrective measures.
- B. Owner shall give any such notice of defect within 60 days of the discovery that such Work or repairs is defective. If such notice is given within such 60 days but after the end of the correction period, the notice will be deemed a notice of defective Work under Paragraph 7.17.B.
- C. If, after receipt of a notice of defect within 60 days and within the correction period, Contractor does not promptly comply with the terms of Owner's written instructions, or in an emergency where delay would cause serious risk of loss or damage, Owner may have the defective Work corrected or repaired or may have the rejected Work removed and replaced. Contractor shall pay all costs, losses, and damages (including but not limited to all fees and charges of engineers, architects, attorneys, and other professionals and all court or arbitration or other dispute resolution costs) arising out of or relating to such correction or repair or such removal and replacement (including but not limited to all costs of repair or replacement of work of others). Contractor's failure to pay such costs, losses, and damages within 10 days of invoice from Owner will be deemed the start of an event giving rise to a Claim under Paragraph 12.01.B, such that any related Claim must be brought within 30 days of the failure to pay.
- D. In special circumstances where a particular item of equipment is placed in continuous service before Substantial Completion of all the Work, the correction period for that item may start to run from an earlier date if so provided in the Specifications.
- E. Where defective Work (and damage to other Work resulting therefrom) has been corrected or removed and replaced under this paragraph, the correction period hereunder with respect to such Work will be extended for an additional period of one year after such correction or removal and replacement has been satisfactorily completed.

- F. Contractor's obligations under this paragraph are in addition to all other obligations and warranties. The provisions of this paragraph are not to be construed as a substitute for, or a waiver of, the provisions of any applicable statute of limitation or repose.

ARTICLE 16—SUSPENSION OF WORK AND TERMINATION

16.01 *Owner May Suspend Work*

- A. At any time and without cause, Owner may suspend the Work or any portion thereof for a period of not more than 90 consecutive days by written notice to Contractor and Engineer. Such notice will fix the date on which Work will be resumed. Contractor shall resume the Work on the date so fixed. Contractor shall be entitled to an adjustment in the Contract Price or an extension of the Contract Times directly attributable to any such suspension. Any Change Proposal seeking such adjustments must be submitted no later than 30 days after the date fixed for resumption of Work.

16.02 *Owner May Terminate for Cause*

- A. The occurrence of any one or more of the following events will constitute a default by Contractor and justify termination for cause:
1. Contractor's persistent failure to perform the Work in accordance with the Contract Documents (including, but not limited to, failure to supply sufficient skilled workers or suitable materials or equipment, or failure to adhere to the Progress Schedule);
 2. Failure of Contractor to perform or otherwise to comply with a material term of the Contract Documents;
 3. Contractor's disregard of Laws or Regulations of any public body having jurisdiction; or
 4. Contractor's repeated disregard of the authority of Owner or Engineer.
- B. If one or more of the events identified in Paragraph 16.02.A occurs, then after giving Contractor (and any surety) 10 days' written notice that Owner is considering a declaration that Contractor is in default and termination of the Contract, Owner may proceed to:
1. declare Contractor to be in default, and give Contractor (and any surety) written notice that the Contract is terminated; and
 2. enforce the rights available to Owner under any applicable performance bond.
- C. Subject to the terms and operation of any applicable performance bond, if Owner has terminated the Contract for cause, Owner may exclude Contractor from the Site, take possession of the Work, incorporate in the Work all materials and equipment stored at the Site or for which Owner has paid Contractor but which are stored elsewhere, and complete the Work as Owner may deem expedient.
- D. Owner may not proceed with termination of the Contract under Paragraph 16.02.B if Contractor within 7 days of receipt of notice of intent to terminate begins to correct its failure to perform and proceeds diligently to cure such failure.
- E. If Owner proceeds as provided in Paragraph 16.02.B, Contractor shall not be entitled to receive any further payment until the Work is completed. If the unpaid balance of the Contract Price exceeds the cost to complete the Work, including all related claims, costs, losses, and damages (including but not limited to all fees and charges of engineers, architects,

attorneys, and other professionals) sustained by Owner, such excess will be paid to Contractor. If the cost to complete the Work including such related claims, costs, losses, and damages exceeds such unpaid balance, Contractor shall pay the difference to Owner. Such claims, costs, losses, and damages incurred by Owner will be reviewed by Engineer as to their reasonableness and, when so approved by Engineer, incorporated in a Change Order. When exercising any rights or remedies under this paragraph, Owner shall not be required to obtain the lowest price for the Work performed.

- F. Where Contractor's services have been so terminated by Owner, the termination will not affect any rights or remedies of Owner against Contractor then existing or which may thereafter accrue, or any rights or remedies of Owner against Contractor or any surety under any payment bond or performance bond. Any retention or payment of money due Contractor by Owner will not release Contractor from liability.
- G. If and to the extent that Contractor has provided a performance bond under the provisions of Paragraph 6.01.A, the provisions of that bond will govern over any inconsistent provisions of Paragraphs 16.02.B and 16.02.D.

16.03 *Owner May Terminate for Convenience*

- A. Upon 7 days' written notice to Contractor and Engineer, Owner may, without cause and without prejudice to any other right or remedy of Owner, terminate the Contract. In such case, Contractor shall be paid for (without duplication of any items):
 - 1. completed and acceptable Work executed in accordance with the Contract Documents prior to the effective date of termination, including fair and reasonable sums for overhead and profit on such Work;
 - 2. expenses sustained prior to the effective date of termination in performing services and furnishing labor, materials, or equipment as required by the Contract Documents in connection with uncompleted Work, plus fair and reasonable sums for overhead and profit on such expenses; and
 - 3. other reasonable expenses directly attributable to termination, including costs incurred to prepare a termination for convenience cost proposal.
- B. Contractor shall not be paid for any loss of anticipated profits or revenue, post-termination overhead costs, or other economic loss arising out of or resulting from such termination.

16.04 *Contractor May Stop Work or Terminate*

- A. If, through no act or fault of Contractor, (1) the Work is suspended for more than 90 consecutive days by Owner or under an order of court or other public authority, or (2) Engineer fails to act on any Application for Payment within 30 days after it is submitted, or (3) Owner fails for 30 days to pay Contractor any sum finally determined to be due, then Contractor may, upon 7 days' written notice to Owner and Engineer, and provided Owner or Engineer do not remedy such suspension or failure within that time, terminate the contract and recover from Owner payment on the same terms as provided in Paragraph 16.03.
- B. In lieu of terminating the Contract and without prejudice to any other right or remedy, if Engineer has failed to act on an Application for Payment within 30 days after it is submitted, or Owner has failed for 30 days to pay Contractor any sum finally determined to be due, Contractor may, 7 days after written notice to Owner and Engineer, stop the Work until payment is made of all such amounts due Contractor, including interest thereon. The

provisions of this paragraph are not intended to preclude Contractor from submitting a Change Proposal for an adjustment in Contract Price or Contract Times or otherwise for expenses or damage directly attributable to Contractor's stopping the Work as permitted by this paragraph.

ARTICLE 17—FINAL RESOLUTION OF DISPUTES

17.01 *Methods and Procedures*

- A. *Disputes Subject to Final Resolution:* The following disputed matters are subject to final resolution under the provisions of this article:
 - 1. A timely appeal of an approval in part and denial in part of a Claim, or of a denial in full, pursuant to Article 12; and
 - 2. Disputes between Owner and Contractor concerning the Work, or obligations under the Contract Documents, that arise after final payment has been made.
- B. *Final Resolution of Disputes:* For any dispute subject to resolution under this article, Owner or Contractor may:
 - 1. elect in writing to invoke the dispute resolution process provided for in the Supplementary Conditions;
 - 2. agree with the other party to submit the dispute to another dispute resolution process; or
 - 3. if no dispute resolution process is provided for in the Supplementary Conditions or mutually agreed to, give written notice to the other party of the intent to submit the dispute to a court of competent jurisdiction.

ARTICLE 18—MISCELLANEOUS

18.01 *Giving Notice*

- A. Whenever any provision of the Contract requires the giving of written notice to Owner, Engineer, or Contractor, it will be deemed to have been validly given only if delivered:
 - 1. in person, by a commercial courier service or otherwise, to the recipient's place of business;
 - 2. by registered or certified mail, postage prepaid, to the recipient's place of business; or
 - 3. by e-mail to the recipient, with the words "Formal Notice" or similar in the e-mail's subject line.

18.02 *Computation of Times*

- A. When any period of time is referred to in the Contract by days, it will be computed to exclude the first and include the last day of such period. If the last day of any such period falls on a Saturday or Sunday or on a day made a legal holiday by the law of the applicable jurisdiction, such day will be omitted from the computation.

18.03 Cumulative Remedies

- A. The duties and obligations imposed by these General Conditions and the rights and remedies available hereunder to the parties hereto are in addition to, and are not to be construed in any way as a limitation of, any rights and remedies available to any or all of them which are otherwise imposed or available by Laws or Regulations, by special warranty, or by other provisions of the Contract. The provisions of this paragraph will be as effective as if repeated specifically in the Contract Documents in connection with each particular duty, obligation, right, and remedy to which they apply.

18.04 Limitation of Damages

- A. With respect to any and all Change Proposals, Claims, disputes subject to final resolution, and other matters at issue, neither Owner nor Engineer or any of their officers, directors, members, partners, employees, agents, consultants, subcontractors, shall be liable to Contractor for any claims, costs, losses, or damages sustained by Contractor on or in connection with any other project or anticipated project.

18.05 No Waiver

- A. A party's non-enforcement of any provision will not constitute a waiver of that provision, nor will it affect the enforceability of that provision or of the remainder of this Contract.

18.06 Survival of Obligations

- A. All representations, indemnifications, warranties, and guarantees made in, required by, or given in accordance with the Contract, as well as all continuing obligations indicated in the Contract, will survive final payment, completion, acceptance of the Work or termination of the Contract or of the services of Contractor.

18.07 Controlling Law

- A. This Contract is to be governed by the law of the state in which the Project is located

18.08 Assignment of Contract

- A. Unless expressly agreed to elsewhere in the Contract, no assignment by either party of this Contract of any rights under or interests in the Contract will be binding on the other party without the written consent of the party sought to be bound; and, specifically but without limitation, money that may become due and money then due may not be assigned without such consent (except to the extent that the effect of this restriction may be limited by law), and unless specifically stated to the contrary in a written consent to an assignment, no assignment will release or discharge the assignor from any duty or responsibility under the Contract.

18.09 Successors and Assigns

- A. Owner and Contractor each binds itself, its successors, assigns, and legal representatives to the other party hereto, its successors, assigns, and legal representatives in respect to all covenants, agreements, and obligations contained in the Contract Documents.

18.10 Headings

- A. Article and paragraph headings are inserted for convenience only and do not constitute parts of these General Conditions.

SUPPLEMENTARY CONDITIONS

OF THE CONSTRUCTION CONTRACT

TABLE OF CONTENTS

	Page
Article 1— Definitions and Terminology	1
Article 2— Preliminary Matters	2
Article 3— Contract Documents: Intent, Requirements, Reuse	2
Article 4— Site, Subsurface and Physical Conditions, Hazardous Environmental Conditions	2
Article 5— Bonds and Insurance	5
Article 6— Contractor’s Responsibilities	6
Article 7— Engineer’s Status During Construction	7
Article 8 – Cost of Work; Allowances, Unit Price Work	7
Article 9— Payments to Contractor, Set Offs; Completions; Correction Period.....	7

SUPPLEMENTARY CONDITIONS

OF THE CONSTRUCTION CONTRACT

These Supplementary Conditions amend or supplement EJCDC® C-700, Standard General Conditions of the Construction Contract (2018). The General Conditions remain in full force and effect except as amended.

The terms used in these Supplementary Conditions have the meanings stated in the General Conditions. Additional terms, if any, used in these Supplementary Conditions have the meanings stated below, which are applicable to both the singular and plural thereof.

The paragraph address system used in these Supplementary Conditions is the same as the paragraph address system used in the General Conditions, with the prefix "SC" added—for example, "Paragraph SC-4.05."

ARTICLE 1—DEFINITIONS AND TERMINOLOGY

- SC-1.01. Add to the list of definitions in Paragraph 1.01.A by inserting the following as numbered items in their proper alphabetical positions:

Geotechnical Baseline Report (GBR) — The interpretive report prepared by or for Owner regarding subsurface conditions at the Site, and containing specific baseline geotechnical conditions that may be anticipated or relied upon for bidding and contract administration purposes, subject to the controlling provisions of the Contract, including the GBR's own terms. The GBR is a Contract Document.

Geotechnical Data Report (GDR) — The factual report that collects and presents data regarding actual subsurface conditions at or adjacent to the Site, including Technical Data and other geotechnical data, prepared by or for Owner in support of the Geotechnical Baseline Report. The GDR's content may include logs of borings, trenches, and other site investigations, recorded measurements of subsurface water levels, the results of field and laboratory testing, and descriptions of the investigative and testing programs. The GDR does not include an interpretation of the data. If opinions, or interpretive or speculative non-factual comments or statements appear in a document that is labeled a GDR, such opinions, comments, or statements are not operative parts of the GDR and do not have contractual standing. Subject to that exception, the GDR is a Contract Document.

- SC-1.01.A.40 Add the following to Paragraph 1.01.A.40:

Trucking, shipping, delivery firms, consultants, and entities performing testing or inspection retained by Contractor or any Subcontractor are considered to be Subcontractors.

- SC-1.01.A.44 Add the following to Paragraph 1.01.A.44:

Entities that rent construction equipment or machinery, but are not incorporated into the Work, are considered to be Suppliers. If such rental entity furnishes both equipment and

one or more personnel to operate and maintain the equipment, such entity is a Subcontractor.

ARTICLE 2—PRELIMINARY MATTERS

2.01 *Delivery of Bonds and Evidence of Insurance*

2.02 *Copies of Documents*

SC-2.02 Add the following new paragraph immediately after Paragraph 2.02.B:

- C. Conformed documents incorporate and integrate Addenda and amendments negotiated prior to the Effective Date of the Contract. The conformed documents are produced for the convenience of the user and are not binding on the Owner nor do conformed documents take the place of the Contract Documents.

ARTICLE 3—CONTRACT DOCUMENTS: INTENT, REQUIREMENTS, REUSE

3.01 *Intent*

SC-3.01 Add the following new paragraphs immediately after Paragraph 3.01.E:

- F. The Specifications and other verbal components of the Contract Documents may vary in form, format, and style. Some Specification sections are written in varying degrees of streamlined or declarative style and some Specifications sections may, in comparison, employ a more-narrative style. Omissions of such words and phrases as "Contractor shall," "in conformity with," "as shown," or "as specified" are intentional in streamlined language in the Contract Documents. Omitted words and phrases are incorporated by inference. Similar types of provisions may appear in various parts of a Specifications section or elsewhere in the Contract Documents. Contractor shall not attempt to take advantage of any variation of form, format or style in Change Proposal(s) and Claim(s).
- G. Cross referencing of Specification sections in a Specifications section's heading "Related Sections includes, but are not necessarily limited to: "and elsewhere within each Specifications section is provided as an aid and convenience to Contractor. Contractor shall not rely on cross referencing indicated and is responsible for coordinating the entire Work and providing a complete Project whether or not cross referencing is provided in each Specifications section or whether or not cross referencing is complete.

ARTICLE 4—SITE, SUBSURFACE AND PHYSICAL CONDITIONS, HAZARDOUS ENVIRONMENTAL CONDITIONS

4.03 *Subsurface and Physical Conditions*

SC/GBR-4.04 Differing Subsurface or Physical Conditions

- A. Notice: If Contractor believes that any subsurface condition that is uncovered or revealed at the Site:
1. differs materially from conditions shown or indicated in the GBR; or
 2. differs materially from conditions shown or indicated in the GDR, to the extent the GBR is inapplicable; or
 3. differs materially from conditions shown or indicated in Contract Documents other than the GBR or GDR, to the extent the GBR and GDR are inapplicable; or
 4. to the extent the GBR and GDR are inapplicable, is of such a nature as to establish that any Technical Data on which Contractor is entitled to rely as provided in Paragraph 5.03 is materially inaccurate; or
 5. to the extent the GBR and GDR are inapplicable, is of such a nature as to require a change in the Drawings or Specifications; or
 6. to the extent the GBR and GDR are inapplicable, is of an unusual nature, and differs materially from conditions ordinarily encountered and generally recognized as inherent in work of the character provided for in the Contract Documents;

then Contractor shall, promptly after becoming aware thereof and before further disturbing the subsurface conditions or performing any Work in connection therewith (except in an emergency as required by Paragraph 7.15), notify Owner and Engineer in writing about such condition. Contractor shall not further disturb such condition or perform any Work in connection therewith (except with respect to an emergency) until receipt of a written statement permitting Contractor to do so.

- B. Engineer's Review: After receipt of written notice as required by the preceding paragraph, Engineer will promptly review the subsurface or physical condition in question; determine the necessity of Owner's obtaining additional exploration or tests with respect to the condition; conclude whether the condition falls within any one or more of the differing site condition categories in Paragraph SC/GBR 5.04.A above; obtain any pertinent cost or schedule information from Contractor; prepare recommendations to Owner regarding the Contractor's resumption or continuation of Work in connection with the subsurface or physical condition in question and the need for any change in the Drawings or Specifications; and advise Owner in writing of Engineer's findings, conclusions, and recommendations.

- C. Owner's Statement to Contractor Regarding Site Condition:

After receipt of Engineer's written findings, conclusions, and recommendations, Owner shall issue a written statement to Contractor (with a copy to Engineer) regarding the subsurface or physical condition in question, addressing the resumption or continuation of Work in connection with such condition, indicating whether any change in the Drawings or Specifications will be made, and adopting

or rejecting Engineer's written findings, conclusions, and recommendations, in whole or in part.

D. Possible Price and Times Adjustments:

1. Contractor shall be entitled to an equitable adjustment in Contract Price or Contract Times, or both, to the extent that the existence of a differing subsurface or physical condition, or any related delay, disruption, or interference, causes an increase or decrease in Contractor's cost of, or time required for, performance of the Work; subject, however, to the following:
 - a. such condition must fall within any one or more of the categories described in Paragraph SC/GBR 5.04.A;
 - b. with respect to Work that is paid for on a unit price basis, any adjustment in Contract Price will be subject to the provisions of Paragraph 13.03 of the General Conditions; and,
 - c. Contractor's entitlement to an adjustment of the Contract Times is conditioned on such adjustment being essential to Contractor's ability to complete the Work within the Contract Times.
2. Contractor shall not be entitled to any adjustment in the Contract Price or Contract Times with respect to a subsurface or physical condition if:
 - a. Contractor knew of the existence of such condition at the time Contractor made a commitment to Owner with respect to Contract Price and Contract Times by the submission of a Bid or becoming bound under a negotiated contract, or otherwise; or
 - b. the existence of such condition reasonably could have been discovered or revealed as a result of any examination, investigation, exploration, test, or study of the Site and contiguous areas expressly required by the Bidding Requirements or Contract Documents to be conducted by or for Contractor prior to Contractor's making such commitment; or
 - c. Contractor failed to give the written notice as required by Paragraph SC/GBR 5.04.A.
3. If Owner and Contractor agree regarding Contractor's entitlement to and the amount or extent of any adjustment in the Contract Price or Contract Times, or both, then any such adjustment shall be set forth in a Change Order.
4. Contractor may submit a Change Proposal regarding its entitlement to or the amount or extent of any adjustment in the Contract Price or Contract Times, or both, no later than 30 days after Owner's issuance of the Owner's written statement to Contractor regarding the subsurface or physical condition in question.

4.06 *Hazardous Environmental Conditions*

- SC 4.06 Delete Paragraphs 5.06.A and 5.06.B in their entirety and insert the following:
- A. No reports or drawings related to Hazardous Environmental Conditions at the Site are known to Owner.
 - B. Not Used.

ARTICLE 5—BONDS AND INSURANCE

5.02 Insurance—General Provisions

1. Contractor may obtain worker's compensation insurance from an insurance company that has not been rated by A.M. Best, provided that such company (a) is domiciled in the state in which the Project is located, (b) is certified or authorized as a worker's compensation insurance provider by the appropriate state agency, and (c) has been accepted to provide worker's compensation insurance for similar projects by the state within the last 12 months.

SC 5.03 Add the following new paragraph immediately after Paragraph 5.03.J:

- K. The limits of liability for the insurance required by Paragraph 5.03 of the General Conditions shall provide coverage for not less than the following amounts or greater where required by Laws and Regulations:

1. Workers' Compensation, and related coverages under Paragraphs 5.03.A.1 and A.2 of the General Conditions:

State:	<u>Statutory</u>
Federal, if applicable (e.g., Longshoreman's):	<u>Statutory</u>
Employer's Liability:	
Bodily injury, each accident	\$ <u>2,000,000</u>
Bodily injury by disease, each employee	\$ <u>2,000,000</u>
Bodily injury/disease aggregate	\$ <u>2,000,000</u>
Foreign voluntary worker compensation	<u>Statutory</u>

2. Contractor's Commercial General Liability under Paragraphs 6.03.B and 6.03.C of the General Conditions:

General Aggregate	\$ <u>2,000,000</u>
Products - Completed Operations Aggregate	\$ <u>2,000,000</u>
Personal and Advertising Injury	\$ <u>2,000,000</u>

- | | |
|---|---------------------|
| Each Occurrence (Bodily Injury and Property Damage) | \$ <u>2,000,000</u> |
|---|---------------------|
3. Automobile Liability under Paragraph 6.03.D. of the General Conditions:
- | | |
|--------------------------|---------------------|
| Bodily Injury: | |
| Each person | \$ <u>2,000,000</u> |
| Each accident | \$ <u>2,000,000</u> |
| Property Damage: | |
| Combined Single Limit of | \$ <u>2,000,000</u> |
4. Excess or Umbrella Liability:
- | | |
|-------------------|---------------------|
| Per Occurrence | \$ <u>1,000,000</u> |
| General Aggregate | \$ <u>2,000,000</u> |
6. Additional Insureds: In addition to Owner and Engineer, include as additional insureds the following:
- Engineer: Henningson, Durham & Richardson Architecture & Engineering, P.C.
7. Contractor's Professional Liability:
- | | |
|------------------|---------------------|
| Each Claim | \$ <u>1,000,000</u> |
| Annual Aggregate | \$ <u>2,000,000</u> |

ARTICLE 6—CONTRACTOR'S RESPONSIBILITIES

6.02 *Supervision and Superintendence*

SC-6.01.B. Amend Paragraph 7.01.B to add the following sentences: "The Contractor shall identify their representative at the Site that shall have authority to act on behalf of Contractor. All communications given to or received from this representative shall be binding on Contractor."

SC-6.01.C. Add the following new paragraph immediately after Paragraph 7.01.B:

Any superintendent or other personnel, who repeatedly fails to follow the Engineer's written or oral orders, directions, instructions, or determinations, shall be subject to removal from the project. Upon the written request of the Engineer, the Contractor shall immediately remove such superintendent or other personnel and name a replacement

in writing. Noncompliance with the Engineer's request to remove and replace personnel at any level shall be grounds for terminating the Contract.

6.03 *Services, Materials, and Equipment*

SC-6.03.B. Add the following new subparagraphs immediately after Paragraph 7.03.B:

1. Where the Work requires equipment be furnished, due to the lack of standardization of equipment as produced by the various manufacturers, it may become necessary to make minor modifications in the structures, buildings, piping, mechanical work, electrical work, accessories, controls, or other work, to accommodate the particular equipment offered. Contractor's bid price for any equipment offered shall include the cost of making any necessary changes subject to the approval of Engineer.

ARTICLE 7—ENGINEER'S STATUS DURING CONSTRUCTION

SC-7.01 *Determinations for Unit Price Work*

- 7.01.A Modify Paragraph GC-10.06.A by adding the following sentence at the end of the first sentence: "Contractor shall, at his own expense, provide help and other assistance as may be required for making measurements of Unit Price Work."

ARTICLE 8 – COST OF WORK; ALLOWANCES, UNIT PRICE WORK

8.03 *Unit Price Work*

- SC-8.03.C. Amend Paragraph 13.03.C to add the following sentences: "Work described in the Contract Documents, or reasonably inferred as required for a functionally complete installation, but not identified in the listing of unit price items, shall be considered incidental to unit price work listed and the cost of incidental work included as a part of the unit price."

ARTICLE 9—PAYMENTS TO CONTRACTOR, SET OFFS; COMPLETIONS; CORRECTION PERIOD

SC-9.07 *Waiver of Claims*

- SC-9.07.B. Amend Paragraph 15.07.B to state "The acceptance of final payment by Contractor will constitute a waiver by Contractor of all claims and rights against Owner and/or Engineer other than those pending matters that have been duly submitted or appealed under the provisions of Article 17."

NYSDOL Prevailing Wage Rates

This page intentionally left blank.

Introduction to the Prevailing Rate Schedule

Information About Prevailing Rate Schedule

This information is provided to assist you in the interpretation of particular requirements for each classification of work contained in the attached Schedule of Prevailing Rates.

Classification

It is the duty of the Commissioner of Labor to make the proper classification of works taking into account whether the work is heavy and highway, building, sewer and water, tunnel work, residential, and to make a determination of wages and supplements to be paid or provided. It is the responsibility of the public work contractor to use the proper rate. If there is a question on the proper classification to be used, please call the district office located nearest the project. District office locations and phone numbers are listed below.

Prevailing Wage Schedules are issued separately for "General Construction Projects" and "Residential Construction Projects" on a county-by-county basis.

General Construction Rates apply to projects such as: Buildings, Heavy & Highway, and Tunnel and Water & Sewer rates.

Residential Construction Rates generally apply to construction, reconstruction, repair, alteration, or demolition of one family, two family, row housing, or rental type units intended for residential use.

Some rates listed in the Residential Construction Rate Schedule have a very limited applicability listed along with the rate. Rates for occupations or locations not shown on the residential schedule must be obtained from the General Construction Rate Schedule. Please contact the local Bureau of Public Work office before using Residential Rate Schedules, to ensure that the project meets the required criteria.

Payrolls and Payroll Records

Contracts and subcontracts are required to establish, maintain, and preserve for not less than six (6) years, contemporaneous, true, and accurate payroll records.

Every contractor and subcontractor shall submit to the Department of Jurisdiction (Contracting Agency), within thirty (30) days after issuance of its first payroll and every thirty (30) days thereafter, a transcript of the original payrolls, subscribed and affirmed as true under penalty of perjury.

Paid Holidays

Paid Holidays are days for which an eligible employee receives a regular day's pay, but is not required to perform work. If an employee works on a day listed as a paid holiday, this remuneration is in addition to payment of the required prevailing rate for the work actually performed.

Overtime

At a minimum, all work performed on a public work project in excess of eight hours in any one day or more than five days in any two weeks is overtime. However, the specific overtime requirements for each trade or occupation on a public work project may differ. Specific overtime requirements for each trade or occupation are contained in the prevailing rate schedules.

Overtime holiday pay is the premium pay that is required for work performed on specified holidays. It is only required when the employee actually performs work on such holidays.

The applicable holidays are listed under HOLIDAYS: OVERTIME. The required rate of pay for these covered holidays can be found in the OVERTIME PAY section listings for each classification.

Supplemental Benefits

Particular attention should be given to the supplemental benefit requirements. Although in most cases the payment or provision of supplements is straight time for all hours worked, some classifications require the payment or provision of supplements, or a portion of the supplements, to be paid or provided at a premium rate for premium hours worked. Supplements may also be required to be paid or provided on paid holidays, regardless of whether the day is worked. The Overtime Codes and Notes listed on the particular wage classification will indicate these conditions as required.

Effective Dates

When you review the schedule for a particular occupation, your attention should be directed to the dates above the column of rates. These are the dates for which a given set of rates is effective. The rate listed is valid until the next effective rate change or until the new annual determination which takes effect on July 1 of each year. All contracts and subcontracts are required to pay the current prevailing rates of wages and supplements. If you have any questions please contact the Bureau of Public Work or visit the New York State Department of Labor website (www.labor.ny.gov) for current wage rate information.

Apprentice Training Ratios

The following are the allowable ratios of registered Apprentices to Journeyworkers.

For example, the ratio 1:1,1:3 indicates the allowable initial ratio is one Apprentice to one Journeyworker. The Journeyworker must be in place on the project before an Apprentice is allowed. Then three additional Journeyworkers are needed before a second Apprentice is allowed. The last ratio repeats indefinitely. The effect, the more Journeyworkers must be present before a third Apprentice can be hired, and so on.

Please call Apprentice Training Central Office at (518) 457-6820 if you have any questions.

Title (T ade)	Ratio
Boile make (Const uction)	1:1,1:4
Boile make (Shop)	1:1,1:3
Ca pente (Bldg.,H&H, Pile D ive /Dockbuilde)	1:1,1:4
Ca pente (Residential)	1:1,1:3
Elect ical (Outside) Lineman	1:1,1:2
Elect ician (Inside)	1:1,1:3
Elevato /Escalato Const uction & Mode nize	1:1,1:2
Glazie	1:1,1:3
Insulation & Asbestos Wo ke	1:1,1:3
I on Wo ke	1:1,1:4
Labo e	1:1,1:3
Mason	1:1,1:4
Millw ight	1:1,1:4
Op Enginee	1:1,1:5
Painte	1:1,1:3
Plumbe & Steamfitte	1:1,1:3
Roofe	1:1,1:2
Sheet Metal Wo ke	1:1,1:3
Sp inkle Fitte	1:1,1:2

If you have any questions conce ning the attached schedule o would like additional info mation, please contact the nea est BUREAU of PUBLIC WORK Dist ict Office o w ite to:

New Yo k State Depa tment of Labo
Bu eau of Public Wo k
State Office Campus, Bldg. 12
Albany, NY 12226

Dist ict Office Locations:	Telephone #	FAX #
Bu eau of Public Wo k - Albany	518-457-2744	518-485-0240
Bu eau of Public Wo k - Binghamton	607-721-8005	607-721-8004
Bu eau of Public Wo k - Buffalo	716-847-7159	716-847-7650
Bu eau of Public Wo k - Ga den City	516-228-3915	516-794-3518
Bu eau of Public Wo k - Newbu gh	845-568-5287	845-568-5332
Bu eau of Public Wo k - New Yo k City	212-932-2419	212-775-3579
Bu eau of Public Wo k - Patchogue	631-687-4882	631-687-4902
Bu eau of Public Wo k - Rocheste	585-258-4505	585-258-4708
Bu eau of Public Wo k - Sy acuse	315-428-4056	315-428-4671
Bu eau of Public Wo k - Utica	315-793-2314	315-793-2514
Bu eau of Public Wo k - White Plains	914-997-9507	914-997-9523
Bu eau of Public Wo k - Cent al Office	518-457-5589	518-485-1870

Orange County General Construction

oilermaker

02/01/2025

JO DESCRIPTION Boile make

DISTRICT 4

ENTIRE COUNTIES

B onx, Dutchess, Kings, Nassau, New Yo k, O ange, Putnam, Queens, Richmond, Rockland, Suffolk, Sullivan, Ulste , Westcheste

WAGES

Pe Hou : 07/01/2024 01/01/2025

Boile make \$ 67.38 \$ 68.88

Repai s & Renovations 67.38 68.88

Repai s & Renovation: Includes Repai ing, Renovating eplacement of pa ts to an existing unit(s).

SUPPLEMENTAL BENEFITS

Pe Hou :

Boile make	33.5% of hou ly	33.5% of Hou ly
Repai & Renovations	Wage Paid	Wage Paid
	+ \$ 26.85	+ \$26.85

NOTE: "Hou ly Wage Paid" shall include any and all p emium(s) pay.

Repai s & Renovation Includes eplacement of pa ts and epai s & enovation of existing unit.

OVERTIME PAY

See (*B, O, **U) on OVERTIME PAGE

Note:* Includes 9th & 10th hou s, double fo 11th o mo e.

** Labo Day ONLY, if wo ked.

Repai s & Renovation see (B,E,Q) on OT Page

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Ove time: See (5, 6, 11, 12, 15, 25, 26, 29) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wage pe hou :

(1/2) Yea Te ms at the following pe centage of Boile make 's Wage

1st	2nd	3 d	4th	5th	6th	7th
65%	70%	75%	80%	85%	90%	95%

Supplemental Benefits Pe Hou :

	33.5% of Hou ly	33.5% of Hou ly
	Wage Paid Plus	Wage Paid Plus
	Amount Below	Amount Below
1st Te m	\$ 20.36	\$ 20.36
2nd Te m	21.28	21.28
3 d Te m	22.22	22.22
4th Te m	23.12	23.12
5th Te m	24.07	24.07
6th Te m	25.00	25.00
7th Te m	25.93	25.93

NOTE: "Hou ly Wage Paid" shall include any and all p emium(s)

4-5

Carpenter

02/01/2025

JO DESCRIPTION Ca pente

DISTRICT 8

ENTIRE COUNTIES

B onx, Dutchess, Kings, Nassau, New Yo k, O ange, Putnam, Queens, Richmond, Rockland, Suffolk, Westcheste

WAGES

Pe Hou : 07/01/2024

Ma ine Const uction:

Ma ine Dive \$ 75.46
+ 10.00*

Ma ine Tende \$ 55.00
+ 10.00*

*This po tion of the benefit is NOT subject to the SAME PREMIUM as shown fo ove time

SUPPLEMENTAL BENEFITS

Pe Hou :

Jou neywo ke \$ 45.65

OVERTIME PAY

See (B, E, E2, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (18, 19) on HOLIDAY PAGE

Ove time: See (5, 6, 11, 13, 16, 18, 19, 25) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wages pe hou :

One (1) yea te ms.

1st yea \$ 26.98
+ 5.50*
2nd yea 32.58
+ 5.50*
3 d yea 40.96
+ 5.50*
4th yea 49.35
+ 5.50*

*This po tion of the benefit is NOT subject to the SAME PREMIUM as shown fo ove time.

Supplemental Benefits

Pe Hou :

All te ms \$ 32.20

8-1456MC

Carpenter

02/01/2025

JO DESCRIPTION Ca pente

DISTRICT 8

ENTIRE COUNTIES

B onx, Kings, Nassau, New Yo k, Queens, Richmond, Rockland, Westcheste

PARTIAL COUNTIES

O ange: South of but including the following, Wate loo Mills, Slate Hill, New Hampton, Goshen, Blooming G ove, Mountainville, east to the Hudson Rive .

Putnam: South of but including the following, Cold Sp ing, TompkinsCo ne , Mahopac, C oton Falls, east to Connecticut bo de .

Suffolk: West of Po t Jeffe son and Patchogue Road to Route 112 to the Atlantic Ocean.

WAGES

Pe hou : 07/01/2024

Co e D illing:

D ille \$ 46.25
+ 3.25*

D ille Helpe \$ 36.28
+ 3.25*

Note: Hazar dous Waste Pay Diffe ential:

Fo Level C, an additional 15% above wage ate pe hou

Fo Level B, an additional 15% above wage ate pe hou

Fo Level A, an additional 15% above wage ate pe hou

Note: When equi ed to wo k on wate : an additional \$ 3.00 pe hou .

*This po tion of the benefit is NOT subject to the SAME PREMIUM as shown fo ove time.

SUPPLEMENTAL ENEFITS

Pe hou :

D ille and Helpe \$ 30.24

O ERTIME PAY

See (B, G, P) on OVERTIME PAGE

HOLIDAY

Paid: See (5, 6) on HOLIDAY PAGE

Ove time: See (5, 6) on HOLIDAY PAGE

8-1536-Co eD ille

Carpenter

02/01/2025

JO DESCRIPTION Ca pente

DISTRICT 8

ENTIRE COUNTIES

Dutchess, O ange

WAGES

Pe hou : 07/01/2024

Building:

Millw ight \$ 46.35
+ 8.44*

*This po tion of the benefit is NOT subject to the SAME PREMIUM as shown fo ove time.

SUPPLEMENTAL ENEFITS

Pe hou :

Jou neyman \$ 34.94

O ERTIME PAY

See (B, E, E2, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (18, 19) on HOLIDAY PAGE

Paid: See (5,6,11,13,16,18,19,25) fo 1st & 2nd y . App entices

Ove time: See (5,6,11,13,16,18,19,25) on HOLIDAY PAGE.

REGISTERED APPRENTICES

Wages pe hou :

One (1) yea te ms:

1st	2nd	3 d	4th
\$ 28.18	\$ 30.51	\$ 34.84	\$ 43.50
+ 4.40*	+ 5.19*	+ 5.94*	+ 7.44*

*This po tion of the benefit is NOT subject to the SAME PREMIUM as shown fo ove time.

Supplemental benefits pe hou :

1st	2nd	3 d	4th
\$ 23.00	\$ 24.79	\$ 26.90	\$ 29.63

8-740.2

Carpenter

02/01/2025

JO DESCRIPTION Ca pente

DISTRICT 8

ENTIRE COUNTIES

Dutchess

PARTIAL COUNTIES

O ange: : The te ito y west dema cated by a line d awn f om the Bea Mountain B idge continuing east to the Bea Mountain Ci cle. The te ito y south dema cated by a line continuing no th on 9W to the town of Co nwall whe e County Road 107 (also known as Quake Rd) c osses unde 9W to the cente line of Route 32, The te ito ies south and east heading no th on Route 32 to O s Mills Rd, then west on O s Mills Rd to Route 94, continue west and south on Route 94 to the Town of Cheste , to the inte section of Kings Highway, continue south on Kings Highway to Bellvale Rd, west on Bellvale Rd to Bellvale Lakes Rd, then south on Bellvale Lakes Rd to Kain Rd, southeast on Kain Rd to Route 17A, then no th and southeast along Route 17A to Route 210, then follow Route 210 to NJ Bo de .

WAGES

Per hour : 07/01/2024

Capet/Resilient
Floor Cove e \$ 34.45
+ 3.25*

*This portion of the benefit is NOT subject to the SAME PREMIUM as shown for above time.

INCLUDES HANDLING & INSTALLATION OF ARTIFICIAL TURF AND SIMILAR TURF INDOORS/OUTDOORS.

SUPPLEMENTAL BENEFITS

Per hour :
\$ 28.33

OVERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (18, 19) on HOLIDAY PAGE

Paid for 1st & 2nd year.

App entices: See (5, 6, 11, 13, 16, 18, 19, 25)

Overtime: See (5, 6, 11, 13, 16, 18, 19, 25) on HOLIDAY PAGE.

REGISTERED APPRENTICES

Wage per hour - (1) year apprentices:	1st	2nd	3rd	4th
	\$15.75	\$18.87	\$23.55	\$28.23
	+ 2.48*	+ 2.48*	+ 2.48*	+ 2.48*

*This portion of the benefit is NOT subject to the SAME PREMIUM as shown for above time.

Supplemental Benefits per hour - All apprentice terms:

\$ 20.87

8-2287D&O

Carpenter - Building / Heavy&Highway

02/01/2025

JO DESCRIPTION Carpenter - Building / Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Columbia, Dutchess, Orange, Sullivan, Ulster

WAGES

WAGES (per hour)

Applies to Carpenter (Building/Heavy & Highway/Tunnel), Dockbuilder, Pile driver, Dive Tender, and Diver (Dry):

	07/01/2024	07/01/2025	07/01/2026
Base Wage	\$ 37.19	Additional \$ 2.23**	Additional \$ 2.30**
	+ 6.31*		

Applies to Diver (Wet):

Base Wage \$ 50.00
+ 6.31*

*For all hours paid straight premium.

**To be allocated at a later date.

SHIFT WORK

SHIFT DIFFERENTIAL: When mandated by a Government Agency regulation, off shift can be worked. The Carpenter shall receive an additional fifteen percent (15%) of the base wage.

SUPPLEMENTAL BENEFITS

Per hour :

Hourly wage \$ 30.65

OVERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

BUILDING:

Paid: See (1) on HOLIDAY PAGE.
Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE.
- Holidays that fall on Sunday will be observed Monday.

HEAVY&HIGHWAY/TUNNEL:

Paid: See (5, 6, 25) on HOLIDAY PAGE
Overtime: See (5, 6) on HOLIDAY PAGE
- Holidays that fall on Sunday will be observed Monday
- Must be employed during the five (5) work days immediately preceding a holiday or during the five (5) work days following the paid holiday to receive holiday pay
- If Employee is entitled to a paid holiday, the Employee is paid the Holiday wage and supplemental benefits whether they work or not. If Employee works the Holiday, the Employee will receive holiday pay (including supplemental benefits), plus the applicable premium wage for working the Holiday. If Employee works in excess of 8 hours on Holiday, then benefits will be paid for any hours in excess of 8 hours.

REGISTERED APPRENTICES

1 Year terms at the following wage rates.

1st	2nd	3rd	4th
\$ 18.60	\$ 22.31	\$ 26.03	\$ 29.75
+3.09*	+3.09*	+3.09*	+3.09*

*For all hours paid straight on premium

SUPPLEMENTAL BENEFITS per hour :

All Terms \$ 16.30

11-279.2B/H&H

Carpenter - Building / Heavy&Highway

02/01/2025

JO DESCRIPTION Carpenter - Building / Heavy&Highway

DISTRICT 2

ENTIRE COUNTIES

Albany, Allegany, Broome, Cattaraugus, Cayuga, Chautauque, Chemung, Chenango, Clinton, Columbia, Cortland, Delaware, Erie, Essex, Franklin, Fulton, Genesee, Greene, Hamilton, Herkimer, Jefferson, Lewis, Livingston, Madison, Monroe, Montgomery, Niagara, Oneida, Onondaga, Ontario, Orleans, Oswego, Otsego, Rensselaer, Saratoga, Schenectady, Schoharie, Schuyler, Seneca, Steuben, Sullivan, Tioga, Tompkins, Ulster, Warren, Washington, Wayne, Wyoming, Yates

PARTIAL COUNTIES

Orange: The area lying on the northern side of Orange County demarcated by a line drawn from the Bear Mountain Bridge continuing west to the Bear Mountain Circle, continue north on 9W to the town of Cornwall where County Road 107 (also known as Quaker Rd) crosses under 9W, then east on County Road 107 to Route 32, then north on Route 32 to Oss Mills Rd, then west on Oss Mills Rd to Route 94, continue west and south on Route 94 to the Town of Chester, to the intersection of Kings Highway, continue south on Kings Highway to Bellvale Rd, west on Bellvale Rd to Bellvale Lakes Rd, then south on Bellvale Lakes Rd to Kain Rd, southeast on Kain Rd to Route 17A, then north and southeast along Route 17A to Route 210, then follow Route 210 to NJ Border.

WAGES

Wages per hour : 07/01/2024

Carpenter - ONLY for
Artificial Turf/Synthetic
Sports Surface

\$ 36.48

Note - Does not include the operation of equipment. Please see Operating Engineer's rates.

SUPPLEMENTAL BENEFITS

Per hour :

Hourly wage \$ 26.55

OVERTIME PAY

See (B, E, Q, X) on OVERTIME PAGE

HOLIDAY

Paid: See (5) on HOLIDAY PAGE
Overtime: See (5, 6, 16) on HOLIDAY PAGE

Notes:

When a holiday falls upon a Saturday, it shall be observed on the preceding Friday. When a holiday falls upon a Sunday, it shall be observed on the following Monday.

An employee taking an unexcused day off the regularly scheduled day before or after a paid Holiday shall not receive Holiday pay.

REGISTERED APPRENTICES

Wages per hour (1300 hours terms at the following percentage of Hourly wage):

1st	2nd	3 d	4th
65%	70%	75%	80%

Supplemental Benefits per hour :

\$18.58	\$19.14	\$21.24	\$21.79
---------	---------	---------	---------

2-42AtSS

Carpenter - Floor Coverer

02/01/2025

JO DESCRIPTION Carpenter - Floor Coverer

DISTRICT 11

ENTIRE COUNTIES

Columbia, Sullivan, Ulster

PARTIAL COUNTIES

Orange: The area lying on the northern side of Orange County demarcated by a line drawn from the Bear Mountain Bridge continuing west to the Bear Mountain Circle, continue north on 9W to the town of Cornwall where County Road 107 (also known as Quaker Rd) crosses under 9W, then east on County Road 107 to Route 32, then north on Route 32 to Oss Mills Rd, then west on Oss Mills Rd to Route 94, continue west and south on Route 94 to the Town of Chester, to the intersection of Kings Highway, continue south on Kings Highway to Bellvale Rd, west on Bellvale Rd to Bellvale Lakes Rd, then south on Bellvale Lakes Rd to Kain Rd, southeast on Kain Rd to Route 17A, then north and southeast along Route 17A to Route 210, then follow Route 210 to NJ Border.

WAGES

WAGES:(per hour)

07/01/2024

07/01/2025

Carpenter/Resilient Floor Coverer

\$ 37.19

Additional

\$ 2.23**

+6.31*

* For all hours paid straight overtime premium

** To be allocated at a later date.

SHIFT WORK

SHIFT DIFFERENTIAL: When mandated by a Government Agency in regulation off shift can be worked. The Carpenter shall receive an additional fifteen (15) percent of wage plus applicable benefits.

SUPPLEMENTAL BENEFITS

Per hour :

Hourly wage

\$ 30.65

OVERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

BUILDING:

Paid: See (1) on HOLIDAY PAGE.

Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE.

- Holidays that fall on Sunday will be observed Monday.

HEAVY&HIGHWAY/TUNNEL:

Paid: See (5, 6, 25) on HOLIDAY PAGE

Overtime: See (5, 6) on HOLIDAY PAGE

- Holidays that fall on Sunday will be observed Monday

- Must be employed during the five (5) work days immediately preceding a holiday or during the five (5) work days following the paid holiday to receive holiday pay

- If Employee is entitled to a paid holiday, the Employee is paid the Holiday wage and supplemental benefits whether they work or not. If Employee works the Holiday, the Employee will receive holiday pay (including supplemental benefits), plus the applicable premium wage for working the Holiday. If Employee works in excess of 8 hours on Holiday, then benefits will be paid for any hours in excess of 8 hours.

REGISTERED APPRENTICES

1 Year apprentices at the following wage rates.

1st	2nd	3 d	4th
\$ 18.60	\$ 22.31	\$ 26.03	\$ 29.75
+3.09*	+3.09*	+3.09*	+3.09*

*For all hours paid straight overtime premium

SUPPLEMENTAL BENEFITS per hour :

All terms

\$ 16.30

11-279.2Floor

Electrician

02/01/2025

JO DESCRIPTION Elect ician

DISTRICT 11

ENTIRE COUNTIES

O ange, Putnam, Rockland

PARTIAL COUNTIES

Dutchess: Towns of Fishkill, East Fishkill, and Beacon.

WAGES

Pe hou :

07/01/2024

Elect ician Wi eman/Technician

\$ 50.50

+ 9.50*

*Fo all hou s paid st aight o p emium, not to be included in 3% calculation fo supplemental benefits.

NOTE ADDITIONAL AMOUNTS PAID FOR THE FOLLOWING WORK LISTED BELOW (subject to ove time p emiums):

- On jobs whe e employees a e equi ed to wo k f om boatswain chai s, swinging scaffolds, etc., fo ty (40) feet o mo e above the g ound, o unde comp essed ai , using Scottai packs, o gas masks, they shall eceive an additional \$2.00 pe hou above the egula st aight time ate.

- Jou neyman Wi eman wo king in Shafts, Tunnels o on Ba ges: \$5.00 above the Jou neyman Wi eman ate of pay

- Jou neyman Wi eman when pe fo ming welding o cable splicing: \$3.00 above the Jou neyman Wi eman ate of pay

- Jou neyman Wi eman equi ed to have a NYS Asbestos Ce tificate: \$3.00 above the Jou neyman Wi eman ate of pay

- Jou neyman Wi eman equi ed to have a CDL: \$3.00 above the Jou neyman Wi eman ate of pay.

SHIFT WORK

SHIFT DIFFERENTIAL: On Public Wo k in New Yo k State when shift wo k is mandated eithe in the job specifications o by the cont acting agency, the following ates apply when shift is wo ked:

Between 4:30pm & 12:30am \$ 59.30

+ 9.50*

Between 12:30am & 8:30am \$66.35

+ 9.50*

SUPPLEMENTAL ENEFITS

Pe hou :

07/01/2024

Jou neyman

\$ 29.68 plus

3% of st aight

o p emium wage

O ERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

Paid:

See (1) on HOLIDAY PAGE

Ove time:

See (5, 6, 13, 15, 16, 25) on HOLIDAY PAGE

When the holiday falls on a Satu day it is obse ved the F iday befo e. When the holiday falls on a Sunday it is obse ved on the Monday afte .

REGISTERED APPRENTICES

WAGES:

(1)yea te ms at the following ates

07/01/2024	1st	2nd	3 d	4th	5th	6th
1st Shift	\$ 16.01	\$ 19.40	\$ 24.25	\$ 29.10	\$ 33.95	\$ 36.38
	+1.00*	+1.00*	+1.50*	+2.00*	+2.50*	+2.50*
2nd Shift	18.78	22.76	28.45	34.13	39.82	42.67
	+1.00*	+1.00*	+1.50*	+2.00*	+2.50*	+2.50*
3 d Shift	21.04	25.49	31.86	38.24	44.61	47.80
	+1.00*	+1.00*	+1.50*	+2.00*	+2.50*	+2.50*
09/01/2024	1st	2nd	3 d	4th	5th	6th
1st Shift	\$ 16.01	\$ 19.40	\$ 24.25	\$ 29.10	\$ 33.95	\$ 36.38
	+1.00*	+1.00*	+1.00*	+2.00*	+2.50*	+2.50*
2nd Shift	18.78	22.76	28.45	34.13	39.82	42.67
	+1.00*	+1.00*	+1.00*	+2.00*	+2.50*	+2.50*
3 d Shift	21.04	25.49	31.86	38.24	44.61	47.80
	+1.00*	+1.00*	+1.00*	+2.00*	+2.50*	+2.50*
04/01/2025	1st	2nd	3 d	4th	5th	6th
1st Shift	\$ 16.34	\$ 19.80	\$ 24.75	\$ 29.70	\$ 34.65	\$ 37.13
	+1.00*	+1.00*	+1.00*	+2.00*	+2.50*	+2.50*
2nd Shift	19.17	23.23	29.03	34.84	40.64	43.55
	+1.00*	+1.00*	+1.00*	+2.00*	+2.50*	+2.50*

3 d Shift	21.47 +1.00*	26.02 +1.00*	32.52 +1.00*	39.03 +2.00*	45.53 +2.50*	48.79 +2.50*
-----------	-----------------	-----------------	-----------------	-----------------	-----------------	-----------------

*For all hours paid straight overtime premium, not to be included in 3% calculation for supplemental benefits.

SUPPLEMENTAL BENEFITS per hour :

07/01/2024

1st term	\$ 16.28 plus 3% of straight overtime premium wage
2nd term	\$ 16.28 plus 3% of straight overtime premium wage
3 d term	\$ 18.28 plus 3% of straight overtime premium wage
4th term	\$ 18.78 plus 3% of straight overtime premium wage
5th term	\$ 20.28 plus 3% of straight overtime premium wage
6th term	\$ 20.28 plus 3% of straight overtime premium wage

09/01/2024

1st term	\$ 16.28 plus 3% of straight overtime premium wage
2nd term	\$ 17.78 plus 3% of straight overtime premium wage
3 d term	\$ 18.78 plus 3% of straight overtime premium wage
4th term	\$ 19.78 plus 3% of straight overtime premium wage
5th term	\$ 21.28 plus 3% of straight overtime premium wage
6th term	\$ 21.28 plus 3% of straight overtime premium wage

11-363/1

Elevator Constructor

02/01/2025

JO DESCRIPTION Elevator Constructor

DISTRICT 1

ENTIRE COUNTIES

Columbia, Dutchess, Greene, Orange, Putnam, Sullivan, Ulster

PARTIAL COUNTIES

Delaware: Towns of Andes, Bovina, Colchester, Davenport, Delhi, Haverhill, Hemdon, Kottig, Meredith, Middletown, Roxbury, Hancock & Stamford

Rockland: Only the Township of Stony Point.

Westchester: Only the Townships of Bedford, Lewisboro, Coxsack, Mt. Kisco, North Salem, Pound Ridge, Somers and Yorktown.

WAGES

Per Hour	07/01/2024	01/01/2025
Mechanic	\$ 70.15	\$ 73.07
Helper	70% of Mechanic Wage Rate	70% of Mechanic Wage Rate

SUPPLEMENTAL BENEFITS

Per hour	07/01/2024	01/01/2025
Journeyworker/Helper	\$ 37.885*	\$ 38.435*

(*)Plus 6% of regular hourly rate if less than 5 years of service. Plus 8% of regular hourly rate if more than 5 years of service.

OVERTIME PAY

See (D, O) on OVERTIME PAGE

HOLIDAY

Paid: See (5, 6, 15, 16) on HOLIDAY PAGE

Overtime: See (5, 6, 15, 16) on HOLIDAY PAGE

Note: When a paid holiday falls on Saturday, it shall be observed on Friday. When a paid holiday falls on Sunday, it shall be observed on Monday.

REGISTERED APPRENTICES

Wages per hour :

0-6 mo*	6-12 mo	2nd y	3 d y	4th y
50 %	55 %	65 %	70 %	80 %

(*)Plus 6% of the hourly rate, no additional supplemental benefits.

Supplemental Benefits per hour worked:

Same as Journeyworker/Helper

Glazier	02/01/2025
----------------	-------------------

JO DESCRIPTION Glazier

DISTRICT 8

ENTIRE COUNTIES

Bronx, Dutchess, Kings, Nassau, New York, Orange, Putnam, Queens, Richmond, Rockland, Suffolk, Sullivan, Ulster, Westchester

WAGES

Per hour :

	07/01/2024	05/01/2025 Additional
Glazier, Glass Tinting and Window Film	\$ 63.28	\$ 1.11***
Scaffolding, including swing scaffold	67.28	
*Mechanical Equipment	64.28	
**Repair & Maintenance	30.76	

*Mechanical equipment, scissor jacks, man lifts, booms & buckets 30' or more, but not pipe scaffolding.

**Repair & Maintenance- All repair & maintenance work on a particular building whenever performed, whether the total cumulative Repair & Maintenance contract value is under \$193,000.

***To be allocated at a later date.

SUPPLEMENTAL BENEFITS

Per hour :

7/01/2024

Glazier, Glass Tinting and Window Film, Scaffolding and Mechanical Equipment

\$ 42.13

Repair & Maintenance

24.62

OVERTIME PAY

See (B, E, Q, V) on OVERTIME PAGE

For 'Repair & Maintenance' see (B, B2, I, S) on overtime page.

HOLIDAY

Paid: See (5, 6, 16, 25) on HOLIDAY PAGE

Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE

For 'Repair & Maintenance'

Paid: See(5, 6, 16, 25)

Overtime: See(5, 6, 16, 25)

REGISTERED APPRENTICES

Wage per hour :

(1) year terms at the following wage rates:

7/01/2024

1st term	\$ 22.34
2nd term	30.64
3rd term	40.87
4th term	50.14

Supplemental Benefits:

(Per hour)

1st term	\$ 19.27
2nd term	27.34
3rd term	32.85
4th term	36.01

8-1087 (DC9 NYC)

Insulator - Heat & Frost	02/01/2025
-------------------------------------	-------------------

JO DESCRIPTION Insulator - Heat & Frost

DISTRICT 8

ENTIRE COUNTIES

Dutchess, Orange, Putnam, Rockland, Westchester

WAGES

Per hour :

07/01/2024

Insulato	\$ 60.85
Discomfo t & Additional T aining**	63.92
Fi e Stop Wo k*	32.97

* Applies on all exclusive Fi e Stop Wo k (When cont act is fo Fi e Stop wo k only). No app entices on these cont acts only.

**Applies to wo k equi ing; ga b o equipment wo n against the body not customa ily wo n by insulato s; psychological evaluation ;special t aining, including but not limited to "Yellow Badge" adiation t aining

Note: Additional \$0.50 pe hou fo wo k 30 feet o mo e above floo o g ound level.

SUPPLEMENTAL ENEFITS

Pe hou :

Jou neywo ke	\$ 38.25
Discomfo t & Additional T aining	40.32
Fi e Stop Wo k: Jou neywo ke	19.48

O ERTIME PAY

See (B, E, E2, Q, *T) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Note: Last wo king day p eceding Ch istmas and New Yea s day, wo ke s shall wo k no late than 12:00 noon and shall eceive 8 h s pay.

Ove time: See (2*, 4, 6, 16, 25) on HOLIDAY PAGE.

*Note: Labo Day t iple time if wo ked.

REGISTERED APPRENTICES

(1) yea te ms:

Insulato App entices:				
1st	2nd	3 d	4th	
\$ 32.97	\$ 38.54	\$ 44.12	\$ 49.70	

Discomfo t & Additional T aining App entices:				
1st	2nd	3 d	4th	
\$ 34.51	\$ 40.38	\$ 46.27	\$ 52.16	

Supplemental Benefits paid pe hou :

Insulato App entices:	
1st te m	\$ 19.48
2nd te m	23.23
3 d te m	26.98
4th te m	30.74

Discomfo t & Additional T aining App entices:	
1st te m	\$ 20.50
2nd te m	24.47
3 d te m	28.43
4th te m	32.39

8-91

Ironworker	02/01/2025
-------------------	-------------------

JO DESCRIPTION I onwo ke

DISTRICT 11

ENTIRE COUNTIES

Dutchess, O ange, Putnam, Rockland, Sullivan, Ulste

WAGES

Pe hou :

	07/01/2024	07/01/2025	07/01/2026
		Additional	Additional
St uctu al	\$ 51.38	\$ 2.00*	\$ 2.00*

Reinforcing	51.38	2.00*	2.00*
Ornamental	51.38	2.00*	2.00*
Chain Link Fence	51.38	2.00*	2.00*

* To be allocated at a later date.

NOTE: For Reinforcing classification ONLY, Ironwork 4-46Reinforcing rates apply in Rockland County's southern section (south of Convent Road and east of Blue Hills Road).

SHIFT WORK

On Government Mandated Holidays or Shift Work, the following wage will be paid:

1st Shift	\$ 51.38
2nd Shift	66.39
3rd Shift	71.39

Note- Any shift that works past 12:00 midnight shall receive the 3rd shift differential.

SUPPLEMENTAL BENEFITS

Per hour :

Journeyman	\$ 45.56
------------	----------

OVERTIME PAY

See (B1, Q, V) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6, 16) on HOLIDAY PAGE

If a holiday falls on Saturday, it will be observed Friday. If a holiday falls on Sunday, it will be observed Monday.

REGISTERED APPRENTICES

Wages:

(1) year terms at the following wage:

	1st y	2nd y	3rd y	4th y
1st Shift	\$ 25.69	\$ 30.83	\$ 35.97	\$ 41.10
2nd Shift	36.15	42.20	48.25	54.29
3rd Shift	39.64	45.99	52.35	58.69

Supplemental Benefits per hour :

	07/01/2024
1st year	\$ 40.94
2nd year	41.86
3rd year	42.79
4th year	43.71

11-417

Laborer - Building

02/01/2025

JO DESCRIPTION Laborer - Building

DISTRICT 11

ENTIRE COUNTIES

Orange, Sullivan, Ulster

PARTIAL COUNTIES

Delaware: Only the Townships of Andes, Bovina, Davenport, Delhi, Franklin, Hamden, Harpersfield, Kortright, Meredith, Middletown, Roxbury, and Stamford.

Greene: Only the Township of Catskill.

WAGES

Class 1: Custodial and janitorial work, general cleanup, and flag person.

Class 2: Concrete laborer, masonry, hod carrier, signal person, pressure blasting and washing, chainsaw, demo saw, jackhammers, general laborer.

Class 3: Jumping jack, air track drills, grading, explosive handling and blasting, grade checker. When OSHA requires negative pressure testing.

Class 4: Environmental work including but not limited to asbestos abatement, toxic and hazardous abatement, lead abatement work, mold remediation and biohazard.

WAGES: (per hour)	07/01/2024	06/01/2025	06/01/2026
		Additional	Additional
Class 1	\$ 43.15	\$ 2.69*	\$ 2.79*
Class 2	43.95	2.72*	2.82*

Class 3	45.90	2.79*	2.89*
Class 4	49.00	2.90*	3.00*

*To be allocated at a later date.

These rates will cover all work within five feet of the building foundation line.

SHIFT WORK

Shift Differential: On all Governmental mandated irregular off shift work, an additional 25% of wage is equated. The 25% shift differential will be paid on public works contracts for shifts of irregular workdays outside the normal working hours for 2nd and 3rd shifts of irregular workday when mandated or equated by state, federal, county, local or other governmental agency contracts.

SUPPLEMENTAL BENEFITS

Per hour:

Journeyman	\$ 33.50
Shift	40.84

OVERTIME PAY

See (B, *E, E5, **Q) on OVERTIME PAGE

*For first 8 hours on Saturday

**When an employee is equated to work on a holiday which falls on a Sunday the employee shall be paid three (3) times the hourly rate and one (1) hour benefits for every hour worked. When an employee is equated to work on a holiday which falls on a Saturday the employee shall be paid two and a half (2.5) times the hourly rate and one hour benefits for every hour worked.

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE

Holidays that fall on Saturday shall be observed on Friday, when holidays fall on Sunday they shall be observed on Monday.

REGISTERED APPRENTICES

(1000) hours terms at the following wages.

	07/01/2024
1st term	\$ 28.05
2nd term	32.35
3rd term	36.70
4th term	41.00

Supplemental Benefits per hour:

All Terms Regular	\$ 29.23
All Terms Shift Rate	35.39

11-17.BA

Laborer - Heavy&Highway

02/01/2025

JO DESCRIPTION Laborer - Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Orange, Sullivan, Ulster

PARTIAL COUNTIES

Delaware: Only the Townships of Andes, Bovina, Middletown, Roxbury, Franklin, Hamden, Stamford, Delhi, Kortright, Harpersfield, Meredith, and Davenport.

Greene: Only the Township of Catskill.

WAGES

CLASS 1: Flag person, gate person.

CLASS 2: General laborer, chuck tender, nipper, powder carrier, magazine tender, concrete men, vibrator men, mason tender, mortar men, traffic control, custodial work, temporary heat, pump men, pit men, dump men, asphalt men, joint setter, signalman, pipe men, inspection, dry stone layers, jackhammer, bushhammer, pavement breaker, men on mulching & seeding machines, all seeding & sod laying, landscape work, walk behind self-propelled power saws, grinder, walk behind rollers and tampers of all types, burner men, filling and wiring of baskets for gabion walls, chain saw operator, railroad track laborer, power buggy, plastic & acoustic pump, power brush cutter, retention lines, walk behind surface plane, chipping hammer, manhole, catch basin or inlet installing, mortar mixer, laser men. *Micro paving and crack sealing.

CLASS 3: Asbestos, toxic, bio remediation and Phyto-remediation, lead or hazardous materials abatement when certification or license is equated, Dilling Equipment Only Where a Separate Air Compensatory Unit Supplies Power.

CLASS 4: Asphalt seedman, blaster, all laborers involved in pipejacking and boring operations not exceeding more than 10 feet into pipe, boring or drilled area.

WAGES: (per hour) 07/01/2024

Class 1	\$ 42.35
Class 2	46.05

Class 3	50.75
Class 4	55.80

* When labo e s a e pe fo ming mic o paving, c ack sealing o slu y application when not pa t of asphalt p ep ope ations labo e s shall
eeive an additional \$2.50 pe hou ove ate.

**To be allocated at a late date.

SHIFT WORK

SHIFT DIFFERENTIAL: Night wo k and i egula shift equi e 20% inc ease on wages fo all Gove nment mandated night and i egula shift
wo k.

SUPPLEMENTAL ENEFITS

Pe hou :	
Jou neyman	\$ 33.38
Shift	39.18

O ERTIME PAY

See (B, E, P, *R, **S, ***T, X) on OVERTIME PAGE

*Fo Mon-F i Holidays, Double Benefits to be paid fo all hou s wo ked.

**Fo Satu day Holidays, Two- and one-half Benefits fo all hou s wo ked.

***Fo Sunday Holidays, T iple Benefits fo all hou s wo ked.

HOLIDAY

Paid: See (5, 6, 15, 25) on HOLIDAY PAGE

Ove time: See (5, 6, 15, 25) on HOLIDAY PAGE

To be eligible fo a paid holiday, an employee must wo k at least two (2) days in the calenda week o pay oll week in which the holiday falls.

REGISTERED APPRENTICES

(1000) hou te ms at the following wages.

	07/01/2024
1st te m	\$ 28.05
2nd te m	32.35
3 d te m	36.70
4th te m	41.00

Supplemental Benefits pe hou :

All Te ms Regula	\$ 29.23
All Te ms Shift Rate	34.16

11-17.1H/H

Laborer - Tunnel

02/01/2025

JO DESCRIPTION Labo e - Tunnel

DISTRICT 11

ENTIRE COUNTIES

Columbia, Dutchess, G eeene, O ange, Otsego, Putnam, Rockland, Sullivan, Ulste , Westcheste

PARTIAL COUNTIES

Chenango: Townships of Columbus, She bu ne and New Be lin.

Delawa e: Townships of Andes, Bovina, Middletown, Roxbu y, F anklin, Hamden, Stamfo d, Delhi, Ko t ight, Ha pe sfield, Me ideth and
Davenpo t.

WAGES

Class 1: All suppo t labo e s/sandhogs wo king above the shaft o tunnel.

Class 2: All labo e s/sandhogs wo king in the shaft o tunnel.

Class 4: Safety Mine s

Class 5: Site wo k elated to Shaft/Tunnel

WAGES: (pe hou)

	07/01/2024	06/01/2025
Class 1	\$ 57.05	\$ 58.55
Class 2	59.20	60.70
Class 4	65.60	67.10
Class 5	49.90	51.40

Toxic and haza dous waste, lead abatement and asbestos abatement wo k will be paid an additional \$ 3.00 an hou .

SHIFT WORK

SHIFT DIFFERENTIAL...On all Gove nment mandated i egula shift wo k:

- Employee shall be paid at time and one half the regular rate Monday through Friday.
- Saturday shall be paid at 1.65 times the regular rate.
- Sunday shall be paid at 2.15 times the regular rate.

SUPPLEMENTAL BENEFITS

Per hour :

Benefit 1	\$ 36.98	\$ 38.23
Benefit 2	55.39	59.99
Benefit 3	74.58	76.73

Benefit 1 applies to straight time hours, paid holidays not worked.

Benefit 2 applies to over 8 hours in a day (M-F), irregular shift work hours not worked, and Saturday hours not worked.

Benefit 3 applies to Sunday and Holiday hours not worked.

OVERTIME PAY

See (B, E, Q, X) on OVERTIME PAGE

HOLIDAY

Paid: See (5, 6, 15, 25) on HOLIDAY PAGE

Overtime: See (5, 6, 15, 16, 25) on HOLIDAY PAGE

When a recognized Holiday falls on Saturday or Sunday, holidays falling on Saturday shall be recognized or observed on Friday and holidays falling on Sunday shall be recognized or observed on Monday. Employees ordered to work on the Saturday or Sunday of the holiday or on the recognized or the observed Friday or Monday for those holidays falling on Saturday or Sunday shall receive double time the established rate and benefits for the holiday.

REGISTERED APPRENTICES

FOR APPRENTICE RATES, refer to the appropriate Laborer Heavy & Highway wage rate contained in the wage schedule for the County and location where the work is to be performed.

11-17/60/235/754Tun

Lineman Electrician

02/01/2025

JO DESCRIPTION Lineman Electrician

DISTRICT 6

ENTIRE COUNTIES

Albany, Allegany, Broome, Cattaraugus, Cayuga, Chautauque, Chemung, Chenango, Clinton, Columbia, Cortland, Delaware, Dutchess, Erie, Essex, Franklin, Fulton, Genesee, Greene, Hamilton, Herkimer, Jefferson, Lewis, Livingston, Madison, Monroe, Montgomery, Niagara, Oneida, Onondaga, Ontario, Orange, Orleans, Oswego, Otsego, Putnam, Rensselaer, Rockland, Saratoga, Schenectady, Schoharie, Schuyler, Seneca, Steuben, Sullivan, Tioga, Tompkins, Ulster, Warren, Washington, Wayne, Wyoming, Yates

WAGES

A Lineman/Technician shall perform all overhead aerial work. A Lineman/Technician on the ground will install all electrical panels, connect all grounds, install and connect all electrical conductors, assembly of all electrical materials, conduit, pipe, raceway; placing of fish wire; pulling of cables, wires or fiber optic cable through such raceways; splicing of conductors; dismantling of such structures, lines or equipment.

Cable Operator: Operation of any type of cable on line projects.

Cable Backhoe: Operation of tracked excavator/cable backhoe with 1/2 yard bucket or larger on line projects.

Digging Machine Operator: All other digging equipment and augering on line projects.

A Groundman/Trench Diver shall: Build and set concrete forms, handle steel mesh, set foot ladders, transport concrete in a wheelbarrow, hand or machine concrete vibrator, finish concrete footings, mix mortar, g out pole bases, cover and maintain footings while curing in cold weather, operate jackhammer, operate hand pavement breaker, tamper, concrete and other motorized saws, as a dill helper, operate and maintain generator sets, water pumps, chainsaws, sand blasting, operate mulching and seeding machine, air tools, electric tools, gas tools, load and unload materials, hand shovel and/or boom, prepare and pour mastic and other fillers, assist digger/operator/equipment operator in ground excavation and restoration, landscape work and painting. Only when assisting a lineman technician, a groundman/trench diver may assist in installing conduit, pipe, cables and equipment.

NOTE: Includes Teledata Work within ten (10) feet of High Voltage Transmission Lines. Also includes digging of holes for poles, anchors, footing, and foundations for electrical equipment.

Below rates applicable on all overhead and underground distribution and maintenance work, and all overhead and underground transmission line work and the installation of fiber optic cable where no other construction trades are involved. Includes access matting for line work.

Per hour : 07/01/2024

Group A:

Lineman, Technician	\$ 58.90
Cable, Cable Backhoe	58.90
Welder, Cable Splice	58.90

G oup B:	
Digging Mach. Ope ato	53.01
T acto T aile D ive	50.07
G oundman, T uck D ive	47.12
Equipment Mechanic	47.12
Flagman	35.34

Additional \$1.00 pe hou fo enti e c ew when a helicopte is used.

Below rates applicable on all elect ical sub-stations, switching st uctu es, fibe optic cable and all othe wo k not defined as "Utility outside elect ical wo k." Includes access matting fo line wo k.

G oup A:	
Lineman, Technician	\$ 58.90
C ane, C awle Backhoe	58.90
Cable Splice	64.79
Ce tified Welde ,	
Pipe Type Cable	61.85

G oup B:	
Digging Mach. Ope ato	53.01
T acto T aile D ive	50.07
G oundman, T uck D ive	47.12
Equipment Mechanic	47.12
Flagman	35.34

Additional \$1.00 pe hou fo enti e c ew when a helicopte is used.

Below rates applicable on all switching st uctu es, maintenance p ojects, ail oad catena y install/maintenance thi d ail installation, bonding of ails and pipe type cable and installation of fibe optic cable. Includes access matting fo line wo k.

G oup A:	
Lineman, Tech, Welde	\$ 60.22
C ane, C awle Backhoe	60.22
Cable Splice	66.24
Ce tified Welde ,	
Pipe Type Cable	63.23

G oup B:	
Digging Mach. Ope ato	54.20
T acto T aile D ive	51.19
G oundman, T uck D ive	48.18
Equipment Mechanic	48.18
Flagman	36.13

Additional \$1.00 pe hou fo enti e c ew when a helicopte is used.

Below rates applicable on all ove head and unde g ound t ansmission line wo k & fibe optic cable whe e othe const uction t ades a e o have been involved. This applies to t ansmission line wo k only, not othe const uction. Includes access matting fo line wo k.

G oup A:	
Lineman, Tech, Welde	\$ 61.41
C ane, C awle Backhoe	61.41

G oup B:	
Digging Mach. Ope ato	55.27
T acto T aile D ive	52.20
G oundman, T uck D ive	49.13
Equipment Mechanic	49.13
Flagman	36.85

Additional \$1.00 pe hou fo enti e c ew when a helicopte is used.

SHIFT WORK

THE FOLLOWING RATES WILL APPLY ON ALL CONTRACTING AGENCY MANDATED MULTIPLE SHIFTS OF AT LEAST FIVE (5) DAYS DURATION WORKED BETWEEN THE HOURS LISTED BELOW:

1ST SHIFT

8:00 AM to 4:30 PM REGULAR RATE

2ND SHIFT	4:30 PM to 1:00 AM REGULAR RATE PLUS 17.3 %
3RD SHIFT	12:30 AM to 9:00 AM REGULAR RATE PLUS 31.4 %

SUPPLEMENTAL BENEFITS

Per hour :

07/01/2024

Group A	\$ 30.90 *plus 7% of the hourly wage paid
---------	--

Group B	\$ 26.90 *plus 7% of the hourly wage paid
---------	--

*The 7% is based on the hourly wage paid, straight time or premium time.

OVERTIME PAY

See (B, E, Q, X) on OVERTIME PAGE. NOTE: Double time for all emergency work designated by the Dept. of Jurisdiction.

WAGE CAP - Double the straight time hourly base wage shall be the maximum hourly wage compensation for any hour worked. Contractor is still responsible to pay the hourly benefit amount for each hour worked.

HOLIDAY

Paid See (5, 6, 8, 13, 25) on HOLIDAY PAGE plus Governor of NYS Election Day.

Overtime See (5, 6, 8, 13, 25) on HOLIDAY PAGE plus Governor of NYS Election Day.

NOTE: All paid holidays falling on Saturday shall be observed on the preceding Friday. All paid holidays falling on Sunday shall be observed on the following Monday. Supplements for holidays paid at straight time.

REGISTERED APPRENTICES

WAGES per hour : 1000 hours at the following percentage of the applicable Journeyworker's Lineman wage.

1st	2nd	3rd	4th	5th	6th	7th
60%	65%	70%	75%	80%	85%	90%

SUPPLEMENTAL BENEFITS per hour :

07/01/2024

\$ 26.90
*plus 7% of
the hourly
wage paid

*The 7% is based on the hourly wage paid, straight time or premium time.

6-1249a

Lineman Electrician - Teledata

02/01/2025

JO DESCRIPTION Lineman Electrician - Teledata

DISTRICT 6

ENTIRE COUNTIES

Albany, Allegany, Broome, Cattaraugus, Cayuga, Chautauqua, Chemung, Chenango, Clinton, Columbia, Cortland, Delaware, Dutchess, Erie, Essex, Franklin, Fulton, Genesee, Greene, Hamilton, Herkimer, Jefferson, Lewis, Livingston, Madison, Monroe, Montgomery, Niagara, Oneida, Onondaga, Ontario, Orange, Orleans, Oswego, Otsego, Putnam, Rensselaer, Rockland, Saratoga, Schenectady, Schoharie, Schuyler, Seneca, St. Lawrence, Steuben, Sullivan, Tioga, Tompkins, Ulster, Warren, Washington, Wayne, Westchester, Wyoming, Yates

WAGES

Per hour :

For outside work, stopping at first point of attachment (demonstration).

07/01/2024

01/01/2025

Cable Splice	\$ 39.24	\$ 40.81
Installation, Repairman	\$ 37.24	\$ 38.73
Teledata Lineman	\$ 37.24	\$ 38.73
Tech., Equip. Operator	\$ 37.24	\$ 38.73
Groundman	\$ 19.74	\$ 20.53

NOTE: EXCLUDES Teledata work within ten (10) feet of High Voltage (600 volts and over) transmission lines. For this work please see LINEMAN.

Above rates are applicable for installation, testing, operation, maintenance and repair on all Traffic Control (Signal) and Illumination (Lighting) projects, Traffic Monitoring Systems, and Road Weather Information Systems. Includes digging of holes for poles, anchors, footings foundations for electrical equipment; assembly of all electrical materials on raceway; placing of fish wire; pulling of cables, wires or fiber optic cable through such raceways; splicing of conductors; dismantling of such structures, lines or equipment.

SHIFT WORK

THE FOLLOWING RATES WILL APPLY ON ALL CONTRACTING AGENCY MANDATED MULTIPLE SHIFTS OF AT LEAST FIVE (5) DAYS DURATION WORKED BETWEEN THE HOURS LISTED BELOW:

1ST SHIFT	8:00 AM TO 4:30 PM REGULAR RATE
2ND SHIFT	4:30 PM TO 1:00 AM REGULAR RATE PLUS 17.3%
3RD SHIFT	12:30 AM TO 9:00 AM REGULAR RATE PLUS 31.4%

SUPPLEMENTAL BENEFITS

Per hour worked:

07/01/2024

Group A: \$ 30.90
*plus 7% of
the hourly
wage paid

Group B \$ 26.90
*plus 7% of
the hourly
wage paid

*The 7% is based on the hourly wage paid, straight time or premium time.

OVERTIME PAY

See (B, E, Q, X) on OVERTIME PAGE. NOTE: Double time for all emergency work designated by the Dept. of Jurisdiction.

WAGE CAP - Double the straight time hourly base wage shall be the maximum hourly wage compensation for any hour worked. Contractor is still responsible to pay the hourly benefit amount for each hour worked.

HOLIDAY

Paid: See (5, 6, 8, 13, 25) on HOLIDAY PAGE and Governor of NYS Election Day.

Overtime: See (5, 6, 8, 13, 25) on HOLIDAY PAGE and Governor of NYS Election Day.

NOTE: All paid holidays falling on Saturday shall be observed on the preceding Friday. All paid holidays falling on Sunday shall be observed on the following Monday. Supplements for holidays paid at straight time.

REGISTERED APPRENTICES

WAGES per hour : 1000 hours at the following percentage of the applicable Journeyworker's Lineman wage.

1st	2nd	3rd	4th	5th	6th	7th
60%	65%	70%	75%	80%	85%	90%

SUPPLEMENTAL BENEFITS per hour :

07/01/2024

\$ 26.90
*plus 7% of
the hourly
wage paid

*The 7% is based on the hourly wage paid, straight time or premium time.

6-1249aReg8LT

Lineman Electrician - Tree Trimmer

02/01/2025

JO DESCRIPTION Lineman Electrician - Tree Trimmer

DISTRICT 6

ENTIRE COUNTIES

Albany, Allegany, Broome, Cattaraugus, Cayuga, Chautauqua, Chemung, Chenango, Clinton, Columbia, Cortland, Delaware, Dutchess, Erie, Essex, Franklin, Fulton, Genesee, Greene, Hamilton, Herkimer, Jefferson, Lewis, Livingston, Madison, Monroe, Montgomery, Niagara, Oneida, Onondaga, Ontario, Orange, Orleans, Oswego, Otsego, Putnam, Rensselaer, Rockland, Saratoga, Schenectady, Schoharie, Schuylle, Seneca, St. Lawrence, Steuben, Sullivan, Tioga, Tompkins, Ulster, Warren, Washington, Wayne, Wyoming, Yates

WAGES

Applies to line clearance, tree work and right-of-way preparation on all new or existing energized overhead underground electrical, telephone and CATV lines. This also includes stump removal near underground energized electrical lines including telephone and CATV lines.

Pe hou : 07/01/2024

T ee T imme	\$ 31.44
Equipment Ope ato	27.80
Equipment Mechanic	27.80
T uck D ive	23.15
G oundman	19.07
Flag pe son	15.00*

*NOTE-Rate effective on 01/01/2025 - \$15.50 due to minimum wage inc ease.

SUPPLEMENTAL ENEFITS

Pe hou :

07/01/2024

Jou neywo ke	\$ 10.48
	*plus 4.5% of the hou ly wage paid

* The 4.5% is based on the hou ly wage paid, st aight time ate o p emium ate.

O ERTIME PAY

See (B, E, Q, X) on OVERTIME PAGE

WAGE CAP - Double the st aight time hou ly base wage shall be the maximum hou ly wage compensation fo any hou wo ked. Cont acto is still esponsible to pay the hou ly benefit amount fo each hou wo ked.

HOLIDAY

Paid: See (5, 6, 8, 15) on HOLIDAY PAGE

Ove time: See (5, 6, 8, 15, 16, 25) on HOLIDAY PAGE

NOTE: All paid holidays falling on a Satu day shall be obse ved on the p eceding F iday. All paid holidays falling on a Sunday shall be obse ved on the following Monday.

6-1249TT

Mason - uilding

02/01/2025

JO DESCRIPTION Mason - Building

DISTRICT 11

ENTIRE COUNTIES

Putnam, Rockland, Westcheste

PARTIAL COUNTIES

O ange: Only the Township of Tuxedo.

WAGES

Pe hou :

07/01/2024

B icklaye	\$ 47.44
Cement Mason	47.44
Plaste e /Stone Mason	47.44
Pointe /Caulke	47.44

Additional \$1.00 pe hou fo powe saw wo k

Additional \$0.50 pe hou fo swing scaffold o staging wo k

SHIFT WORK

SHIFT WORK: When shift wo k o an i egula wo kday is mandated o equi ed by state, fede al, county, local o othe gove nmental agency cont acts, the following p emiums apply:

I egula wo kday equi es 15% p emium

Second shift an additional 15% of wage plus benefits to be paid

Thi d shift an additional 25% of wage plus benefits to be paid

SUPPLEMENTAL ENEFITS

Pe hou :

Jou neyman	\$ 38.50
------------	----------

O ERTIME PAY

OVERTIME:

Cement Mason See (B, E, Q, W) on OVERTIME PAGE.
All Othe s See (B, E, Q) on OVERTIME PAGE.

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Ove time: See (5, 6, 16, 25) on HOLIDAY PAGE

Wheneve any of the above holidays fall on Sunday, they will be obse ved on Monday. Wheneve any of the above holidays fall on Satu day, they will be obse ved on F iday.

REGISTERED APPRENTICES

Wages pe hou :

750 hou te ms at the following pe centage of Jou neyman's wage

1st	2nd	3 d	4th	5th	6th	7th	8th
50%	55%	60%	65%	70%	75%	80%	85%

Supplemental Benefits pe hou

750 hou te ms at the following pe centage of jou neyman supplements

1st	2nd	3 d	4th	5th	6th	7th	8th
50%	55%	60%	65%	70%	75%	80%	85%

App entices indentu ed befo e June 1st, 2011 eceive full jou neyman benefits

11-5wp-b

Mason - uilding

02/01/2025

JO DESCRIPTION Mason - Building

DISTRICT 9

ENTIRE COUNTIES

B onx, Dutchess, Kings, Nassau, New Yo k, O ange, Putnam, Queens, Richmond, Rockland, Suffolk, Sullivan, Ulste , Westcheste

WAGES

Pe Hou :

07/01/2024

01/06/2025

Ma ble Cutte s & Sette s

\$ 63.92

\$ 64.21

SUPPLEMENTAL ENEFITS

Pe Hou :

Jou neywo ke

\$ 40.05

\$ 40.51

O ERTIME PAY

See (B, E, Q, V) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Ove time: See (5, 6, 8, 11, 15, 16, 25) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wage Pe Hou :

750 hou te ms at the following wage

1st	2nd	3 d	4th	5th	6th	7th	8th
0-3000	3001-3750	3751-4500	4501-5250	5251-6000	6001-6750	6751-7500	7500+
07/01/2024							
\$ 27.01	\$ 40.52	\$ 43.88	\$ 47.26	\$ 50.64	\$ 54.32	\$ 60.71	\$ 63.92
01/06/2025							
\$ 27.24	\$ 40.84	\$ 44.25	\$ 47.63	\$ 51.05	\$ 54.58	\$ 60.99	\$ 64.21

Supplemental Benefits pe hou :

1st	2nd	3 d	4th	5th	6th	7th	8th
07/01/2024							
\$ 26.42	\$ 29.76	\$ 30.61	\$ 31.44	\$ 32.28	\$ 37.55	\$ 39.23	\$ 40.05
01/06/2025							
\$ 26.88	\$ 30.14	\$ 30.95	\$ 31.78	\$32.59	\$38.07	\$ 39.71	\$ 40.51

9-7/4

Pe Hou :
Jou neywo ke : \$ 25.11* \$ 25.56*
+6.14 +6.15

* This po tion of benefits subject to same p emium ate as shown fo ove time wages.

O ERTIME PAY

See (B, E, Q) on OVERTIME PAGE

Double time ate applies afte 10 hou s

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Ove time: See (5, 6, 11, 15, 16, 25) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wage pe hou :

(Counties of O ange & Putnam)

750 hou te ms at the following wage ate:

1st	2nd	3 d	4th	5th	6th	7th	8th	9th	10th
1-	751-	1501-	2251-	3001-	3751-	4501-	5251-	6001-	6751-
750	1500	2250	3000	3750	4500	5250	6000	6750	7500
07/01/2024									
\$22.19	\$27.21	\$34.45	\$39.46	\$43.07	\$46.58	50.23	\$55.24	\$57.71	\$62.00
12/02/2024									
\$22.29	\$27.35	\$34.36	\$39.41	\$43.05	\$46.60	\$50.29	\$55.33	\$57.84	\$62.20

Supplemental Benefits pe hou :

(Counties of O ange & Putnam)

1st	2nd	3 d	4th	5th	6th	7th	8th	9th	10th
07/01/2024									
\$12.55*	\$12.55*	\$15.36*	\$15.36*	\$16.36*	\$17.86*	\$18.86*	\$18.86*	\$18.86*	\$24.11*
+ 0.76	+ 0.81	+ 0.91	+ 0.96	+ 1.43	+ 1.48	+ 1.91	+ 1.97	+ 4.57	+ 5.18
12/02/2024									
\$12.70*	\$12.70*	\$15.81*	\$15.81*	\$16.81*	\$18.31*	\$19.31*	\$19.31*	\$19.31*	\$24.56*
+ 0.76	+ 0.81	+ 0.91	+ 0.96	+ 1.43	+ 1.48	+ 1.91	+ 1.97	+ 4.57	+ 5.18

Wages pe hou :

(Counties of Dutchess, Sullivan, Ulste)

750 hou te ms at the following wage ate:

1st	2nd	3 d	4th	5th	6th	7th	8th	9th	10th
1-	751-	1501-	2251-	3001-	3751-	4501-	5251-	6001-	6751-
750	1500	2250	3000	3750	4500	5250	6000	6750	7500
07/01/2024									
\$22.06	\$26.44	\$28.50	\$32.88	\$35.84	\$39.71	\$43.21	\$46.59	\$47.95	\$51.44
12/02/2024									
\$22.06	\$26.44	\$28.50	\$32.88	\$35.84	\$39.71	\$43.21	\$46.59	\$47.95	\$51.94

Supplemental Benefits pe hou :

(Counties of Dutchess, Sullivan, Ulste)

1st	2nd	3 d	4th	5th	6th	7th	8th	9th	10th
07/01/2024									
\$12.55*	\$12.55*	\$14.86*	\$14.86*	\$15.86*	\$16.36*	\$16.86*	\$17.86*	\$17.86*	\$22.61*
+ 0.76	+ 0.80	+ 0.85	+ 0.89	+ 1.35	+ 1.40	+ 1.82	+ 1.87	+ 4.93	+ 5.02
12/02/2024									
\$12.55*	\$12.55*	\$14.86*	\$14.86*	\$15.86*	\$16.36*	\$16.86*	\$17.86*	\$17.86*	\$22.61*
+ 0.76	+ 0.80	+ 0.85	+ 0.89	+ 1.35	+ 1.40	+ 1.82	+ 1.87	+ 4.93	+ 5.02

* This portion of benefits subject to same premium rate as shown for overtime wages.

9-7/52B

Mason - Building	02/01/2025
-------------------------	-------------------

JO DESCRIPTION Mason - Building

DISTRICT 9

ENTIRE COUNTIES

Dutchess, Orange, Putnam, Sullivan, Ulster

WAGES

Per hour :	07/01/2024	12/02/2024
Building		
Tile, Marble, &		
Terrazzo Finishes	\$ 47.74	\$ 47.82

*To be allocated at a later date.

SUPPLEMENTAL BENEFITS

Jobneywork :

Per Hour	\$ 22.11*	\$ 22.56*
	+ 6.01	+ 6.02

*This portion of benefits subject to same premium rate as shown for overtime wages

OVERTIME PAY

See (A, *E, Q) on OVERTIME PAGE

Double time rate applies after 10 hours on Saturdays.

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6, 11, 15, 16, 25) on HOLIDAY PAGE

9-7/88B-tf

Mason - Heavy&Highway	02/01/2025
----------------------------------	-------------------

JO DESCRIPTION Mason - Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Putnam, Rockland, Westchester

PARTIAL COUNTIES

Orange: Only the Township of Tuxedo.

WAGES

Per hour :	07/01/2024
Bricklayer	\$ 47.94
Cement Mason	47.94
Marble/Stone Mason	47.94
Plaster	47.94
Pointing/Caulking	47.94

Additional \$1.00 per hour for power saw work

Additional \$0.50 per hour for swing scaffold or staging work

SHIFT WORK

When shift work on a regular workday is mandated or required by state, federal, county, local or other governmental contracts, the following rates apply:

Regular workday requires 15% premium
Second shift an additional 15% of wage plus benefits to be paid
Third shift an additional 25% of wage plus benefits to be paid

SUPPLEMENTAL BENEFITS

Per hour :

Jobneyman \$ 38.50

OVERTIME PAY

Cement Mason See (B, E, Q, W)
All Others See (B, E, Q,)

HOLIDAY

Paid: See (5, 6, 16, 25) on HOLIDAY PAGE
Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE

- Whenever any of the above holidays fall on Sunday, they will be observed on Monday. Whenever any of the above holidays fall on Saturday, they will be observed on Friday.
- Supplemental Benefits are not paid for paid Holiday
- If Holiday is worked, Supplemental Benefits are paid for hours worked.
- Whenever an Employee works within three (3) calendar days before a holiday, the Employee shall be paid for the Holiday.

REGISTERED APPRENTICES

Wages per hour :

750 hours at the following percentage of Journeyman's wage

1st	2nd	3rd	4th	5th	6th	7th	8th
50%	55%	60%	65%	70%	75%	80%	85%

Supplemental Benefits per hour

750 hours at the following percentage of journeyman supplements

1st	2nd	3rd	4th	5th	6th	7th	8th
50%	55%	60%	65%	70%	75%	80%	85%

Apprentices indentured before June 1st, 2011 receive full journeyman benefits

11-5WP-H/H

Mason - Heavy&Highway

02/01/2025

JO DESCRIPTION Mason - Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Dutchess, Sullivan, Ulster

PARTIAL COUNTIES

Orange: Entire county except the Township of Tuxedo.

WAGES

Per hour :

07/01/2024

Bicklaye	\$ 46.95
Cement Mason	46.95
Masonry/Stone Mason	46.95
Plaster	46.95
Pointing/Caulking	46.95

Additional \$1.00 per hour for power saw work

Additional \$0.50 per hour for swing scaffold or staging work

SHIFT WORK

When shift work on a regular workday is mandated or required by state, federal, county, local or other governmental contracts, the following rates apply:

Regular workday requires 15% premium

Second shift an additional 15% of wage plus benefits to be paid

Third shift an additional 25% of wage plus benefits to be paid

SUPPLEMENTAL BENEFITS

Per hour :

Journeyman \$ 38.00

OVERTIME PAY

Cement Mason See (B, E, Q, W)

All Others See (B, E, Q)

HOLIDAY

Paid: See (5, 6, 16, 25) on HOLIDAY PAGE

Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE

- Whenever any of the above holidays fall on Sunday, they will be observed on Monday. Whenever any of the above holidays fall on Saturday, they will be observed on Friday.
- Supplemental Benefits are not paid for paid Holiday
- If Holiday is worked, Supplemental Benefits are paid for hours worked.
- Whenever an Employee works within three (3) calendar days before a holiday, the Employee shall be paid for the Holiday.

REGISTERED APPRENTICES

Wages per hour :

750 hours at the following percentage of Journeyman's wage

1st	2nd	3rd	4th	5th	6th	7th	8th
50%	55%	60%	65%	70%	75%	80%	85%

Supplemental Benefits per hour

750 hours at the following percentage of journeyman supplements

1st	2nd	3rd	4th	5th	6th	7th	8th
50%	55%	60%	65%	70%	75%	80%	85%

Apprentices indentured before June 1st, 2011 receive full journeyman benefits

11-5du-H/H

Operating Engineer - Building / Heavy&Highway

02/01/2025

JO DESCRIPTION Operating Engineer - Building / Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Delaware, Orange, Rockland, Sullivan, Ulster

WAGES

CLASS A5: Cranes, Derricks and Pile Drivers 100 tons or more and Tower Cranes, with 140ft boom and over.

CLASS A4: Cranes, Derricks and Pile Drivers 100 tons or more and Tower Cranes, with 100ft to 139ft boom.

CLASS A3: Cranes, Derricks and Pile Drivers 100 tons or more and Tower Cranes with a boom under 100ft.

CLASS A2: Cranes, Derricks and Pile Drivers less than 100 tons with 140ft boom and over.

CLASS A1: Cranes, Derricks and Pile Drivers less than 100 tons with a 100ft to 139ft boom.

CLASS A: Cranes, Derricks and Pile Drivers less than 100 tons with a boom under 100ft.; Autograde Combination Subgrade, Base Material Spreader and Base Trencher (CMI and Similar Types); Autograde Pavement Profile (CMI and Similar Types); Autograde Pavement Profile and Recycle type (CMI and Similar Type); Autograde Place-Trencher-Spreader Comb. (CMI & Similar types); Autograde Slipform Pave (CMI & Similar Types); Central Power Plants (all types); Chief of Party; Concrete Paving Machines; Drill (Bauger, AMI and Similar Types); Drillmaster, Quaymaster (Down the Hole Drill), Rotary Drill, Self-Propelled Hydraulic Drill, Self-Powered Drill; Draglines; Elevator Gages; Excavator; Front End Loaders (5 yds. and over); Graders; Grader-Roller; Helicopters (Co-Pilot); Helicopters (Communications Engineer); Juntann Pile Driver; Locomotive (Large); Mucking Machines; Pavement & Concrete Breaker, i.e., Superhammer & Hoe Ram; Roadway Surface Grinder; Protective Truck; Scooper (Loader and Shovel); Shovels; Tee Chopper with Boom; Trench Machines (Cable Plow); Tunnel Boring Machine; Vacuum Truck

CLASS B: "A" Frame; Backhoe (Combination); Boom Attachment on Loaders (Rate based on size of Bucket) not applicable to Pipehook; Boring and Drilling Machines; Bush Chopper, Shredder and Tee Shredder, Tee Shearer; Bulldozer (Fine Grader); Cableways; Caissons; Concrete Pump; Concrete Pumping System, Pump Concrete and Similar Types; Conveyors (125 ft. and over); Drill Doctor (duties incl. Dust Collector Maintenance); Front End Loaders (2 yds. but less than 5 yds.); Graders (Finish); Groove Cutting Machine (Ride on Type); Heater Plane; Hoists (all type Hoists, shall also include Steam, Gas, Diesel, Electric, Air Hydraulic, Single and Double Drum, Concrete, Brick Shaft Caisson, Sunkel Roof, and/or any other Similar Type Hoisting Machines, portable or stationary, except Chicago Boom Type); Long Boom Rate to be applied if Hoist is "Outside Material Tower Hoist"; Hydraulic Cranes-10 tons and under; Hydraulic Dredge; Hydraulic Axe; Hydraulic Blaster; Jacks-Scissor Air Hydraulic Power Operated Unit or Console Type (not hand Jack or Pile Load Test Type); Log Skidder; Pans; Pavers (all concrete); Plate and Frame Filter Press; Pumpcrete Machines, Squeezecrete & Concrete Pumping (regardless of size); Scrapers; Side Booms; "Staddle" Crane-Roller and similar types; Winch Trucks (Hoisting); Whip Hammer

CLASS C: Asphalt Curbing Machine; Asphalt Plant Engineer; Asphalt Spreader; Autograde Tube Finisher and Texturing Machine (CMI & Similar types); Autograde Curer Machine (CMI & Similar Types); Autograde Curb & Sidewalk, Shoulder, Slipform (CMI & Similar Types); Batching Machines (Power); Batching Moving Machine-Zipper; Batchers, Batching Plant and Crushers on Site; Belt Conveyor Systems; Boom Type Skimmer Machines; Bridge Deck Finisher; Bulldozer (except fine grade); Caisson Dumps (Railroad); Compactor and Blower Type Units (used independently or mounted on dual purpose Trucks, on Job Site or in conjunction with jobsite, in Loading and Unloading of Concrete, Cement, Fly Ash, Instant Concrete, or Similar Type Materials); Compactors (2 or 3 in Battery); Concrete Finishing Machines; Concrete cleaning decontamination machine operator; Concrete Saws and Cutters (Ride-on type); Concrete Spreader (Hetzl, Rexomatic and Similar Types); Concrete Vibrators; Conveyors (under 125 feet); Crushing Machines; Directional Boring Machines; Ditching Machine-small (Ditch-witch, Vermeer, or Similar type); Dope Pots (Mechanical with or without pump); Dumpsters; Elevator; Fireman; Fork Lifts (Economobile, Lull and Similar Types of Equipment); Front End Loaders (1 yd. and over but under 2 yds.); Generator (2 or 3 in Battery); Grapple Grinders; Grout Pump; Gunnite Machines (excluding nozzle); Hammer Vibrator (in conjunction with Generator); Heavy Equipment Robotics Operator Technician; Hoists-Roof, Tugger, Aerial Platform Hoist & House Caisson; Hoppers; Hopper Dumps (power operated); Hydraulic Blaster; Hydraulic Jacking Tackle; Ladders (motorized); Ladder Vator; Locomotive-dinky type; Maintenance -Utility Man; Master Environmental Maintenance Technician; Mechanics; Mixers (Excepting Paving Mixers); Motor Pavers; Pavement Breakers (small self-propelled ride on type-also maintains compactor hydraulic unit); Pavement Breaker-truck mounted; Pipe Bending Machine (Power); Pitch Pump; Plastic Pump (regardless of size); Post Hole Digger (Post Pounder & Auger); Pot Hole Kicker Trucks or equivalent; Rod Bending Machines (Power); Roller-Black Top; Scales (Power); Seaman pulverizing mixer; Shoulder Widener; Silos; Skidsteer (all attachments); Skimmer Machines (boom-type); Steel Cutting Machine (see vice & maintain); Tam Rock Drill; Tactors; Transfer Machine; Captain (Power Boats); Tug Master (power boats); Ultra High Pressure Water Jet Cutting Tool System operator/maintenance technician; Vacuum Blasting Machine; Vibrating Plants (used in conjunction with unloading); Welder and Repair Mechanics

CLASS D: Brooms and Sweepers; Chippers; Compactor (single); Concrete Spreader (small type); Conveyor Loaders (not including Elevator Grade); Engines-large diesel (1620 HP) and Staging Pump; Farm Tractors; Fertilizing Equipment (Operation & Maintenance of); Fine Grade Machine (small type); Form Line Grader (small type); Front End Loader (under 1 yard); Generator (single); Grease, Gas, Fuel and Oil supply trucks; Heaters (Nelson or other type incl. Popane, Natural Gas or Flow type Units); Lights, Portable Generating Light Plants; Mixers (Concrete, small); Mulching Equipment (Operation and Maintenance of); Pumps (2 or less than 4 inch suction); Pumps (4 inch suction and over incl. submersible pumps); Pumps (Diesel Engine and Hydraulic-immature of power); Road Finishing Machines (small type); Roller-scraper, fill or stone base; Seeding Equip. (Operation and Maintenance of); Sprinkle & Water Pump Trucks (used on jobsite or in conjunction with jobsite); Steam Jennies and Boilers-respective of use; Stone Spreader; Tamping Machines, Vibrating Ride-on; Tempo a y Heating Plant (Nelson or other type, incl. Popane, Natural Gas or Flow Type Units); Water & Sprinkle Trucks (used on or in conjunction with jobsite); Welding Machines (Gas, Diesel, and/or Electric Conveyors of any type, single, two, or three in a battery); Wellpoint Systems (including installation by Bull Gang and Maintenance of)

CLASS E: Assistant Engineer/Oiler; Drills Helper; Maintenance Apprentice (Deck Hand); Maintenance Apprentice (Oiler); Mechanics' Helper; Tire Repair and Maintenance; Transit/Instrument Man

WAGES:(per hour)

	07/01/2024	07/01/2025 Additional
Class A5	\$ 66.97 plus 5.00*	\$ 2.50***
Class A4	65.97 plus 5.00*	2.50***
Class A3	64.97 plus 5.00*	2.50***
Class A2	62.47 plus 5.00*	2.50***
Class A1	61.47 plus 5.00*	2.50***
Class A	60.47 plus 5.00*	2.50***
Class B	58.88 plus 5.00*	2.50***
Class C	56.97 plus 5.00*	2.50***
Class D	55.34 plus 5.00*	2.50***
Class E	51.63 plus 5.00*	2.50***
Safety Engineer	61.21 plus 5.00*	2.50***
Helicopter :		
Pilot/Engineer	62.29 plus 5.00*	2.50***
Co Pilot	60.47 plus 5.00*	2.50***
Communications Engineer	60.47 plus 5.00*	2.50***
Surveying:		
Chief of Party	60.47 plus 5.00*	2.50***
Transit/Instrument Man	51.63 plus 5.00*	2.50***
Rod/Chainman	51.05 plus 5.00*	2.50***
Additional \$0.75 for Survey work Tunnel under compressed air.		
Additional \$0.50 for Hydrographic work.		

*The \$5.00 is added to the Class Base Wage for all hours worked. Additionally, the \$5.00 is subject to the V-Code listed on the OVERTIME CODE Sheet.

**Outside Material Hoist (Class B) receives additional \$ 1.00 per hour on 110 feet up to 199 feet total height, \$ 2.00 per hour on 200 feet and over total height.

***To be allocated at a later date

- On HAZARDOUS WASTE REMOVAL or ASBESTOS REMOVAL work, on any state or federally DESIGNATED HAZARDOUS WASTE SITE:

For projects bid on or before April 1, 2020...Where the Operating Engineer is in direct contact with hazardous material and when personal protective equipment is required for respiratory, skin and eye protection, the Operating Engineer shall receive the hourly wage plus an additional twenty percent (20%) of that wage for the entire shift.

For projects bid after April 1, 2020...On hazardous waste removal work of any kind, including state or federally designated sites where the operating engineer is required to wear level A, B, or C personal protection the operating engineer shall receive an hourly wage rate of his regular hourly wage plus \$5.00 per hour. An operating engineer working at a hazardous waste removal project on site at a task requiring hazardous waste related certification, but who is not working in a zone requiring level A, B, or C personal protection, shall receive an hourly wage rate of his regular rate plus \$ 1.00 per hour. This shall also apply to sites where the level D personal protection is required.

SHIFT WORK

- SHIFT WORK: On all Government mandated irregular or off shift work, an additional 15% on straight time hours.

SUPPLEMENTAL BENEFITS

Per hour :

Journeyman \$ 34.00*

*15% premium is also required on shift work benefits

OVERTIME PAY

See (B, E, Q, *V, X) on OVERTIME PAGE

*15% premium is also required on shift work benefits

HOLIDAY

Paid: See (5, 6, 10, 13, 15) on HOLIDAY PAGE

Overtime: See (5, 6, 10, 13, 15) on HOLIDAY PAGE

Holidays falling on Sunday will be celebrated on Monday.

REGISTERED APPRENTICES

(1) years at the following percentage of journeyman's wage:

1st year	60% of Class base wage plus \$5.00*
2nd year	70% of Class base wage plus \$5.00*
3rd year	80% of Class base wage plus \$5.00*
4th year	90% of Class base wage plus \$5.00*

*The \$5.00 is added to the Class Base Wage for all hours worked. Additionally, the \$5.00 is subject to the V-Code listed on the OVERTIME CODE Sheet.

Supplemental Benefits per hour :

Apprentices \$ 34.00

11-825

Operating Engineer - Marine Dredging

02/01/2025

JO DESCRIPTION Operating Engineer - Marine Dredging

DISTRICT 4

ENTIRE COUNTIES

Albany, Bronx, Cayuga, Clinton, Columbia, Dutchess, Essex, Franklin, Greene, Jefferson, Kings, Monroe, Nassau, New York, Orange, Oswego, Putnam, Queens, Rensselaer, Richmond, Rockland, St. Lawrence, Suffolk, Ulster, Washington, Wayne, Westchester

WAGES

These wages do not apply to Operating Engineers on land based construction projects. For those projects, please see the Operating Engineer Heavy/Highway Rates. The wage rates below for all equipment and operators are only for marine dredging work in navigable waters found in the counties listed above.

Per Hour : 07/01/2024

CLASS A1 \$ 45.26

Deck Captain, Levee man,
Mechanical Dredge Operator,
Licensed Tug Operator 1000HP or more.

CLASS A2 C ane Ope ato (360 swing)	40.33
CLASS B Doze , F ont Loade Ope ato on Land	To confo m to Ope ating Enginee P evailing Wage in locality whe e wo k is being pe fo med including benefits.
CLASS B1 De ick Ope ato (180 swing) Spide /Spill Ba ge Ope ato Ope ato II, Fill Place , Enginee Chief Mate, Elect ician,Chief Welde , Maintenance Enginee ,Licensed Boat, C ew Boat Ope ato	39.14
CLASS B2 Ce tified Welde	36.84
CLASS C1 D ag Ba ge Ope ato , Stewa d, Mate, Assistant Fill Place	35.83
CLASS C2 Boat Ope ato	34.68
CLASS D Sho eman, Deckhand, Oile , Rodman, Scowman, Cook, Messman, Po te /Janito	28.81

SUPPLEMENTAL ENEFITS

Pe Hou :

THE FOLLOWING SUPPLEMENTAL BENEFITS APPLY TO ALL CATEGORIES

All Classes A & B \$ 12.00 plus 7%
of st aight time
wage, Ove time hou s
add \$ 0.63

All Class C & D \$ 11.75 plus 7%
of st aight time
wage, Ove time hou s
add \$ 0.50

O ERTIME PAY

See (B2, F, R) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Ove time: See (5, 6, 8, 15, 26) on HOLIDAY PAGE

4-25a-Ma D edge

Operating Engineer - Steel Erectors	02/01/2025
--	-------------------

JO DESCRIPTION Ope ating Enginee - Steel E ecto s

DISTRICT 11

ENTIRE COUNTIES

Delawa e, O ange, Rockland, Sullivan, Ulste

WAGES

CLASS A3: C anes, De icks and Pile D ive s 100 tons o mo e and Towe C anes, with a 140 ft. boom and ove .

CLASS A2: C anes, De icks and Pile D ive s 100 tons o mo e and Towe C anes, with up to a 139 ft. boom and unde .

CLASS A1: C anes, De icks and Pile D ive s less than 100 tons with a 140 ft. boom and ove .

CLASS A: C anes, De icks and Pile D ive s less than 100 tons with up to a 139 ft. boom and unde .

CLASS B: "A" F ame; Che y Picke s(10 tons and unde); Hoists (all type Hoists, shall also include Steam, Gas, Diesel, Elect ic, Ai Hyd aulic, Single and Double D um, Conc ete, B ick Shaft Caisson, Sno kel Roof, and/o any othe Simila Type Hoisting Machines, po table o stationa y, except Chicago Boom Type); Jacks-Sc ew Ai Hyd aulic Powe Ope ated Unit o Console Type (not hand Jack o Pile Load Test Type); Side Booms; St addle Ca ie

CLASS C: Ae ial Platfo m used as Hoist; Comp esso s (2 o 3 in Batte y); Conc ete cleaning/ decontamination machine ope ato ; Di ectional Bo ing Machines; Elevato o House Ca s; Conveye s and Tugge Hoists; Fi eman; Fo k Lifts; Gene ato s (2 o 3 in Batte y); Heavy Equipment Robotics Ope ato /Technician; Mast e Envi onmental Maintenance Technician; Maintenance -Utility Man; Rod Bending Machines (Powe); Captain(powe boat); Tug Mast e ; Ult a High P essu e Wate jet Cutting Tool System; Vacuum Blasting Machine; Welding Machines(gas o elect ic,2 o 3 in batte y, including diesels); T ansfe Machine; App entice Enginee /Oile with eithe one comp esso o one welding machine when used fo decontamination and emediation

CLASS D: Comp esso (single); Welding Machines (Gas, Diesel, and/o Elect ic Conve te s of any type); Welding System Multiple (Rectifie T ansfo me type)

CLASS E: Assistant Enginee /Oile ; Maintenance App entice (Deck Hand);D ille s Helpe ; Maintenance App entice (Oile); Mechanics' Helpe ; T ansit/Inst ument Man

WAGES:(pe hou)

	07/01/2024	07/01/2025 Additional
Class A3	\$ 68.99 plus 5.00*	\$ 2.50**
Class A2	67.33 plus 5.00*	2.50**
Class A1	64.49 plus 5.00*	2.50**
Class A	62.83 plus 5.00*	2.50**
Class B	60.04 plus 5.00*	2.50**
Class C	57.38 plus 5.00*	2.50**
Class D	55.85 plus 5.00*	2.50**
Class E	52.09 plus 5.00*	2.50**
Vacuum T uck	60.80 plus 5.00*	2.50**
Safety Enginee	61.66 plus 5.00*	2.50**
Helicopte :		
Pilot/Enginee	64.49 plus 5.00*	2.50**
Co Pilot	64.10 plus 5.00*	2.50**
Communications Enginee	64.10 plus 5.00*	2.50**
Su veying:		
Chief of Pa ty	60.80 plus 5.00*	2.50**
T ansit/Inst ument man	52.09 plus 5.00*	2.50**
Rod/Chainman	51.05 plus 5.00*	2.50**
Additional \$0.75 fo Su vey wo k Tunnels unde comp essed ai .		
Additional \$0.50 fo Hyd og aphic wo k.		

*The \$5.00 is added to the Class Base Wage fo all hou s wo ked. Additionally, the \$5.00 is subject to the V-Code listed on the OVERTIME CODE Sheet.

**To be allocated at a late date

- On HAZARDOUS WASTE REMOVAL o ASBESTOS REMOVAL wo k, o any state o fede ally DESIGNATED HAZARDOUS WASTE SITE:

Fo p ojects bid on o befo e Ap il 1, 2020...Whe e the Ope ating Enginee is in di ect contact with haza dous mate ial and when pe sonal p otective equipment is equi ed fo espi ato y, skin and eye p otection, the Ope ating Enginee shall eceive the hou ly wage plus an additional twenty pe cent (20%) of that wage fo the enti e shift.

Fo p ojects bid afte Ap il 1, 2020...On haza dous waste emoval wo k of any kind, including state o fede ally designated site whe e the ope ating enginee is equi ed to wea level A, B, o C pe sonal p otection the ope ating enginee shall eceive an hou ly wage ate of his egula hou ly wage plus \$5.00 pe hou . An ope ating enginee wo king at a haza dous waste emoval p oject o site at a task equi ing haza dous waste elated ce tification, but who is not wo king in a zone equi ing level A, B, o C pe sonal p otection, shall eceive an hou ly wage ate of his egula ate plus \$ 1.00 pe hou . This shall also apply to sites whe e the level D pe sonal p otection is equi ed.

SHIFT WORK

- SHIFT WORK: On all Gove nment mandated i egula o off shift wo k, an additional 15% on st aight time hou s.

SUPPLEMENTAL ENEFITS

Pe hou :

Jou neyman \$ 34.00*

*15% p emium is also equi ed on shift wo k benefits

O ERTIME PAY

See (B, E, Q, *V, X) on OVERTIME PAGE

*15% p emium is also equi ed on shift wo k benefits

HOLIDAY

Paid: See (5, 6, 10, 13, 15) on HOLIDAY PAGE

Ove time: See (5, 6, 10, 13, 15) on HOLIDAY PAGE

Holidays falling on Sunday will be celeb ated on Monday.

REGISTERED APPRENTICES

(1) yea te ms at the following pe centage of jou neyman's wage.

1st yea	60% of Class base wage plus \$5.00*
2nd yea	70% of Class base wage plus \$5.00*
3 d yea	80% of Class base wage plus \$5.00*
4th yea	90% of Class base wage plus \$5.00*

*The \$5.00 is added to the Class Base Wage fo all hou s wo ked. Additionally, the \$5.00 is subject to the V-Code listed on the OVERTIME CODE Sheet.

Supplemental Benefits pe hou :

App entices \$ 34.00

11-825SE

Painter

02/01/2025

JO DESCRIPTION Painte

DISTRICT 1

ENTIRE COUNTIES

Columbia, Dutchess, G eene, O ange, Sullivan, Ulste

WAGES

Pe hou

07/01/2024

05/01/2025

Additional

B ush/Pape Hange	\$ 38.81	\$ 1.99*
D y Wall Finishe	38.81	1.99*
Lead Abatement	38.81	1.99*
Sandblaste -Painte	38.81	1.99*
Sp ay Rate	39.81	1.99*

(*) To be allocated at late date.

See B idge Painting ates fo the following wo k:

St uctu al Steel, all wo k pe fo med on tanks, ALL BRIDGES, towe s, smoke stacks, flag poles. Rate shall apply to all of said a eas f om the g ound up.

SUPPLEMENTAL ENEFITS

Pe hou

Jou neywo ke \$ 27.37

O ERTIME PAY

See (B, E, E2, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Ove time: See (5, 6) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wages pe hou

Six (6) month te ms at the following pe centage of Jou neype son's wage

1st	2nd	3 d	4th	5th	6th
50%	55%	65%	75%	85%	95%

Supplemental Benefits pe hou wo ked

1st te m \$ 11.39
All othe s 27.37

1-155

Painter - ridge & Structural Steel

02/01/2025

JO DESCRIPTION Painte - B idge & St uctu al Steel

DISTRICT 8

ENTIRE COUNTIES

Albany, B onx, Clinton, Columbia, Dutchess, Essex, F anklin, Fulton, G eene, Hamilton, Kings, Montgome y, Nassau, New Yo k, O ange, Putnam, Queens, Rensselaer , Richmond, Rockland, Sa atoga, Schenectady, Schoha ie, Suffolk, Sullivan, Ulste , Wa en, Washington, Westcheste

WAGES

Pe Hou :

STEEL:

B idge Painting: 07/01/2024
\$ 56.00
+ 10.35*

ADDITIONAL \$7.00 pe hou fo POWER TOOL/SPRAY, whethe st aight time o ove time.

NOTE: All p emium wages a e to be calculated on base ate pe hou only.

* Fo the pe iod of May 1st to Novembe 15th, this amount is payable up to 40 hou s. Fo the pe iod of Nov 16th to Ap il 30th, this amount is payable up to 50 hou s. EXCEPTION: Fi st and last week of employment, and fo the weeks of Memo ial Day, Independence Day and Labo Day, whe e the amount is paid fo the actual numbe of hou s wo ked (50 hou cap).

NOTE: Gene ally, fo B idge Painting Cont acts, ALL WORKERS on and off the b idge (including Flagmen) a e to be paid Painte 's Rate; the cont act must be ONLY fo B idge Painting.

SHIFT WORK

When di ectly specified in public agency o autho ity cont act documents fo an employe to wo k a second shift and wo ks the second shift with employees othe than f om the fi st shift, all employees who wo k the second shift will be paid 10% of the base wage shift diffe ential in lieu of ove time fo the fi st eight (8) hou s wo ked afte which the employees shall be paid at time and one half of the egula wage ate. When a single i egula wo k shift is mandated in the job specifications o by the cont acting agency, wages shall be paid at time and one half fo single shifts between the hou s of 3pm-11pm o 11pm-7am.

SUPPLEMENTAL BENEFITS

Pe Hou :

Jou neywo ke :
\$ 12.43
+ 31.55*

* Fo the pe iod of May 1st to Novembe 15th, this amount is payable up to 40 hou s. Fo the pe iod of Nov 16th to Ap il 30th, this amount is payable up to 50 hou s. EXCEPTION: Fi st and last week of employment, and fo the weeks of Memo ial Day, Independence Day and Labo Day, whe e the amount is paid fo the actual numbe of hou s wo ked (50 hou cap).

OVERTIME PAY

See (B, F, R) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Ove time: See (4, 6) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wage - Pe hou :

App entices: (1) yea te ms.

1st yea \$ 22.40
+ 4.14

2nd yea \$ 33.60
+ 6.21

3 d yea \$ 44.80
+ 8.28

Supplemental Benefits - Pe hou :

1st yea \$ 1.16
+ 12.62

2nd yea \$ 7.46

+ 18.93

3 d yea

\$ 9.94
+ 25.24

NOTE: All premium wages are to be calculated on base rate per hour only.

8-DC-9/806/155-B SS

Painter - Line Striping

02/01/2025

JO DESCRIPTION Painter - Line Striping

DISTRICT 8

ENTIRE COUNTIES

Albany, Clinton, Columbia, Dutchess, Essex, Franklin, Fulton, Genesee, Hamilton, Montgomery, Nassau, Orange, Putnam, Rensselaer, Rockland, Saratoga, Schenectady, Schoharie, Suffolk, Sullivan, Ulster, Warren, Washington, Westchester

WAGES

Per hour :

Painter (Striping-Highway):	07/01/2024	04/01/2025	04/01/2026
Striping-Machine Operator *	\$ 34.12	\$ 35.49	\$ 36.93
Line man The moplastic	41.12	42.74	44.44

Note: * Includes but is not limited to: Positioning of cones and directing of traffic using hand held devices. Excludes the Drive /Operator of equipment used in the maintenance and protection of traffic safety.

SHIFT WORK

When directly specified in public agency or authority contract documents the rate shall be a 30% night shift premium pay differential for all work performed after 9:00pm and before 5:00am.

SUPPLEMENTAL BENEFITS

Per hour paid:

Jobneywork :

Striping Machine Operator :	\$23.65	\$ 24.30	\$ 24.95
Line man The moplastic:	23.65	24.30	24.95

OVERTIME PAY

See (B, B2, E2, F, S) on OVERTIME PAGE

HOLIDAY

Paid: See (5, 20) on HOLIDAY PAGE
Overtime: See (5, 20) on HOLIDAY PAGE

REGISTERED APPRENTICES

One (1) year trainees at the following wage rates:

	07/01/2024	01/01/2025	04/01/2025	04/01/2026
1st Term:	\$ 16.00	\$ 16.50	\$ 16.50	\$ 16.50
2nd Term:	20.47	20.47	21.29	22.16
3rd Term:	27.30	27.30	28.39	29.54

Supplemental Benefits per hour :

All trainees:	\$ 23.65	\$ 23.65	\$ 24.30	\$ 24.95
---------------	----------	----------	----------	----------

8-1456-LS

Painter - Metal Polisher

02/01/2025

JO DESCRIPTION Painter - Metal Polisher

DISTRICT 8

ENTIRE COUNTIES

Albany, Allegany, Bronx, Broome, Cattaraugus, Cayuga, Chautauqua, Chemung, Chenango, Clinton, Columbia, Cortland, Delaware, Dutchess, Erie, Essex, Franklin, Fulton, Genesee, Hamilton, Herkimer, Jefferson, Kings, Lewis, Livingston, Madison, Monroe, Montgomery, Nassau, New York, Niagara, Oneida, Onondaga, Ontario, Orange, Orleans, Oswego, Otsego, Putnam, Queens, Rensselaer, Richmond, Rockland, Saratoga, Schenectady, Schoharie, Schuylle, Seneca, St. Lawrence, Steuben, Suffolk, Sullivan, Tioga, Tompkins, Ulster, Warren, Washington, Wayne, Westchester, Wyoming, Yates

WAGES

	07/01/2024
Metal Polisher	\$ 39.33
Metal Polisher *	40.43

Metal Polisher ** 43.33

*Note: Applies on New Construction & complete renovation

** Note: Applies when working on scaffolds over 34 feet.

SUPPLEMENTAL BENEFITS

Per Hour : 07/01/2024

Job category :

All classification \$ 12.79

OVERTIME PAY

See (B, E, P, T) on OVERTIME PAGE

HOLIDAY

Paid: See (5, 6, 11, 15, 16, 25, 26) on HOLIDAY PAGE

Overtime: See (5, 6, 11, 15, 16, 25, 26) on HOLIDAY PAGE

REGISTERED APPRENTICES

Wages per hour :

One (1) year term at the following wage rates:

07/01/2024

1st year \$ 19.67

2nd year 21.63

3rd year 23.60

1st year * \$ 22.06

2nd year * 22.07

3rd year * 24.14

1st year ** \$ 22.17

2nd year ** 24.13

3rd year ** 26.10

*Note: Applies on New Construction & complete renovation

** Note: Applies when working on scaffolds over 34 feet.

Supplemental benefits:

Per hour :

1st year \$ 8.69

2nd year 8.69

3rd year 8.69

8-8A/28A-MP

Plumber

02/01/2025

JO DESCRIPTION Plumber

DISTRICT 11

ENTIRE COUNTIES

Orange, Rockland, Sullivan

PARTIAL COUNTIES

Ulster : Only the Townships of Plattekill, Marlboro, Wawarsing, and Shawangunk (except for Wallkill and Shawangunk Portions).

WAGES

REFRIGERATION: For commercial and industrial refrigeration which means service, maintenance, and installation work where the combined compressor tonnage does not exceed 40 tons.

AIR CONDITIONING: Air conditioning to be installed that is water cooled shall not exceed 25 tons. This will include the piping of the component system and erection of water tower. Air conditioning that is air cooled shall not exceed 50 tons.

WAGES: (per hour)

07/01/2024

05/01/2025

Plumber \$ 40.09

Additional
\$ 2.50*

*To be allocated at a later date

State Certification: an additional \$ 1.00 per hour over scale will be paid to all those who have State Certification.

SHIFT WORK

Shift Differential: When mandated by the governmental agency, an additional 15% premium will be paid for irregular workday of 2nd and 3rd shift.

SUPPLEMENTAL BENEFITS

Per hour :

Journeyman

\$ 36.78*

*For overtime on shift differential work, \$0.10 is paid at straight time, the remaining balance is paid at the same premium as the wages.

OVERTIME PAY

See (B, G, P, *V) on OVERTIME PAGE

*A portion of the benefit amount is subject to the V code for overtime and shift differential work.

HOLIDAY

Paid: See (5, 6, 13, 15, 25) on HOLIDAY PAGE

Overtime: See (5, 6, 13, 15, 25) on HOLIDAY PAGE

REGISTERED APPRENTICES

(1)year terms at the following wage.

07/01/2024

1st term	\$ 18.04
2nd term	22.05
3rd term	26.06
4th term	30.07
5th term	34.08

Supplemental Benefits per hour :

Apprentices

1st term	\$ 16.62*
2nd term	20.29*
3rd term	23.95*
4th term	27.63*
5th term	31.19*

*For overtime on shift differential work, \$0.10 is paid at straight time, the remaining balance is paid at the same premium as the wages.

11-373 Ref ig

Plumber

02/01/2025

JO DESCRIPTION Plumbe

DISTRICT 11

ENTIRE COUNTIES

Orange, Rockland, Sullivan

PARTIAL COUNTIES

Ulster : Only the Townships of Plattekill, Marlboro, Wawarsing, and Shawangunk (except for Wallkill and Shawangunk Portions).

WAGES

WAGES:(per hour) 07/01/2024

Plumber /Steamfitter \$ 51.20

Note: For all work 40-60 feet above ground add \$ 0.25 per hour , over 60 feet add \$ 0.50 per hour .

SHIFT WORK

Shift Differential: When mandated by the governmental agency, an additional 15% premium will be paid for irregular workday of 2nd and 3rd shift.

SUPPLEMENTAL BENEFITS

Per hour :

Journeyman

\$ 45.57

*For overtime on shift differential work, \$0.10 is paid at straight time, the remaining balance is paid at the same premium as the wages.

OVERTIME PAY

See (B, E, Q, *V) on OVERTIME PAGE

*A portion of the benefit amount is subject to the V code for overtime and shift differential work.

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Overtime: See (5, 6, 15, 16) on HOLIDAY PAGE

When a holiday falls on a Saturday, the day prior shall be considered and recognized as the holiday. When a holiday falls on a Sunday, the day proceeding shall be considered and recognized as the holiday to be observed.

REGISTERED APPRENTICES

(1) year terms at the following wages.

	07/01/2024
1st term	\$ 17.92
2nd term	23.04
3rd term	28.16
4th term	33.28
5th term	40.96

Supplemental Benefits per hour :

1st term	\$ 16.03*
2nd term	20.58*
3rd term	25.12*
4th term	29.68*
5th term	36.48*

*For overtime on shift differential work, \$0.10 is paid at straight time, the remaining balance is paid at the same premium as the wages.
11-373 SF

Roofer

02/01/2025

JO DESCRIPTION Roofer

DISTRICT 9

ENTIRE COUNTIES

Bronx, Dutchess, Kings, New York, Orange, Putnam, Queens, Richmond, Rockland, Sullivan, Ulster, Westchester

WAGES

Per Hour : 07/01/2024

Roofer /Waterproofing \$ 48.50
+ \$7.00*

* This position is not subjected to overtime premiums.

Note: Abatement/Removal of Asbestos containing roofs and roofing material is classified as Roofer.

SUPPLEMENTAL BENEFITS

Per Hour : \$ 31.87

OVERTIME PAY

See (B, H) on OVERTIME PAGE

Note: An observed holiday that falls on a Sunday will be observed the following Monday.

HOLIDAY

Overtime: See (5, 6) on HOLIDAY PAGE

REGISTERED APPRENTICES

(1) year term apprentices indentured prior to 01/01/2023

1st	2nd	3rd	4th
\$ 16.97	\$ 24.25	\$ 29.10	\$ 36.37
	+ 3.50*	+ 4.20*	+ 5.26*

Supplements:

1st	2nd	3rd	4th
\$ 4.10	\$ 16.17	\$ 19.31	\$ 24.02

* This position is not subjected to overtime premiums.

(1) year term apprentices indentured after 01/01/2023

1st	2nd	3rd	4th	5th
\$ 18.43	\$ 21.82	\$ 24.25	\$ 29.10	\$ 36.37
	+ 3.16*	+ 3.50*	+ 4.20*	+ 5.26

Supplements:

1st	2nd	3rd	4th	5th
\$ 7.73	\$ 14.59	\$ 16.17	\$ 19.31	\$ 24.02

* This position is not subjected to overtime premiums.

9-8R

Sheetmetal Worker

02/01/2025

JO DESCRIPTION Sheetmetal Worker

DISTRICT 8

ENTIRE COUNTIES

Dutchess, Orange, Putnam, Rockland, Sullivan, Ulster, Westchester

WAGES

	07/01/2024
SheetMetal Worker	\$ 49.51
	+ 3.71*

*This portion of the benefit is NOT subject to the SAME PREMIUM as shown for overtime.

SHIFT WORK

For all NYS D.O.T. and other Governmental mandated off-shift work:
10% increase for additional shifts for a minimum of five (5) days

SUPPLEMENTAL BENEFITS

Unemployment \$ 46.20

OVERTIME PAY

OVERTIME: See (B, E, Q,) on OVERTIME PAGE.

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6, 8, 15, 16, 23) on HOLIDAY PAGE

REGISTERED APPRENTICES

1st	2nd	3rd	4th	5th	6th	7th	8th
\$ 20.20	\$ 20.81	\$ 23.12	\$ 25.42	\$ 27.74	\$ 30.08	\$ 32.86	\$ 35.63
+ 1.48*	+ 1.67*	+ 1.86*	+ 2.04*	+ 2.23*	+ 2.41*	+ 2.60*	+ 2.78*

*This portion of the benefit is NOT subject to the SAME PREMIUM as shown for overtime.

Supplemental Benefits per hour:

Apprentices	
1st term	\$ 18.07
2nd term	22.24
3rd term	24.71
4th term	27.21
5th term	29.67
6th term	32.12
7th term	34.12
8th term	36.15

8-38

Sprinkler Fitter

02/01/2025

JO DESCRIPTION Sprinkler Fitter

DISTRICT 1

ENTIRE COUNTIES

Dutchess, Orange, Putnam, Rockland, Sullivan, Ulster, Westchester

WAGES

Per hour 07/01/2024

Sprinkler Fitter \$ 53.34

SUPPLEMENTAL BENEFITS

Per hour

Unemployment \$ 30.77

OVERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6) on HOLIDAY PAGE

Note: When a holiday falls on Sunday, the following Monday shall be considered a holiday and all work performed on either day shall be at the double time rate. When a holiday falls on Saturday, the preceding Friday shall be considered a holiday and all work performed on either day shall be at the double time rate.

REGISTERED APPRENTICES

Wages per hour

One Half Year terms at the following wage.

1st	2nd	3rd	4th	5th	6th	7th	8th	9th	10th
\$ 25.89	\$ 28.77	\$ 31.39	\$ 34.27	\$ 37.14	\$ 40.02	\$ 42.90	\$ 45.77	\$ 48.65	\$ 51.53

Supplemental Benefits per hour

1st	2nd	3rd	4th	5th	6th	7th	8th	9th	10th
\$ 9.18	\$ 9.18	\$ 20.90	\$ 20.90	\$ 21.15	\$ 21.15	\$ 21.15	\$ 21.15	\$ 21.15	\$ 21.15
									1-669.2

Teamster - Building / Heavy&Highway	02/01/2025
--	-------------------

JO DESCRIPTION Teamster - Building / Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Dutchess, Orange, Rockland, Sullivan, Ulster

WAGES

GROUP 1: Lettuce Trucks, Double Barrel Euclids, Athney Wagons and similar equipment (except when hooked to scrapers), I-Beam and Pole Trucks, Tire Trucks, Tractors and Trailers with 5 axles and over, Articulated Back Dumps and Road Oil Distributors, Articulated Water Trucks and Fuel Trucks/Trailers, positions requiring a HAZMAT CDL endorsement.

GROUP 1A: Drivers on detachable Gooseneck Low Bed Trailers rated over 35 tons.

GROUP 2: All equipment 25 years and up to and including 30-year bodies and cable Dump Trucks and Powder and Dynamite Trucks.

GROUP 3: All Equipment up to and including 24-year bodies, Mixer Trucks, Dump Crete Trucks and similar types of equipment, Fuel Trucks, Batch Trucks and all other Tractor Trailers, Hi-Rail Truck.

GROUP 4: Tri-Axles, Ten Wheelers, Garbage Trucks, Tiller man, Pallet Trucks, Attenuator Trucks, Water Trucks, Buses.

GROUP 5: Street Trucks.

GROUP 6: Pick-up Trucks for hauling materials and parts, and Escorted Man over-the-road.

WAGES: (per hour) 07/01/2024

GROUP 1	\$ 34.58
GROUP 1A	35.72
GROUP 2	34.02
GROUP 3	33.80
GROUP 4	33.69
GROUP 5	33.57
GROUP 6	33.57

NOTE ADDITIONAL PREMIUMS:

- Employees engaged in hazardous/toxic waste removal, on a State or Federally designated hazardous/toxic waste site, where the employee comes in contact with hazardous/toxic waste material and when personal protective equipment is required for respiratory, skin, or eye protection, the employee shall receive an additional 20% premium above the hourly wage.

SHIFT WORK

- On projects requiring an irregular shift a premium of 10% will be paid on wages. The premium will be paid for off-shift or irregular shift work when mandated by Governmental Agency.

SUPPLEMENTAL BENEFITS

Per hour:

First 40 hours	\$ 44.59
Over 40 hours	36.99

OVERTIME PAY

See (*B, E, **E2, ***P, X) on OVERTIME PAGE

*Holidays worked Monday through Friday receive Double Time (2x) after 8 hours.

**Makeup day limited to the employees who were working on the site that week.

***Sunday Holidays are paid at a rate of double time and one half (2.5x) for all hours worked.

HOLIDAY

Paid: See (5, 6, 15, 25) on HOLIDAY PAGE

Overtime: See (*1) on HOLIDAY PAGE

- Any employee working two (2) days in any calendar week during which a holiday occurs shall receive a day's pay for each holiday occurring during said week. This provision shall also apply if a holiday falls on a Saturday or Sunday.

*See OVERTIME PAY section for when additional premium is applicable on Holiday hours worked.

11-445B/HH

Teamster - Delivery - uilding / Heavy&Highway

02/01/2025

JO DESCRIPTION Teamste - Delive y - Building / Heavy&Highway

DISTRICT 11

ENTIRE COUNTIES

Dutchess, O ange, Rockland, Sullivan, Ulste

WAGES

G oup 1 T acto T aile D ive s

G oup 2 T i- Axle

Wages: 07/01/2024

G oup 1 \$ 33.70

G oup 2 29.70

Haza dous/Toxic Waste Removal additional 20% when pe sonal p otective equipment is equi ed.

SUPPLEMENTAL ENEFITS

Pe hou paid:

Fi st 40 hou s \$ 32.30

Ove 40 hou s 0.00

O ERTIME PAY

See (B, E, Q, X) on OVERTIME PAGE

HOLIDAY

Paid: See (5, 13, 15, 16, 20, 22, 25, 26) on HOLIDAY PAGE

Ove time: See (5, 13, 15, 16, 20, 22, 25, 26) on HOLIDAY PAGE

- Employee must wo k eithe the scheduled day of wo k befo e o the scheduled day of wo k afte the holiday in the wo kweek.

- Any employee wo king one (1) day in the calenda week du ing which a holiday occu s shall eceive a day's pay fo each holiday occu ing du ing said week. This p ovision shall also apply if a holiday falls on a Satu day.

- When any of the ecognized holidays occu on Sunday and a e celeb ated any day befo e o afte the holiday Sunday, such days shall be conside ed as the holiday and paid fo as such.

11-445 B/HH Delive y

Welder

02/01/2025

JO DESCRIPTION Welde

DISTRICT 1

ENTIRE COUNTIES

Albany, Allegany, B onx, B oome, Catta agus, Cayuga, Chautauqua, Chemung, Chenango, Clinton, Columbia, Co tland, Delawa e, Dutchess, E ie, Essex, F anklin, Fulton, Genesee, G eene, Hamilton, He kime , Jeffe son, Kings, Lewis, Livingston, Madison, Mon oe, Montgome y, Nassau, New Yo k, Niaga a, Oneida, Onondaga, Onta io, O ange, O leans, Oswego, Otsego, Putnam, Queens, Rensselaie , Richmond, Rockland, Sa atoga, Schenectady, Schoha ie, Schuyle , Seneca, St. Law ence, Steuben, Suffolk, Sullivan, Tioga, Tompkins, Ulste , Wa en, Washington, Wayne, Westcheste , Wyoming, Yates

WAGES

Pe hou 07/01/2024

Welde : To be paid the same ate of the mechanic pe fo ming the wo k.*

*EXCEPTION: If a specific welde ce tification is equi ed, then the 'Ce tified Welde ' ate in that t ade tag will be paid.

O ERTIME PAY

HOLIDAY

1-As Pe T ade

Orange County Residential

Carpenter - Residential

02/01/2025

JO DESCRIPTION Carpenter - Residential

DISTRICT 11

ENTIRE COUNTIES

Columbia, Dutchess, Orange, Sullivan, Ulster

WAGES

***IMPORTANT NOTE: Residential construction consists of those projects involving the construction, alteration, or repair of single-family houses or apartment buildings of no more than four (4) floors in height, town homes, row houses, single family homes, mobile homes, multi-family houses, apartment building of four (4) floors or less and assisted living facilities of four (4) floors or less. Excluding dormitories and student housing. Four (4) stories shall be above ground level and shall not include the building's basement nor unfinished attic space.

07/01/2024

Carpenter \$ 24.17
+ 4.14*

*For all hours paid straight overtime premium.

SUPPLEMENTAL BENEFITS

Per hour:

Journeyman \$ 19.98

OVERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Overtime: See (5, 6, 16, 25) on HOLIDAY PAGE

Holidays that fall on Sunday will be observed Monday.

REGISTERED APPRENTICES

1 year apprentices at the following rates:

1st	2nd	3rd	4th
\$ 15.06	\$ 15.82	\$ 16.92	\$ 19.34
+2.04*	+2.04*	+2.04*	+2.04*

*For all hours paid straight overtime premium.

SUPPLEMENTAL BENEFITS per hour:

Apprentices all trades \$ 10.65

11-279.2

Electrician - Residential

02/01/2025

JO DESCRIPTION Electrician - Residential

DISTRICT 11

ENTIRE COUNTIES

Orange, Putnam, Rockland

PARTIAL COUNTIES

Dutchess: Towns of Fishkill, East Fishkill and Beacon.

WAGES

---IMPORTANT NOTE: Applies to all electrical wiring of single or multiple family dwellings and apartments up to and including two (2) stories that do not exceed four (4) unit apartments.

Per hour:

07/01/2024

Electrician Wireman/Technician \$ 50.50
+ 9.50*

*For all hours paid straight overtime premium, not to be included in 3% calculation for supplemental benefits.

NOTE ADDITIONAL AMOUNTS PAID FOR THE FOLLOWING WORK LISTED BELOW (subject to overtime premiums):

- On jobs where employees are required to work from boatswain chairs, swinging scaffolds, etc., forty (40) feet or more above the ground, or underground, using Scottair packs, or gas masks, they shall receive an additional \$2.00 per hour above the regular straight time rate.

- Journeyman Wireman working in Shafts, Tunnels or on Barges: \$5.00 above the Journeyman Wireman rate of pay

4th te m	\$ 19.78 plus 3% of st aight o p emium wage
5th te m	\$ 21.28 plus 3% of st aight o p emium wage
6th te m	\$ 21.28 plus 3% of st aight o p emium wage

11-R363/1

Insulator - Heat & Frost - Residential

02/01/2025

JO DESCRIPTION Insulator - Heat & Frost - Residential

DISTRICT 8

ENTIRE COUNTIES

Dutchess, Orange, Putnam, Rockland, Westchester

WAGES

***IMPORTANT NOTE: All residential plumbing, heating and air conditioning and site work in a single-family residence or a single family residential development under one roof, regardless of cost and garden type apartment buildings or developments which do not exceed three stories high.

Per hour : 07/01/2024

Asbestos Work \$ 49.70

App entices 32.97

Fire Stop Work*

Asbestos Work 32.97

* Applies on all exclusive Fire Stop Work (when contract is for Fire Stop Work only). No app entices on these contracts only.

Note: Additional \$0.50 per hour for work 30 feet or more above floor or ground level.

SUPPLEMENTAL BENEFITS

Per hour :

Journeywork \$ 30.74

App entice 19.48

Fire Stop Work:

Journeywork 19.48

OVERTIME PAY

OVERTIME: See (B, E, Q, T, V) on OVERTIME PAGE.

HOLIDAY

Paid: See (1) on HOLIDAY PAGE

Paid:..... See (1) on HOLIDAY PAGE.

Overtime:.. See (2, 4, 6, 16, 25) on HOLIDAY PAGE.

8-91R

Laborer - Residential

02/01/2025

JO DESCRIPTION Laborer - Residential

DISTRICT 11

ENTIRE COUNTIES

Orange, Otsego, Sullivan, Ulster

PARTIAL COUNTIES

Chenango: Only the Townships of Columbus, Shesheburne and New Berlin.

Delaware: Only the Townships of Andes, Bovina, Middletown, Roxbury, Franklin, Hamden, Stamford, Delhi, Kortright, Harpersfield, Meredith and Davenport.

Greene: Only the Township of Catskill.

WAGES

GENERAL LABORER: Laborer .

PREMIUM LABORER: Asbestos abatement work, toxic and hazardous abatement, lead abatement work, environmental work.

WAGES:(per hour)

07/01/2024

General \$ 32.50

Premium \$ 37.50

This shall cove wo k within five feet of the building foundation line. This applies to the const uction, alte ations and epai s of detached houses, townhouses, duplexes, apa tments not exceeding th ee sto ies in height and condominiums all of which shall se ve as a p ima y esidency.

SUPPLEMENTAL ENEFITS

Pe hou :

Jou neyman \$ 19.20

O ERTIME PAY

See (B, E, E2, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Ove time: See (5, 6) on HOLIDAY PAGE

11-17R

Plumber - Residential

02/01/2025

JO DESCRIPTION Plumbe - Residential

DISTRICT 11

ENTIRE COUNTIES

O ange, Rockland, Sullivan

PARTIAL COUNTIES

Ulste : Only the Townships Plattekill, Ma lbo o,Wawa sing, and Shawangunk (except fo Walkill and Shawangunk P isons).

WAGES

RESIDENTIAL (One and Two Family).

Plumbing /HVAC fo const uction and epai to plumbing and heating systems in single o two-family houses and not to be used on municipality wo k.

WAGES: (pe hou)

07/01/2024

Plumbe /Steamfitte \$ 36.00

SUPPLEMENTAL ENEFITS

SUPPLEMENTAL BENEFITS pe hou :

Jou neyman \$ 20.90

O ERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Ove time: See (5, 6, 15, 16) on HOLIDAY PAGE

REGISTERED APPRENTICES

(1) yea te ms at the following wages.

07/01/2024

1st te m \$ 18.00

2nd te m 19.80

3 d te m 21.60

4th te m 25.20

5th te m 30.60

Supplemental Benefits pe hou :

1st te m \$ 12.65

2nd te m 13.48

3 d te m 14.30

4th te m 15.95

5th te m 18.43

11-373.

Sheetmetal Worker - Residential

02/01/2025

JO DESCRIPTION Sheetmetal Wo ke - Residential

DISTRICT 8

ENTIRE COUNTIES

Dutchess, O ange, Putnam, Rockland, Sullivan, Ulste , Westcheste

WAGES

***IMPORTANT NOTE: HVAC wo k on single family dwellings, multiple family housing units, apa tments and condominium homes whe e each individual family apa tment is individually conditioned by sepa ate and independent unit o system.

Pe hou : 07/01/2024

Sheetmetal Worker \$ 34.40
+ 1.91*

*This portion of the benefit is NOT subject to the SAME PREMIUM as shown for overtime.

SHIFT WORK

For all NYS D.O.T. and other Governmental mandated off-shift work:
10% increase for additional shifts for a minimum of five (5) days

SUPPLEMENTAL BENEFITS

Journeyworker \$ 24.11

OVERTIME PAY

See (B, E, Q) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6, 8, 15, 16, 23) on HOLIDAY PAGE

REGISTERED APPRENTICES

WAGES - Per hour:

(1/2) years at the following rates.

1st	2nd	3rd	4th	5th	6th	7th	8th
\$18.12	\$19.81	\$21.49	\$23.10	\$25.13	\$27.01	\$29.07	\$30.86
+\$.96*	+\$1.07*	+\$1.18*	+\$1.29*	+\$1.40*	+\$1.49*	+\$1.60*	+\$1.71*

*This portion of the benefit is NOT subject to the SAME PREMIUM as shown for overtime.

Supplemental Benefits - Per hour:

1st	\$ 14.13
2nd	15.35
3rd	16.59
4th	17.88
5th	18.78
6th	19.83
7th	20.67
8th	21.79

8-38

Sprinkler Fitter - Residential

02/01/2025

JO DESCRIPTION Sprinkler Fitter - Residential

DISTRICT 1

ENTIRE COUNTIES

Dutchess, Orange, Putnam, Rockland, Sullivan, Ulster, Westchester

WAGES

IMPORTANT NOTE: "Residential fire protection work" is applicable to one or two family dwellings, all multiple family dwelling units which are permitted to have a single exterior up to and including four stories, townhouses with units stacked vertically up to and including four stories and group residential care facilities and protective care homes (sheltered housing), not to include nursing homes or ambulatory care facilities.

Per hour

07/01/2024

Sprinkler Fitter \$ 43.15

SUPPLEMENTAL BENEFITS

Per hour

Journeyworker \$ 30.77

OVERTIME PAY

See (B, H) on OVERTIME PAGE

HOLIDAY

Paid: See (1) on HOLIDAY PAGE
Overtime: See (5, 6) on HOLIDAY PAGE

Note: When a holiday falls on Sunday, the following Monday shall be considered a holiday and all work performed on either day shall be at the double time rate. When a holiday falls on Saturday, the preceding Friday shall be considered a holiday and all work performed on either day shall be at the double time rate.

1-669 2

Overtime Codes

Following is an explanation of the code(s) listed in the OVERTIME section of each classification contained in the attached schedule. Additional requirements may also be listed in the HOLIDAY section.

NOTE: Supplemental Benefits are 'Per hour worked' (for each hour worked) unless otherwise noted

- (AA) Time and one half of the hourly rate after 7 and one half hours per day
- (A) Time and one half of the hourly rate after 7 hours per day
- (B) Time and one half of the hourly rate after 8 hours per day
- (B1) Time and one half of the hourly rate for the 9th & 10th hours week days and the 1st 8 hours on Saturday.
Double the hourly rate for all additional hours
- (B2) Time and one half of the hourly rate after 40 hours per week
- (B3) Time and one half of the hourly rate after 40 straight hours per week
- (C) Double the hourly rate after 7 hours per day
- (C1) Double the hourly rate after 7 and one half hours per day
- (D) Double the hourly rate after 8 hours per day
- (D1) Double the hourly rate after 9 hours per day
- (E) Time and one half of the hourly rate on Saturday
- (E1) Time and one half 1st 4 hours on Saturday; Double the hourly rate all additional Saturday hours
- (E2) Saturday may be used as a make-up day at straight time when a day is lost during that week due to inclement weather
- (E3) Between November 1st and March 3rd Saturday may be used as a make-up day at straight time when a day is lost during that week due to inclement weather, provided a given employee has worked between 16 and 32 hours that week
- (E4) Saturday and Sunday may be used as a make-up day at straight time when a day is lost during that week due to inclement weather
- (E5) Double time after 8 hours on Saturday
- (F) Time and one half of the hourly rate on Saturday and Sunday
- (G) Time and one half of the hourly rate on Saturday and Holidays
- (H) Time and one half of the hourly rate on Saturday, Sunday, and Holidays
- (I) Time and one half of the hourly rate on Sunday
- (J) Time and one half of the hourly rate on Sunday and Holidays
- (K) Time and one half of the hourly rate on Holidays
- (L) Double the hourly rate on Saturday
- (M) Double the hourly rate on Saturday and Sunday
- (N) Double the hourly rate on Saturday and Holidays
- (O) Double the hourly rate on Saturday, Sunday, and Holidays
- (P) Double the hourly rate on Sunday
- (Q) Double the hourly rate on Sunday and Holidays
- (R) Double the hourly rate on Holidays

&(% % !: 9 +87 ! !
! % :

~
^
.
~°
! (~°
% !)^ * ! ! ,+ ° ~
~ & ~ + -

\$ # . %

$$\frac{1}{\sqrt{\pi}} \int_{-\infty}^{\infty} f(x) e^{-x^2} dx = \frac{1}{\sqrt{\pi}} \int_{-\infty}^{\infty} f(x) e^{-x^2} dx$$
$$Q \approx \frac{1}{2} \left(\frac{1}{\omega} + \frac{1}{\omega_0} \right)$$
$$87 \frac{4}{5} (.$$
 $\sim \sim f$

Federal Prevailing Wage Rates

This page intentionally left blank.

Superseded General Decision Number: NY20240007

State: New York

Construction Types: Building, Heavy and Highway

Counties: Dutchess, Orange, Sullivan and Ulster Counties in New York.

BUILDING CONSTRUCTION PROJECTS FOR ALL COUNTIES EXCEPT SULLIVAN (does not include single family homes and apartment up to and including 4 stories), HEAVY AND HIGHWAY CONSTRUCTION PROJECTS

Note: Contracts subject to the Davis-Bacon Act are generally required to pay at least the applicable minimum wage rate required under Executive Order 14026 or Executive Order 13658. Please note that these Executive Orders apply to covered contracts entered into by the federal government that are subject to the Davis-Bacon Act itself, but do not apply to contracts subject only to the Davis-Bacon Related Acts, including those set forth at 29 CFR 5.1(a)(1).

If the contract is entered into on or after January 30, 2022, or the contract is renewed or extended (e.g., an option is exercised) on or after January 30, 2022:	. Executive Order 14026 generally applies to the contract. . The contractor must pay all covered workers at least \$17.75 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on the contract in 2025.
If the contract was awarded on or between January 1, 2015 and January 29, 2022, and the contract is not renewed or extended on or after January 30, 2022:	. Executive Order 13658 generally applies to the contract. . The contractor must pay all covered workers at least \$13.30 per hour (or the applicable wage rate listed on this wage determination, if it is higher) for all hours spent performing on that contract in 2025.

The applicable Executive Order minimum wage rate will be adjusted annually. If this contract is covered by one of the Executive Orders and a classification considered necessary for performance of work on the contract does not appear on this wage determination, the contractor must still submit a conformance request.

Additional information on contractor requirements and worker protections under the Executive Orders is available at <http://www.dol.gov/whd/govcontracts>.

Modification Number Publication Date
0 01/03/2025

ASBE0040-003 05/01/2024

SULLIVAN AND ULSTER COUNTIES

	Rates	Fringes
HAZARDOUS MATERIAL HANDLER		
Duties limited to preparation wetting; stripping; removal; scrapping; vacuuming; bagging; and disposing of all insulation materials whether they contain asbestos or not from mechanical systems.....	\$ 38.40	24.42
Insulator/asbestos worker (includes application of all insulating materials, protective coverings, coatings and finishes to all types of mechanical systems).....	\$ 40.46	26.86

ASBE0091-002 06/03/2024

DUTCHESS AND ORANGE COUNTIES

	Rates	Fringes
HAZARDOUS MATERIAL HANDLER		
Duties limited to preparation, wetting, stripping, removal scrapping, vacuuming, bagging and disposing of all insulation materials; whether they contain asbestos or not from mechanical systems.....	\$ 45.37	48.65
Insulator/asbestos worker (Includes application of all insulating materials, protective coverings, coatings, and finishes to all types of mechanical systems).....	\$ 45.37	48.65

BOIL0005-001 01/01/2024

	Rates	Fringes
BOILERMAKER.....	\$ 67.38	49.33+a

FOOTNOTE:

a. PAID HOLIDAYS: New Year's Day, Thanksgiving Day, Memorial
Day, Independence Day, Labor Day and Good Friday, Friday
after Thanksgiving, Christmas Eve Day and New Year's Eve

	Rates	Fringes
BRICKLAYER (BUILDING CONSTRUCTION)		
DUTCHESS, ORANGE (Excluding the town of Tuxedo) and ULSTER COUNTIES Bricklayers, Cement Masons, Plasterers, Stone Masons.....\$ 45.00		36.89
ORANGE COUNTY (Town of Tuxedo) Bricklayers, Cement Masons, Plasterers, Stone Masons.....\$ 45.89		37.45
BRICKLAYER (HEAVY CONSTRUCTION)		
DUTCHESS, ORANGE (Excluding the town of Tuxedo) and ULSTER COUNTIES Bricklayers, Cement Masons, Plasterers, Stone Masons.....\$ 45.50		36.89
ORANGE COUNTY (Town of Tuxedo) Bricklayers, Cement Masons, Plasterers, Stone Masons.....\$ 46.39		37.45
BRICKLAYER (HIGHWAY CONSTRUCTION)		
DUTCHESS, ORANGE (Excluding the town of Tuxedo), SULLIVAN and ULSTER COUNTIES Bricklayers, Cement Masons, Plasterers, Stone Masons.....\$ 45.50		36.89

CARP0279-005 07/01/2024

	Rates	Fringes
Carpenters:		
BUILDING CONSTRUCTION Carpenters, Millwrights, Pile Drivers.....\$ 43.50		30.22
HEAVY & HIGHWAY CONSTRUCTION Carpenters, Millwrights, Pile Drivers.....\$ 43.50		30.22

CARP0740-002 07/01/2024

DUTCHESS AND ORANGE COUNTIES

	Rates	Fringes
MILLWRIGHT.....\$ 46.35		43.52

CARP1556-005 07/01/2024

DUTCHESS AND ORANGE COUNTIES

	Rates	Fringes
Diver Tender.....	\$ 55.00	55.84
Diver.....	\$ 75.46	55.84
Dock Builder & Piledrivermen.....	\$ 60.59	55.84

ELEC0363-001 04/01/2023		

	Rates	Fringes
ELECTRICIAN		
DUTCHESS (Remaining Townships), ULSTER AND SULLIVAN COUNTIES.....	\$ 45.50	3%+37.67+a
ORANGE and DUTCHESS (Townships of Fishkill, East Fishkill and Beacon) COUNTIES.....	\$ 49.50	3%+37.67+a

FOOTNOTE:

a. Paid Holidays: New Year's Day, President's Day, Memorial Day, Fourth of July, Labor Day, Presidential Election Day, Veteran's Day, Thanksgiving Day, Day after Thanksgiving, Christmas Day

ELEC1249-002 05/01/2023

	Rates	Fringes
ELECTRICIAN (LINE CONSTRUCTION-LIGHTING AND TRAFFIC SIGNAL INCLUDING ANY AND ALL FIBER OPTIC CABLE NECESSARY FOR THE TRAFFIC SIGNAL SYSTEMS, AND TRAFFIC MONITORING SYSTEMS, ROAD WEATHER INFORMATION SYSTEMS)		
Flagman.....	\$ 30.36	7%+35.40
Groundman (Digging Machine Operator).....	\$ 45.54	7%+35.40
Groundman (Truck Driver)....	\$ 40.48	7%+35.40
Groundman Truck Driver (Tractor Trailer Unit).....	\$ 43.01	7%+35.40
Lineman and Technician.....	\$ 50.60	7%+38.40
Mechanic.....	\$ 40.48	7%+35.40

PAID HOLIDAYS:

a. Memorial Day, New Year's Day, President's Day, Good Friday, Decoration Day, Independence Day, Labor Day, Thanksgiving Day, Christmas Day, and Election Day for the President of the United States and Election Day for the Governor of New York State, provided the employee works two days before or two days after the holiday.

ELEC1249-004 05/01/2023

	Rates	Fringes
ELECTRICIAN (Line Construction) Overhead and underground distribution and		

maintenance work and all
overhead and underground
transmission line work
including any and all
fiber optic ground wire,
fiber optic shield wire or
any other like product by
any other name
manufactured for the dual
purpose of ground fault
protection and fiber optic
capabilities :

Flagman.....	\$ 34.44	7%+35.40
Groundman digging machine operator.....	\$ 51.66	7%+35.40
Groundman truck driver (tractor trailer unit).....	\$ 48.79	7%+35.40
Groundman Truck driver.....	\$ 45.92	7%+35.40
Lineman and Technician.....	\$ 57.40	7%+38.40
Mechanic.....	\$ 45.92	7%+35.40
Substation:		
Cable Splicer.....	\$ 63.14	7%+38.40
Flagman.....	\$ 34.44	7%+35.40
Ground man truck driver....	\$ 45.92	7%+35.40
Groundman digging machine operator.....	\$ 51.66	7%+35.40
Groundman truck driver (tractor trailer unit).....	\$ 48.79	7%+35.40
Lineman & Technician.....	\$ 57.40	7%+38.40
Mechanic.....	\$ 45.92	7%+35.40

Switching structures;
railroad catenary
installation and
maintenance, third rail
type underground fluid or
gas filled transmission
conduit and cable
installations (including
any and all fiber optic
ground product by any
other name manufactured
for the dual purpose of
ground fault protection
and fiber optic
capabilities), pipetype
cable installation and
maintenance jobs or
projects, and maintenance
bonding of rails; Pipetype
cable installation

Cable Splicer.....	\$ 64.59	7%+38.40
Flagman.....	\$ 35.23	7%+35.40
Groundman Digging Machine Operator.....	\$ 52.85	7%+35.40
Groundman Truck Driver (tractor-trailer unit).....	\$ 49.91	7%+35.40
Groundman Truck Driver.....	\$ 46.98	7%+35.40
Lineman & Technician.....	\$ 58.72	7%+38.40
Mechanic.....	\$ 46.98	7%+35.40

FOOTNOTE:

a. PAID HOLIDAYS: New Year's Day, Presidents' Day, Memorial Day, Good Friday, Independence Day, Labor Day, Thanksgiving Day, Christmas Day, and Election Day for the President of

the United States and Election Day for the Governor of New York State, provided the employee works two days before or two days after the holiday.

ELEC1249-005 05/01/2023

SULLIVAN COUNTY

	Rates	Fringes
ELECTRICIAN (LIGHTING AND TRAFFIC SIGNAL LINEMAN INCLUDING ANY AND ALL FIBER OPTIC CABLE NECESSARY FOR THE TRAFFIC SIGNAL SYSTEM, TRAFFIC MONITORING SYSTEMS AND ROAD WEATHER INFORMATION SYSTEMS.)		
Flagman.....	\$ 29.59	7%+35.40
Groundman (Digging Machine Operator).....	\$ 44.39	7%+35.40
Groundman (Truck Driver)....	\$ 39.46	7%+35.40
Groundman Truck Driver (tractor trailer unit).....	\$ 41.92	7%+35.40
Lineman & Technician.....	\$ 49.32	7%+38.40
Mechanic.....	\$ 39.46	7%+35.40

FOOTNOTE:

a. New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day, Christmas Day, plus President's Day, Good Friday, Decoration Day, Election Day for the President of the United States and Election Day for the Governor of the State of New York, provided the employee works the day before or the day after the holiday.

ELEC1249-008 01/01/2024

	Rates	Fringes
ELECTRICIAN (Line Construction) TELEPHONE, CATV FIBEROPTICS CABLE AND EQUIPMENT		
Cable splicer.....	\$ 39.24	3%+5.70
Groundman.....	\$ 19.74	3%+5.70
Installer Repairman- Teledata Lineman/Technician- Equipment Operator.....	\$ 37.24	3%+5.70
Tree Trimmer.....	\$ 31.45	3%+10.48

a. New Year's Day, President's Day, Good Friday, Decoration Day, Independence Day, Labor Day, Veteran's Day, Thanksgiving Day, Day after Thanksgiving, Christmas Day.

ELEV0138-001 01/01/2024

	Rates	Fringes
ELEVATOR MECHANIC.....	\$ 70.15	37.885+a+b

FOOTNOTE:

- a. Vacation: 6%/under 5 years based on regular hourly rate for all hours worked. 8%/over 5 years based on regular hourly rate for all hours worked.
- b. PAID HOLIDAYS: New Year's Day; Memorial Day; Independence Day; Labor Day; Veterans' Day; Thanksgiving Day; the Friday after Thanksgiving Day; and Christmas Day.

ENGI0137-001 03/04/2024

DUTCHESS COUNTY (POUGHKEEPSIE AND SOUTH THEREOF)

BUILDING CONSTRUCTION

	Rates	Fringes
Power Equipment Operator		
GROUP 1A.....	\$ 59.04	31.32+a
GROUP 1B.....	\$ 54.41	31.32+a
GROUP 2A.....	\$ 56.97	31.32+a
GROUP 3A.....	\$ 54.88	31.32+a
GROUP 3B.....	\$ 52.25	31.32+a
GROUP 4A.....	\$ 54.33	31.32+a
GROUP 4B.....	\$ 45.94	31.32+a
GROUP 5.....	\$ 49.53	31.32+a
GROUP 5A.....	\$ 61.95	31.32+a
GROUP 5B.....	\$ 47.00	31.32+a
GROUP 6.....	\$ 49.26	31.32+a

NOTES: Hazmat: 20% above regular rate
Pumping operation Premium .50

Crane Operators (100-149 ft) 2.00

Crane Operators (149 ft +) 3.00

Loader Operators (over 5 cu y) .50

Shovel Operators (over 4 cu yd) 1.00

FOOTNOTE:

- a. New Years Day, Memorial Day, Independence Day, Labor Day
Thanksgiving Day, Christmas Day, plus Lincoln's Birthday,
Washington's Birthday, Good Friday, Columbus Day, November
Election Day, Veteran's Day.

POWER EQUIPMENT OPERATORS CLASSIFICATION

GROUP 1-A: Carrier- trailer horse; concret-portable hoist;
crane & hoist engineer-steel (concrete, material, super
structure sub- structure); derrick (stone-steel); elevator
& cage; hoist- single/double or triple drum; hoist-portable
mobile unit; hoist engineer-concert (crane-derrick-mine
hoist); hoist engineer- material; overhead crane; power
house plant; telephies (cableway); whirly; maintenance
engineer; Lull hiliift or similar; hydraulic crane 25 ton
and over; cherry picker 25 tons and over; backhoe Oliver
88; fordson; dynahoe; dual purpose and similar machines;
Barber Green Loader-euclid loader or similar type; conway
or similar mucking macking machines; dragline; gradall;
shovel; backhoe etc. (crawler or truck); front end loaders;
hydraulic boom; jersey spreader; lift slab console;
letournequ or tounapull (scrappers over 20 yds struck);

mucking machines; pavement breaker (air ram); paver (concrete); road boring machine; road mix machines; road carrier and similar machines; post hole digger; shovel (tunnels); side boom; spreader (asphalt); scoopmobile-tractor-shovel over 1 1/2 yds. trenching machines vermeer concrete saw trencher and similar; tractor type demolition equipment; winch truck (a frame); hydraulic crane over 10 ton up to 25 ton); cherry picker over 10 ton up to 25 ton)

GROUP 1-B: Compressor (steel erection); pulse meter and push button buzz box; elevator; mechanic (outside) all types; welder; scrapers 20 yds struck and under; machine pulling sheep's foot roller; vibratory rollers; roller 4 tons and over.

GROUP 2-A: Compactor self-propelled; grader; bulldoze D7 and similar tractors with a draw bar horsepower of 100 or over; bulldozer D6 and under; welder; scraper 20 yds struck and under; machine pulling sheep's foot roller; vibratory rollers.

GROUP 3-A: Asphalt plant; boiler (high pressure); concrete mixing plants; concrete pump; firemen; forklift; forklift (electric); joy drill or similar tractor drilling machine; loader - 1 1/2 yards and under; locomotive (all sizes); mixer concrete - 21E and over; portable asphalt plant; portable batch plant; portable crusher; quarry master; stone crusher; well drilling machine and well point system; cherry picker under 10 tons; hydraulic crane under 10 tons; concert buffy; one yard an up ride on dumper (benford or similar).

GROUP 3-B: Compressor over 125 cu. feet; conveyor belt machine regardless of size; lighting unit (portable & generator); welding machine (steel erection and excavation); and compressor plant; stud machine; ladder hoist.

GROUP 4-A: Air tractor drill; batch plant; bending machine; concrete breaker; concrete spreader; curb cutter machine; farm tractor (all types); finishing machine-concrete; hepavac clean air machine (all similar types: removal of asbestos etc.); material hopper-sand-stone-cement; mixer-concrete-under 21E; mulching grass spreader; pump-gypsum, etc., pump-plaster-grout -fireproofing; shop mechanic (not employed on job site); roller under 4 ton; spreading and fine grading machine; steel cutting machine; syphon pump-air-steam; tar joint machine; turbo jet burner or similar equipment; vibrator (1 to 5); fine grading machine; roof hoist (tugger hoist); television cameras-water- sewer-gas-etc.

GROUP 4-B: Compressor to 125 feet; dust; dust collector; heater all types; pump; pump station (water and sewer); steam jenny; sweeper; chipper; mulcher.

GROUP 5: Motorized roller (walk behind)

GROUP 5-A: Master Mechanic

GROUP 5-B: Utility Man

GROUP 6: Warehouse Man

Poughkeepsie and South thereof

	Rates	Fringes
Power Equipment Operator (HEAVY & HIGHWAY)		
GROUP 1.....	\$ 68.63	35.25+a
GROUP 1-A.....	\$ 60.42	35.25+a
GROUP 1-B.....	\$ 63.70	35.25+a
GROUP 2-A.....	\$ 57.84	35.25+a
GROUP 2-B.....	\$ 59.67	35.25+a
GROUP 3.....	\$ 56.81	35.25+a
GROUP 4-A.....	\$ 51.57	35.25+a
GROUP 4-B.....	\$ 44.19	35.25+a
GROUP 5.....	\$ 64.02	35.25+a
GROUP 5-A-1.....	\$ 64.02	35.25+a
GROUP 5-A-2.....	\$ 77.82	35.25+a
GROUP 5-A-3.....	\$ 75.13	35.25+a
GROUP 5-A-4.....	\$ 70.41	35.25+a
GROUP 5-A-5.....	\$ 59.19	35.25+a

POWER EQUIPMENT OPERATORS CLASSIFICATIONS (HEAVY & HIGHWAY)

GROUP 1: Boom Truck; Cherry Picker; Clamshell; Crane,
 (Crawler, Truck); Dragline; Rough Terrain Crane

GROUP 1-A: Auger; Auto Grader; Dynahoe and Dual purpose and
 similar machines; Boat Captain; Boring Machine (all types);
 Bull Dozer-all sizes; Central Mix Plant Operator;
 Chipper-all types; Close circuit t.v.; Compactor with
 Blade; Concrete Portable Hoist; C.M.I. or similar; Conway
 or similar mucking machines; Gradall, Shovel Backhoe, etc.
 Grader; Derrick, (Stone- Steel; Elevator & cage, materials
 or passengers; Front end loaders over 1 1/2 yds.; Hoist
 Single, Double, Triple Drum, Hoist Portable Mobile Unit;
 Hoist Engineer-Concrete (Crane-Derrick-Mine Hoist); Hoist
 Engineer-Material, Hydraulic Boom; Letourneau or Tournapull
 (Scrapers over 20 yds. struck); Log Skidder; Movable
 Concrete Barrier Transfer & Transport Vehicle; mucking
 machines; overhead crane; paver (concrete); pulsemeter;
 push button (buzz box) elevator; road mix machines; Robot
 Hammer (brock or similar), Ross carrier and similar
 machines; shovels (tunnels); side boom; Slip Form Machine;
 spreader (asphalt); scoopmobile-tractor-shovel over 1 1/2
 yards; trenching machines; telephies- vermeer concrete saw
 trencher and/or similar; tractor-type demolition equipment,
 Whirly

GROUP 1-B: Road Paver, Asphalt

GROUP 2-A: Ballast Regulators; Compactor self-propelled; Cow
 Tracks; Fusion Machine; Rail Anchor Machines; Roller 4 ton
 and over; Scrapers - 20 yards struck; Switch Tampers;
 Vibratory roller, etc.

GROUP 2-B: Mechanic (outside) all types

GROUP 3-A: Air tractor drill; asphalt plant; batch plant;
 boiler (high pressure; concrete breaker; concrete pump
 concrete spreader; curb cutter machine; farm tractor (all
 types); finishing machine (concrete); fine grading machine;
 fireman; forklift; forklift (electric); joy drill or

similar tractor drilling machine; loader - 1 1/2 yards and under; locomotive (all sizes), maintenance engineer; machine pulling sheeps foot roller; material hopper; mixer concrete - 21-E and over; mulching grass spreader; portable asphalt plant, portable batch plant, portable crusher; powerhouse plant; quarry master; roller under 4 ton; spreading and fine grading machine; steel cutting machine; stone crusher; sweeper; turbojet burner or similar; well drilling machine ; winch truck ""A"" frame. John Henry Drill or similar.

GROUP 4-A: Service men (fuel or grease truck).

GROUP 4-B: Oiler; Compressor - compressor plant; paint compressor-steel erection; conveyor belt machine; lighting unit (portable & generator); oiler; pumps - pump station-water-sewer- gypsum- plaster, etc.; roller-motorized (walk-behind); welding machine (steel erection excavation); well point system; bending machine; dust collector; mixer - concrete under 21-E; heater all types; steam jenny; syphon pump-air-steam; tar joint machine; vibrator (1 to 5); Compressor Truck Mounted (2-6)

GROUP 5: Oiler
 GROUP 5-A-1: Master Mechanic

GROUP 5-A-2: Engineer - all tower cranes, all climbing cranes and all cranes of 100 ton capacity or greater (3900 Manitowac or similar) irrespective of manufacturer and regardless of how the same is rigged (except for pile rigs).

GROUP 5-A-3: Engineer-- Pile Driver

GROUP 5-A-4: Hoist Engineer- Steel -Sub Structure

GROUP 5-A-5: Jersey-spreader, pavement breaker (air ram); Post Hole Digger

NOTES:
 Loader Operator (over 5 cu yds) .50
 Shoval Operators (over 4 cu yd) 1.00
 Hazmat premium over regular rate 20%

CRANES:

100 ft- 149 ft: receive \$2.00 more than Group 1 rate
 149 ft and over receive \$3.00 more than Group 1 rate

FOOTNOTE:
 a. PAID HOLIDAYS: New Year's Day; Lincoln's Birthday; Good Friday; Memorial Day; Independence Day; Labor Day; Veterans Day; Columbus Day; November Election Day; Thanksgiving Day; and Christmas Day

 ENGI0158-006 07/01/2024

NORTHERN PART OF DUTCHESS (TO THE NORTHEN BOUNDARY LINE OF THE CITY OF POUGHKEEPSIE) BUILDING CONSTRUCTION

	Rates	Fringes
Power equipment operators:		
GROUP A(1).....	\$ 53.11	32.58
1.....	\$ 49.06	30.74

2.....	\$ 50.06	30.74
GROUP A.....	\$ 52.62	32.58
GROUP B.....	\$ 51.60	32.58
GROUP C.....	\$ 48.70	32.58

Hazardous work - Anytime Operating Engineers are involved with level C or above, \$2.50 per hour over regular rate.

FOOTNOTE:

a. Paid Holiday: New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day, Christmas Day

POWER EQUIPMENT OPERATOR CLASSIFICATIONS

GROUP A(1): Crane, hydraulic cranes, tower crane, locomotive crane, piledriver, cableway, derricks, whirllies, dragline, boom truck (over 5 tons)

GROUP A(1): Crane Premiums

- 1 over 150' :add \$1.00
- 2 over 200': add \$2.00

GROUP A: Shovel, All excavator (except tractor mounted rubber tired John Deere 510 or smaller), gradalls, power road grader, all CMI equipment, front-end rubber tire loader, tractor-mounted drill (quarry master), mucking machine, concrete central mix plant, concrete pump, Belcrete system, automated asphalt concrete plant and tractor road paver, boom truck (5 tons and under).

GROUP B: Backhoe, (tractor mounted rubber tired equivalent to John Deere 510 or less), bulldozer, pushcat, tractor, traxcavator, scraper, LeTourneau grader, form fine grader, road roller, blacktop roller, blacktop spreader, power brooms, sweepers, trenching machine, Barber Green loader, side booms, hydrohammer, concrete spreader, concrete finishing machine, one drum hoist, power hosting (single drum), hoist - two drum or more, three drum engine, power hoisting (two drum and over), two drum and swinging engine, three drum swinging engine, hod hoist, A-L frame winches, cord and well drillers (one drum), post hole digger, model CHB Vibro-Tamp or similar machine, batch bin and plant operator, dinkey locomotive, skid steer loader, track excavator 5/8 cu. yd. or smaller.

GROUP C: Fork lift, high lift, lull, Oiler, fireman and heavy- duty greaser, boilers, and steam generators, pump, vibrator, motor mixer, air compressor, dust collector, welding machine, well point, mechanical heater, generators, temporary light plants, concrete pumps, electric submersible pump 4" and over, murphy type diesel generator, conveyor, elevators, concrete mixer and belcrete power pack (belcrete system), seeding, and mulching machines, pumps.

ENGI0158-018 07/01/2024

NORTHERN PART OF DUTCHESS (To The Northern Boundary line of the City of Poughkeepsie)

Rates

Fringes

Power Equipment Operator

HEAVY & HIGHWAY

GROUP 1.....	\$ 54.90	32.45
GROUP 2.....	\$ 53.99	32.45
GROUP 3.....	\$ 51.42	32.45
GROUP 4.....	\$ 60.90	32.45
GROUP 5.....	\$ 59.40	32.45
GROUP 6.....	\$ 57.90	32.45
GROUP 7.....	\$ 57.01	32.45

POWER EQUIPMENT OPERATORS HEAVY & HIGHWAY CLASSIFICATIONS

GROUP 1: Asphalt Curb Machine, Self Propelled, Slipform, Automated Concrete Spreader (CMI Type), Automatic Fine Grader, Backhoe (Except Tractor Mounted, Rubber Tired), Backhoe Excavator Full Swing (CAT 212 or similar type), Back Filling Machine, Belt Placer (CMI Type), Blacktop Plant (Automated), Boom truck , Cableway, Caisson Auger, Central Mix Concrete Plant (Automated), Concrete Curb Machine, Self Propelled, Slipform, Concrete Pump, Crane, Cherry Picker, Derricks (steel erection), Dragline, Overhead Crane (Gantry or Straddle type), Pile Driver, Truck Crane, Directional Drilling Machine, Dredge, Dual Drum Paver, Excavator (All Purpose Hydraulically Operated) (Gradall or Similar), Front End Loader (4 cu. yd. and Over), Head Tower (Sauerman or Equal), Hoist (Two or Three Drum), Holland Loader, Maintenance Engineer, Mine Hoist, Mucking Machine or Mole Pavement Breaker(SP) Wertgen; PB-4 and similar type, Power Grader, Profiler (over 105 H.P.) Quad 9, Quarry Master (or equivalent), Scraper, Fireman, Form Tamper, Grout Pump, Guniting Machine, Hammers (Hydraulic self-propelled), Hydra-Spiker, ride-on, Hydraulic Pump (jacking system), Hydro-Blaster (Water), Mulching Machine, Oiler, Parapet Concrete or Pavement, Shovel, Side Boom, Slip Form Paver, Tractor Drawn, BeltType Loader, Truck or Trailer Mounted Log , Chipper (Self Feeder), Tug Operator (Manned Rented Equipment Excluded), Tunnel Shovel

GROUP 2: Asphalt Paver, Backhoe (Tractor Mounted, Rubber Tired), Bituminous Recycler Machine, Bituminous Spreader and Mixer, Blacktop Plant (NonAutomated), Blast or Rotary Drill (Truck or Tractor Mounted), Boring Machine, Cage Hoist, Central Mix Plant (NonAutomated) and All Concrete Batching Plants, Cherry Picker (5 tons capacity and under), Concrete Paver (Over 16S), Crawler Drill, Self-contained, Crusher, Diesel Power Unit, Drill Rigs, Tractor Mounted, Front End Loader (Under 4 cu. yd.), Greaseman/Lubrication Engineer, HiPressure Boiler (15 lbs. and over), Hoist (One Drum), Hydro-Axe, Kolman Plant Loader and Similar Type Loaders, L.C.M. Work Boat Operator, Locomotive Mixer (for stabilized base selfpropelled), Monorail Machine, Plant Engineer, Profiler (105 H.P. and under), Grinder, Post Hole Digger and Post Driver, Power Broom (towed), Power Heaterman, Power Sweeper, Revinius Widener, Roller (Grade and Fill), Scarifier, ride-on, Shell Winder, Skid steer loader (Bobcat or similar), Span-Saw, ride-on, Steam Cleaner, Pug Mill, Pump Crete Ready Mix Concrete Plant Refrigeration Equipment (for soil stabilization)Road Widener, Roller (all above subgrade), Sea Mule, Self-contained Ride-on Rock Drill, Excluding Air-Track Type Drill, Skidder, Tractor with Dozer and/or Pusher, Trencher. Tugger Hoist, Vermeer saw (ride on, any size or type), Winch, Winch Cat

GROUP 3: A Frame Winch Hoist on Truck , Articulated Heavy

Hauler, Aggregate Plant, Asphalt or Concrete Grooving, Machine (ride on), Ballast Regulator, Ride-on Boiler (used in conjunction with production), Bituminous Heater, self-propelled, Boat (powered), Cement and Bin Operator, Compressors, Dust Collectors, Fork Lift, Generators, Pumps, Welding Machines, Light Plants, Heaters (hands-off equipment), Concrete Pavement Spreader and Finisher, Concrete Paver or Mixer (16S and under), Concrete Saw (self-propelled), Conveyor, Deck Hand, Directional Drill Machine Locator, Drill, (Core), Drill, (Well,) Farm Tractor with accessories, Fine Grade Machine, Tamper, ride-on, Tie Extractor, ride-on, Tie Handler, ride-on, Tie Insertter, ride-on, Tie Spacer, ride-on, Tire Repair, Track Liner, ride-on, Tractor, Tractor (with towed accessories), Vibratory Compactor, Vibro Tamp, Well Point

GROUP 4: Tower Cranes

GROUP 5: Cranes 50 tons and over

GROUP 6: Cranes 49 tons and below

GROUP 7: Master Mechanic

FOOTNOTES:

a. PAID HOLIDAYS: New Year's Day, Memorial Day, Independence Day, Labor Day, Thanksgiving Day, and Christmas Day

ENGI0825-007 07/01/2024

ORANGE, ULSTER AND SULLIVAN COUNTIES

	Rates	Fringes
Power Equipment Operator		
BUILDING, HEAVY & HIGHWAY		
GROUP 1.....	\$ 60.47	36.25
GROUP 2.....	\$ 58.88	36.25
GROUP 3.....	\$ 56.97	36.25
GROUP 4.....	\$ 55.34	36.25
GROUP 5.....	\$ 51.63	36.25
GROUP 6.....	\$ 62.29	36.25

NOTES:

Hazmat Premium 20%
Hydrographic Premium .50

POWER EQUIPMENT OPERATORS CLASSIFICATIONS (BLDG, HEAVY & HWY)

GROUP 1: Autograde-Pavement-Profiler (CMI and Similar Type); utograde-Pavement-Profiler (CMI and Similar Types);Autograde Slipform Paver (CMI and Similar Types); Backhoe; Central Power Plants (all types); Concrete Paving Machine (s-240 and Similar Types); Cranes (All Types, Including Overhead and Straddle Traveling Type); Cranes, Gantry; Derricks (Land, Floating or Chicago Boom Type); Drillmaster/Quartmaster (Down the Hole Drill) Rotary Drill; Self-Propelled, Hydraulic Drill, Self-Powered Drill Draglines, Elevator Graders, Front End Loaders (5 yds. and over), Gradalls, Grader: Rago, Helicopters (Copilot), Helicopters, (Communication Engineer), Locomotive (large), Mucking Machines, Pavement and Concrete Breaker

(Superhammer, Hoe Ram, Brokk 250 and Similar Types), Pile Driver (length of boom including length of leads shall determine premium rate applicable), Roadway Surface Grinder Scooper (loader and shovel), Shovels, Tree Chooper with Boom, Trench Machines, Tunnel Boring Machines.

GROUP 2: "'A"' Frame; Backhoe (Combination); Boom Attachment on Loaders (Rate based on size of bucket) not applicable to Pipehook) Boring and Drilling Machines, Brush Chopper, Shredder and Tree Shredder Tree Shearer, Cableways, Carry-alls, Concrete Pump, Concrete Pumping System, Pumpcrete and Similar Types, Conveyors, 125 ft and over; Drill Doctor (duties include dust collector, maintenance), Front End Loader (22 yds. but less than 2 yds.), Graders (Finish); Groove Cutting Machine (ride on type), Heater Planer; Hoists: (all type hoists, Shall Also Include Steam, Gas, Diesel, Electric, Air Hydraulic, Single and Double Drum, Concrete, Brick Shaft, Caisson, Snorkel Roof, and or any other similar type Hoisting Machines, Portable or Stationary, Except Chicago Boom Type). Long Boom Rate to Be Applied if Hoist is "'outside material lower hoist"; Hydraulic Cranes-10tons and Under; Hydro-Axe; Hydro-Blaster; Jacket (Screw Air Hydraulic Power Operated Unit or Console Type: Not Hand Jack or Pile Load Test Type), Log Skidder; Pans, Pavers (all) Concrete; Plate and Frame Filter Press; Pumpcrete Machines; Squeeze Crete and Concrete Pumping (regardless of size); Scrapers; Sidebooms; Straddle Carrier, Ross and Similar Types; Vacuum Truck; Whip Hammer; Winch Trucks (Hoisting).

GROUP 3: Asphalt Curbing Machine, Asphalt Plant Engineer, Asphalt Spreader; Autograde Tube Finisher & Texturing Machine (CMI and Similar types) Autograde Curecrete Machine (CMI and Similar Types); Bar Bending Machines (power), Batchers, Batching Plant and Crusher on-site; Belt Conveyor Systems; Boom Type Skimmer Machines; Bridge Deck Finisher; Bulldozers (all); Car Dumpers (A:road); Chief of Party; Compressor and Blower Type Units (used) Independently or Mounted On Dual Purpose Trucks, On Job Site or In Conduction with Job Site, In Loading and Unloading of Concrete, Cement, Fly Ash, Instantcrete, or Similar Type Materials); Compressor 92 or 3 in Battery); Concrete Finishing Machines; Concrete Saws and Cutters (ride on type); Concrete Spreaders, Hetzel, Rexomatic and Similar types; Concrete Vibrators; Conveyors, Under 125 ft), Crushing Machines, Ditching Machine, Small (ditchwitch, Vermeer or Similar type); Dope Dots (mechanical with or without pump), dumpsters; Elevator; Fireman; Forklifts (economobile, lull, and similar types of equipment); Front End Loaders (1 yd. and over but less than 2 yds.); Generators (2 or 3 in Battery/ within 100 ft); Giraffe Grinders, Graders and Motor Patrols; Grout Pump; Gunnite Machines (excluding nozzle); Hammer Vibratory (in conduction with generators); Hoists (Roof, Tuggeraerial Platfrom Hoist and House Cars), Hoppers, Hoppers Doors (power operated); Hydro-Blaster (where required); Ladders (Motorized); Laddervator; Locomotive, Dinky type; Maintenance, Utility Man; Mechanics; Mixers (Excepting Paving Mixers); Motor Patrols and Graders; Pavement Breakers, Small, Self-Propelled ride on type (also maintains compressor or hydraulic unit); Pavement Breaker, Truck Mounted; Pipe Bending Machine (power); Pitch Pump; Plaster Pump (regardless of size); Post Hole Digger (post pounder and auger); Rod Bending Machines (power); Roller, Black Top; Scales, (power); Seaman Pulverizing Mixer;

Shoulder Widener; Silos; Skimmer Machines (Boom Type); Steel Cutting Machine, Services and Maintains; Tamrock Drill; Tractors; Tug Captain; Vibrating Plants (used in conduction with unloading); welder and Repair Machines. Concrete cleaning/decontamination machine operator; Directional boring machine; Heavy equipment robotics operator; Master environmental maintenance operator; Ultra high pressure waterjet cutting tool system operator; maintenance operator; Vacuum blasting machine operator

GROUP 4: Brooms and Sweepers; Chippers; Compressors (single); Concrete Spreaders (small type); Conveyor Loaders (not including Elevator Graders); Engines, Large Diesel (1620 h.p.) and Staging Pump; Farm Tractors; Fertilizing Equipment (Operator and Maintenance of); Fine Grade Machine (small type); Form Line Graders (small type); Front End Loader (under 1 yd); Generator (single); Grease, Gas, Fuel and Oil Supply Trucks; Heaters (Nelson or Other Type Including Propane, Natural Gas or Flowtype Units); Lights, Portable Generating Light Plants; Mixers, Concrete Small; Mulching Equipment (Operation and Maintenance of); Pumps (2 of Less Than 4 Inch Suction); Pumps 94 Inch Suction and Over Including Submersible Pumps); Pumps (Diesel Engine and Hydraulic); Immaterial of Power; Road Finishing Machines (Small Type); Rollers, Grade, Full Or Stone Base; Seeding Equipment (Operation and maintenance of); Sprinkler and Water Pump Trucks (Used on job Site or in conduction with Job Site); Steam Jennies and Boilers, Irrespective of Use; Stone Spreader; Tamping Machines, Vibrating Ride On; Temporary Heating Plant (nelson or Other Type, Including Propane, Natural Gas or Flow Type Units); Water and Sprinkler Trucks (Used On Job Site In Conduction with Job Site); Welding Machines-Within 100 ft (Gas, and /or Electric Converters of any type, single, tow or three in a battery). welding system, multiple (rectifier transformer type) well point systems (including installation by bull gang and maintenance of); Off Road back dumps.

GROUP 5: Oiler

GROUP 6: Helicopter Pilot

a. PAID HOLIDAYS: New Years Day, Washington's Birthday Memorial Day, July 4th, Labor Day, Veteran's Day, Election Day, Thanksgiving Day, and Christmas Day, provided the employee works one day during the calendar week in which the holiday occurs.

ENGI0825-008 07/01/2024

ORANGE, ULSTER AND SULLIVAN COUNTIES

	Rates	Fringes
Power equipment operators:		
BUILDING CONSTRUCTION		
STEEL ERECTION		
GROUP 1.....	\$ 68.99	36.25
GROUP 2.....	\$ 67.33	36.25
GROUP 3.....	\$ 60.04	36.25
GROUP 4.....	\$ 57.38	36.25
GROUP 5.....	\$ 55.85	36.25
GROUP 6.....	\$ 52.09	36.25

GROUP 7.....	\$ 64.49	36.25
BUILDING CONSTRUCTION TANK ERECTION		
GROUP 1.....	\$ 68.71	36.25
GROUP 2.....	\$ 67.12	36.25
GROUP 3.....	\$ 63.60	36.25
GROUP 4.....	\$ 60.03	36.25
GROUP 5.....	\$ 52.82	36.25
OILOSTATIC MAINLINES AND TRANSPORTATION PIPE LINES		
GROUP 1.....	\$ 61.10	36.25
GROUP 2.....	\$ 59.45	36.25
GROUP 3.....	\$ 57.31	36.25
GROUP 4.....	\$ 55.81	36.25
GROUP 5.....	\$ 52.09	36.25
GROUP 6.....	\$ 63.03	36.25

NOTES:

Hydrographic Premium	50	
Hazmat Premium	20%	
Tunnel Premium	.75	

STEEL ERECTION CLASSIFICATIONS

GROUP 1: Cranes (All Cranes, Land or Floating with Booms Including Jib 140 ft and over, Above Ground); Derricks, Land, Floating or Chicago Boom Type with Booms including Jib 140 ft and over above ground).

GROUP 2: Cranes (All Cranes, Land or Floating with Booms Including Jib Less Than 140 ft Above Ground); Derricks, Land, Floating or Chicago Boom Type with Booms Including Jib Less Than 140 ft above Ground).

GROUP 3: ""A"" Frame, Cherry Pickers 10 tons and under, Hoists Shall Also Include Steam, Gas, Desel, Electric, Air Hydraulic, Single and Double Drum Concrete, Brick Shaft Caisson, or Any Other Similar Type Hoisting Machines, Portable or Stationary, Except Chicago Boom Type; Jacks: Screw Air Hydraulic Power Operated unit or Console Type (not hand Jack or Pile Load Test Type); Side Booms.

GROUP 4: Aerial Platform used as Hoist; Compressor: 2 or 3 in Battery; Elevators or House Cars; Conveyors and Tugger Hosits; Chief of Party; Firemanp; Forklift; Generators (2 or 3); Maintenance (Utility Man); Rod Bending Machine (power); Welding Machines (Gas or Electric, 2 or 3 in Battery, Including Diesels); Captain: Power Boats: Tug Master: Power Boats.

GROUP 5: Compressor, Single; Welding Machine, Single, Gas, Diesel, and Electric Converters of any Type: Welding System Multiple (Rectifier Transformer Type); Generator, Single.

GROUP 6: Oiler

GROUP 7: Helicopter Pilot .

FOOTNOTE: a. PAID HOLIDAYS: New Years Day, Washington's Birthday, Memorial Day, Independence Day, Labor Day, Veteran's Day, Election Day, Thanksgiving Day, and Christmas Day, provided the employee works one day in the calendar week during which the holiday occurs.

For BUILDING CONSTRUCTION TANK ERECTION CLASSIFICATIONS

NOTES: Tunnel Premium	.75
Hazmat Premium	20%
Hydrographic Premium	.50

TANK ERECTION CLASSIFICATIONS

GROUP 1: Operating Engineers on all Cranes, Derricks, ets with Booms Including Jib 140 ft or More Above Ground.

GROUP 2: Operating Engineer on all Equipment, Including Cranes, Derricks, ets with Booms Including Jib, Less Than 140 ft above the ground.

GROUP 3: Helicopter Pilot Engineer.

GROUP 4: Air Compressors, Welding Machines and Generators are Covered and are Defined as Cover: Gas, Diesel, or Electric Driven Equipment and Sources of Power from a Permanent Plant: ie: Staem, Comgressed Air, Hydraulic or Other Power, For The Operating of any Machine or Automatic Tools, Used In The Erection, Alteration, Repair and Dismantling of Tanks and Any and All ""Dual Purpose"" Trucks Used On The Construction Job Site, or in the Loading and Unloading of Materials, at the Construction Job Sited or in Conjunction with the Job Site.

GROUP 5: Oiler

FOOTNOTE:

a. PAID HOLIDAYS: New Years Day, Washington's Birthday, Memorial Day, Independence Day, Labor Day, Veteran's Day, Election Day, Thanksgiving Day, and Christmas Day provided the Employee works one day in the calendar week during which the holiday occurs

For OILOSTATIC MAINLINES AND TRANSPORTATION PIPE LINE CLASSIFICATIONS

NØTES:	
Hydrographic Premium	.50
Hazmat Premium	20%
Tunnel Premium	.75

OILSTATIC MAINLINES AND TRANSPORTATION PIPE LINES CLASSIFICATIONS

GROUP 1: Backhoe; Cranes (all types); Draglines, Front End Loaders (5yds. and over), Gradalls, Helicopters (co-pilot), Helicopters (Communication Engineer); Scooper (Loader and Shovel) Koehring; Trench Machines.

GROUP 2: ""A"" Frame; Backhoe (Combination Hoe Loader); Boring and Drilling Machines; Ditching Machines, Small, Ditchwitch, Vermeer or Similar type; Forklifts; Front End Loaders 92 yds. and over but less than 5 yds.); Graders, Finish (fine); Hydraulic Cranes 10 tons and under (over 10 tons) Cranes Rate Applies); Side Booms: Winch Trucks (Hoisting).

GROUP 3: Backfiller; Brooms and Sweepers; Bulldozers; Compressor (2 or 3 in battery); Chief of Party; Front End Loaders (under 2 yds); Generators; Giraffe Grinders; Graders and Motor Patrols; Machnic; Pipe Bending Machine (power);Tractors; Water and Sprinkler Trucks used on Job Site or in Conduction with Job Site); Welder and Repair Mechanic; Captain (power boats); Tug Master (power boats).

GROUP 4: Compressor (single); Dope Pots (Mechanical with or without Pump); Dust Collectors; Pumps (4 inch suction and over); Pumps (2 of less than 4 inche suction); Pumps, Diesel Engine and Hydraulic (immaterial of power); Welding Machines, Gas or Electric Converters of any type- 2 or 3 in Battery Mulptle Welders; Well Point Systems (including installation and Maintenance); Fram Tractors.

GROUP 5: Oiler, grease, gas, fuel and oil supply trucks; Tire repair and maintenance

GROUP 6: Helicopter Pilot

FOOTNOTE:

a. Paid Holidays: New Years Day, Washington's Birthday, Memorial Day, Independence Day, Labor Day, Veteran's Day, Election Day, Thanksgiving Day and Christmas Day provided the Employee works one day in calendar week during which the holidays occurs.

IRON0417-001 07/01/2024

	Rates	Fringes
IRONWORKER.....	\$ 42.38	47.70+a

a) Paid Holidays: New Year's Day, Memorial Day, Fourth of July, Labor Day, Thanksgiving Day, Day after Thanksgiving (unpaid), Christmas Day.

LAB00017-002 06/01/2023

	Rates	Fringes
LABORER		
DUTCHESS COUNTY (Asbestos, lead, toxic and hazardous waste abatement and any other environmental related work): (BUILDING CONSTRUCTION)		
GROUP 1.....	\$ 35.95	27.15
GROUP 2.....	\$ 37.75	27.15
DUTCHESS COUNTY (Asbestos, lead, toxic and hazardous waste abatement and any other environmental related work): (HEAVY & HIGHWAY:)		
GROUP 2.....	\$ 44.80	32.45+a
GROUP 3.....	\$ 49.40	32.45+a
ORANGE AND ULSTER COUNTIES (BUILDING CONSTRUCTION:)		
GROUP 1.....	\$ 35.95	27.15

GROUP 2.....	\$ 37.75	27.15
GROUP 3.....	\$ 40.50	27.15
ORANGE, ULSTER, AND SULLIVAN COUNTIES (HEAVY & HIGHWAY)		
GROUP 1.....	\$ 40.80	32.45+a
GROUP 2.....	\$ 44.80	32.45+a
GROUP 3.....	\$ 49.40	32.45+a
GROUP 4.....	\$ 54.70	32.45+a
TUNNEL, SHAFT & CAISSON WORK		
GROUP 1.....	\$ 48.05	29.50+a

LABORERS BUILDING CLASSIFICATIONS

GROUP 1: Custodial work, flag person, portable generator tender, portable pump tender, pitman and dumpman, firewatch, temporary heat tender, temporary light tender, traffic control, tool room tender; Artificial turf, air chipping hammer acoustic pump and mixer, carpenter tender, concrete, concrete curb and sidewalk form setter, concrete form stripping, concrete sealing, concrete curing, concrete finisher, concrete vibrator, compressor, clean up after trades, dismantling demolition, excavation, fireproofing, foundation and building piping, pump and mixer, gunite, general clean up, grade checker, grading and backfilling, hoists, hod carrier, landscaping, mason tender, multi building trades tender, jackhammer, pavement breaker, poured gypsum roof work, power tampers, power walk behind roller, pressure blasting, power mixer, scaffolding, snow removal, signal person, sandblasting, styrofoam and similar installation, radio control equipment including but not limited to radio control tampers and rollers, radio control excavator, all erecting and dismantling of scaffold for masonry regardless of height, walking and riding power buggies, temporary weather protection, wrecking, waterproofing, stone and tile tenders, radio controlled hammers and breakers, unloading of trucks, air track, assembling and placing gabion baskets, asphalt, blaster, bob cat type machine for demo and clean up, chain link fence, chain saw, chipping hammer, concrete conveyor belt, saw, core drill, corrugated pipe, construction specialist, cleaning machine, concrete form setter, conduit layer, cutting torch, discharge pipe, drill chuck tender, duct bank layer, explosive handler, hydraulic splitter, granite or stone curbing, handler, joy and jib drill, Ingersoll Rand heavy duty crawler master type HCMZ drill machines or equivalent, laser level, nonmetallic pipe layer, metallic pipe layer, LeRoi hydraulic drill or similar, mega mixer, power fork lift, prestressed and precast concrete, power brush cutter, pump crete machine, retaining walls, rip rap, retention and toxic and hazardous waste liners, setting of block, setting of block, setting of brick, setting of stone, sound barriers, transit under laborers jurisdiction, tow behind concrete or grout pump, traffic and pedestrian stripping, surface planner, manufactured curb, walk behind durface planner, wagon drill, welding; * asbestos abatement work, lead abatement work, toxic and hazardous waste related work; when protective equipment and clothing are not required.

GROUP 2: Forklift for masonry purposes

GROUP 3: Asbestos Abatement work, toxic and hazardous abatement, lead abatement work, environmental work.

BUILDING CLASSIFICATIONS

GROUP 1: Asbestos abatement work, lead abatement work, toxic and hazardous waste related work; when protective equipment and clothing are not required.

GROUP 2: Asbestos abatement work, toxic and hazardous abatement, lead abatement work, environmental work.

LABORERS HEAVY AND HIGHWAY CLASSIFICATIONS

GROUP 1: Flagperson, gateperson

GROUP 2: General laborers, chuck tender, handling and distributing drinking water, distributing all tools and supplies of laborers, nipper, powder carrier, magazine tender, warehouse laborers, concrete man, vibrator man, mason tender, mortar man, spraying, brushing and covering of concrete for curing and preservative purposes, traffic striping, scaffold builder, concrete curb and sidewalk form setter; permanent traffic striping and reflective devices, placing and maintenance of all flares, cones, lights, signs, barricades, traffic patterns, and all temporary reflective type materials for traffic control, custodial work, traffic directors, temporary heat or light tenders, tool room, dewatering pump men, pitman, dumpmen, snow removal and firewatch, asphalt man, joint setter, signal person, pipelayer, pipelining and relining, wellpoints, conduit and duct layer, wire puller rip rap and dry stone layer, steel rod carrier, core drill, rock splitter, Hilti gun air or electric, jackhammer, bush hammer, pavement breaker, chipping hammer, wagon drill, air track, jib rig, joy drill, gunite and sand blasting, coal passer and other machine operators, power tool operator, sprayer and nozzle man on mulching and seeding machine, all guard rail and fence, all seeding and sod laying, all landscape work, grade checker, all bridge work, walk behind self-propelled power saw, grinder, groover or similar type machine, walk behind tamper and roller of all types, salvage, stripping, wrecking and dismantling laborer (including barman, cutting torch and burner man), sheeting and shoring coming under laborers

jurisdiction, bit grinder, operator of form pin puller and drivers, sandblasting, joint and jet sealer, filling and wiring baskets for gabion walls, permanent sign man, median barrier,

sta-wall or similar type product, chain saw operator, railroad track laborer, waterproofer, pre-stressed and pre-cast concrete brick, block and stone pavers, power tools used to perform work usually done by laborers, power buggy and pumpcrete operator, fireproof, plaster and acoustic pump, asbestos, toxic, bio-remediation, phyto-remediation, lead or hazardous materials abatement when protective clothing and equipment is not required, power brush cutter, retention liners, artificial turf, retaining walls, walk behind surface planer, welding related to laborers work, remote controlled equipment normally operated by laborers, all technician work including but not limited to stitching, seaming, heat welding, fireproof sprayer, mortar mixer, concrete finisher, form setter for concrete curbs and flatwork. Gunite nozzle man, stone cutters, granite stone layer, manhole, catch basin or inlet installing, laser men. Ground man on milling machine.

GROUP 3: Ingersoll Rand eavy duty crawler master type HCMZ any drill using 4"" or larger bit, asbestos, toxic, bio-remediation, phyto-remediation, lead or hazardous material abatement when protective clothing and equipment is required, all working foremen including grade, pipe, concrete, clearing, blacktop, drill, paving and blaster etc., Hydraulic drill or similar, forklift for masonry only, Blaster and asphalt screedman.

GROUP 4: Asbestos, toxic, lead or hazardous material abatement foreman.

HEAVY & HIGHWAY CLASSIFICATIONS

GROUP 1: Asbestos, toxic, bio-remediation, phyto-remediation, lead or hazardous material abatement; when protective equipment and clothing are not required.

GROUP 2: Asbestos toxic, bio-remediation, phyto-remediation, lead or hazardous material abatement when protective clothing and equipment is required.

FOOTNOTE:

PAID HOLIDAYS: New Years Day, Presidents's Day, Memorial Day, Independence Day, Labor Day, Election Day, Veterans Day, Thanksgiving Day, Christmas Day

TUNNEL, SHAFT & CASSION CLASSIFICATIONS

GROUP 1: Laborer, Pit and Dumpman, Chuck Tender, Brakeman and Powder; Miner and all mavhine men, Safety Miner, all shaft work, casson work, drilling, blow pipe, all air tools, tugger scaling, nipper gunniting srom pot to nozzle, bit grinder, singal man (top and bottom), shift steward, concrete man, shield driven tunnel, mixed face and soft ground liner plate tunnel in free air.

LAB00235-003 05/01/2016

DUTCHESS COUNTY

	Rates	Fringes
--	-------	---------

Laborers:

BUILDING CONSTRUCTION

GROUP 1.....	\$ 33.30	26.25
GROUP 2.....	\$ 33.30	26.25
GROUP 3.....	\$ 33.30	26.25

LABORERS CLASSIFICATIONS (BUILDING)

GROUP 1: Mason tenders, carpenter tenders, laborer stripping and cleaning forms, laborer grading and digging ditches, sweepers, cleaners.

GROUP 2: Hod carriers, plasterers' tenders, scaffold builders (padlock and self-supporting scaffold 14 ft. or under all runways, mortar mixers) machine and hand, concrete mixers by machine under 21e, vibrators, form setters, asphalt rakers, handling reinforcement rods, drillers, jackhammer, operator, signalman, gunniting, motorbugs, water pump 2"" or under barco machine, wreckers,

paving breakers, power saw operators, other machine operators.

GROUP 3: Blasters, Laser beam operator.

LAB00235-005 05/01/2023

DUTCHESS COUNTY

	Rates	Fringes
Laborers:		
HEAVY & HIGHWAY		
GROUP 1.....	\$ 36.45	27.80+a
GROUP 2.....	\$ 42.80	27.80+a
GROUP 3.....	\$ 43.90	27.80+a

LABORERS CLASSIFICATIONS (HEAVY & HIGHWAY)

GROUP 1: Flagperson, placing and maintenance of all flares, cones, light, signs, barricades, traffic control, custodial work, traffic directors, temporary heat or light tenders, tool rooms.

GROUP 2: General Laborers, Dumpman, Pitman, Concrete Man, Signal Man, Pipelayer, Rip Rap, Dry Stone Layer, Jackhammer, Powderman, Highscalers, Power Buggy Operator, Steel Rod Carrier, Vibratory Operator, Other Machine Operator, Wrecking, Vibrator Operator-Compactor, Guniting and Sand Blasting, Water Pump 2" or under, Nipper, Chucker, Asphalt Workers.

GROUP 3: Asphalt Raker, Asphalt Screener, Drillers (all), Laser Beam Operator, Form Setter/Aligners, Blasters.

FOOTNOTE:

a. PAID HOLIDAYS: New Year's Day, Lincoln's Birthday, Good Friday, Washington's Birthday, November Election Day, Memorial Day, Independence Day, Labor Day, Columbus Day, Thanksgiving Day and Christmas Day and Veteran's Day.

PAIN0009-004 05/01/2024

DUTCHESS, ORANGE, SULLIVAN and ULSTER COUNTIES

	Rates	Fringes
GLAZIER.....	\$ 49.00	55.75

PAIN0155-003 05/01/2021

	Rates	Fringes
Painters:		
Drywall Finishers.....	\$ 35.94	24.66
Lead Abatement Work.....	\$ 35.94	24.66
Painter/Paperhanger.....	\$ 35.94	24.66
Spray Rate.....	\$ 36.94	24.66

PAIN0806-008 10/01/2024

DUTCHESS, ORANGE, SULLIVAN AND ULSTER COUNTIES

	Rates	Fringes
PAINTER		
Structural steel and Bridge.	\$ 56.25	55.14

PLUM0021-005	05/01/2024	

ZONE 2

DUTCHESS COUNTY AND THE REMAINDER OF ULSTER COUNTY

	Rates	Fringes
PLUMBER/PIPEFITTER.....	\$ 59.35	43.61

PLUM0373-002	05/01/2024	

ORANGE COUNTY Towns of Lakeville, Four Corners, Sterling Forest, Tuxedo Park, Southfields, Arden, Newburgh Junction, Greenwood Lake, Monroe, Harriman, Woodbury Falls, Woodbury, Woodbury Station, Central Valley, and the Palisades Interstate Park and Bear Mountain Park

	Rates	Fringes
Plumber; Steamfitter.....	\$ 51.20	45.57
REFRIGERATION MECHANIC.....	\$ 40.09	36.42

PLUM0373-003	05/01/2024	

SULLIVAN COUNTY (Townships of Lumberland, Forestburgh, Highland, Tusten, Mamakating, Fallsburgh, Thompson, Bethel, Cohecton, Delaware, Freemont, Callicoon, Liberty, Monticello, Neversink and Rockland); ORANGE COUNTY (Remaining Townships) and ULSTER COUNTY (Towns of Shawangurk, Wawarsing, Plattekill, Marlboro and Ellenville up to Napanoch Prison)

	Rates	Fringes
Plumber; Steamfitter.....	\$ 51.20	45.57

ROOF0008-002	05/01/2024	

	Rates	Fringes
ROOFER.....	\$ 48.50	38.87

SFNY0669-002	04/01/2024	

	Rates	Fringes
SPRINKLER FITTER.....	\$ 53.34	30.77

SHEE0038-001	07/01/2024	

	Rates	Fringes
Sheet metal worker.....	\$ 53.22	46.20

TEAM0445-001	05/01/2024	

	Rates	Fringes
--	-------	---------

Truck drivers:

GROUP 1.....	\$ 36.32	45.14+a
GROUP 1A.....	\$ 37.44	45.14+a
GROUP 2.....	\$ 37.44	45.14+a
GROUP 3.....	\$ 35.54	45.14+a
GROUP 4.....	\$ 35.43	45.14+a
GROUP 5.....	\$ 35.31	45.14+a

FOOTNOTE:

a. PAID HOLIDAYS: New Year's Day, Labor Day, President's Day, Presidential Election Day, Veterans Day, Decoration Day, Independence Day, Thanksgiving Day and Christmas Day provided the employee works two days in any calendar week during which the holidays occurs.

TRUCK DRIVER CLASSIFICATIONS

GROUP 1: Drivers on Letourneau tractors, double barrel euclids, Athey wagons and similar equipment (except when hooked to scrapers), I-beam and pole trailers, drivers of road oil distributors, tire trucks and tractors and trailers with 5 axles and over, Articulated Back Dumps and Articulated Water Trucks.

GROUP 1A: Drivers on detachable Gooseneck Low bed Trailers rated over 35 tons.

GROUP 2: Drivers on all equipment 25 yards and over, up to and including 30 yard bodies and cable dump trailers and powder and dynamite trucks.

GROUP 3: Drivers on all equipment up to and including 24 yard bodies, mixer trucks, dump crete trucks and similar types of equipment, fuel trucks, batch trucks and all other tractor trailers.

GROUP 4: Drivers on tri axles, ten-wheelers, grease trucks and tillermen.

GROUP 5: Drivers on pick-up trucks used for materials & parts, drivers on escort man over-the-road and drivers on straight trucks.

WELDERS - Receive rate prescribed for craft performing operation to which welding is incidental.

=====
Note: Executive Order (EO) 13706, Establishing Paid Sick Leave for Federal Contractors applies to all contracts subject to the Davis-Bacon Act for which the contract is awarded (and any solicitation was issued) on or after January 1, 2017. If this contract is covered by the EO, the contractor must provide employees with 1 hour of paid sick leave for every 30 hours they work, up to 56 hours of paid sick leave each year. Employees must be permitted to use paid sick leave for their own illness, injury or other health-related needs, including preventive care; to assist a family member (or person who is like family to the employee) who is ill, injured, or has other health-related needs, including preventive care; or for reasons resulting from, or to assist a family member (or person who is like family to the employee) who is a victim of, domestic

violence, sexual assault, or stalking. Additional information on contractor requirements and worker protections under the EO is available at <https://www.dol.gov/agencies/whd/government-contracts>.

Unlisted classifications needed for work not included within the scope of the classifications listed may be added after award only as provided in the labor standards contract clauses (29CFR 5.5 (a) (1) (iii)).

The body of each wage determination lists the classifications and wage rates that have been found to be prevailing for the type(s) of construction and geographic area covered by the wage determination. The classifications are listed in alphabetical order under rate identifiers indicating whether the particular rate is a union rate (current union negotiated rate), a survey rate, a weighted union average rate, a state adopted rate, or a supplemental classification rate.

Union Rate Identifiers

A four-letter identifier beginning with characters other than ""SU"", ""UAVG"", ?SA?, or ?SC? denotes that a union rate was prevailing for that classification in the survey. Example: PLUM0198-005 07/01/2024. PLUM is an identifier of the union whose collectively bargained rate prevailed in the survey for this classification, which in this example would be Plumbers. 0198 indicates the local union number or district council number where applicable, i.e., Plumbers Local 0198. The next number, 005 in the example, is an internal number used in processing the wage determination. The date, 07/01/2024 in the example, is the effective date of the most current negotiated rate.

Union prevailing wage rates are updated to reflect all changes over time that are reported to WHD in the rates in the collective bargaining agreement (CBA) governing the classification.

Union Average Rate Identifiers

The UAVG identifier indicates that no single rate prevailed for those classifications, but that 100% of the data reported for the classifications reflected union rates. EXAMPLE: UAVG-OH-0010 01/01/2024. UAVG indicates that the rate is a weighted union average rate. OH indicates the State of Ohio. The next number, 0010 in the example, is an internal number used in producing the wage determination. The date, 01/01/2024 in the example, indicates the date the wage determination was updated to reflect the most current union average rate.

A UAVG rate will be updated once a year, usually in January, to reflect a weighted average of the current rates in the collective bargaining agreements on which the rate is based.

Survey Rate Identifiers

The ""SU"" identifier indicates that either a single non-union rate prevailed (as defined in 29 CFR 1.2) for this classification in the survey or that the rate was derived by computing a weighted average rate based on all the rates reported in the survey for that classification. As a weighted

average rate includes all rates reported in the survey, it may include both union and non-union rates. Example: SUFL2022-007 6/27/2024. SU indicates the rate is a single non-union prevailing rate or a weighted average of survey data for that classification. FL indicates the State of Florida. 2022 is the year of the survey on which these classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 6/27/2024 in the example, indicates the survey completion date for the classifications and rates under that identifier.

?SU? wage rates typically remain in effect until a new survey is conducted. However, the Wage and Hour Division (WHD) has the discretion to update such rates under 29 CFR 1.6(c)(1).

State Adopted Rate Identifiers

The ""SA"" identifier indicates that the classifications and prevailing wage rates set by a state (or local) government were adopted under 29 C.F.R 1.3(g)-(h). Example: SAME2023-007 01/03/2024. SA reflects that the rates are state adopted. ME refers to the State of Maine. 2023 is the year during which the state completed the survey on which the listed classifications and rates are based. The next number, 007 in the example, is an internal number used in producing the wage determination. The date, 01/03/2024 in the example, reflects the date on which the classifications and rates under the ?SA? identifier took effect under state law in the state from which the rates were adopted.

WAGE DETERMINATION APPEALS PROCESS

1) Has there been an initial decision in the matter? This can be:

- a) a survey underlying a wage determination
- b) an existing published wage determination
- c) an initial WHD letter setting forth a position on a wage determination matter
- d) an initial conformance (additional classification and rate) determination

On survey related matters, initial contact, including requests for summaries of surveys, should be directed to the WHD Branch of Wage Surveys. Requests can be submitted via email to davisbaconinfo@dol.gov or by mail to:

Branch of Wage Surveys
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

Regarding any other wage determination matter such as conformance decisions, requests for initial decisions should be directed to the WHD Branch of Construction Wage Determinations. Requests can be submitted via email to BCWD-Office@dol.gov or by mail to:

Branch of Construction Wage Determinations
Wage and Hour Division
U.S. Department of Labor
200 Constitution Avenue, N.W.

Washington, DC 20210

2) If an initial decision has been issued, then any interested party (those affected by the action) that disagrees with the decision can request review and reconsideration from the Wage and Hour Administrator (See 29 CFR Part 1.8 and 29 CFR Part 7). Requests for review and reconsideration can be submitted via email to dba.reconsideration@dol.gov or by mail to:

Wage and Hour Administrator
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210

The request should be accompanied by a full statement of the interested party's position and any information (wage payment data, project description, area practice material, etc.) that the requestor considers relevant to the issue.

3) If the decision of the Administrator is not favorable, an interested party may appeal directly to the Administrative Review Board (formerly the Wage Appeals Board). Write to:

Administrative Review Board
U.S. Department of Labor
200 Constitution Avenue, N.W.
Washington, DC 20210.

=====
END OF GENERAL DECISION"

PERFORMANCE BOND

Contractor Name: _____ Address <i>(principal place of business)</i> : _____	Surety Name: _____ Address <i>(principal place of business)</i> : _____
Owner Name: _____ Mailing address <i>(principal place of business)</i> : _____	Contract Description <i>(name and location)</i> : _____ Contract Price: _____ Effective Date of Contract: _____
Bond Bond Amount: _____ Date of Bond: _____ <i>(Date of Bond cannot be earlier than Effective Date of Contract)</i> Modifications to this Bond form: ☐ None ☐ See Paragraph 16	
Surety and Contractor, intending to be legally bound hereby, subject to the terms set forth in this Performance Bond, do each cause this Performance Bond to be duly executed by an authorized officer, agent, or representative.	
Contractor as Principal	Surety
_____ <i>(Full formal name of Contractor)</i>	_____ <i>(Full formal name of Surety) (corporate seal)</i>
By: _____ <i>(Signature)</i>	By: _____ <i>(Signature)(Attach Power of Attorney)</i>
Name: _____ <i>(Printed or typed)</i>	Name: _____ <i>(Printed or typed)</i>
Title: _____	Title: _____
Attest: _____ <i>(Signature)</i>	Attest: _____ <i>(Signature)</i>
Name: _____ <i>(Printed or typed)</i>	Name: _____ <i>(Printed or typed)</i>
Title: _____	Title: _____
<i>Notes: (1) Provide supplemental execution by any additional parties, such as joint venturers. (2) Any singular reference to Contractor, Surety, Owner, or other party is considered plural where applicable.</i>	

1. The Contractor and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to the Owner for the performance of the Construction Contract, which is incorporated herein by reference.
2. If the Contractor performs the Construction Contract, the Surety and the Contractor shall have no obligation under this Bond, except when applicable to participate in a conference as provided in Paragraph 3.
3. If there is no Owner Default under the Construction Contract, the Surety's obligation under this Bond will arise after:
 - 3.1. The Owner first provides notice to the Contractor and the Surety that the Owner is considering declaring a Contractor Default. Such notice may indicate whether the Owner is requesting a conference among the Owner, Contractor, and Surety to discuss the Contractor's performance. If the Owner does not request a conference, the Surety may, within five (5) business days after receipt of the Owner's notice, request such a conference. If the Surety timely requests a conference, the Owner shall attend. Unless the Owner agrees otherwise, any conference requested under this Paragraph 3.1 will be held within ten (10) business days of the Surety's receipt of the Owner's notice. If the Owner, the Contractor, and the Surety agree, the Contractor shall be allowed a reasonable time to perform the Construction Contract, but such an agreement does not waive the Owner's right, if any, subsequently to declare a Contractor Default;
 - 3.2. The Owner declares a Contractor Default, terminates the Construction Contract and notifies the Surety; and
 - 3.3. The Owner has agreed to pay the Balance of the Contract Price in accordance with the terms of the Construction Contract to the Surety or to a contractor selected to perform the Construction Contract.
4. Failure on the part of the Owner to comply with the notice requirement in Paragraph 3.1 does not constitute a failure to comply with a condition precedent to the Surety's obligations, or release the Surety from its obligations, except to the extent the Surety demonstrates actual prejudice.
5. When the Owner has satisfied the conditions of Paragraph 3, the Surety shall promptly and at the Surety's expense take one of the following actions:
 - 5.1. Arrange for the Contractor, with the consent of the Owner, to perform and complete the Construction Contract;
 - 5.2. Undertake to perform and complete the Construction Contract itself, through its agents or independent contractors;
 - 5.3. Obtain bids or negotiated proposals from qualified contractors acceptable to the Owner for a contract for performance and completion of the Construction Contract, arrange for a contract to be prepared for execution by the Owner and a contractor selected with the Owners concurrence, to be secured with performance and payment bonds executed by a qualified surety equivalent to the bonds issued on the Construction Contract, and pay to the Owner the amount of damages as described in Paragraph 7 in excess of the Balance of the Contract Price incurred by the Owner as a result of the Contractor Default; or
 - 5.4. Waive its right to perform and complete, arrange for completion, or obtain a new contractor, and with reasonable promptness under the circumstances:

- 5.4.1 After investigation, determine the amount for which it may be liable to the Owner and, as soon as practicable after the amount is determined, make payment to the Owner; or
 - 5.4.2 Deny liability in whole or in part and notify the Owner, citing the reasons for denial.
- 6. If the Surety does not proceed as provided in Paragraph 5 with reasonable promptness, the Surety shall be deemed to be in default on this Bond seven days after receipt of an additional written notice from the Owner to the Surety demanding that the Surety perform its obligations under this Bond, and the Owner shall be entitled to enforce any remedy available to the Owner. If the Surety proceeds as provided in Paragraph 5.4, and the Owner refuses the payment, or the Surety has denied liability, in whole or in part, without further notice, the Owner shall be entitled to enforce any remedy available to the Owner.
- 7. If the Surety elects to act under Paragraph 5.1, 5.2, or 5.3, then the responsibilities of the Surety to the Owner will not be greater than those of the Contractor under the Construction Contract, and the responsibilities of the Owner to the Surety will not be greater than those of the Owner under the Construction Contract. Subject to the commitment by the Owner to pay the Balance of the Contract Price, the Surety is obligated, without duplication for:
 - 7.1. the responsibilities of the Contractor for correction of defective work and completion of the Construction Contract;
 - 7.2. additional legal, design professional, and delay costs resulting from the Contractor's Default, and resulting from the actions or failure to act of the Surety under Paragraph 5; and
 - 7.3. liquidated damages, or if no liquidated damages are specified in the Construction Contract, actual damages caused by delayed performance or non-performance of the Contractor.
- 8. If the Surety elects to act under Paragraph 5.1, 5.3, or 5.4, the Surety's liability is limited to the amount of this Bond.
- 9. The Surety shall not be liable to the Owner or others for obligations of the Contractor that are unrelated to the Construction Contract, and the Balance of the Contract Price will not be reduced or set off on account of any such unrelated obligations. No right of action will accrue on this Bond to any person or entity other than the Owner or its heirs, executors, administrators, successors, and assigns.
- 10. The Surety hereby waives notice of any change, including changes of time, to the Construction Contract or to related subcontracts, purchase orders, and other obligations.
- 11. Any proceeding, legal or equitable, under this Bond must be instituted in any court of competent jurisdiction in the location in which the work or part of the work is located and must be instituted within two years after a declaration of Contractor Default or within two years after the Contractor ceased working or within two years after the Surety refuses or fails to perform its obligations under this Bond, whichever occurs first. If the provisions of this paragraph are void or prohibited by law, the minimum periods of limitations available to sureties as a defense in the jurisdiction of the suit will be applicable.
- 12. Notice to the Surety, the Owner, or the Contractor must be mailed or delivered to the address shown on the page on which their signature appears.
- 13. When this Bond has been furnished to comply with a statutory or other legal requirement in the location where the construction was to be performed, any provision in this Bond conflicting with said statutory or legal requirement will be deemed deleted therefrom and provisions conforming to such

statutory or other legal requirement will be deemed incorporated herein. When so furnished, the intent is that this Bond will be construed as a statutory bond and not as a common law bond.

14. Definitions

- 14.1. *Balance of the Contract Price*—The total amount payable by the Owner to the Contractor under the Construction Contract after all proper adjustments have been made including allowance for the Contractor for any amounts received or to be received by the Owner in settlement of insurance or other claims for damages to which the Contractor is entitled, reduced by all valid and proper payments made to or on behalf of the Contractor under the Construction Contract.
 - 14.2. *Construction Contract*—The agreement between the Owner and Contractor identified on the cover page, including all Contract Documents and changes made to the agreement and the Contract Documents.
 - 14.3. *Contractor Default*—Failure of the Contractor, which has not been remedied or waived, to perform or otherwise to comply with a material term of the Construction Contract.
 - 14.4. *Owner Default*—Failure of the Owner, which has not been remedied or waived, to pay the Contractor as required under the Construction Contract or to perform and complete or comply with the other material terms of the Construction Contract.
 - 14.5. *Contract Documents*—All the documents that comprise the agreement between the Owner and Contractor.
15. If this Bond is issued for an agreement between a contractor and subcontractor, the term Contractor in this Bond will be deemed to be Subcontractor and the term Owner will be deemed to be Contractor.

PAYMENT BOND

Contractor Name: Address <i>(principal place of business)</i> :	Surety Name: Address <i>(principal place of business)</i> :
Owner Name: Mailing address <i>(principal place of business)</i> :	Contract Description <i>(name and location)</i> : Contract Price: Effective Date of Contract:
Bond Bond Amount: Date of Bond: <i>(Date of Bond cannot be earlier than Effective Date of Contract)</i> Modifications to this Bond form: ☐ None ☐ See Paragraph 18	
Surety and Contractor, intending to be legally bound hereby, subject to the terms set forth in this Payment Bond, do each cause this Payment Bond to be duly executed by an authorized officer, agent, or representative.	
Contractor as Principal	Surety
<i>(Full formal name of Contractor)</i>	<i>(Full formal name of Surety) (corporate seal)</i>
By: _____ <i>(Signature)</i>	By: _____ <i>(Signature)(Attach Power of Attorney)</i>
Name: _____ <i>(Printed or typed)</i>	Name: _____ <i>(Printed or typed)</i>
Title: _____	Title: _____
Attest: _____ <i>(Signature)</i>	Attest: _____ <i>(Signature)</i>
Name: _____ <i>(Printed or typed)</i>	Name: _____ <i>(Printed or typed)</i>
Title: _____	Title: _____
<i>Notes: (1) Provide supplemental execution by any additional parties, such as joint venturers. (2) Any singular reference to Contractor, Surety, Owner, or other party is considered plural where applicable.</i>	

1. The Contractor and Surety, jointly and severally, bind themselves, their heirs, executors, administrators, successors, and assigns to the Owner to pay for labor, materials, and equipment furnished for use in the performance of the Construction Contract, which is incorporated herein by reference, subject to the following terms.
2. If the Contractor promptly makes payment of all sums due to Claimants, and defends, indemnifies, and holds harmless the Owner from claims, demands, liens, or suits by any person or entity seeking payment for labor, materials, or equipment furnished for use in the performance of the Construction Contract, then the Surety and the Contractor shall have no obligation under this Bond.
3. If there is no Owner Default under the Construction Contract, the Surety's obligation to the Owner under this Bond will arise after the Owner has promptly notified the Contractor and the Surety (at the address described in Paragraph 13) of claims, demands, liens, or suits against the Owner or the Owner's property by any person or entity seeking payment for labor, materials, or equipment furnished for use in the performance of the Construction Contract, and tendered defense of such claims, demands, liens, or suits to the Contractor and the Surety.
4. When the Owner has satisfied the conditions in Paragraph 3, the Surety shall promptly and at the Surety's expense defend, indemnify, and hold harmless the Owner against a duly tendered claim, demand, lien, or suit.
5. The Surety's obligations to a Claimant under this Bond will arise after the following:
 - 5.1. Claimants who do not have a direct contract with the Contractor
 - 5.1.1. have furnished a written notice of non-payment to the Contractor, stating with substantial accuracy the amount claimed and the name of the party to whom the materials were, or equipment was, furnished or supplied or for whom the labor was done or performed, within ninety (90) days after having last performed labor or last furnished materials or equipment included in the Claim; and
 - 5.1.2. have sent a Claim to the Surety (at the address described in Paragraph 13).
 - 5.2. Claimants who are employed by or have a direct contract with the Contractor have sent a Claim to the Surety (at the address described in Paragraph 13).
6. If a notice of non-payment required by Paragraph 5.1.1 is given by the Owner to the Contractor, that is sufficient to satisfy a Claimant's obligation to furnish a written notice of non-payment under Paragraph 5.1.1.
7. When a Claimant has satisfied the conditions of Paragraph 5.1 or 5.2, whichever is applicable, the Surety shall promptly and at the Surety's expense take the following actions:
 - 7.1. Send an answer to the Claimant, with a copy to the Owner, within sixty (60) days after receipt of the Claim, stating the amounts that are undisputed and the basis for challenging any amounts that are disputed; and
 - 7.2. Pay or arrange for payment of any undisputed amounts.
 - 7.3. The Surety's failure to discharge its obligations under Paragraph 7.1 or 7.2 will not be deemed to constitute a waiver of defenses the Surety or Contractor may have or acquire as to a Claim, except as to undisputed amounts for which the Surety and Claimant have reached agreement. If, however, the Surety fails to discharge its obligations under Paragraph 7.1 or 7.2, the Surety shall indemnify the Claimant for the reasonable attorney's fees the Claimant incurs thereafter to recover any sums found to be due and owing to the Claimant.

8. The Surety's total obligation will not exceed the amount of this Bond, plus the amount of reasonable attorney's fees provided under Paragraph 7.3, and the amount of this Bond will be credited for any payments made in good faith by the Surety.
9. Amounts owed by the Owner to the Contractor under the Construction Contract will be used for the performance of the Construction Contract and to satisfy claims, if any, under any construction performance bond. By the Contractor furnishing and the Owner accepting this Bond, they agree that all funds earned by the Contractor in the performance of the Construction Contract are dedicated to satisfying obligations of the Contractor and Surety under this Bond, subject to the Owner's priority to use the funds for the completion of the work.
10. The Surety shall not be liable to the Owner, Claimants, or others for obligations of the Contractor that are unrelated to the Construction Contract. The Owner shall not be liable for the payment of any costs or expenses of any Claimant under this Bond, and shall have under this Bond no obligation to make payments to or give notice on behalf of Claimants, or otherwise have any obligations to Claimants under this Bond.
11. The Surety hereby waives notice of any change, including changes of time, to the Construction Contract or to related subcontracts, purchase orders, and other obligations.
12. No suit or action will be commenced by a Claimant under this Bond other than in a court of competent jurisdiction in the state in which the project that is the subject of the Construction Contract is located or after the expiration of one year from the date (1) on which the Claimant sent a Claim to the Surety pursuant to Paragraph 5.1.2 or 5.2, or (2) on which the last labor or service was performed by anyone or the last materials or equipment were furnished by anyone under the Construction Contract, whichever of (1) or (2) first occurs. If the provisions of this paragraph are void or prohibited by law, the minimum period of limitation available to sureties as a defense in the jurisdiction of the suit will be applicable.
13. Notice and Claims to the Surety, the Owner, or the Contractor must be mailed or delivered to the address shown on the page on which their signature appears. Actual receipt of notice or Claims, however accomplished, will be sufficient compliance as of the date received.
14. When this Bond has been furnished to comply with a statutory or other legal requirement in the location where the construction was to be performed, any provision in this Bond conflicting with said statutory or legal requirement will be deemed deleted here from and provisions conforming to such statutory or other legal requirement will be deemed incorporated herein. When so furnished, the intent is that this Bond will be construed as a statutory bond and not as a common law bond.
15. Upon requests by any person or entity appearing to be a potential beneficiary of this Bond, the Contractor and Owner shall promptly furnish a copy of this Bond or shall permit a copy to be made.
16. Definitions
 - 16.1. *Claim*—A written statement by the Claimant including at a minimum:
 - 16.1.1. The name of the Claimant;
 - 16.1.2. The name of the person for whom the labor was done, or materials or equipment furnished;
 - 16.1.3. A copy of the agreement or purchase order pursuant to which labor, materials, or equipment was furnished for use in the performance of the Construction Contract;
 - 16.1.4. A brief description of the labor, materials, or equipment furnished;

- 16.1.5. The date on which the Claimant last performed labor or last furnished materials or equipment for use in the performance of the Construction Contract;
- 16.1.6. The total amount earned by the Claimant for labor, materials, or equipment furnished as of the date of the Claim;
- 16.1.7. The total amount of previous payments received by the Claimant; and
- 16.1.8. The total amount due and unpaid to the Claimant for labor, materials, or equipment furnished as of the date of the Claim.
- 16.2. *Claimant*—An individual or entity having a direct contract with the Contractor or with a subcontractor of the Contractor to furnish labor, materials, or equipment for use in the performance of the Construction Contract. The term Claimant also includes any individual or entity that has rightfully asserted a claim under an applicable mechanic's lien or similar statute against the real property upon which the Project is located. The intent of this Bond is to include without limitation in the terms of "labor, materials, or equipment" that part of the water, gas, power, light, heat, oil, gasoline, telephone service, or rental equipment used in the Construction Contract, architectural and engineering services required for performance of the work of the Contractor and the Contractor's subcontractors, and all other items for which a mechanic's lien may be asserted in the jurisdiction where the labor, materials, or equipment were furnished.
- 16.3. *Construction Contract*—The agreement between the Owner and Contractor identified on the cover page, including all Contract Documents and all changes made to the agreement and the Contract Documents.
- 16.4. *Owner Default*—Failure of the Owner, which has not been remedied or waived, to pay the Contractor as required under the Construction Contract or to perform and complete or comply with the other material terms of the Construction Contract.
- 16.5. *Contract Documents*—All the documents that comprise the agreement between the Owner and Contractor.
- 17. If this Bond is issued for an agreement between a contractor and subcontractor, the term Contractor in this Bond will be deemed to be Subcontractor and the term Owner will be deemed to be Contractor.

ATTACHMENT 1

Geotechnical Report

This page intentionally left blank.



PRACTICAL SOLUTIONS. EXCEPTIONAL SERVICE.

GEOTECHNICAL EVALUATION
PROPOSED NEW CULVERT
BALL ROAD
TOWN OF WARWICK, NEW YORK

Submitted To:

Town Of Warwick

132 Kings Highway
Warwick, NY 10990

W.O. 12020.03

December 5, 2023

Submitted By:

**Tectonic Engineering
Consultants, Geologists & Land
Surveyors, D.P.C.**

1279 Route 300, 2nd Floor
Newburgh, NY 12550

(P) 845.567.6656
(F) 845.567.6248

Town Of Warwick
132 Kings Highway
Warwick, NY 10990

Attention: c/o Laura A. Barca - HDR, Inc
Via email (Laura.Barca@hdrinc.com)

December 5, 2023

**RE: W.O. 12020.03
GEOTECHNICAL EVALUATION
PROPOSED NEW CULVERT
BALL ROAD
TOWN OF WARWICK, NEW YORK**

Dear Ms. Barca;

Tectonic Engineering Consultants, Geologists & Land Surveyors, D.P.C. is pleased to submit this subsurface investigation and geotechnical engineering evaluation for the proposed replacement of an existing culvert, located on Ball Road in the Town of Warwick, Orange County, New York. This report presents the scope of the investigation, findings, conclusions, and recommendations for design and construction of the proposed foundations for a replacement culvert.

We appreciate this opportunity to assist you with this project. If you have any questions, please do not hesitate to contact the undersigned.

Sincerely,

TECTONIC ENGINEERING CONSULTANTS, GEOLOGISTS & LAND SURVEYORS, D.P.C.

Christopher Burke, Ph.D., P.E., PMP
Vice President, Geotechnical



"G:\Newburgh\Geotechnical\12000\12020.01 Warwick Culvert\Reports\12020.03 (Ball)\TEC Cover Letter.docx"

Newburgh Office

1279 Route 300 | Newburgh, NY 12550
845.567.6656 Tel | 845.567.6248 Fax

tectonicengineering.com
Equal Opportunity Employer

GEOTECHNICAL EVALUATION
PROPOSED NEW CULVERT
BALL ROAD
TOWN OF WARWICK, NEW YORK

TABLE OF CONTENTS

<u>SECTION</u>	<u>ITEM</u>	<u>PAGE</u>
1.0	INTRODUCTION	1
2.0	SCOPE OF WORK	1
3.0	SITE AND PROJECT DESCRIPTION	1
4.0	SUBSURFACE INVESTIGATION	2
5.0	LABORATORY TESTING	3
6.0	SUBSURFACE CONDITIONS	3
6.1	Embankment Fill	3
6.2	Native Soils	4
6.3	Groundwater	5
7.0	DISCUSSION AND CONCLUSIONS	5
8.0	RECOMMENDATIONS	6
8.1	Shallow Foundations	6
8.2	Design for Lateral Loading	8
8.3	Drainage	9
8.4	Seismic Design and Liquefaction Potential	10
9.0	EARTHWORK AND CONSTRUCTION CRITERIA	10
9.1	General Site Preparation	10
9.2	General Excavation	10
9.3	Foundation Subgrade Preparation	11
9.4	Dewatering and Protection of Subgrades	11
9.5	Culvert Backfill Material and Placement Recommendations	12
10.0	CONSTRUCTION MONITORING	14
11.0	LIMITATIONS	14

FIGURE 1 BORING LOCATION PLAN

APPENDIX I BORING LOGS

APPENDIX II LABORATORY TEST RESULTS

1.0 INTRODUCTION

Tectonic Engineering Consultants, Geologists & Land Surveyors D.P.C. (Tectonic) has performed a subsurface investigation and geotechnical engineering evaluation for the proposed replacement of an existing culvert, located on Ball Road in the Town of Warwick, Orange County, New York. This report presents the scope of the investigation, findings, conclusions, and recommendations for design and construction of the proposed foundations for a replacement culvert.

2.0 SCOPE OF WORK

The geotechnical engineering services described below were performed for the Town of Warwick, herein referred to as the Client, and their Engineer, HDR.

- Performance of two (2) test borings to identify the subsurface conditions near the replacement culvert structure.
- Field inspection of the borings by a Tectonic representative, which included locating the borings, logging the subsurface soil and groundwater conditions, and collecting soil samples for laboratory testing.
- Laboratory testing of representative soil samples to assist in the evaluation of the engineering properties of the encountered soils and verification of the field classifications of soils.
- Geotechnical engineering analysis of the subsurface conditions as related to the design and construction of the replacement culvert foundations and wingwalls.
- Preparation of this engineering report presenting the results of the subsurface investigation and geotechnical recommendations for the design and construction of the foundations for the replacement culvert structure.

3.0 SITE AND PROJECT DESCRIPTION

The project is located on Ball Road, at its intersection with Brady Road and South Street Extension, in the Town of Warwick, Orange County, New York (at Lat. 41.243°, Lon. -74.354°). The existing culvert carries a small tributary to Wawayanda Creek beneath Ball Road, a two-lane asphalt paved roadway. A site survey drawing provided by HDR shows that the existing corrugated metal pipe culvert has dimensions of 68 inches by 72 inches. It is assumed that this is an originally round pipe that has been slightly compressed into a slightly elliptical shape. The survey drawing also shows that the streambed has a maximum elevation of approximately +596 feet on the upstream side of Ball Road, and +592 feet on its downstream side. However, the survey drawing has a contour interval of 2 feet and spot elevations are not shown. Observations made in the field,

indicate that the distance from the road surface to the top of the water in the creek is approximately 7 feet, at either end of the culvert.

Based on the measured depths to the top of the water within the creek, it is anticipated that the new culvert will have foundations ranging from approximately 9 to 14 feet below the road surface, depending upon the type of culvert that will be used and the anticipated scour depth. These depths roughly correspond to anticipated bearing elevations between approximately +586 and +591 feet.

Preliminary information about the proposed culvert was provided at the time of this report. It is our understanding that the Client intends to replace the existing culvert with a precast concrete three-sided, or four-sided culvert at approximately the same location. It is assumed that the culvert would be supported on cast-in-place footings; however precast concrete footings can also be used. It is also assumed that precast wing walls will be installed and they too, may be supported on either cast-in-place or precast footings.

4.0 SUBSURFACE INVESTIGATION

The subsurface investigation consisted of drilling two (2) test borings, designated as B-1 and B-2, in the westbound lane and in the eastbound paved shoulder of Ball Road, approximately 25 to 60 feet from the centerline of the existing culvert, respectively. Note that the geometry of the intersection prevented the drilling crew from safely drilling a boring north of the culvert. See the attached Boring Location Plan, Figure 1, for the approximate boring locations.

The borings were performed by Craig Geotechnical Drilling Company, Inc., on May 12, 2023, utilizing a truck-mounted CME 75 drill rig, equipped with an automatic hammer. The borings were advanced through soil using mud-rotary drilling methods, with a 3⁷/₈-inch diameter tri-cone drill bit and 4-inch inside diameter casing. Standard Penetration Testing (SPT) and split-spoon sampling were generally performed continuously to a depth of 12 feet below existing grade, and at 5-foot intervals, thereafter. The SPT sampling was performed in general accordance with the requirements of ASTM Standard D1586 *“Standard Test Method for Penetration Test and Split-Barrel Sampling of Soils”*. SPT N-values were recorded in the field for each soil sample taken.

Samples of the soil obtained during the investigation were collected and retained in glass jars. All samples are currently stored at our material testing laboratory. Each boring was backfilled with cuttings and the surface was patched to match the existing surface.

A representative of Tectonic observed the subsurface investigation and prepared logs of the subsurface conditions under the purview of a Professional Engineer licensed in New York State. All soils encountered were classified in accordance with the Unified Soil Classification System (ASTM D2488), and the Modified Burmister Soil Classification System. Copies of the boring logs are included in Appendix I.

5.0 LABORATORY TESTING

Laboratory testing was conducted on samples selected to verify the soil descriptions and to assist in identifying the soils' engineering properties. The laboratory testing is summarized in Table 5.1 below.

Table 5.1 Laboratory Tests		
Lab Test Description	ASTM Standard	Quantity
Grain Size Distribution	D6913	3

The results of the laboratory testing have been incorporated into the soil descriptions given below and in the boring logs and are provided in Appendix II of this report.

6.0 SUBSURFACE CONDITIONS

The subsurface conditions encountered at the site generally consist of approximately 1 to 2 inches of asphalt concrete pavement, underlain by embankment fill, and native soils extending to the termination depth of the borings. The following subsections provide generalized descriptions of the encountered soil and groundwater conditions. Detailed descriptions of the subsurface conditions are provided in the boring logs included in Appendix I.

As noted above, an automatic hammer was used in the SPT sampling of the borings. Given that an automatic hammer imparts more energy into the split spoon sampler than a safety hammer (N_{60}) – the standard hammer used for most geotechnical engineering calculations – an energy correction factor of 1.3 is applied to the field N-values to obtain the N_{60} -values.

6.1 Embankment Fill

Borings B-1 and B-2 encountered approximately 2 to 4 feet of embankment fill, with bottom elevations between approximately +597 and +600 feet, respectively. However, because the borings were drilled some distance from the existing culvert, it is expected that the depth of fill will extend to approximately

the existing culvert's foundation depth immediately adjacent to the culvert. The bearing depth of the existing culvert is unknown, but based on the current depth to the water surface within the stream noted above, it can be expected that the fill will extend to roughly 8 or 9 feet below the road surface adjacent to the existing culvert.

The fill can typically be described as brown coarse to fine sand, with 10 to 35 percent coarse to fine gravel, and up to 10 percent silt. The fill soils have a USCS designation of SP.

Field SPT N-values within the fill range from 11 to 25 blows per foot (bpf). When the energy correction for the use of an automatic hammer is applied to the field N-values shown on the boring logs, we find that the N_{60} -values within the fill range from 14 to 33 bpf. These N_{60} -value indicate that the existing fill is in a medium dense to dense condition.

6.2 Native Soils

A review of the Surficial Geology Map of the Lower Hudson Valley and the Quaternary Map of the Northeastern United States shows that glacial till generally exists at the site. Based on our observations of the soil encountered immediately below the fill, the soils appear to match the mapped glacial till. Glacial till is a mixed soil, with a very wide range of particle sizes, spanning from clay to boulders, produced by the continental glacier that covered the area up until some 15,000 years ago.

The native soils tend to range from brown coarse to fine sand, with up to 35 percent coarse fine gravel, and 10 to 45 percent silt near the ground surface; to brown to gray coarse to fine gravel, with up to 45 percent silt and similar percentages of coarse to fine sand at depths greater than approximately 8 to 15 feet (below elevation +593 feet, in boring B-1, and below elevation +587 feet, in boring B-2). It is noted, however, that many of the split spoon samples collected from the borings had low recoveries, indicating that the split spoons often became blocked by gravel. This may have skewed some of the sample descriptions toward the coarser particle sizes. The native soils have USCS designations of SM, GP, GM and occasionally CL-ML. It is also noted that a boulder was encountered in boring B-1, between the depths of 5 and 6.5 feet. These soils were found to extend to the full penetration depth of the borings (32 to 37 feet).

Field SPT N-values within the glacial till range from 10 to greater than 63 bpf, which correlate to N_{60} -values ranging from 13 to greater than 82 bpf. However, four (4) split spoon refusals – defined as less than 6 inches of split spoon refusal after at least 50 blows of the 140-pound hammer – occurred within boring B-1. If these are discounted the maximum field N-value is reduced to 59 bpf, which corresponds to a maximum N_{60} -value of 78 bpf and overall, the native soils have an average N_{60} -value of 39 bpf. These N_{60} -values indicate that the glacial till ranges from medium dense to very dense and is typically dense, on average.

6.3 Groundwater

Saturated soil samples were encountered below a depth of 8 feet in both borings. It is anticipated that the groundwater table at the site reflects the water level within the stream, and therefore, is expected to be at a depth of approximately 7 to 8 feet below the road surface at the culvert. Furthermore, the groundwater depth is expected to fluctuate with season and changing weather conditions, and may fluctuate with the water depth in the stream.

7.0 DISCUSSION AND CONCLUSIONS

The primary geotechnical issues associated with the proposed construction are the proximity to the stream, relatively shallow groundwater, and native soils that may be susceptible to disturbance when wet.

Based on the limited available information, we have estimated that the new culvert's foundations may bear at depths ranging from approximately 9 to 14 feet below the road surface, as noted in Section 3 of this report. It is anticipated that the bearing depth will depend upon the type of structure – four-sided culverts bear just below the streambed, while three-sided culverts should bear below the scour depth, to be determined by others. Recommendations for the design and construction of these foundations is provided in the following section.

Assuming that the new culvert will be constructed to bear at the estimated depths above, it is also expected that the wing walls will retain approximately 9 to 14 feet of soil. If adequate scour protection is not provided, it can be assumed that the walls will need to support more soil. Precast or cast-in-place wing walls should be designed to bear below the scour depth of the creek (to be determined by others). However, the client may also elect to drive sheet piles for the wing walls. Given the density of the soils below a depth of 15 feet, it is anticipated that the sheet piles can be cantilevered, if driven with a sufficiently powerful and heavy vibratory hammer. However, the presence of cobbles and boulders could make driving of some sheet piles difficult.

Other conclusions regarding the investigation and proposed construction follow:

- Excavations into the fill and native soils should be feasible with conventional heavy-duty construction equipment; however, cobbles and boulders will likely be encountered.
- Groundwater will likely be encountered at or slightly above the stream level during foundation excavation. Dewatering of the excavations will be required. It is also expected that cofferdams or a stream diversion will also be required during construction.
- A design groundwater depth of 5 feet (2 feet above the measured depth to the water surface at the time of the investigation) has been used in the analyses leading to the recommendations presented in this report.
- Laboratory testing of the native soils within 10 feet of the ground surface show that their fines contents range from approximately 23 to 43 percent. This indicates that the soils at the site are likely be susceptible to disturbance, when wet. Consequently, subgrade protection, such as crushed stone or a mud mat may be required to prevent weakening of subgrade material during construction. It is also anticipated that dewatering may be difficult, due to the high percentages of silt within the native soils.
- It is not anticipated that the on-site soils will be suitable for select granular fill against precast culvert walls, due to the high fines-contents of the native soil; however, these local soils might be suitable for embankment fill (with adequate moisture control), away from the culvert. If the Client intends to use the on-site soils as embankment fill, bulk samples of the existing embankment materials should be tested to better-evaluate their suitability for abutment backfill during construction. In addition, the specifications should require the contractor to protect stockpiled soils from rain and should note that the contractor may need to dry the soil to achieve compaction and produce a stable embankment.
- It is anticipated that the subsurface soils are unlikely to liquefy based on the relatively high fines contents and density of the glacial till soils.

8.0 RECOMMENDATIONS

The following subsections provide our recommendations for design and construction of the proposed new culvert across the tributary to Wawayanda Creek on Ball Road. These recommendations are based on the results of the subsurface investigation, our understanding of the proposed construction, and our general experience with similar projects near the proposed construction.

8.1 Shallow Foundations

The foundations for a three- or four-sided box culvert, and the associated wing wall foundations, should be constructed to bear directly on the medium dense to very dense native glacial till, found at depths greater than approximately 8 feet below the existing roadway surface. The foundations for a three-

sided box culvert should bear at least 4 feet below the streambed for protection against frost penetration, or below the calculated scour depth (to be determined by others), whichever is greater. The foundation for a four-sided box culvert should bear a minimum of 1 foot below the streambed elevation at the downstream end of the culvert. Based on the provided survey, we anticipate that these depths will correspond to a bearing elevation of approximately +586 to +587 feet for a three-sided culvert and approximately +589 to +590 feet for a four-sided box culvert.

It is also recommended that the culvert be designed in general agreement with the New York State Department of Transportation's (NYSDOT's) plans and sections for precast box culverts or three-sided structures. However, NYSDOT generally does not allow for their structures to bear upon shallow foundations, unless bearing on rock, and therefore, scour analyses should be performed (by others), and adequate scour protection should be placed along the toes of the culvert and wing wall foundations. If sheet pile wing walls are used, they should be combined with armor to control scour. If scour prevention is not used, the sheet piles should be designed to support both the walls and backfill loads, with scour at its full calculated depth within the stream bed.

Based on the results of our subsurface investigation, the culvert foundations can be designed using a maximum allowable bearing capacity of 3 tons per square foot, when bearing at depths greater than 8 feet below the existing road surface elevation above the culvert. However, it is recommended that the foundations be constructed with a minimum width of 2 feet. If the foundation subgrades need to be protected from disturbance, up to 6 inches of clean crushed stone, flowable fill or lean concrete may be placed beneath the foundations as protection.

Based on this bearing pressure, the total settlements of the culvert and wing walls are expected to be less than 1-inch, with differential settlements less than approximately 1/2-inch over the width of the culvert. The bearing pressure applied at any location of the foundation should not exceed the design allowable value given above. This bearing capacity value is suitable for use when bearing on the native soil directly, or when using a thin stabilization layer, such as crushed stone, flowable fill or lean concrete.

The foundation subgrade should be inspected by a geotechnical engineer and subgrade preparation should be specified as recommended in Section 9 of this report.

8.2 Design for Lateral Loading

The culvert walls and wingwalls should be designed in accordance with the following lateral earth pressure criteria, assuming that the walls will be backfilled with NYSDOT Select Granular Fill in accordance with the requirements listed in Section 9.5:

Table 8.2.1 – Lateral Soil Parameters for Culvert and Wing Walls		
Soil Parameter	Existing On-Site Soils ⁽¹⁾	Structural Backfill (level)
Angle of Internal Friction (degrees)	36	34
Active Earth Pressure Coefficient (K_a) ⁽²⁾	0.26	0.28
At-rest Earth Pressure Coefficient (K_o) ⁽³⁾	0.41	0.44
Passive Earth Pressure Coefficient (K_p) ⁽⁴⁾	3.85	3.54
Total Unit Weight of Soil (pounds per cubic foot) ⁽⁵⁾	140	135
Buoyant Unit Weight of Soil (pounds per cubic foot) ⁽⁶⁾	78	73

Notes:

- 1) The Existing On-Site Soil parameters should only be used for the design of sheet pile wingwalls. The Structural Backfill parameters should be used for the design of the culvert and other types of wingwalls.
- 2) Use for free standing walls where movement of up to 0.0015 X height of wall is both possible and tolerable. Otherwise, use at-rest coefficient.
- 3) Use only for walls restrained against active movement, such as culvert walls.
- 4) Reduce the passive pressure above a depth of 4 feet below exterior grade by half to account for frost disturbance.
- 4) Assumes the walls will be constructed with drains and/or weep holes to prevent hydrostatic pressure build-up behind the culvert and wing walls.
- 5) Use the total unit weight above the design groundwater depth (5 feet) and the buoyant unit weight below design groundwater depth.
- 6) The coefficients provided assume a level backfill and vertical walls. The coefficients should be re-evaluated for other conditions.

The design of the culvert walls and wingwalls should incorporate a surcharge loading due to compaction equipment, construction traffic and regular truck traffic loads. It is recommended that passive resistance be ignored, when calculating sliding stability, except when evaluating soil resistance to the outward thrust of the legs of an arch.

Recommended sliding coefficients for various types of culvert and wing wall materials, and subgrade soils are presented in Table 8.2.2, below.

Table 8.2.2 – Sliding Coefficients for Culverts and Sheet Pile	
Structure Material on Backfill Soil	Coefficient of Base Friction
Cast-in-Place Concrete on Select Granular Fill or Crushed Stone	0.40
Precast Concrete on Select Granular Fill or Crushed Stone	0.35
Cast-in-Place Concrete on Existing Native Soils	0.4
Precast Concrete on Existing Native Soils	0.24
Smooth Steel (e.g., sheet pile) on Existing Fill or Select Granular Fill	0.20

Note:

- 1) The coefficients presented in Table 8.2.2 incorporate a reduction factor of 0.8, as recommended by AASHTO.

The groundwater level for design should be assumed to be 2 feet above the normal stream level (estimated to be approximately 5 feet below the existing road surface, or at an approximate elevation of +595 feet, for this report); however, for extreme loading conditions, it may be prudent to assume that the groundwater level coincides with the design flood elevation. The buoyant weights of soil and concrete should be used below this elevation unless the drainage system and backfill allow for a free-draining condition.

8.3 Drainage

We recommend that weep holes or other drainage provisions be included into the culvert design to prevent the buildup of groundwater behind the culvert walls and wingwalls. One option is to include a 12-inch-thick zone of free-draining material placed directly behind the culvert walls and wingwalls extending from the footings to at least 2 feet above the design flood elevation. Gradation recommendations for the drainage material are provided in Section 9.5. The free-draining stone should be separated from the backfill by a non-woven filter fabric having an apparent opening size equal to or finer than the #70 US sieve, such as TenCate Mirafi® 140N, or an approved equal. A second option is to utilize Select Structure Fill with a prefabricated composite structural drain, such as TenCate Mirafi® G100N, or an approved equal, placed against the culvert walls and wingwalls.

8.4 Seismic Design and Liquefaction Potential

We have evaluated an appropriate site coefficient for use in seismic design using the latest AASHTO and FHWA standards. The subsurface conditions should be considered Site Class D, with a peak horizontal ground acceleration (PHGA) of 0.083g, and an A_s of 0.132g. A maximum spectral response acceleration for short periods (S_s) of 0.161g and for a 1-second period (S_1) of 0.038g should be used for design of the proposed culvert. The corresponding five-percent damped design spectral response acceleration at short periods (S_{DS}) is equal to 0.258g, and at 1-second (S_{D1}) is equal to 0.090g. These parameters should be used for design of the proposed culvert.

Liquefaction of soils can be caused by a strong vibratory motion due to earthquakes. Both research and historical data indicate that loose, granular soils saturated by a shallow groundwater table are most susceptible to liquefaction. Liquefaction occurs when an earthquake and associated ground shaking of sufficient duration results in the loss of grain-to-grain contact due to a rapid increase in pore water pressure, causing the soil to behave as a fluid for short periods. Given the relatively high fines contents and density of the glacial till at the site, it is unlikely that liquefaction could occur within the site soils.

9.0 EARTHWORK AND CONSTRUCTION CRITERIA

The following subsections present our recommendations regarding earthwork, excavations, and fill placement.

9.1 General Site Preparation

The site should be cleared of tree roots, asphalt, concrete, existing foundations, and other surface and subsurface obstructions. Debris and vegetation from the clearing operations should be removed from the site and disposed of at a legal disposal facility. Existing utilities within the project limits, such as the gas main shown along the eastern shoulder of Ball Road on the provided site survey drawing, should be re-routed, or protected from damage by construction equipment.

9.2 General Excavation

All excavations should conform to the latest OSHA requirement regarding worker safety. The fill and native soils at the site should be considered to have the OSHA designation of "Type C" soils. If required, all shoring and bracing should be designed by a professional engineer. Any vertical cut more than 4

feet in height should be sloped back for safety unless sheeting and shoring is used. OSHA requirements pertaining to worker safety should be met during excavation, dewatering, and backfilling activities.

9.3 Foundation Subgrade Preparation

Dewatering should be implemented to lower the groundwater level below the depth of excavation. Shallow foundation subgrades should be prepared by removing all soil loosened by machine excavation. The foundation subgrades should consist of undisturbed glacial till, as encountered within the borings.

The foundation subgrades should be inspected by a qualified geotechnical engineer prior to rebar or concrete placement. Any areas deemed unsuitable by the inspecting engineer during inspection should be removed and replaced with crushed stone, flowable fill or lean concrete having a 28-day unconfined compressive strength of at least 150 psi.

9.4 Dewatering and Protection of Subgrades

All subgrades should be protected from the effects of frost, construction traffic, groundwater, and surface water. The necessary protection should be provided immediately after excavation and inspection and be maintained until concrete or backfill has been placed. Temporary surface drainage measures are recommended to divert runoff away from the proposed construction limits.

Cofferdams or stream diversions can be constructed to divert water from entering the areas of the proposed culvert and wing walls. The design of the cofferdams or stream diversions should be as needed to prevent the flow of water into the foundation subgrade. The primary purpose of dewatering will be to keep the excavations free of standing water, provide a stable bearing surface for foundations, and to maintain stable excavation slopes. The contractor should be prepared to perform dewatering activities as excavation progresses, to maintain stable excavation slopes.

The operation of sumps directly in the footing excavations should not be allowed. Sump pits should be located at least 1 foot beyond the edge of the footing for every foot that they extend below the bearing elevation. The dewatering system should be designed by a Professional Engineer licensed in New York State, and it should be designed to ensure that dewatering does not result in any loss of soil.

As previously mentioned, silty soils, which tend to be moisture sensitive, were encountered within the native soils during the investigation. They could soften, experience a reduction in load-carrying capacity, and may become unstable or unworkable, if disturbed. These soils are also frost susceptible and could become disturbed if allowed to freeze during construction. Additional excavation and material removal may be required if excavation subgrades and slopes are allowed to be exposed for long durations without fill or concrete placement. Additionally, construction traffic could also disturb the existing fill and native soils.

9.5 Culvert Backfill Material and Placement Recommendations

The proposed culvert and wingwalls should be backfilled with compacted Select Granular Fill. Backfill should extend a distance of at least 2 feet behind the culvert and wingwalls. The backfill should be well-graded durable granular material consisting of clean sand, gravel, or a mixture of these, and it should be free of trash, debris, roots, vegetation, or other deleterious materials. The backfill should conform to requirements of NYSDOT Select Granular Fill, the gradation for which is provided below:

<u>Sieve Size</u>	<u>Percent Finer by Weight</u>
4-inch	100
No. 40	0 to 70
No. 200	0 to 15

At distances greater than 3 feet from the walls, the backfill may also consist of material meeting the requirements for NYSDOT Specification Section 733.08 - Embankment in Place. As previously noted, our laboratory testing showed that some of the on-site soils have relatively high fines contents (25 to 35 percent). Based on these results of laboratory testing, the on-site soils are not expected to be suitable for use as Select Granular Fill, but may meet the requirements for Embankment in Place fill. Further laboratory testing of bulk samples collected from the culvert approaches should be collected and tested during construction to verify whether the on-site soils meet the specifications. The on-site soils may be moisture sensitive due to their high fines content and their use may result in construction delays if they become wet.

Crushed gravel to be placed beneath foundations as replacement for undercuts of unsuitable bearing material, or as a working pad beneath the foundations should confirm with the NYSDOT requirements for Coarse Aggregate (Item Number 703.0202, Size 2) and the following gradation:

<u>Sieve Size</u>	<u>Percent Finer by Weight</u>
1½ inch	100
1 inch	90 - 100
½ inch	0 - 15
No. 200	0 - 1

If utilized, the drainage layer immediately behind the proposed culvert stem walls and wingwalls should conform to the NYSDOT requirements for Underdrain Filter Type I material with the following gradation:

<u>Sieve Size</u>	<u>Percent Finer by Weight</u>
1 inch	100
½ inch	30 - 100
¼ inch	0 - 30
No. 10	0 - 10
No. 20	0 - 5

Material meeting the specifications for ASTM C33, No. 57 stone may also be used as for the drainage layer.

Flowable fill may also be used as backfill to restore the grade as culvert and wing wall backfill within the streambed. Flowable fill, should have a minimum 28-day unconfined compressive strength of 150 psi. If specified, flowable fill should meet the requirements for Controlled Low Strength Material (CLSM), as specified in Section 733-01 – “Flowable Fill” of the NYSDOT Standard Specifications.

All culvert stem wall and wingwall backfill, and all embankment fill, should be compacted to at least 95 percent of the maximum dry density at near optimum moisture contents, as determined by ASTM D1557, “*Test Method for Laboratory Compaction Characteristics of Soil Using Standard Effort (12,400 ft-lbf/ft³ (600 kN-m/m³))*”. The lift thickness for the fill soils will vary depending on the type of compaction equipment used. Fills should generally be placed in uniform horizontal lifts not exceeding 12 inches in loose thickness, in open areas. In confined areas, the loose lift thickness should be reduced to 4 inches or less and each lift should be compacted with sufficient passes of hand operated vibratory or impact compaction equipment. Compaction within 5 feet of culvert stem walls and wingwalls should only be done with a trench roller or hand-operated equipment.

A qualified geotechnical engineer, with appropriate field and laboratory support, should inspect all footing subgrades, approve materials for use as fill, and test backfill materials for compliance with the recommended compaction. Each lift of fill placed at the site should be tested for compaction.

10.0 CONSTRUCTION MONITORING

An engineer familiar with the existing subsurface conditions and having the appropriate laboratory and field-testing support should observe that all earthwork is performed in accordance with the specifications, and the design criteria provided in this report.

It is recommended that the following work should be performed under the observation of the geotechnical engineer:

- Dewatering/stream diversion (cofferdam construction)
- Subgrade preparation
- Sheet pile installation, if selected
- Placement and compaction of fill and backfill

Materials proposed for use as culvert stem wall and wingwall backfill should be tested and approved prior to delivery or use on-site. All fill materials should be tested as they are being placed to verify that the required compaction is being achieved.

11.0 LIMITATIONS

Our professional services have been performed using that degree of care and skill ordinarily exercised under similar circumstances by reputable geotechnical engineers and geologists practicing in this or similar situations. The interpretation of the field data is based on good judgment and experience. However, no matter how qualified the geotechnical engineer or detailed the investigation, subsurface conditions cannot always be predicted beyond the points of actual sampling and testing. No other warranty, expressed or implied, is made as to the professional advice included in this report.

The recommendations contained in this report are intended for design purposes only. Contractors and others involved in the construction of this project are advised to make an independent assessment of the soil and groundwater conditions for the purpose of establishing quantities, schedules and construction techniques.

This report has been prepared for the exclusive use of the Client for the specific application to the proposed project. In the event that any changes in the design or location of the proposed structure are planned, Tectonic Engineering Consultants, Geologists & Land Surveyors D.P.C. (Tectonic) shall not consider the conclusions and recommendations contained in this report valid unless reviewed and verified in writing. It is further recommended that Tectonic be retained to provide construction monitoring and inspection services to ensure proper implementation of the recommendations contained herein, which would otherwise limit our professional liability.

CBB/MCC File: G:\Newburgh\Geotechnical\12000\12020.01 Warwick Culvert\Reports\12020.03\12020.01 Ball Road Culvert geoinv.docx

FIGURE I



Legend:		Notes:		Tectonic PLANNING ENGINEERING SURVEYING CONSTRUCTION MANAGEMENT PRACTICAL SOLUTIONS. EXCEPTIONAL SERVICE.			
 B-1	BORING LOCATION (TYP)	THIS DRAWING IS BASED ON THE 2022 ORTHOIMAGE OF THE SITE, AS SHOWN ON THE ORANGE COUNTY GIS WEBSITE: (https://gis.orangecountygov.com/portal/apps/webappviewer/index.html?id=b2e034661d86490aaca1ee67a25dffab) THE BORING LOCATIONS SHOWN HEREIN WERE NOT SURVEYED, AND THEREFORE, SHOULD BE CONSIDERED APPROXIMATE.		Tectonic Engineering Consultants, Geologists & Land Surveyors D.P.C. 1279 Route 300 Newburgh, NY 12550 Phone: (845) 567-6566 Fax: (845) 567-6248			
				BORING LOCATION PLAN			
				BALL ROAD CULVERT TOWN OF WARWICK, NEW YORK			
				Date 6/28/2023	Work Order No. 12020.01	Drawing No. Figure 1 Page 254 of 323	Rev. No. 0

APPENDIX I

CLIENT: Town of Warwick				GROUND WATER	DATE	TIME	DEPTH	INSPECTOR: Drew Bugna			
CONTRACTOR: Craig Geotechnical Drilling Co., Inc.					5/12/23	8:30 am	8'	DRILLER: G. Zackman			
METHOD OF ADVANCING BORING		DIA.	DEPTH					SURFACE ELEVATION: 601.0			
POWER AUGER:			TO		MON. WELL ☐ YES ☒ NO			DATUM: See Remarks			
ROT. DRILL:		3 7/8"	0	TO	30'	SCREEN DEPTH: --- TO ---			DATE START: 5/12/23		
CASING:		4"	0	TO	25'	WEATHER: Clear TEMP: 60° F			DATE FINISH: 5/12/23		
DIAMOND CORE:			TO		DEPTH TO ROCK: Not Encountered'			UNCONFINED COMPRESS. STRENGTH ● (TONS/FT)			1 2 3 4 5 PLASTIC LIMIT % WATER CONTENT % LIQUID LIMIT % STANDARD PENETRATION (BLOWS/FT.)
CME 75 Truck Mounted Drill Rig with Automatic Hammer					*CHANGES IN STRATA ARE INFERRED						

DEPTH (FT.)	N OR MIN./FT.	PENETRATION RESISTANCE (BLU/6 IN.)	SAMPLES			UNIFIED SOIL CLASS.	DESCRIPTION OF MATERIAL	LITHOLOGY*	ELEVATION (FT.)
			SAMPLE NUMBER	RECOV. LENGTH (IN.)	RQD (%)				
1	24	8	S-1	12		M	SP	1" Asphalt pavement	
2		13							
3	25	7	S-2	10		M	SP	Bwn c-f SAND, some c-f Gravel, trace Silt (FILL)	
4		13							
5	50+	18	S-3	3		M	SM	Bwn c-f SAND, little c-f Gravel, trace Silt (FILL)	
6		50/5							
7								Bwn c-f SAND, little Silt, trace c-f Gravel	
8									
9	28	10	S-4	8		W	GM	Boulder encountered @ 5' to 6.5'	
10		21							
11	28	7	S-5	8		W	GM	Bwn c-f GRAVEL, and c-f Sand, some Silt	
12		10							
13		13						Bwn c-f GRAVEL, little c-f Sand, little Clayey Silt	
14		13							
15		15							
16		16							
17	63+	9	S-6	2		W	GP	Gy c-f GRAVEL, trace c-f Sand, trace Silt	
18		13							
19		50/3							
20									
21	50+	50/0	S-7	0				Split spoon refusal @ 20'	
22									
23									
24									
25									

REMARKS: Surface elevation was estimated by interpolating between contour lines shown on a topographic survey of the site provided by the Client's Agent.




CLIENT: **Town of Warwick**

CONTRACTOR: **Craig Geotechnical Drilling Co., Inc.**

DEPTH (FT.)	N OR MIN./FT.	PENETRATION RESISTANCE (BL/6 IN.)	SAMPLES				UNIFIED SOIL CLASS.	DESCRIPTION OF MATERIAL	LITHOLOGY*	UNCONFINED COMPRESS. STRENGTH (TONS/FT.)			ELEVATION (FT.)	
			SAMPLE NUMBER	RECOV.		MOISTURE				1	2	3		
				LENGTH (IN.)	RQD (%)									
										PLASTIC LIMIT % X-----X 10 20 30 40 50		WATER CONTENT % -----X----- 10 20 30 40 50	LIQUID LIMIT % -----A----- 10 20 30 40 50	
										STANDARD PENETRATION (BLOWS/FT.) ●-----●----- 10 20 30 40 50				
26	50+	14 50/5	S-8	3		W	GP	Same						
27														
28														
29														
30														
31	39	12 18 21 16	S-9	15		W	SM	Bwn-tn c-f SAND, and Silt, little c-f Gravel					571.0	
32								End of Boring at 32'						
33														
34														
35														
36														
37														
38														
39														
40														
41														
42														
43														
44														
45														
46														
47														
48														
49														
50														
51														
52														
53														
54														
55														

REMARKS: Surface elevation was estimated by interpolating between contour lines shown on a topographic survey of the site provided by the Client's Agent.

CLIENT: Town of Warwick				GROUND WATER	DATE	TIME	DEPTH	INSPECTOR: Drew Bugna				
CONTRACTOR: Craig Geotechnical Drilling Co., Inc.					5/12/23	12:20 pm	8'	DRILLER: G. Zackman				
METHOD OF ADVANCING BORING		DIA.	DEPTH					SURFACE ELEVATION: 602.0				
POWER AUGER:			TO		MON. WELL ☐ YES ☒ NO			DATUM: See Remarks				
ROT. DRILL:		3 7/8"	0	TO	25'	SCREEN DEPTH: --- TO ---			DATE START: 5/12/23			
CASING:		4"	0	TO	25'	WEATHER: Clear TEMP: 75° F			DATE FINISH: 5/12/23			
DIAMOND CORE:			TO		DEPTH TO ROCK: Not Encountered'			UNCONFINED COMPRESS. STRENGTH ● (TONS/FT)				
CME 75 Truck Mounted Drill Rig with Automatic Hammer					*CHANGES IN STRATA ARE INFERRED			1 2 3 4 5				

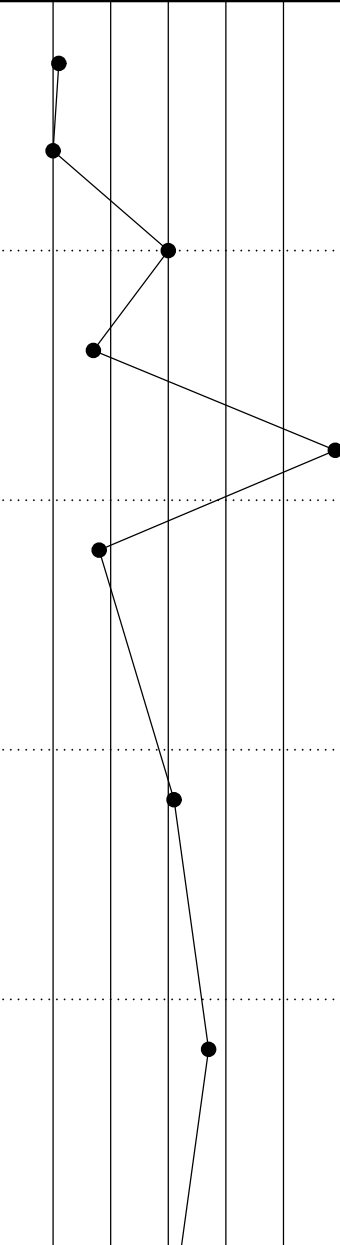DEPTH (FT.)	N OR MIN./FT.	PENETRATION RESISTANCE (BL/6 IN.)	SAMPLES				UNIFIED SOIL CLASS.	DESCRIPTION OF MATERIAL	LITHOLOGY*	PLASTIC LIMIT %			WATER CONTENT %			LIQUID LIMIT %			ELEVATION (FT.)	
			SAMPLE NUMBER	RECOV.		MOISTURE				X	20	30	40	50	X	20	30	40		50
				LENGTH (IN.)	RQD (%)															
STANDARD PENETRATION (BLOWS/FT.)																				
1	11	8	S-1	4		M	SP	2" Asphalt Pavement												
2		7																		
3	10	4	S-2	3		M	SM	Bwn-blk c-f SAND, and Silt, little f Gravel												
4		2																		
5	30	2	S-3	5		M	SM	Same												
6		10																		
7	17	20	S-4	0				No Recovery												
8		15																		
9	59	10	S-5	4		W	GP	Gy c-f GRAVEL, trace Silt, trace c-f Sand												
10		17																		
11	18	30	S-6	5		W	SM	Bwn-or SILT, some c-f Sand, some c-f Gravel												
12		29																		
13		14																		
14		12																		
15		9																		
16	31	9	S-7	1		W	GP	Gy c-f GRAVEL, trace c-f Sand, trace Silt												
17		8																		
18		23																		
19		11																		
20																				
21	37	7	S-8	4		W	GM	Bwn-gy c-f GRAVEL, and Silt, trace c-f Sand												
22		10																		
23		27																		
24		30																		
25																				

REMARKS: Surface elevation was estimated by interpolating between contour lines shown on a topographic survey of the site provided by the Client's Agent.

PROJECT No. **12020.03**
 PROJECT: **Town of Warwick Culvert Replacement**
 LOCATION: **Ball Road, Warwick, NY**

BORING No. B-2

SHEET No. 2 of 2

CLIENT: **Town of Warwick**

CONTRACTOR: **Craig Geotechnical Drilling Co., Inc.**

DEPTH (FT.)	N OR MIN./FT.	PENETRATION RESISTANCE (BL/6 IN.)	SAMPLES				UNIFIED SOIL CLASS.	DESCRIPTION OF MATERIAL	LITHOLOGY*	UNCONFINED COMPRESS. STRENGTH (TONS/FT.)					ELEVATION (FT.)
			SAMPLE NUMBER	RECOV.		MOISTURE				PLASTIC LIMIT %	WATER CONTENT %	LIQUID LIMIT %			
				LENGTH (IN.)	RQD (%)										
26	31	17	S-9	12		W	CL-ML	Bwn-tn CLAYEY SILT, some c-f Gravel, trace c-f Sand		●	3	30			
27		18													
28		13													
29		29						End of Boring at 27'							
30															
31															
32															
33															
34															
35															
36															
37															
38															
39															
40															
41															
42															
43															
44															
45															
46															
47															
48															
49															
50															
51															
52															
53															
54															
55															

REMARKS: Surface elevation was estimated by interpolating between contour lines shown on a topographic survey of the site provided by the Client's Agent.

LEGEND FOR SOIL DESCRIPTION

COARSE GRAINED SOIL			(Coarser than No. 200 Sieve)		
DESCRIPTIVE TERM & GRAIN SIZE					
TERM		SAND		GRAVEL	
coarse	- c	No.	4 Sieve to No.	10 Sieve	3" to 3/4"
medium	- m	No.	10 Sieve to No.	40 Sieve	3/4" to 3/16"
fine	- f	No,	40 Sieve to No.	200 Sieve	
COBBLES		3" to 10"		BOULDERS 10" +	
GRADATION DESIGNATIONS			PROPORTIONS OF COMPONENT		
fine, f			Less than 10% coarse to medium		
medium to fine, m-f			Less than 10% coarse		
medium, m			Less than 10% coarse and fine		
coarse to medium, c-m			Less than 10% fine		
coarse, c			Less than 10% medium and fine		
coarse to fine, c-f			All greater than 10%		

FINE GRAINED SOIL			(Finer than No. 200 Sieve)		
DESCRIPTION		PLASTICITY INDEX		PLASTICITY	
Silt		0 - 1		none	
Clayey Silt		2 - 5		slight	
Silt & Clay		6 - 10		low	
Clay & Silt		11 - 20		medium	
Silty Clay		21 - 40		high	
Clay		greater than 40		very high	


PROPORTION	
DESCRIPTIVE TERM	PERCENT OF SAMPLE WEIGHT
trace	1 - 10
little	10 - 20
some	20 - 35
and	35 - 50
The primary component is fully capitalized if >50% of sample	

COLOR		
Blue - blue	Gy - gray	Wh - white
Blk - black	Or - orange	Yl - yellow
Bwn - brown	Rd - red	Lgt - light
Gn - green	Tn - tan	Dk - dark

SAMPLE NOTATION	
S - Split Spoon Soil Sample	WOC - Weight of Casing
U - Undisturbed Tube Sample	WOR - Weight of Rods
C - Core Sample	WOH - Weight of Hammer
B - Bulk Soil Sample	PPR - Compressive Strength based on Pocket Penetrometer
NR - No Recovery of Sample	TV - Shear Strength (tsf) based on Torvane

ADDITIONAL CLASSIFICATIONS	
New York City Building Code soil classifications are given in parentheses at the end of each description of material, if applicable. See sections 1804.2 of the 2008 Building Code for further details.	

APPENDIX II

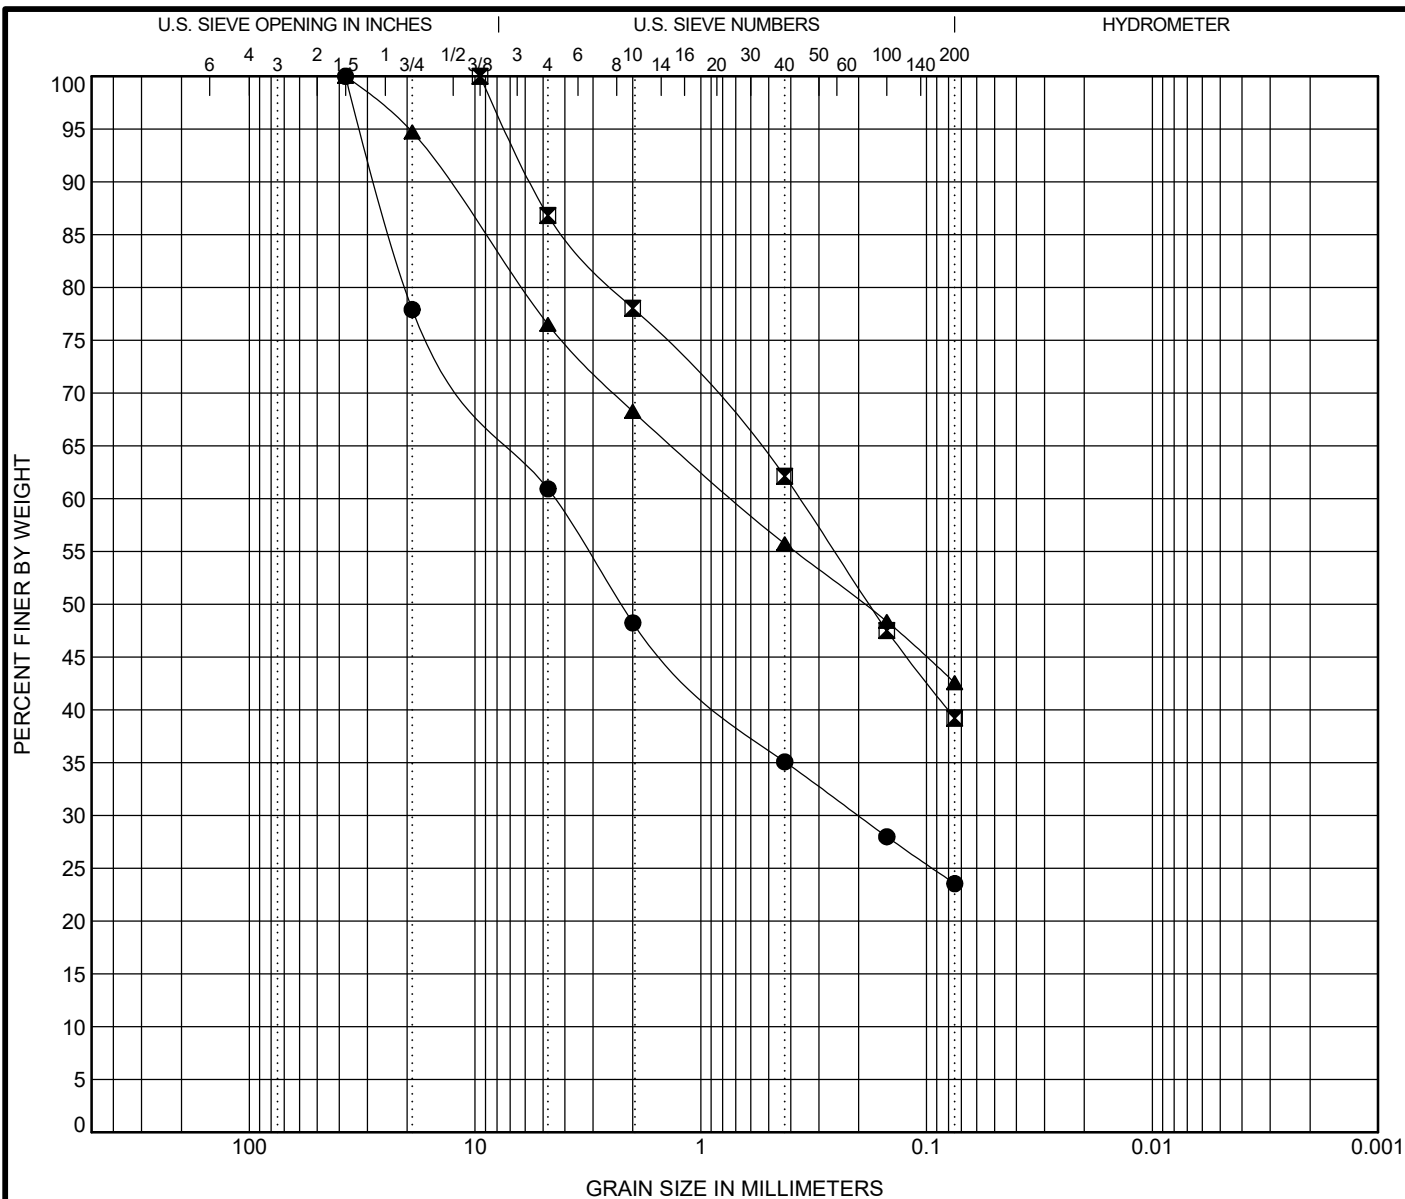

COBBLES	GRAVEL		SAND			SILT OR CLAY
	coarse	fine	coarse	medium	fine	

Sample Identification				Classification				WC%	LL	PL	PI	Cc	Cu
●	B-1	8.0	S-4	Bwn c-f Gravel, and c-f Sand, some Silt				11.1					
☒	B-2	4.0	S-3	Bwn-Blk c-f Sand, and Silt, little f Gravel				18.4					
▲	B-2	10.0	S-6	Bwn-Or Silt, some c-f Sand, some c-f Gravel				10.9					

Sample Identification				D100	D60	D30	D10	%Gravel	%Sand	%Silt	%Clay	Source of Material	
●	B-1	8.0	S-4	37.5	4.46	0.202		39.1	37.4	23.5		Boring	
☒	B-2	4.0	S-3	9.5	0.365			13.2	47.6	39.2		Boring	
▲	B-2	10.0	S-6	37.5	0.72			23.5	33.9	42.6		Boring	

Tectonic

280 Little Britain Road, Bldg. 2
Newburgh, NY 12550
Telephone: (845) 563-9081

Fax: (845) 563-9085

GRAIN SIZE DISTRIBUTION

Project No: 12020.03

Date: 6/9/23

Project: Warwick Culverts - Ball Rd.

Location: Warwick, NY

Our Story

For the past 30 years, Tectonic has delivered quality professional services in a timely and cost effective manner by pooling its talented staff into project teams that think, act, and perform as one integral unit. By carefully listening and collaborating with its clients, the firm is able to identify the key issues and assure stakeholder objectives are met in the final deliverables. Through innovating and adopting technological advances, the firm is able to generate unique solutions to improve our nation's deteriorating infrastructure and build safe sustainable communities.

As the world evolves, and its challenges grow more complex, Tectonic continues to innovate and provide the practical solutions and exceptional customer service its clients have trusted since its founding.

ATTACHMENT 2

Applicable Permits

This page intentionally left blank.



**New York State
Parks, Recreation and
Historic Preservation**

KATHY HOCHUL
Governor

RANDY SIMONS
Commissioner Pro Tempore

October 08, 2024

Abigail Megna
Environmental Planner
HDR
711 Westchester Ave, Suite 103
White Plains, NY 10604

Re: DEC
Ball Road Culvert Replacement Over Unnamed Creek
24PR08771

Dear Abigail Megna:

Thank you for requesting the comments of the Office of Parks, Recreation and Historic Preservation (OPRHP). We have reviewed the project in accordance with the New York State Historic Preservation Act of 1980 (Section 14.09 of the New York Parks, Recreation and Historic Preservation Law). These comments are those of the OPRHP and relate only to Historic/Cultural resources. They do not include potential environmental impacts to New York State Parkland that may be involved in or near your project.

Based upon this review, it is the opinion of OPRHP that no properties, including archaeological and/or historic resources, listed in or eligible for the New York State and National Registers of Historic Places will be impacted by this project.

If further correspondence is required regarding this project, please be sure to refer to the OPRHP Project Review (PR) number noted above. If you have any questions, please contact Olivia Holland at the following email address:

Olivia.Holland@parks.ny.gov

Sincerely,

R. Daniel Mackay

Deputy Commissioner for Historic Preservation
Division for Historic Preservation



PERMIT
Under the Environmental Conservation Law (ECL)

GENERAL PERMIT GP-0-20-002
Stream Activities General Permit

Permittee and Facility Information

Permit Issued To:

Town of Warwick

132 Kings Highway

Warwick, NY 10990

Facility:

Ball Rd Culvert

~ 51-99 Ball Road

Warwick, NY 10990

Applicable DEC Region(s): ALL

General Permit Authorized Activity: This general permit authorizes the activities listed below that occur within regulated streams and rivers, in accordance with the special and general conditions included in this permit, and the project-specific plans approved by Department countersignature to this permit.

When Department approval is obtained by countersignature to this permit, one or more of the following activities may be authorized by this general permit:

1. In-place repair, replacement or re-setting of existing culverts and bridges.
2. Installation of a single new culvert or bridge to serve a single-family residence on an approved building lot, with no impact to state-regulated freshwater wetlands or adjacent areas;
3. In-place repair and replacement of existing bank stabilization structures.
4. Bank stabilization up to 500 linear feet using vegetation-based or bioengineering techniques (e.g., toe-wood structures, fascines, root-wads, brush mattresses, live-staking, etc.).
5. Bank stabilization up to 150 linear feet using rip-rap or similar materials, where use of vegetation-based or bioengineering techniques are not feasible.
6. Installation or repair of in-stream grade control structures consisting of rock or other natural materials (e.g., j-hooks, rock vanes, rock riffles, etc.).
7. Debris, gravel, and streambed material removal not exceeding 100 linear feet of the water course to remove blockages and restore natural stream channel dimensions and flows.
8. Installation or maintenance of dry hydrants for fire protection.
9. Repair of existing utility lines and associated structures (e.g., water, sewer, telecommunications, etc.).
10. Repair or installation of utility lines to serve a single-family, two-family, or three-family residence.
11. Temporary access or dewatering measures necessary to complete other activities authorized by this general permit.
12. Maintenance or repair of existing boat ramps, and access sites.

Specific Activities Authorized for this Permit:

- removal of damaged culvert
- replace with wider, open-bottomed culvert

**Permit Authorizations****Excavation & Fill in Navigable Waters - Under Article 15, Title 5**Effective Date: 05/21/2021 Expiration Date: 05/20/2026**Freshwater Wetlands - Under Article 24**Effective Date: 05/21/2021 Expiration Date: 05/20/2026**Stream Disturbance - Under Article 15, Title 5**Effective Date: 05/21/2021 Expiration Date: 05/20/2026**Water Quality Certification - Under Section 401 - Clean Water Act**Effective Date: 05/21/2021 Expiration Date: 05/20/2026**NYSDEC Approval**

By acceptance of this permit, the permittee agrees that the permit is contingent upon strict compliance with the ECL, all applicable regulations, and all conditions included as part of this permit.

General Permit Authorized by

Permit Administrator: SCOTT E SHEELEY, Chief Permit Administrator

Address: NYSDEC Headquarters
625 Broadway
Albany, NY 12233

Authorized Signature: _____

Date: 05/21/2021**This permit is not effective without the signature below:****Validation under this General Permit**

Authorized By: _____

Michael Fraatz

Biologist 1

NYSDEC Region 3 - New Paltz

michael.fraatz@dec.ny.gov

845-256-3057

Authorized Signature: _____

Date 2 / 18 / 2025**Permit Components**

NATURAL RESOURCE PERMIT CONDITIONS

WATER QUALITY CERTIFICATION SPECIFIC CONDITION

GENERAL CONDITIONS, APPLY TO ALL AUTHORIZED PERMITS

NOTIFICATION OF OTHER PERMITTEE OBLIGATIONS



**NATURAL RESOURCE PERMIT CONDITIONS - Apply to the Following
Permits: WATER QUALITY CERTIFICATION; STREAM DISTURBANCE;
FRESHWATER WETLANDS; EXCAVATION & FILL IN NAVIGABLE
WATERS**

- 1. Request for Authorization** Prior to the use of this General Permit for a project, the Applicant must submit a Joint Application Form with the required attachments to the Regional Permit Administrator. On review of the project NYSDEC will determine if the project can be authorized under this General Permit. No work is authorized until the Applicant receives the countersigned General Permit containing a description of the specific activities authorized. NYSDEC retains the right to exclude a proposed activity from authorization under this General Permit and require the Applicant to obtain an individual permit.
- 2. Conformance With Plans** All activities authorized by this permit must be in strict conformance with the approved plans submitted by the applicant or applicant's agent as part of the permit application. Such approved plans were prepared by the applicant or their agent and are attached to this permit.
- 3. Prohibited Locations** Work under this general permit is not authorized in the following locations:
 - a. Any tidal waters of New York State, including those brackish and fresh waters north of the former Tappan Zee Bridge not designated and regulated as tidal wetlands under Article 25 of the Environmental Conservation Law (ECL)
 - b. Coastal Erosion Hazard Areas designated by the state pursuant to Article 34 of the ECL;
 - c. Any locations determined by the Department where a proposed project is likely to result in a taking of a species, listed as threatened or endangered in New York State, as taking is defined in 6 NYCRR Part 182, or likely to result in adverse impacts to freshwater mussel species designated by the New York Natural Heritage Program as S1 or S2.
 - d. Any location where a proposed project may affect a property listed on the National or State Registers of Historic Places, or has been determined by the New York State Office of Parks, Recreation and Historic Preservation to be eligible for listing on the State Register of Historic Places.
- 4. Bridge and Culvert Requirements** To be covered under this general permit, all the following criteria must be met:
 - a. All culverts with closed bottoms (including round culvert pipes) must be appropriately embedded. Round culverts must be installed so that at least 20% of the culvert's vertical height is embedded below the existing stream bed at the outlet end of the culvert.
 - b. Appropriately-sized substrate shall be brought in, or the streambed material that was excavated to accommodate culvert placement shall be used, for culvert embedding (where appropriate) and spread evenly throughout the bottom of the new culvert. The substrate or material shall be thoroughly wetted prior to returning flow through the culvert.
 - c. The width of the structure must be a minimum of 1.25 times the width of the channel at the Mean High Water level, generally measured bank-to-bank between the edges of terrestrial, rooted vegetation, unless otherwise described in the approved plans.
 - d. The culvert bed slope shall remain consistent with the slope of the adjacent stream channel. For slopes greater than 3%, an open bottom culvert must be used.



- e. This general permit does not authorize culvert rehabilitation projects that involve invert paving, slip-lining, or similar treatments.
- f. Bridges and culverts and any associated scour protection must be installed in a manner so that they do not constitute a barrier to upstream movement of fish and other aquatic species under normal flow conditions or constrict the stream channel.
- g. Stone aprons and scour protection placed in streams or rivers shall be installed flush with the invert elevation and filled with native bed material and supplemented with similarly sized material, if needed to fill interstitial spaces.
- h. Publicly-owned bridges and culverts shall be designed as follows:
 - i. Open-bottom culverts, box culverts, and culvert pipes shall be designed to pass the peak flow from a storm event with an annual chance of 2% or less (i.e., 50-year storm or greater) such that the water surface remains below the top of the inlet opening.
 - ii. Bridges shall be designed to pass the peak flow from a storm event with an annual chance of 1% or less (i.e., 100-year storm or greater) such that all flow passes beneath the lowest chord of the structure without going into pressure flow.
 - iii. The peak design flows applied in h.i and h.ii above shall be adjusted by the appropriate design flow multipliers in Table 3 and Figure 3 of the "New York State Flood Risk Management Guidance for Implementation of the Community Risk and Resiliency Act", August 2020.
- i. For projects involving over 100 linear feet of stream disturbance, or a critical bridge or culvert, the applicant must address the recommended flood risk management guidelines for transportation infrastructure contained in "New York State Flood Risk Management Guidance for Implementation of the Community Risk and Resiliency Act", August 2020 (p. 35 of the guidance also describes "critical transportation infrastructure"). The structure design must incorporate the flood risk management guidelines, or the applicant must demonstrate that the guidelines were considered and determined infeasible.

5. Bank Stabilization Requirements To be covered under this general permit, all the following criteria must be met:

- a. New vertical bank stabilization measures are prohibited.
- b. All existing vegetation shall be preserved to the extent practicable.
- c. The channel width must not be constricted but match the existing upstream and downstream channel widths outside the project site.
- d. The slope of new bank stabilization measures shall not be steeper than a ratio of 1-1/2 horizontal units to 1 vertical unit.
- e. Measures must be properly keyed into the stream bank(s) to prevent scouring.
- f. Measures using live vegetation shall consist only of native plant species.
- g. Measures must not include geotextile fabric as part of the final structure.

6. In-stream Grade Control Requirements To be covered under this general permit, the following criteria must be met:

- a. Installed measures must not create a vertical drop exceeding six (6) inches.
- b. Measures must be constructed to maintain a low-flow channel
- c. Measures must be properly keyed into the stream bank(s) to prevent scouring.
- d. Use of sheet-piling is prohibited.
- e. Measures must not include geotextile fabric as part of the final structure.



7. Debris, Gravel, and Streambed Material Removal Requirements To be covered under this general permit, the following criteria must be met:

- a. Only recently deposited debris, gravel and other streambed material may be removed, and only where it can be demonstrated that deposited material has resulted in one of the following conditions: loss of stream function; active erosion; or the need to maintain infrastructure (e.g. culvert blockages);
- b. The resulting channel width must not be over-widened or over-deepened, but match the existing upstream and downstream channel widths and depths outside the project area.
- c. Completion of the project must maintain a low-flow channel; and
- d. Excavated materials shall not be placed along the top of the bank or used to create a berm or increase berm bank height. Building berms with the excavated material is expressly prohibited.

8. Time of Year Restriction - Fisheries All instream work, as well as any work that may result in the suspension of sediment, is prohibited during the fish spawning and incubation period specified in the description of specific activities authorized by this permit. The restriction period(s) that shall apply, when specified, are as follows:

Specification Time of Year Restriction

- | | |
|----------|--|
| A | None |
| B | Natural spawning brook and brown trout, commencing September 15 and ending May 15 |
| C | Natural spawning rainbow trout, commencing January 1 and ending June 15 |
| D | Natural spawning brook trout, brown trout, and rainbow trout, commencing September 15 and ending June 15 |
| E | Walleye and warmwater fish (bass and sunfish) spawning commencing March 1 and ending June 30 |
| F | Warmwater fish (bass and sunfish) spawning only commencing May 1 and ending June 30 |

At the written request of a permittee, work windows may be temporarily modified by the Regional Natural Resources Supervisor or their designee to address extenuating circumstances.

9. Tree Removal Restriction When specified in the description of specific activities authorized by this permit, tree removal is prohibited during the following periods to protect listed bat species:

- a. beginning March 1 and ending November 30 in Suffolk County; or
- b. beginning April 1 and ending October 31 in the rest of New York State.

At the written request of a permittee, the work window may be modified by the Regional Natural Resources Supervisor or their designee to address extenuating circumstances.

10. No Work During High Flow No in-stream work shall occur during periods of high flow, except for work that occurs in dewatered areas behind temporary diversions, cofferdams or causeways; to unplug culverts and bridges; or to install temporary culverts or bridges for emergency access.

11. Precautions Against Contamination of Waters All necessary precautions shall be taken to preclude contamination of any wetland or waterway by suspended solids, sediments, fuels, solvents, lubricants, epoxy coatings, paints, concrete, leachate or any other environmentally deleterious materials associated with the project.



12. Erosion and Sediment Controls Appropriate soil erosion and sediment controls (such as silt fences, turbidity curtains, straw bales, and other appropriate measures) shall be installed, used, and maintained in effective operating condition during all work. Controls shall be installed prior to ground disturbance, inspected periodically to ensure that they are not damaged, repaired promptly when needed, and remain in place until the site is stabilized by the regrowth of suitable vegetation. Erosion controls shall be removed after the site is stabilized by the regrowth of suitable vegetation.

13. Dry Stream Crossing Methods For projects involving culvert, bridge, or utility installations across streams, dry stream crossing methods (e.g., passive flow bypass, cofferdam, pump around and/or flume) shall be used within stream channels to reduce downstream impacts from turbidity and sedimentation, as specified on the approved plans. Any pump intakes must be screened or otherwise protected to prevent fish impingement and entrainment.

14. Diversion Channels When the use of a diversion channel is specified on the approved plans, the diversion channel shall be excavated and restored in the dry using channel plugs. Diversion channels through soil, silt, or clay shall be lined with non-erodible material such as stone, or plastic to limit erosion and reduce particle suspension. If a diversion channel through gravel results in continuous turbidity, the use of channel lining material is required.

15. Temporary Dewatering Structures Where temporary dewatering is required or specified on the approved plans, temporary dewatering measures shall comply with the following:

- a. Temporary dewatering structures shall be constructed of clean material such as prefabricated impervious dikes/berms or sandbags. If stone is used, it shall be protected from erosion by plastic liners or filter fabric.
- b. Waters accumulated in isolated work areas shall be discharged to an upland settling basin, well vegetated area, or silt containment bag, to provide for settling and filtering of solids and sediments. Return waters shall be as clear as the flowing water upstream of the work area.
- c. Temporary dewatering structures, including any plastic liners or filter fabric, and associated fill shall be completely removed, and the affected waters restored, immediately following the completion of work.
- d. To the maximum extent practicable, any fish trapped within the work area shall be netted and placed, alive and unharmed, in the water outside the work area.

16. Stockpiles Fill or other excavated materials shall not be stockpiled in a manner conducive to erosion, or in areas with the potential to cause turbid runoff during storm events. Mats or geotextile fabric shall be placed under any temporary fill or stockpile and shall be removed following construction.

17. Excavated Materials All materials excavated from regulated waters that is not used as backfill shall be deposited in uplands, outside of any floodplain, and be contained from re-entering any regulated waters. Any temporary dewatering of such material must be controlled to prevent turbid discharges or release of excavated materials into regulated waters or wetlands. Disposal sites must be identified in the application.

18. Maintain Floodplain Connection Any material that has been excavated and stockpiled on site must not interfere with stream or floodwater conveyance during the duration of the work and activities shall not result in the disconnection of the waterbody from its floodplain.



19. Material Sizing Materials temporarily or permanently installed within or on the bed or banks of a stream or river must be of adequate size or placed in a manner that will resist erosion or remobilization of the material during normal or expected high flow events. Furthermore, the activity shall not restrict or impede the passage of normal or expected high flows.

20. No Rock from Stream No rock for use in construction is to come from the stream bed, except as allowed under Condition 4.b of this permit.

21. Construction Access Construction access shall be by means that avoid aquatic sites (e.g., upland access temporary bridges, equipment mats, etc.), unless specifically authorized on the approved plans.

22. Temporary Work Areas Temporary causeways and work pads within regulated waters shall be constructed within the confines of a water control structure and shall consist of clean non-erodible material such as stone, timber, or steel. The temporary causeways and work pads shall not be installed until the water control structure is in place and the area has been completely dewatered and shall be removed prior to removal of the water control structure. Equipment staging and lay down areas shall not be located in wetlands, unless specifically authorized on the approved plans.

23. Heavy Equipment Operation in Wetlands Heavy equipment working in wetlands must be placed on equipment mats, or other measures must be taken to minimize soil disturbance and compaction to the maximum extent practicable. Mats or other temporary measures shall be removed when access is no longer needed and the area restored to pre-project conditions.

24. Work from Land Whenever feasible, bank grading and in-water removal or installation of material shall be carried out by land-based equipment rather than from the stream or riverbed or within flowing water. Generally, work shall proceed from the downstream end to the upstream end of the project reach, unless specifically authorized on the approved plans.

25. Concrete Leachate During construction no fresh or wet concrete or leachate shall be allowed to escape into any wetland or water of New York State, nor shall washings from ready-mix concrete trucks, mixers, or other devices be allowed to enter any waters or wetlands. Wet concrete shall not be poured to displace water within the forms. Leakage from forms must be prevented from entering any wetland or water of New York State.

26. Seed/Mulch Streambanks Within one week of final grading, all areas of soil disturbance from this project shall be seeded with an appropriate perennial seed (grass or conservation mix) and, unless hydroseeded, mulched with straw. Mulch shall be maintained until a suitable vegetative cover is established. If seeding is impracticable due to the time of year, a temporary mulch shall be applied (with a temporary seeding of an annual cover species if appropriate) and final seeding shall be performed at the earliest opportunity when weather conditions favor germination and growth, but not more than six months after project completion.

27. Erosion Control Fabric Erosion control fabrics that will be left in place must be made from 100% biodegradable materials and contain no plastic fibers or netting. Fabrics containing "photodegradable" materials are expressly prohibited.

28. Equipment Cleaning Before equipment and materials are used in any project work area involving regulated waters, the equipment must be inspected for, and cleaned of, any visible soils, vegetation, and debris to prevent the potential introduction of invasive species into regulated waters from other areas.



29. Vegetation Debris Disposal Invasive species, host material and attached soil material that has been removed from vehicles, equipment, and materials, or generated from cleaning operations shall be rendered incapable of any growth or reproduction by placing in plastic bags at least 3 mil thick, hauled in a covered truck, and properly disposed of offsite; or the material shall be managed within the infested project area, provided that no filling of any wetlands or adjacent areas will occur. A list of prohibited and regulated invasive species is contained within 6 NYCRR Part 575 and available at <https://www.dec.ny.gov/animals/99141.html>.

30. Floodplains Fills within 100-year floodplains must comply with applicable Federal Emergency Management Agency (FEMA) approved state or local floodplain management requirements.

31. Limitations on Wetland Disturbance Temporary and permanent disturbances to state-regulated freshwater wetlands and wetland adjacent areas authorized under this permit are incidental to the activities authorized in protected streams and navigable waters, and must not exceed a combined total of 1/10th of one acre.

32. Native Plant Materials Unless otherwise allowed under this permit, only native plant materials shall be used for any project authorized under this general permit, and the use of non-native plant materials is prohibited.

33. No Interference With Navigation There shall be no unreasonable interference with navigation by the work herein authorized.

34. State May Order Removal or Alteration of Work If future operations by the State of New York require an alteration in the position of the structure or work herein authorized, or if, in the opinion of the Department of Environmental Conservation it shall cause unreasonable obstruction to the free navigation of said waters or flood flows or endanger the health, safety or welfare of the people of the State, or cause loss or destruction of the natural resources of the State, the owner may be ordered by the Department to remove or alter the structural work, obstructions, or hazards caused thereby without expense to the State, and if, upon the expiration or revocation of this permit, the structure, fill, excavation, or other modification of the watercourse hereby authorized shall not be completed, the owners, shall, without expense to the State, and to such extent and in such time and manner as the Department of Environmental Conservation may require, remove all or any portion of the uncompleted structure or fill and restore to its former condition the navigable and flood capacity of the watercourse. No claim shall be made against the State of New York on account of any such removal or alteration.

35. State May Require Site Restoration If upon the expiration or revocation of this permit, the project hereby authorized has not been completed, the applicant shall, without expense to the State, and to such extent and in such time and manner as the Department of Environmental Conservation may lawfully require, remove all or any portion of the uncompleted structure or fill and restore the site to its former condition. No claim shall be made against the State of New York on account of any such removal or alteration.

36. State Not Liable for Damage The State of New York shall in no case be liable for any damage or injury to the structure or work herein authorized which may be caused by or result from future operations undertaken by the State for the conservation or improvement of navigation, or for other purposes, and no claim or right to compensation shall accrue from any such damage.



WATER QUALITY CERTIFICATION SPECIFIC CONDITIONS

1. Water Quality Certification The authorized project, as conditioned pursuant to the Certificate, complies with Section 301, 302, 303, 306, and 307 of the Federal Water Pollution Control Act, as amended and as implemented by the limitations, standards, and criteria of state statutory and regulatory requirements set forth in 6 NYCRR Section 608.9(a). The authorized project, as conditioned, will also comply with applicable New York State water quality standards, including but not limited to effluent limitations, best usages and thermal discharge criteria, as applicable, as set forth in 6 NYCRR Parts 701, 702, 703, and 704.

GENERAL CONDITIONS - Apply to ALL Authorized Permits:

1. Facility Inspection by The Department The permitted site or facility, including relevant records, is subject to inspection at reasonable hours and intervals by an authorized representative of the Department of Environmental Conservation (the Department) to determine whether the permittee is complying with this permit and the ECL. Such representative may order the work suspended pursuant to ECL 71-0301 and SAPA 401(3).

The permittee shall provide a person to accompany the Department's representative during an inspection to the permit area when requested by the Department.

A copy of this permit, including all referenced maps, drawings and special conditions, must be available for inspection by the Department at all times at the project site or facility. Failure to produce a copy of the permit upon request by a Department representative is a violation of this permit.

2. Relationship of this Permit to Other Department Orders and Determinations Unless expressly provided for by the Department, issuance of this permit does not modify, supersede or rescind any order or determination previously issued by the Department or any of the terms, conditions or requirements contained in such order or determination.

3. Applications For Permit Renewals, Modifications or Transfers The permittee must submit a separate written application to the Department for permit renewal, modification or transfer of this permit. Such application must include any forms or supplemental information the Department requires. Any renewal, modification or transfer granted by the Department must be in writing. Submission of applications for permit renewal, modification or transfer are to be submitted to:

Regional Permit Administrator

In the DEC region where the project is located.

Directory at: <https://www.dec.ny.gov/about/39381.html>

4. Submission of Renewal Application The permittee must submit a renewal application at least 30 days before permit expiration for the following permit authorizations: Excavation & Fill in Navigable Waters, Freshwater Wetlands, Stream Disturbance, Water Quality Certification.



5. Permit Modifications, Suspensions and Revocations by the Department The Department reserves the right to exercise all available authority to modify, suspend or revoke this permit. The grounds for modification, suspension or revocation include:

- a. materially false or inaccurate statements in the permit application or supporting papers;
- b. failure by the permittee to comply with any terms or conditions of the permit;
- c. exceeding the scope of the project as described in the permit application;
- d. newly discovered material information or a material change in environmental conditions, relevant technology or applicable law or regulations since the issuance of the existing permit;
- e. noncompliance with previously issued permit conditions, orders of the commissioner, any provisions of the Environmental Conservation Law or regulations of the Department related to the permitted activity.

6. Permit Transfer Permits are transferrable unless specifically prohibited by statute, regulation or another permit condition. Applications for permit transfer should be submitted prior to actual transfer of ownership.

NOTIFICATION OF OTHER PERMITTEE OBLIGATIONS
--

Item A: Permittee Accepts Legal Responsibility and Agrees to Indemnification

The permittee, excepting state or federal agencies, expressly agrees to indemnify and hold harmless the Department of Environmental Conservation of the State of New York, its representatives, employees, and agents ("DEC") for all claims, suits, actions, and damages, to the extent attributable to the permittee's acts or omissions in connection with the permittee's undertaking of activities in connection with, or operation and maintenance of, the facility or facilities authorized by the permit whether in compliance or not in compliance with the terms and conditions of the permit. This indemnification does not extend to any claims, suits, actions, or damages to the extent attributable to DEC's own negligent or intentional acts or omissions, or to any claims, suits, or actions naming the DEC and arising under Article 78 of the New York Civil Practice Laws and Rules or any citizen suit or civil rights provision under federal or state laws.

Item B: Permittee's Contractors to Comply with Permit

The permittee is responsible for informing its independent contractors, employees, agents and assigns of their responsibility to comply with this permit, including all special conditions while acting as the permittee's agent with respect to the permitted activities, and such persons shall be subject to the same sanctions for violations of the Environmental Conservation Law as those prescribed for the permittee.

Item C: Permittee Responsible for Obtaining Other Required Permits

The permittee is responsible for obtaining any other permits, approvals, lands, easements and rights-of-way that may be required to carry out the activities that are authorized by this permit.



Item D: No Right to Trespass or Interfere with Riparian Rights

This permit does not convey to the permittee any right to trespass upon the lands or interfere with the riparian rights of others in order to perform the permitted work nor does it authorize the impairment of any rights, title, or interest in real or personal property held or vested in a person not a party to the permit.



DEPARTMENT OF THE ARMY
NEW YORK DISTRICT, CORPS OF ENGINEERS
JACOB K. JAVITS FEDERAL BUILDING
26 FEDERAL PLAZA
NEW YORK, NEW YORK 10278-0090

Regulatory Branch

January 31, 2025

SUBJECT: Permit Application Number NAN-2025-00088-MMI
by Town of Warwick – Ball Road Culvert Replacement

Town of Warwick
Attn: Jesse Dwyer
132 Kings Highway
Warwick, New York 10990

Dear Mr. Dwyer:

On January 16, 2025, the New York District of the U.S. Army Corps of Engineers received a request for Department of the Army authorization for the discharge of fill material into and/or the placement of structures in and over navigable waters of the United States. The proposed work includes the removal of an existing 41 foot long, 60-inch Ball Road culvert and replacement with a new 44-foot-long, 12-foot by 5-foot three sides culvert. The culvert replacement will include the replacement of the existing culvert structure, foundations, headwalls, wingwalls and roadway improvements including the discharge of approximately 1,313 cubic yards of stone, bedding and clean fill for stream bed establishment in the new culvert. The site is located at the intersection of Ball Road and South Street in an unnamed creek (Waters Index #855.5-223), in the Town of Warwick, Orange County, New York.

The specific applicant-provided details are as shown on the attached permit drawings titled "Ball Road Culvert Replacement", prepared by HDR, dated January 2025.

Based on the information submitted to this office, and accomplishment of notification in accordance with the applicable federal requirements, our review of the project indicates that an individual permit is not required. It appears that the activities within the jurisdiction of this office could be accomplished under Department of the Army Nationwide General Permit Number 3. The nationwide permits are prescribed as a Reissuance and Modification of Nationwide Permits in the Federal Register dated December 27, 2021 (86 FR 73522). The work may be performed without further authorization from this office provided the activity complies with the permit conditions listed in Section B, No. 3, Section C, any applicable New York District regional conditions, and any applicable regional conditions added by the State of New York, copies enclosed. The 2021 nationwide general permits in the State of New York, including their regional conditions, water quality certifications, and coastal zone management concurrence statements are also available at:

<https://www.nan.usace.army.mil/Missions/Regulatory/Nationwide-Permits/>.

Regulatory Branch

SUBJECT: Permit Application Number NAN-2025-00088-MMI
by Town of Warwick – Ball Road Culvert Replacement

- 2 -

This determination covers only the work described in the submitted material. Any major changes in the project may require additional authorizations from the New York District.

Care should be taken so that construction materials, including debris, do not enter any waterway to become drift or pollution hazards. You are to contact the appropriate state and local government officials to ensure that the subject work is performed in compliance with their requirements.

This verification is valid until March 14, 2026, unless the nationwide permit is modified, reissued, or revoked. This verification will remain valid until March 14, 2026, if the activity complies with the terms of any subsequent modifications of the nationwide permit authorization. If the nationwide permits are suspended, revoked, or modified in such a way that the activity would no longer comply with the terms and conditions of a nationwide permit, and the proposed activity has commenced, or is under contract to commence, the permittee shall have 12 months from the date of such action to complete the activity.

Within 30 days of the completion of the activity authorized by this permit and any mitigation required by this permit, you are to sign and submit the attached compliance certification form to this office.

In order for us to better serve you, please complete our Customer Service Survey located at <https://www.nan.usace.army.mil/Missions/Regulatory/Customer-Survey/>.

If any questions should arise concerning this matter, please contact me at Christopher.W.Minck@usace.army.mil.

Sincerely,

A handwritten signature in black ink, appearing to read "Christopher Minck", with a stylized flourish at the end.

Christopher Minck
Regulatory Subject Matter Expert
Metro NY/NJ Section

Enclosures

NATIONWIDE GENERAL PERMIT **COMPLIANCE CERTIFICATION** **AND REPORT FORM**

Permit File Number: NAN-2025-00088-MM

Permittee: Town of Warwick

Location: Intersection of Ball Road and South Street, Town of Warwick, Orange County, New York

Date Permit Letter Issued: January 31, 2025

Within 30 days of the completion of the activity authorized by this nationwide general permit and any mitigation required in the verification letter, please sign this certification and return it to the address at the bottom of this form.

Please note that your permitted activity is subject to a compliance inspection by a U.S. Army Corps of Engineers representative. If you fail to comply with the permit's terms and conditions you are subject to permit suspension, modification or revocation.

I hereby certify that the work authorized by the above referenced nationwide general permit has been completed in accordance with the terms and conditions of said permit, and required mitigation was completed in accordance with the permit conditions.

Signature of Permittee

Date


FOLD THIS FORM INTO THIRDS, WITH THE BOTTOM THIRD FACING OUTWARD. TAPE IT TOGETHER AND MAIL TO THE ADDRESS BELOW OR EMAIL TO CENAN-R-PERMIT-APP@USACE.ARMY.MIL.

PLACE
STAMP
HERE

DEPARTMENT OF THE ARMY
NEW YORK DISTRICT CORPS OF ENGINEERS
USACE OPERATIONS/REGULATORY 16-406
C/O PSC MAIL CENTER 26 FEDERAL PLAZA
NEW YORK, NEW YORK 10278



DEPARTMENT OF PUBLIC WORKS
TOWN OF WARWICK
ORANGE COUNTY, NEW YORK

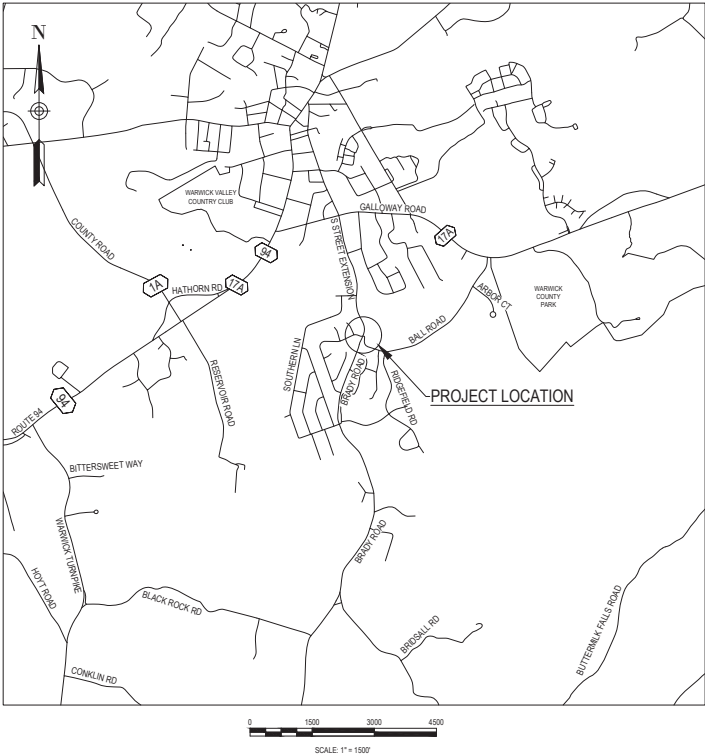

Contract Drawings For

Ball Road Culvert Replacement

Removal and Replacement of
Existing Culvert

Project No.
10400319

Town of Warwick, NY
January 2025

INDEX OF DRAWINGS	
SHEET	DESCRIPTION
01G-1.01	TITLE SHEET
01G-1.02	GENERAL NOTES, ABBREVIATIONS AND ESTIMATE OF QUANTITIES
01G-1.03	SURVEY PLAN
01C-1.01	TYPICAL SECTIONS
01C-1.02	ROADWAY PLAN AND PROFILE
01C-1.03	CULVERT PLAN AND PROFILE
01C-1.04	GUIDE RAILING PLAN
01C-1.05	PAVEMENT LAYOUT PLAN
01C-1.06	CONSTRUCTION DETAILS - 1
01C-1.07	CONSTRUCTION DETAILS - 2
01C-1.08	EROSION CONTROL DETAILS
01C-1.09	DETOUR PLAN
01S-1.01	CULVERT EARTHWORK DETAILS
01S-1.02	PRECAST CULVERT PLAN AND ELEVATION
01S-1.03	LONGITUDINAL ELEVATION
01S-1.04	PRECAST WINGWALL DETAILS

RECOMMENDED BY:

01XAGS
BENJAMIN D. ASTORINO
TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS COMMISSIONER

DATE

IT IS A VIOLATION OF LAW FOR ANY PERSON, UNLESS THEY ARE ACTING UNDER THE DIRECTION OF A LICENSED PROFESSIONAL ENGINEER, ARCHITECT, LANDSCAPE ARCHITECT, OR LAND SURVEYOR, TO ALTER AN ITEM IN ANY WAY. IF AN ITEM BEARING THE STAMP OF A LICENSED PROFESSIONAL IS ALTERED, THE ALTERING ENGINEER, ARCHITECT, LANDSCAPE ARCHITECT, OR LAND SURVEYOR SHALL STAMP THE DOCUMENT AND INCLUDE THE NOTATION "ALTERED BY" FOLLOWED BY THEIR SIGNATURE, THE DATE OF SUCH ALTERATION, AND A SPECIFIC DESCRIPTION OF THE ALTERATION.

DRAWINGS PREPARED BY:

Jim Jankel
JESSE R. JANKEL, P.E.
HDR
N.Y.S. P.E. NO. 002789

01-15-25
DATE

GENERAL NOTES:

- DESIGN SPECIFICATIONS NEW YORK STATE DEPARTMENT OF TRANSPORTATION STANDARD SPECIFICATIONS FOR HIGHWAY BRIDGES WITH ALL PROVISIONS IN EFFECT AS OF NOVEMBER 2022.
2. FOOTINGS ARE DESIGNED USING AASHTO STANDARD SPECIFICATIONS, 17TH EDITION.
3. LIVE LOAD: HL-93
4. CONSTRUCTION AND MATERIALS SPECIFICATIONS: STANDARD SPECIFICATIONS, CONSTRUCTION AND MATERIALS, NEW YORK STATE DEPARTMENT OF TRANSPORTATION, OFFICE OF ENGINEERING, MAY 1, 2024 AND ANY ASSOCIATED ADDENDUMS.
5. CONTRACTOR'S FABRICATOR IS RESPONSIBLE FOR THE DESIGN OF THE PRECAST THREE SIDED CULVERT AND PRECAST WINGWALLS BASED ON THE THREE SIDED CULVERT DESIGN DATA AND OTHER DETAILS PROVIDED IN THE PROJECT PLANS. CONTRACTOR TO TAKE NOTICE THAT THIS STRUCTURE MUST BE CONSTRUCTED IN ACCORDANCE WITH NYSDOT REGULATIONS AND SPECIFICATIONS. DRAWINGS SHALL BE STAMPED AND SIGNED BY A NY STATE REGISTERED PE.
6. THE CONTRACTOR SHALL PREPARE AND SUBMIT A LIFTING PLAN IN ACCORDANCE WITH NYSDOT SECTION 107.05 SAFETY AND HEALTH REQUIREMENTS, SECTION P (LIFTING) STAMPED AND SIGNED BY A NY STATE REGISTERED PE.
7. ALL SHOP DRAWINGS SUBMITTED FOR THIS PROJECT SHALL BE IN US CUSTOMARY.
8. THE COST OF ALL JOINT MATERIAL SHALL BE INCLUDED IN THE UNIT PRICES BID FOR VARIOUS ITEMS IN THE CONTRACT, UNLESS OTHERWISE SPECIFIED IN THE PLANS.
9. THE CONTRACTOR SHALL PERFORM ALL WORK WITH CARE SO THAT ANY MATERIALS WHICH ARE TO REMAIN IN PLACE, OR WHICH ARE TO REMAIN THE PROPERTY OF THE TOWN, WILL NOT BE DAMAGED. IF THE CONTRACTOR DAMAGES ANY MATERIALS WHICH ARE TO REMAIN IN PLACE, OR WHICH ARE TO REMAIN THE PROPERTY OF THE TOWN, THE DAMAGED MATERIALS SHALL BE REPAIRED OR REPLACED IN A MANNER SATISFACTORY TO THE TOWN ENGINEER AT THE EXPENSE OF THE CONTRACTOR.
10. NO PAYMENT WILL BE MADE FOR WORK CALLED FOR BY NOTES, ON THE PLANS, OR IN THE SPECIFICATIONS UNLESS PAYMENT IS SPECIFICALLY INDICATED BY AN ITEM NUMBER. THE COST OF WORK FOR WHICH NO PAYMENT IS INDICATED SHALL BE INCLUDED IN THE UNIT PRICE BID FOR THE VARIOUS ITEMS OF THE CONTRACT.
11. ALL WORK ZONE TRAFFIC CONTROL, INCLUDING MAINTENANCE AND PROTECTION OF TRAFFIC PROCEDURES AND ALL TEMPORARY TRAFFIC CONTROL DEVICES SHALL COMPLY WITH NEW YORK STATE MANUAL OF TRAFFIC CONTROL DEVICES OR AS MODIFIED BY THE ENGINEER TO SUIT FIELD CONDITIONS.
12. REINFORCING STEEL SHALL CONFORM TO ASTM SPECIFICATION A615 AND FURNISHED AS GRADE 60.
13. ALL REINFORCING STEEL TO BE EPOXY COATED.
14. REINFORCING SHALL HAVE 3" COVER UNLESS NOTED OTHERWISE.
15. THE CONTRACTOR'S ATTENTION IS DIRECTED TO THE FACT THAT, DUE TO THE NATURE OF RECONSTRUCTION PROJECTS, THE EXACT EXTENT OF RECONSTRUCTION WORK CANNOT ALWAYS BE ACCURATELY DETERMINED PRIOR TO THE COMMENCEMENT OF WORKS. THESE CONTRACT DOCUMENTS HAVE BEEN PREPARED BASED ON FIELD INSPECTIONS AND OTHER INFORMATION AVAILABLE AT THE TIME. ACTUAL FIELD CONDITIONS MAY REQUIRE MODIFICATIONS TO CONSTRUCTION DETAILS AND WORK QUANTITIES. THE CONTRACTOR SHALL PERFORM THE WORK IN ACCORDANCE WITH FIELD CONDITIONS.
16. BASED ON THE AVAILABLE DATA, THE DEPTH OF GROUND WATER IS APPROXIMATELY 7 TO 8 FEET BELOW THE EXISTING ROADWAY ELEVATION AT THE CULVERT AND MAY VARY. THE COST OF DEWATERING SHALL BE INCLUDED IN VARIOUS ITEMS OF THE CONTRACT. TO SEE THE FOUNDATION DESIGN REPORT FOR BALL ROAD CULVERT REPLACEMENT BY TECTONIC ENGINEERING CONSULTANTS, GEOLOGISTS & LAND SURVEYORS, D.P.C. DATED DECEMBER 5, 2023 FOR GROUNDWATER MANAGEMENT MEASURES.
17. CONTRACTOR SHALL PERFORM HIS OPERATIONS TO MINIMIZE AREAS OF DISTURBANCE. ALL DISTURBED AREAS SHALL BE FULLY RESTORED TO THE ORIGINAL CONDITION. FOR CULVERT WORK, COST OF TOP SOIL, PERMANENT SEEDING, ETC. SHALL BE INCLUDED IN THE VARIOUS PAYMENT ITEMS. FOR STREAM RESTORATION WORK, TOPSOIL AND SEEDING PAY ITEMS ARE INCLUDED.
18. THE CONTRACTOR SHALL PROTECT HIS WORKERS AT ALL TIMES IN CONFORMANCE WITH APPLICABLE OSHA REQUIREMENTS.
19. THE PROJECT IS ANTICIPATED TO BE AUTHORIZED UNDER NYSDEC ARTICLE 15 AND USACE PERMIT, NATIONWIDE PERMIT #3 (MAINTENANCE). COPIES OF THE PERMITS SHALL BE POSTED AT THE PROJECT SITE. THE WORK SHOULD BE COMPLETED FOLLOWING THE GENERAL, REGIONAL, AND ANY PROJECT-SPECIFIC CONDITIONS IN THE PERMITS. THE ENGINEER SHALL BE NOTIFIED WHEN ANY PERMIT CONDITIONS CANNOT BE MET.
20. CONTRACTOR SHALL SUBMIT A DEWATERING AND EROSION AND SEDIMENT CONTROL PLAN TO THE ENGINEER FOR APPROVAL PRIOR TO THE START OF WORK.
21. EROSION CONTROL MEASURES NOT LISTED FOR PAYMENT UNDER THE SPECIFIC ITEMS UNDER THIS CONTRACT SHALL BE INCLUDED UNDER THE VARIOUS PAY ITEMS WITHIN THIS CONTRACT.
22. IF THE CONTRACTOR EXPOSES TRANSITE PIPE, JOINT CAULKING, OR SIMILAR ITEMS DURING DEMOLITION WHICH MAY CONTAIN HAZARDOUS MATERIALS, THE MATERIALS SHALL BE TESTED AND DISPOSED OF IN ACCORDANCE WITH LOCAL, STATE AND FEDERAL REGULATIONS.

REMOVAL NOTES:

- WHENEVER ITEMS IN THE CONTRACT REQUIRE MATERIALS TO BE REMOVED AND DISPOSED OF, THE COST OF SUPPLYING A DISPOSAL AREA AND TRANSPORTATION TO THAT AREA SHALL BE INCLUDED IN THE UNIT PRICES BID FOR THOSE ITEMS.
- THE EXISTING 68'X72' CMP CULVERT SHALL BE REMOVED UNDER ITEM 202.19.
- PRIOR TO SUBMITTION OF THE BID THE CONTRACTOR SHALL SURVEY THE PROJECT SITE TO ESTIMATE THE REQUIRED AMOUNT OF TREE REMOVAL WITHIN THE TOWN OF WARWICK AND THE VILLAGE OF WARWICK RIGHT-OF-WAY NECESSARY TO COMPLETE THE WORK.
- ALL TREES, SHRUBS AND BRUSH REQUIRED TO BE REMOVED TO COMPLETE ITEMS UNDER THIS CONTRACT SHALL BE INCLUDED IN CONTRACTOR BID AND WILL BE PAID FOR UNDER ITEM 201.06. ALL REMOVALS SHALL BE APPROVED BY THE ENGINEER IN ADVANCE.
- THE CONTRACTOR'S ATTENTION IS DIRECTED TO THE REQUIREMENTS OF SUBSECTION 202-3.01 GENERAL AND SAFETY REQUIREMENTS. A REMOVAL PLAN SHALL BE SUBMITTED TO THE ENGINEER FIFTEEN (15) DAYS PRIOR TO BEGINNING OF THE WORK. THE REQUIREMENT THAT IT BE SIGNED BY A REGISTERED PROFESSIONAL ENGINEER IS WAIVED.
- THE COST OF FURNISHING, INSTALLING, MAINTAINING, REMOVING AND DISPOSING OF ALL PLATFORMS, NETS, SCREENS, SHIELDS OR OTHER PROTECTIVE DEVICES SHALL BE INCLUDED IN THE UNIT PRICES BID FOR THE APPROPRIATE ITEMS OF THE CONTRACT.

UTILITY NOTES:

- THE ACCURACY INDICATED FOR THE LOCATIONS OF OVERHEAD AND UNDERGROUND UTILITIES SHOWN ON THESE PLANS ARE DEFINED AS FOLLOWS:
- A. THIS INFORMATION DOES NOT RELIEVE THE CONTRACTOR OF HIS OBLIGATIONS UNDER SECTIONS 660 THROUGH 680 OF THE STANDARD SPECIFICATIONS, NOR DOES IT RELIEVE THE UTILITY OWNERS OF THEIR OBLIGATION TO ACCURATELY LOCATE THEIR FACILITIES.
 - B. ALL KNOWN PUBLIC AND PRIVATE UTILITY LINES WITHIN OR ADJACENT TO THE SITE OF THE WORK AND SHOWN ON THEIR EXISTING APPROXIMATE LOCATIONS ON THE CONTRACT PLANS. THE CONTRACTOR IS CAUTIONED THAT THESE LOCATIONS ARE NOT GUARANTEED NOR IS THERE A GUARANTEE THAT ALL SUCH LINES IN EXISTENCE HAVE BEEN SHOWN ON THE PLANS.
 - C. ADDITIONAL UTILITY LINES, WHETHER ABANDONED OR IN SERVICE, MAY EXIST AND IT SHALL BE THE CONTRACTOR'S RESPONSIBILITY TO CONDUCT HIS OPERATIONS AND TAKE THE NECESSARY PRECAUTIONS TO PREVENT INTERFERENCE WITH OR DAMAGE TO THESE OR OTHER FACILITIES DURING THE COURSE OF CONSTRUCTION.
 - D. THE CONTRACTOR SHALL CONDUCT HIS OPERATIONS AS TO PREVENT DAMAGE TO SUCH FACILITIES. HE SHALL MAKE SUCH EXPLORATIONS AS MAY BE NECESSARY TO DETERMINE THE DIMENSIONS AND LOCATIONS OF LINES THAT MAY BE SUBJECT TO DAMAGE. NOTIFICATION TO THE VARIOUS OWNERS OF FACILITIES SHALL BE IN ACCORDANCE WITH NEW YORK STATE INDUSTRIAL CODE 753, CURRENT EDITION.
 - E. THE CONTRACTOR SHALL SATISFY HIMSELF AS TO THE EXACT LOCATION OF UTILITY LINES AND SHALL PROTECT AND SUPPORT IN A SUITABLE MANNER AT HIS OWN EXPENSE ALL UNDERGROUND UTILITIES ENCOUNTERED IN HIS EXCAVATING AND TRENCHING OPERATIONS. THE CONTRACTOR SHALL MAKE GOOD ANY DAMAGE TO THOSE UTILITIES CAUSED BY THE NATURE OF THE DAMAGE IS SUCH AS TO EXHAUST THE UTILITY'S CAPABILITY OF SATISFACTORY OPERATIONS OF THE UTILITIES AND THE NECESSARY REPAIRS ARE NOT IMMEDIATELY MADE BY THE CONTRACTOR, THE WORK MAY BE DONE BY THE RESPECTIVE OWNING COMPANIES AND THE COST THEREOF CHARGED AGAINST THE CONTRACTOR.
 - F. PRIOR TO THE COMMENCEMENT OF CONSTRUCTION, THE CONTRACTOR SHALL MEET WITH ALL THE KNOWN PUBLIC AND PRIVATE UTILITY COMPANIES OCCUPYING THE WORK SITE. THE CONTRACTOR SHALL AT THIS MEETING INFORM THE UTILITY COMPANIES OF HIS SCHEDULE OF OPERATIONS AND SO COORDINATE HIS WORK WITH THESE COMPANIES.

STREAM PROTECTION NOTES:

1. ANY CONSTRUCTION IN THE STREAM MUST TAKE PLACE BETWEEN JUNE 1ST AND SEPTEMBER 30TH.
2. THE CREEK TRIBUTARY IS CLASSIFIED AS A CLASS C(1) WATERBODY AT THIS LOCATION.
3. STREAM FLOW SHALL BE MAINTAINED DURING THE WORK. CONTRACTOR SHALL PROVIDE METHOD OF MAINTAINING STREAM FLOW TO THE ENGINEER FOR APPROVAL PRIOR TO START OF CONSTRUCTION. THE COST OF MAINTAINING STREAM FLOW SHALL BE INCLUDED IN VARIOUS ITEMS IN THE CONTRACT.
4. DURING THE COURSE OF CONSTRUCTION, THE CONTRACTOR SHALL CONDUCT OPERATIONS IN SUCH A MANNER AS TO PREVENT ANY DAMAGE TO ANY STREAM FROM POLLUTION BY DEBRIS, SEDIMENTATION OR OTHER FOREIGN MATERIAL. SO AS TO CATCH THE MATERIAL, THE ENGINEER RECOMMENDS THAT ADEQUATE PROTECTIVE DEVICES ARE NOT BEING EMPLOYED. THE WORK SHALL BE SUSPENDED UNTIL ADEQUATE PROTECTION IS PROVIDED. THE LOCATION FOR STOCKPILING OF MATERIAL SHALL BE COORDINATED WITH AND APPROVED BY THE ENGINEER PRIOR TO REMOVAL OF MATERIAL. STOCKPILING OF MATERIAL SHALL BE LOCATED UPSTREAM OF THE WATER COURSE AND EROSION CONTROL MEASURES SHALL BE DEPLOYED TO CONTAIN THE MATERIAL FROM MIGRATING.
5. DURING REMOVAL OPERATIONS, THE CONTRACTOR SHALL NOT BE ALLOWED TO DROP CONCRETE WASTE, DEBRIS, AND OTHER MATERIAL INTO THE WATER COURSE, PLATFORMS, NETS, SCREENS, OR OTHER PROTECTIVE DEVICES SHALL BE USED TO CATCH THE MATERIAL. THE ENGINEER RECOMMENDS THAT ADEQUATE PROTECTIVE DEVICES ARE NOT BEING EMPLOYED. THE WORK SHALL BE SUSPENDED UNTIL ADEQUATE PROTECTION IS PROVIDED. THE LOCATION FOR STOCKPILING OF MATERIAL SHALL BE COORDINATED WITH AND APPROVED BY THE ENGINEER PRIOR TO REMOVAL OF MATERIAL. STOCKPILING OF MATERIAL SHALL BE LOCATED UPSTREAM OF THE WATER COURSE AND EROSION CONTROL MEASURES SHALL BE DEPLOYED TO CONTAIN THE MATERIAL FROM MIGRATING.
6. THE EXISTING STREAMBED SHALL NOT BE DISTURBED BEYOND THE LIMITS SHOWN ON THE PLANS. STREAM DIVERSION OR CONTAINMENT METHODS SHALL BE SIZED WITH REGARD TO THE NATURAL FLOW OF THE STREAM. THE COST OF DEWATERING SHALL BE INCLUDED IN VARIOUS ITEMS IN THE CONTRACT.

ABBREVIATIONS:

GENERAL		GENERAL	
B	BASELINE	R&D	REMOVE AND DISPOSE
BW	BOTTOM OF WALL	R&R	REMOVE AND RESET
C	CENTERLINE	RCP	REINFORCED CONCRETE PIPE
INV	INVERT	RET	RETAIN
LF	LINEAR FEET	SPA	SPACE
MAX	MAXIMUM	STA	STATION
MIN	MINIMUM	TPY	TYPICAL
OFF	OFFSET	TW	TOP OF WALL
PROP	PROPOSE		

ESTIMATE OF QUANTITIES:

ESTIMATE OF QUANTITIES			
ITEM	DESCRIPTION	UNIT	QUANTITY
201.06	CLEARING AND GRUBBING	LS	1
202.19	REMOVAL OF SUBSTRUCTURES	CY	45
203.02	UNCLASSIFIED EXCAVATION AND DISPOSAL	CY	180
203.03	EMBANKMENT IN PLACE (CULVERT)	CY	110
203.07	SELECT GRANULAR FILL	CY	40
207.21	GEOTEXTILE SEPARATION	SY	175
209.13	SILT FENCE-TEMPORARY	LF	465
210.3001	REMOVAL AND DISPOSAL OF CONCRETE-ENCASED PIPE ACM	LF	5
304.12	SUBBASE COURSE, TYPE 2 (1 1/2" DEPTH)	CY	290
404.0683	6.3 F3 TOP COURSE ASPHALT, 80 SERIES COMPACTION (1" DEPTH)	TON	20
404.1279	12.5 F9 BINDER COURSE ASPHALT, 70 SERIES COMPACTION (2" DEPTH)	TON	40
404.3779	37.5 F19 BASE COURSE ASPHALT, 70 SERIES COMPACTION (4" DEPTH)	TON	75
556.0202	EPOXY-COATED BAR REINFORCEMENT FOR STRUCTURES (REBAR IN CLOSURE POUR #4 BARS)	LB	321
556.0202	EPOXY-COATED BAR REINFORCEMENT FOR STRUCTURES (WINGWALL UNIT REINFORCEMENT #4 BARS)	LB	1123
562.0101	PRECAST THREE SIDE STRUCTURE	SY	65
562.03	WINGWALL WITH FOOTING (CONCRETE)	SY	10
595.98200018	SPRAY-APPLIED WATERPROOF MEMBRANE	SF	690
606.10	BOX BEAM GUIDE RAILING	LF	340
606.100003	BOX BEAM GUIDE RAILING (SHOP MITERED)	LF	45
606.120201	BOX BEAM GUIDE RAILING, END ASSEMBLY, TYPE IIA	EA	2
606.71000015	REMOVE AND DISPOSE OF CORRUGATED BEAM GUIDE RAILING AND STORE POSTS	LF	220
606.8101	GUIDE RAIL TRANSITION WEAK-POST CORRUGATED BEAM TO BOX BEAM GUIDE RAIL (ONE OR TWO-WAY OPERATION)	EA	1
606.8201	GUIDE RAIL TRANSITION BOX BEAM TO WEAK-POST CORRUGATED BEAM GUIDE RAIL (ONE WAY ONLY)	EA	1
608.020101	3" VEGETATION CONTROL STRIP	CY	20
610.1402	4" TOPSOIL ROADSIDE	CY	30
615.01010108	MATERIAL FOR STREAM BED ESTABLISHMENT	CY	50
619.01	BASIC WORK ZONE TRAFFIC CONTROL	LS	1
619.04	TYPE III CONSTRUCTION BARRICADES	EA	5
619.1701	TEMPORARY CONCRETE BARRIER	LF	100
620.04	STONE FILL - MEDIUM (GENERALLY 100 LB MIN, 6")	CY	10
623.12	CRUSHED STONE (IN-PLACE MEASURE)	CY	10
645.13070010	REINSTALL GUIDE SIGN POSTS	ELOC	1
645.13080010	REINSTALL SIGN PANELS ASSEMBLIES	SF	2
699.040001	MOBILIZATION/DEMOBILIZATION	LS	1


C:\PWW\CRKING\EA\ST01D3857543.10400319-00G-102 GENERAL NOTES.DWG
20/11/2023 8:27:10 AM

[illegible]

TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

GENERAL NOTES, ABBREVIATIONS
AND ESTIMATE OF QUANTITIES
BALL ROAD


SHEET
01G-1.02

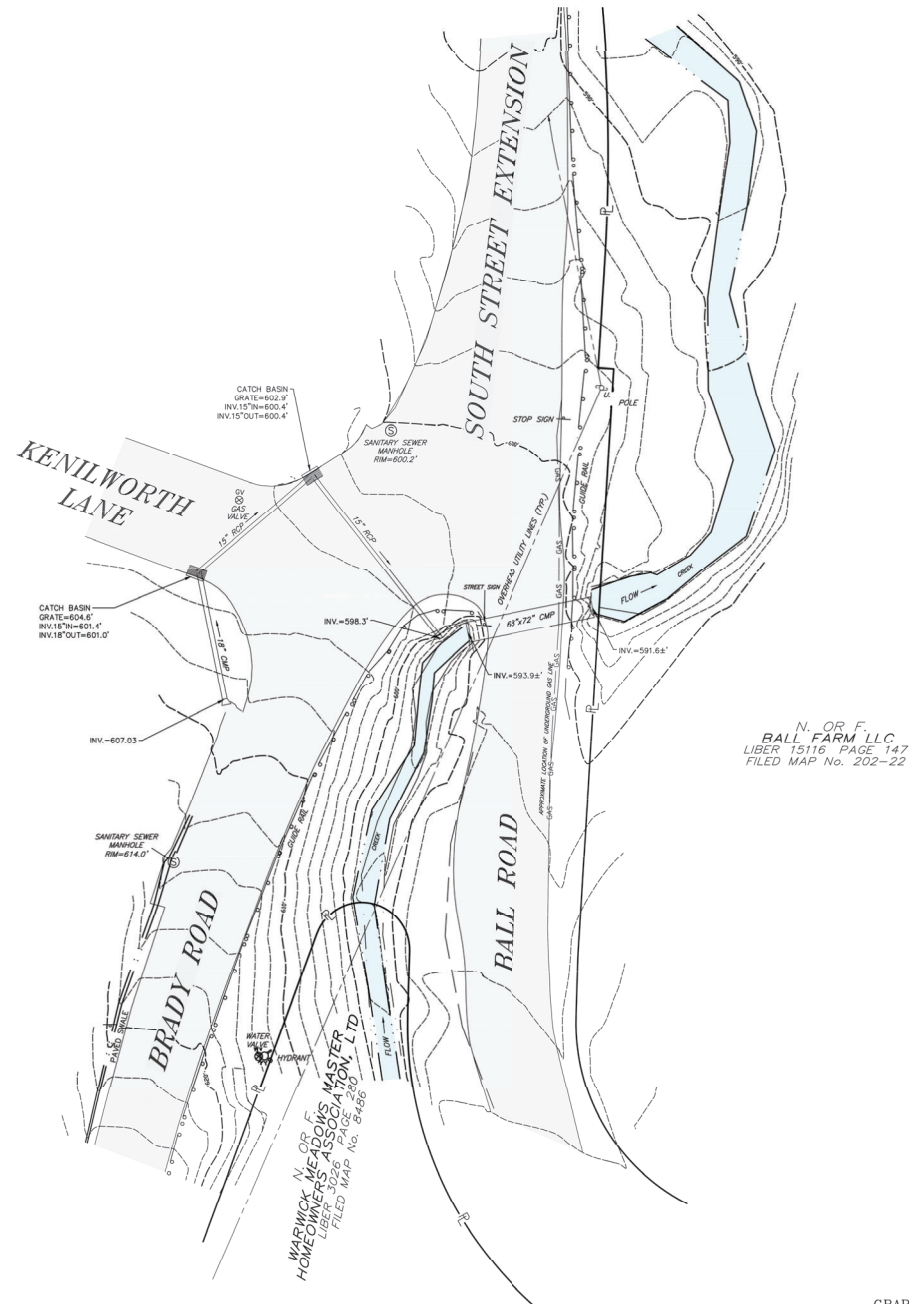

MAP NOTES

1. PROPERTY LINES SHOWN HEREON ARE BASED ON DEEDS OF RECORD AND MONUMENTATION FOUND IN THE FIELD.
2. UNDERGROUND UTILITY LOCATIONS ARE BASED ON FIELD MARKINGS BY OTHERS. ALL UTILITY LOCATIONS SHALL BE VERIFIED. UTILITY LINE DEPTHS SHALL BE VERIFIED PRIOR TO ANY CONSTRUCTION COMMENCING.
3. HORIZONTAL DATUM: NEW YORK STATE PLANE.
4. VERTICAL DATUM: NAVD 1989
5. WE DO HEREBY CERTIFY THAT THIS MAP IS THE RESULT OF AN ACTUAL FIELD SURVEY COMPLETED ON SEPTEMBER 15, 2023

GRAPHIC SCALE




COPIES OF THIS SURVEY NOT BEARING THE EMBOSSED SEAL OF THE LAND SURVEYOR SHALL NOT BE VALID. GUARANTEES OF CERTIFICATIONS ARE NOT TRANSFERABLE TO ADDITIONAL INSTITUTIONS OR SUBSEQUENT OWNERS.

UNAUTHORIZED ALTERATION OF THIS DOCUMENT, IN ANY WAY, CONSTITUTES A VIOLATION OF THE NEW YORK STATE EDUCATION LAW, SECTION 7209, SUB-DIVISION 2.

JOHN A. McGLOIN, N.Y. LIC.#49689
PROFESSIONAL LAND SURVEYOR
32 COLONIAL AVENUE
WARWICK, NEW YORK 10990

ROBERT H. SCHMICK N.Y. LIC. #50573
PROFESSIONAL LAND SURVEYOR
5 OVERLOOK DR.
WARWICK, NEW YORK 10990

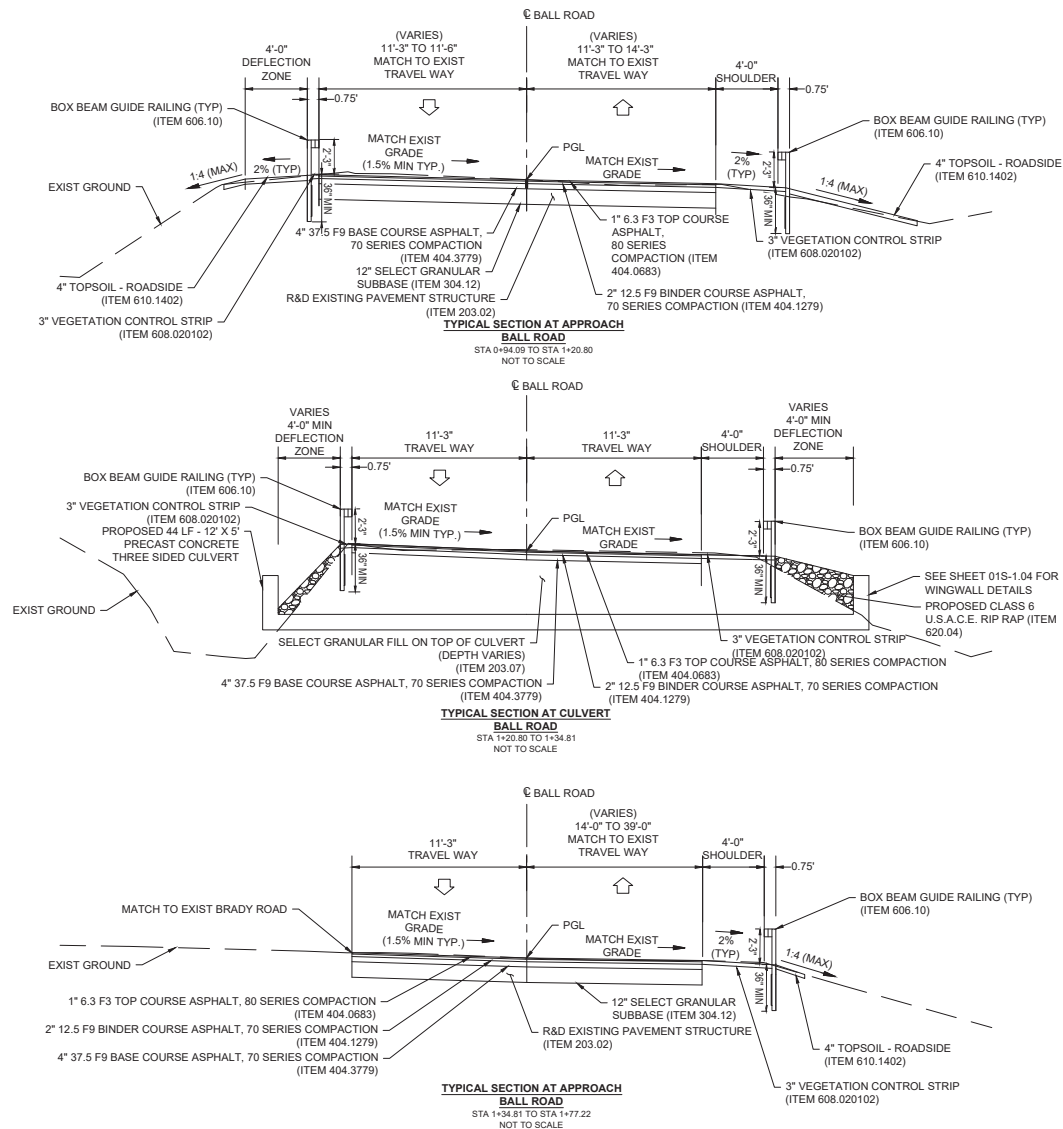

C:\PWW\CRKING\EA\ST01D3857543\10400319-0\IC-1.01 TYPICAL SECTIONS.DWG
7/17/2024 10:51:53 PM



			PROJECT NUMBER	DATE DUE
1	7-15-06	ISSUED FOR PERMITTING		
ISSUE	DATE	DESCRIPTION	PROJECT NUMBER	10000319




TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

TYPICAL SECTIONS BALL ROAD

SHEET
01C-1.01



SHEET
01C-1.02

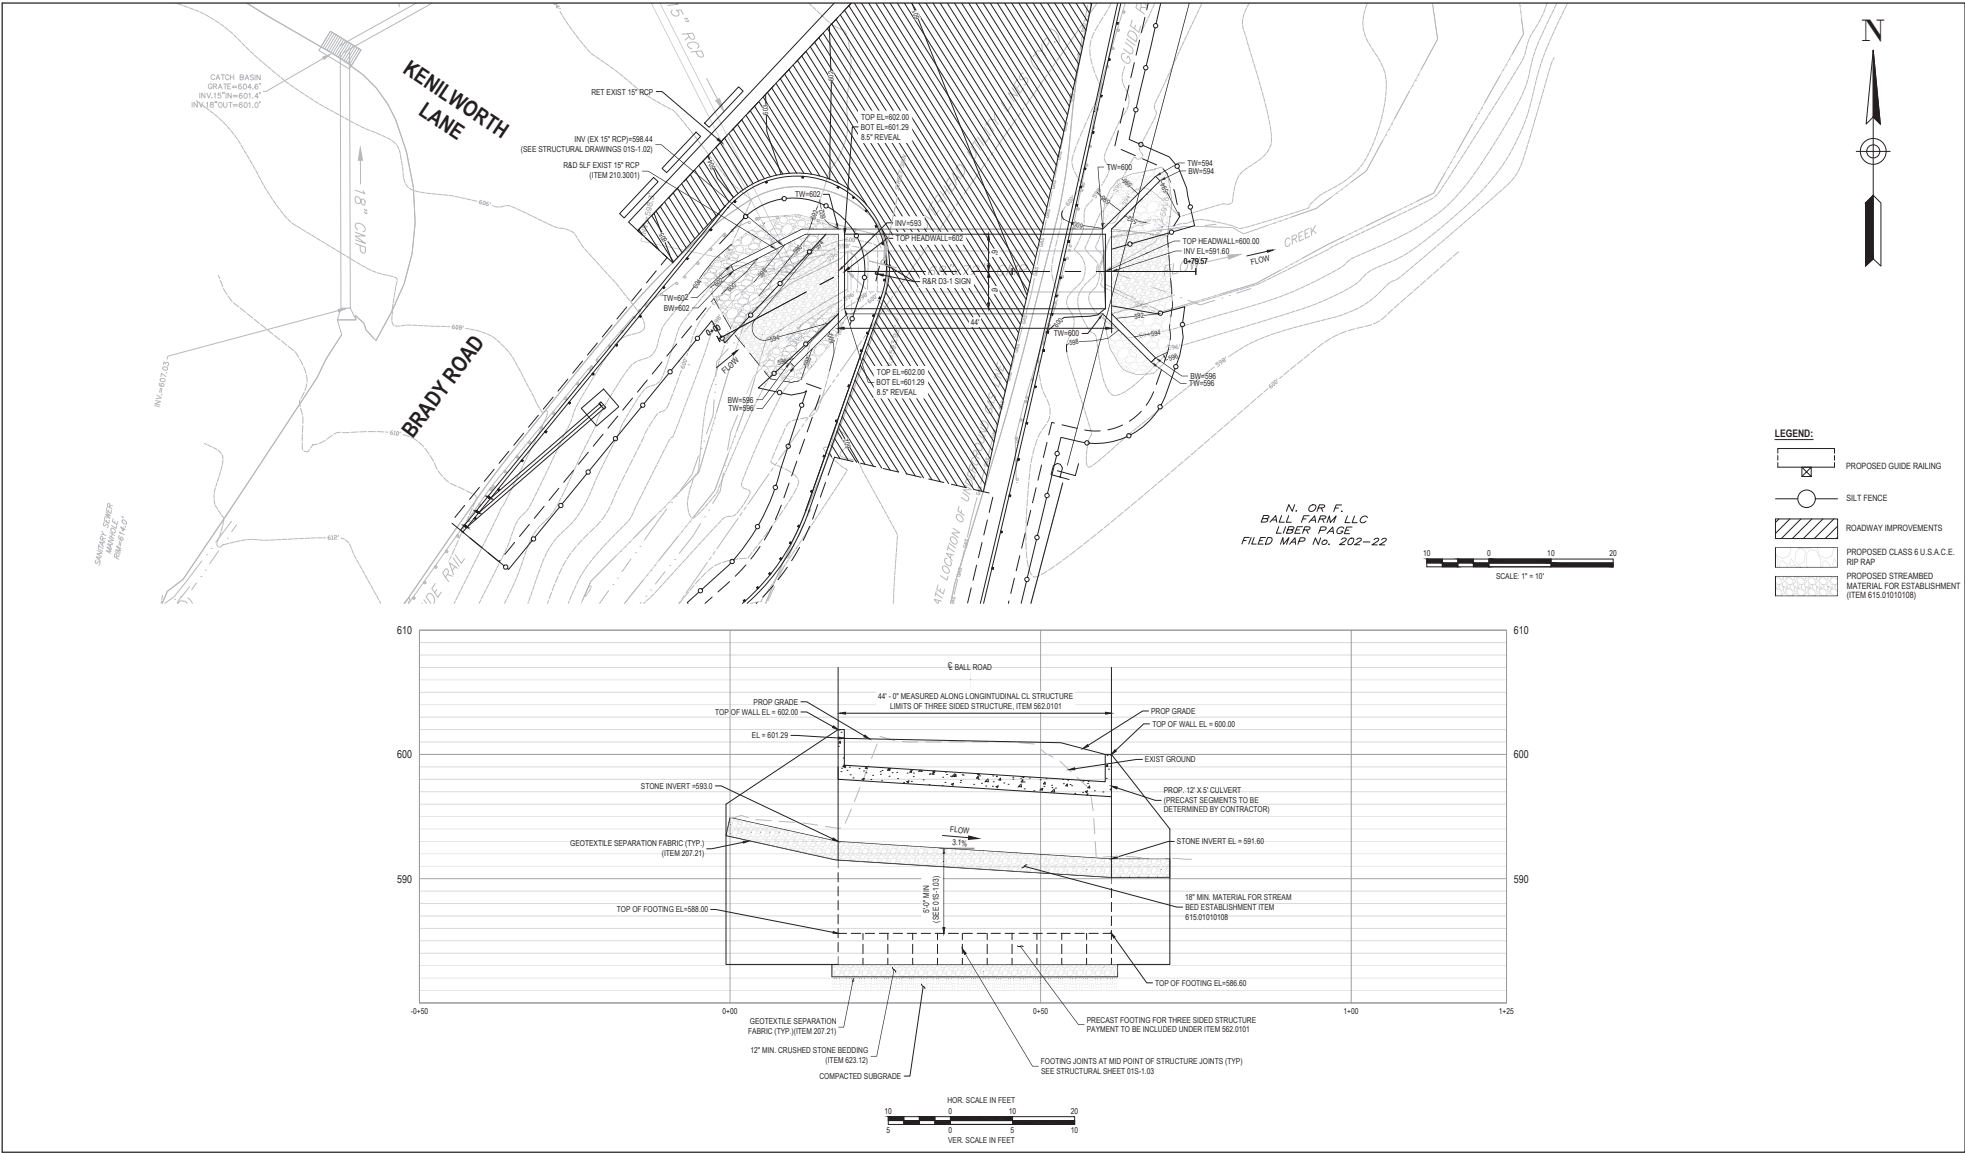

C:\P\WORKING\2025\10352543\1000319\5-1.02\ROADWAY PLAN AND PROFILE.DWG
1/31/2025 8:27:19 AM



1	1-15-25	ISSUED FOR PERMITTING
ISSUE DATE DESCRIPTION		


PROJECT MANAGER LAURA BARCA	
PROJECT NUMBER 10400319	




TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

CULVERT PLAN AND PROFILE
BALL ROAD

SHEET
01C-1.03

[illegible]

SHEET
01C-1.04

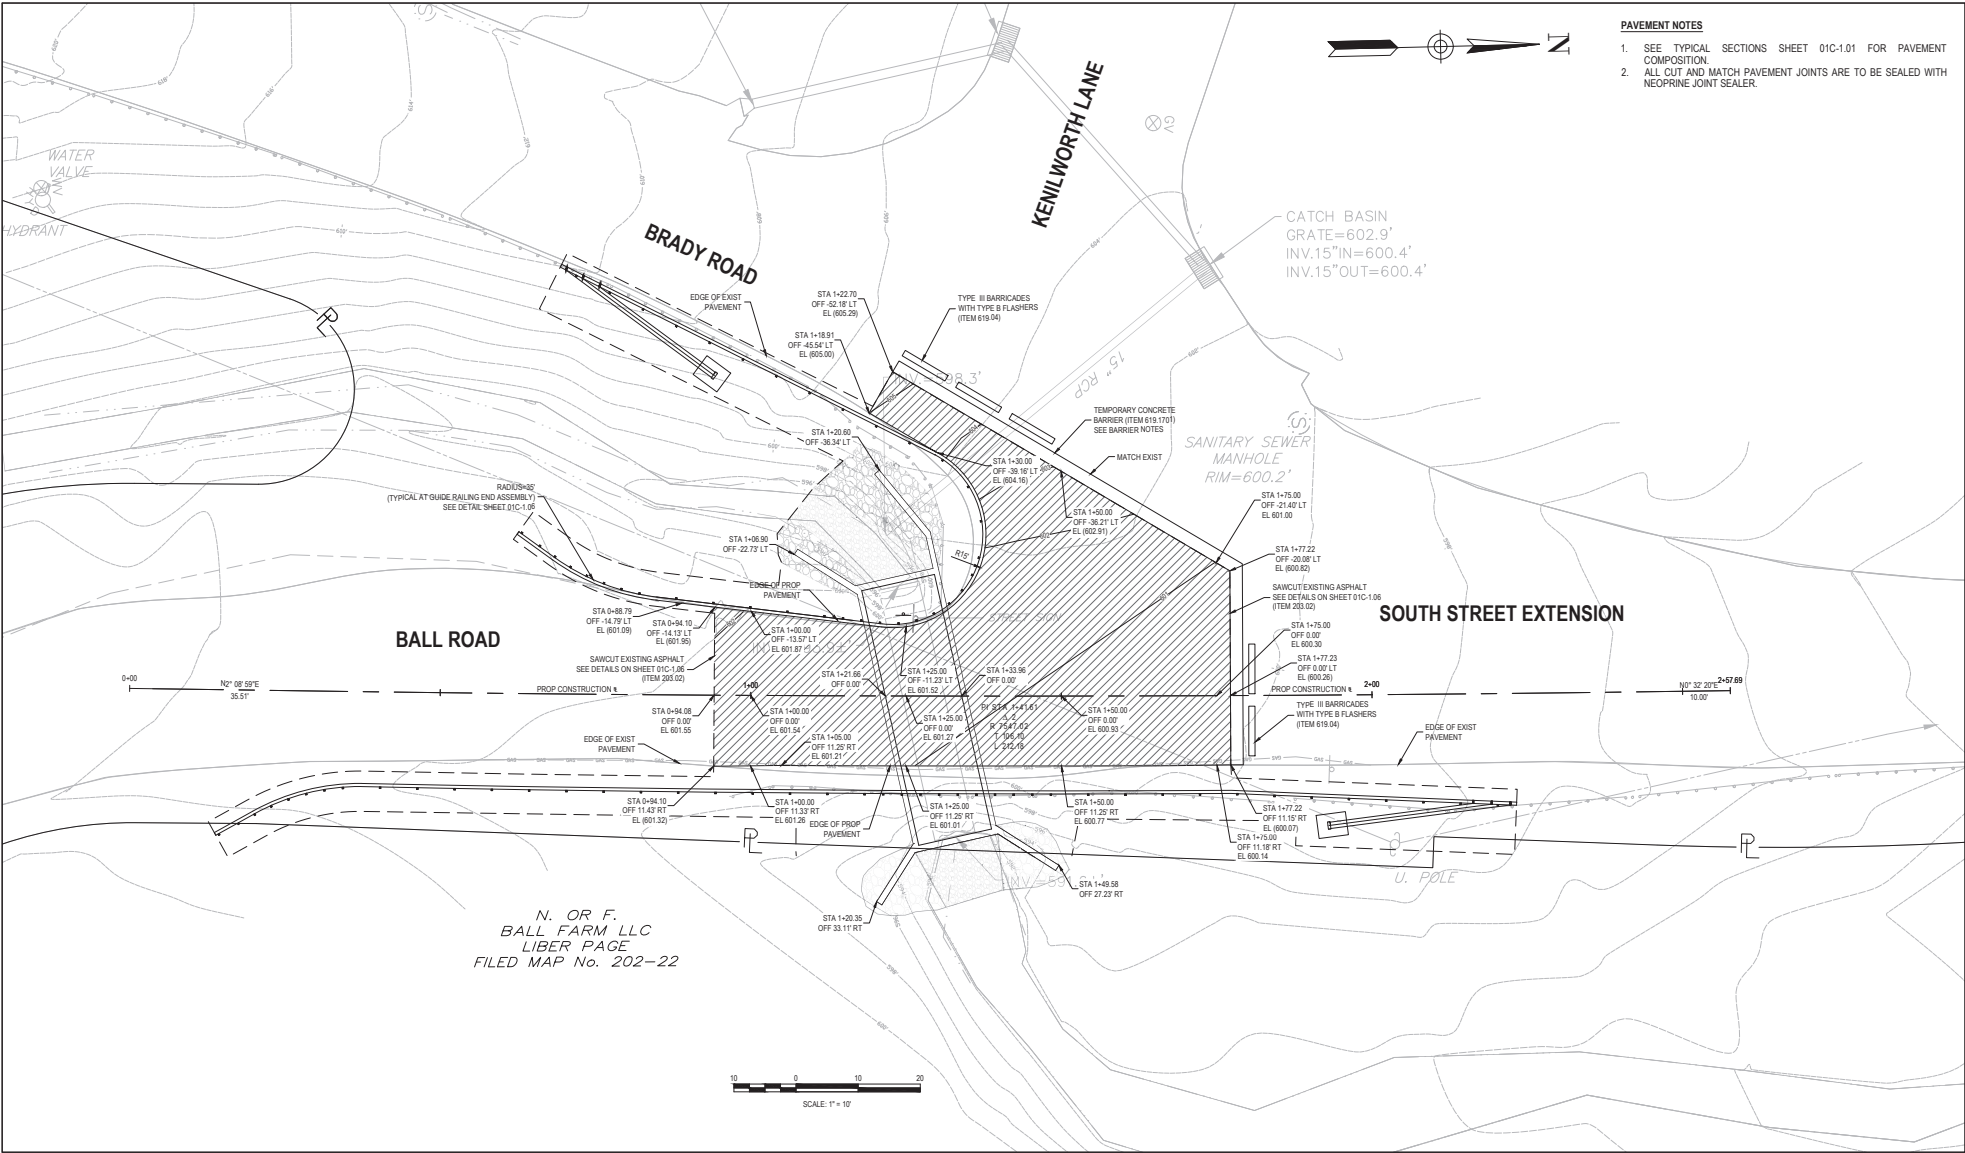

- PAVEMENT NOTES**
1. SEE TYPICAL SECTIONS SHEET 01C-1.01 FOR PAVEMENT COMPOSITION.
 2. ALL CUT AND MATCH PAVEMENT JOINTS ARE TO BE SEALED WITH NEOPRENE JOINT SEALER.

C:\P\WORKING\2025\10355\4310002039-05-C-1-04 PAVEMENT LAYOUT PLAN.DWG
07/02/2025 12:34:43 PM



ISSUE	DATE	DESCRIPTION
1	1-16-25	ISSUED FOR PERMITTING


PROJECT MANAGER: LAURA BARCA
PROJECT NUMBER: 10400319



TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

PAVEMENT LAYOUT PLAN
BALL ROAD

SHEET
01C-1.05

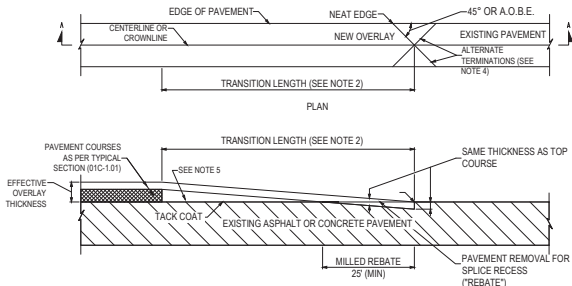


PAVEMENT TERMINATION DETAIL

NOTES

- 1. ASPHALT OVERLAY SPICES SHALL BE USED AT: ENDS OF ASPHALT OVERLAY HIGHWAY SECTIONS, MAJOR INTERSECTIONS, AND OTHER LOCATIONS INDICATED IN THE PLANS.
- 2. THE TRANSITION LENGTH IN FEET SHALL NOT BE LESS THAN THE VALUE OBTAINED BY MULTIPLYING THE EFFECTIVE OVERLAY THICKNESS IN INCHES (DIFFERENCE BETWEEN THE EXISTING AND THE OVERLAY ELEVATIONS) BY THE K VALUE FROM THE TABLE FOR THE POSTED SPEED OF THE HIGHWAY. THE MINIMUM TRANSITION LENGTH IS 30'.
- 3. ALL SURFACES OF THE ASPHALT OVERLAY SPICE TRANSITION AREA SHALL BE CLEANED AND TACK-COATED PRIOR TO ASPHALT PLACEMENT. THE COST OF MILLING REBATES, AND TACK COAT IN THE ASPHALT OVERLAY SPICE TRANSITION AREA SHALL BE PAID FOR UNDER THEIR RESPECTIVE ITEMS. COST OF LEAVING A NEAT EDGE SHALL BE INCLUDED IN THE MILLING ITEM.
- 4. SAW CUTS SHALL BE MADE SO THAT SURFACE RUNOFF IS DIRECTED TO THE EDGE OF PAVEMENT.
- 5. IN THE TRANSITION AREA, PAVEMENT COURSES OTHER THAN THE TOP COURSE SHALL BE FEATHERED OUT USING TOP COURSE OR OTHER APPROPRIATE MATERIAL. PAYMENT SHALL BE MADE UNDER THE APPROPRIATE ITEM.


K VALUE TABLE FT/IN										
POSTED SPEED MPH	10	15	20	25	30	35	40	45	50	55
K	0.40	0.57	0.74	0.91	1.08	1.25	1.42	1.59	1.76	1.93

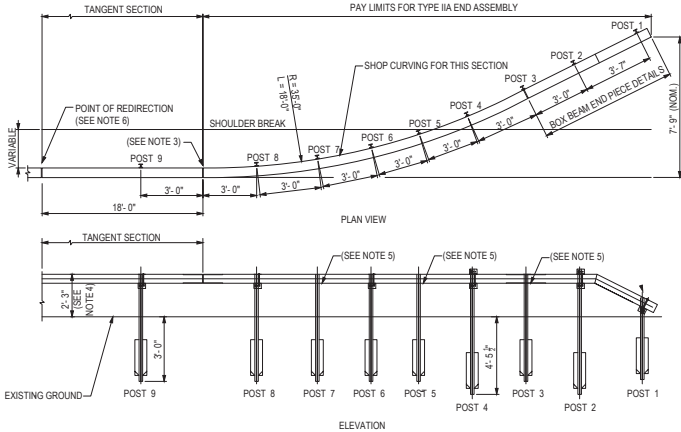

END ASSEMBLY TYPE IIA

NOTES


- 1. POSTS 2, AND 4 SHALL BE EXTRA LONG POSTS. POSTS 3, 5, 6, 7, 8, AND 9 SHALL BE STANDARD LENGTH.
- 2. POSTS 2 AND 4 SHALL BE FASTENED TO THE RAIL USING DETAIL "A".
- 3. FOR SIDE SLOPES 1:5 OR FLATTER, THE 18" OF CURVED BOX BEAM MAY BE PROVIDED IN A CURVED PORTION OF A 24' OR 36' PIECE. OTHERWISE, AN 18" SECTION IS TO BE SPICED AT THE POINT OF TANGENCY.
- 4. THE DRAWING INDICATES THE TERMINAL INSTALLED ON LEVEL GROUND. WHEN INSTALLED OVER A SLOPE OR DITCH, THE TERMINAL END SHOULD BE PUSHED DOWN WITH THE EQUIVALENT OF APPROXIMATELY 100 LBS EFFORT TO DEPRESS THE TERMINAL DOWN.
- 5. POSTS 3, 5, AND 7 SHALL NOT BE CONNECTED TO BOX BEAM GUIDE RAIL. HOWEVER, FOR RUNS LESS THAN 130' IN LENGTH, ALL BACKUP POSTS SHALL BE FASTENED TO THE RAIL.
- 6. FOR DESIGN SPEEDS UNDER 50 MPH THE POINT OF REDIRECTION WILL BE AT THE POINT OF TANGENCY.

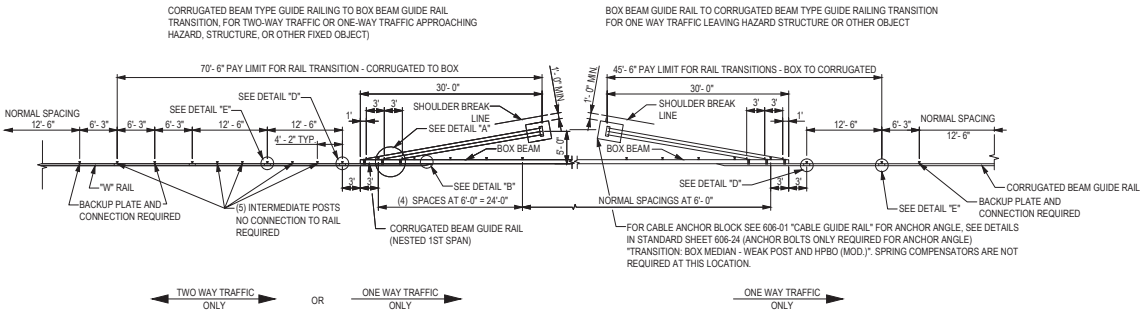

TRANSITION BOX - W-BEAM

NOTE:

- 1. SEE DETAILS A, B, C, D, AND E IN SHEET 606-20 IN THE BOOK 2 OF 4 OF THE NEW YORK STANDARD SHEETS DATED MAY 01, 2024.



UNIVERSAL POST





PROJECT MANAGER: LAURA BARCA		
1	1-15-25	ISSUED FOR PERMITTING
ISSUE	DATE	DESCRIPTION
PROJECT NUMBER: 10400319		



TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

CONSTRUCTION DETAILS - 1
BALL ROAD

SHEET
01C-1.06

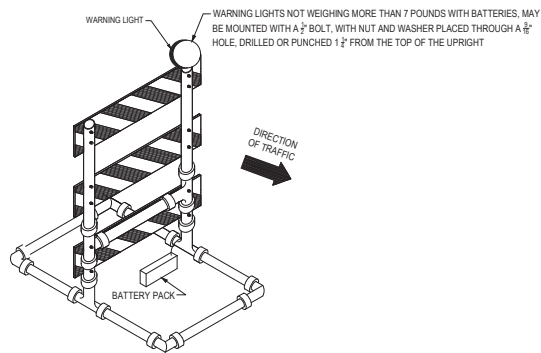
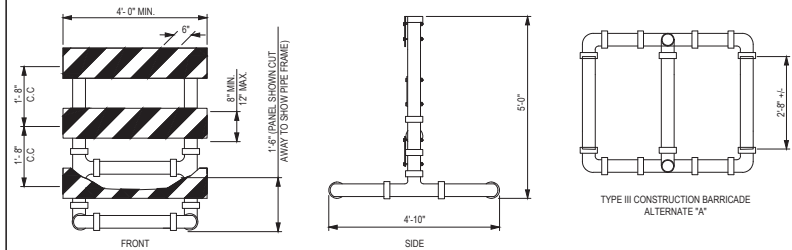


DETAILS FOR FASTENING LIGHTS ON TOP OF BARRICADE

NOT TO SCALE

NOTES:

- NOTES:
1. THE DETAILS AND MATERIALS FOR TYPE III IN CONSTRUCTION BARRICADES ARE NCHRP 350 APPROVED. IF THE CONTRACTOR ELECTS TO USE AN ALTERNATE DESIGN OR MATERIALS, THE ALTERNATIVE SHALL BE NCHRP 350 APPROVED.
 2. THE ALTERNATES SHOWN ON SHEET 619-002 IN THE NY STANDARD SPECS ARE EQUALLY ACCEPTABLE AND THE CONTRACTOR MAY USE ANY ONE OR A MIXTURE OF TYPES.
 3. STRIP SHALL BE REFLECTORIZED DIAGONAL STRIPES OF TYPE I (OR TYPE II) SHEETING SLOPING AT AN ANGLE OF 45° IN ACCORDANCE WITH §729-08. TYPE II IN CONSTRUCTION BARRICADES, THE STRIPES SHALL SLOPE DOWNWARD TOWARD THE SIDE ON WHICH TRAFFIC IS TO PASS.
 4. BALLAST MAY BE PLACED ON THE BASE MEMBERS OF THE BARRICADE. BALLAST SHALL NOT EXTEND INTO THE ACCESSIBLE PASSAGE WIDTH OF 5' WHERE BARRICADES ARE USED TO CHANNELIZE PEDESTRIANS.
 5. PANELS FOR BARRICADES MAY BE WOOD, PLASTIC, OR ALUMINUM. PIPE FOR BARRICADES SHALL USE SDR SIZES 21 TO 32.5.
 6. WHEN THE BATTERY AND LIGHT WEIGHT MORE THAN 1 LBS, THE BATTERY SHALL BE MOUNTED ON THE BOTTOM OF THE BARRICADE.
 7. IF PIPES SHALL BE WHITE, WHITE FITTINGS ARE PREFERRED. BLACK MAY BE USED. ALL JOINTS IN ALTERNATE "A" SHALL BE GLUED WITH A SOLVENT CEMENT COMPATIBLE WITH THE P.V.C. PIPE.
 8. ALL JOINTS IN ALTERNATE "B" SHALL BE FREE TO SEPARATE UPON VEHICLE IMPACT. SHADED PIPES AND FITTINGS SHALL BE TIED TOGETHER WITH A MINIMUM 3/16" DIA. NYLON, OR EQUIVALENT ROPE THREADED INTO THE PIPE AND FITTING INTERIOR.
 9. IF BARRICADES ARE USED TO TEMPORARILY CHANNELIZE PEDESTRIANS, THERE SHALL BE A CONTINUOUS DETECTABLE BOTTOM AND TOP RAILS WITH NO GAP BETWEEN INDIVIDUAL BARRICADES TO BE DETECTABLE TO BLIND OR VISUALLY IMPAIRED USERS OF LONG CANES. THE BOTTOM OF THE BOTTOM RAIL SHALL BE NO HIGHER THAN 2" ABOVE THE GROUND AND THE TOP OF THE TOP RAIL SHALL BE NO LOWER THAN 3' ABOVE THE GROUND.

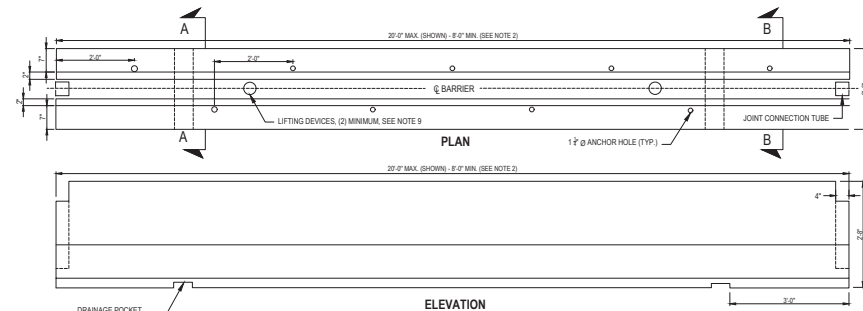


SECTION A-A

FULL SECTION BAR LIST							
MARK	SIZE	NUMBER PER SECTION	LENGTH	TYPE	A	B	C LOCATION
4B1	4	6	4'-11"	I	0'-0"	2'-4"	0'-1" STIRRUPS
4B4	4	1 PER RECESS	3'-1"	I	0'-0"	1'-3 1/2"	ANCHOR RECESS HOOP
4B5	4	SEE TABLE	4'-11"	I	0'-0"	2'-4"	0'-1" STIRRUPS
6B2	6	2	SEE NOTE 7	STR.			LONGITUDINAL (TOP)
6B3	6	2	SEE NOTE 7	STR.			LONGITUDINAL (BOTTOM)
6B4	6	2	1'-2"	STR.			TRANSVERSE (BOTTOM)
6B5	6	2	0'-6"	STR.			TRANSVERSE (TOP)

485 BAR LOCATION TABLE

NOMINAL LENGTH OF BARRIER UNIT	X	NO. EACH SECTION
20'	6'-11"	2
18'	6'-5"	2
16'	5'-11"	2
14'	7'-0"	1
12'	6'-0"	1
10'	5'-0"	1
8'	N/A	0

"X" DISTANCE FROM END OF BARRIER TO 485 BARRIER



OPTIONAL BATTERED BOTTOM CORNER DETAIL

TEMPORARY POSITIVE BARRIER

NOT TO SCALE

NOTES:

- NOTES:
1. TEMPORARY POSITIVE BARRIER SHALL BE PRECAST IN ACCORDANCE WITH THE REQUIREMENTS OF §704-05 PRECAST CONCRETE BARRIER.
 2. TEMPORARY POSITIVE BARRIER SHALL BE PRECAST UNITS OF ONE OF THE FOLLOWING NOMINAL LENGTHS 8', 10', 12', 14', 16', 18', 20'.
 3. STEEL PLATE REINFORCEMENT SHALL BE ASTM A631, A572M, GRADE 345 STEEL. TUBE REINFORCEMENT SHALL BE ASTM A500, GRADE B OR C, AND REINFORCING BARS SHALL BE #4 OR #5 EPOXY BARS ARE NOT REQUIRED.
 4. ALL WELDING SHALL BE PERFORMED BY A WELDER QUALIFIED IN ACCORDANCE WITH SECTION 8 OF THE NY'S STEEL CONSTRUCTION MANUAL.
 5. SURFACES TO BE WELDED SHALL BE FREE OF SLAG, RUST, MOISTURE, GREASE OR ANY OTHER MATERIAL THAT WILL PREVENT PROPER WELDING OR PRODUCE OBSERVABLE FLUMES.
 6. SHIELDING GAS SHALL BE SHIELDED METAL ARC WELDING USING PROPERLY DRIED 532° E7018 ELECTRODES CONFORMING TO THE REQUIREMENTS OF SECTION 7 OF THE NY'S STEEL CONSTRUCTION MANUAL.
 7. THE LENGTH OF THE 682 AND 683 BARS WILL VARY WITH THE LENGTH OF THE BARRIER SEGMENT.
 8. CONCRETE CLEAR COVER FOR REINFORCING BARS SHALL BE 1/2" (MIN.) UNLESS OTHERWISE SPECIFIED.
 9. A MINIMUM OF (2) TWO RECESSED LIFTING DEVICES, EACH WITH THE CAPACITY TO LIFT A MASS OF 6 TONS (MINIMUM), SHALL BE INSTALLED ON EACH SEGMENT. SEGMENT MASS IS APPROXIMATELY 4,500 LB/FT.
 10. ONE DRAINAGE GROUT PEG SHALL BE INCLUDED IN THE CENTER OF 8'-0" AND 10'-0" SEGMENTS. TWO DRAINAGE PEGS SHALL BE IN ALL OTHER SEGMENTS.
 11. CONNECTION KEY COVER PLATE SHALL BE INSTALLED FLUSH WITH THE BARRIER TOP.
 12. 1" ASTM A36 ANCHOR PINS SHALL BE PLACED IN FOUR ANCHOR HOLES OF EACH SEGMENT TO BE PINNED. PINS SHALL BE PLACED ON THE WORKZONE SIDE OF THE BARRIER, UNLESS OTHERWISE SPECIFIED ON THE PLANS OR DIRECTED BY THE ENGINEER.
 13. BASED ON SEGMENT LENGTH AND MAXIMUM JOINT OCCURRENCE, TEMPORARY POSITIVE BARRIER CANNOT BE INSTALLED ON RADII TIGHTER THAN THE FOLLOWING MINIMUMS: § 92, 10', 115', 12', 14', 16', 18', 18', 20', 20', 230'.


PROJECT MANAGER LAURA BARCA

[illegible]


TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

CONSTRUCTION DETAILS - 2
BALL ROAD


SHEET
01C-1.07

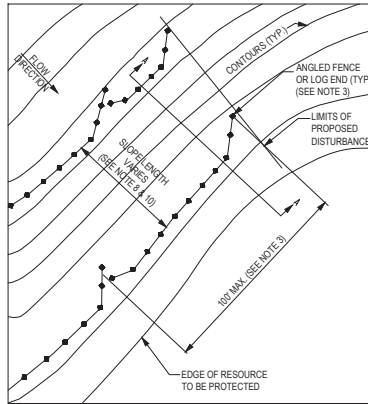


PLAN
EXAMPLE LAYOUT OF SILT FENCE OR SEDIMENT FILTER LOG
NOT TO SCALE

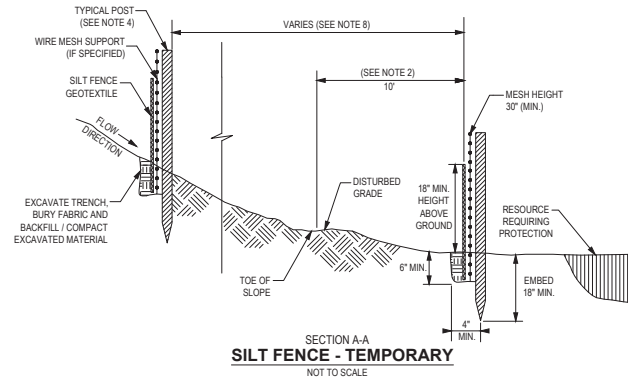


SECTION A-A
SILT FENCE - TEMPORARY
NOT TO SCALE



SILT FENCE PLACEMENT
NOT TO SCALE

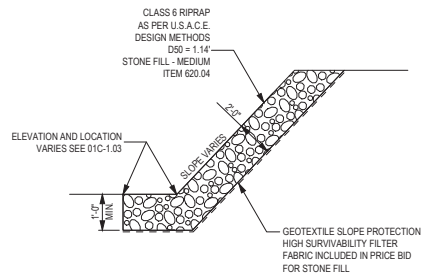

RIPRAP SLOPE PROTECTION
NOT TO SCALE

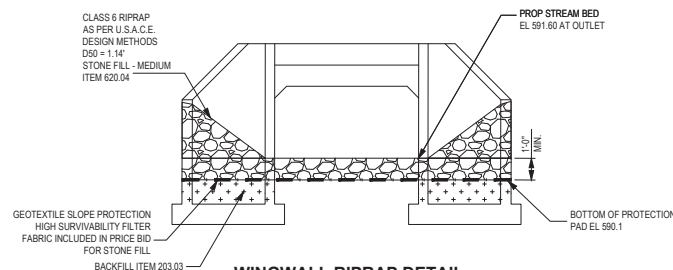

WINGWALL RIPRAP DETAIL
OUTLET SHOWN, INLET SIMILAR
NOT TO SCALE

EROSION CONTROL NOTES:

1. FULL SEDIMENT CONTROL MEASURES WILL BE INCORPORATED INTO THE PROJECT CONSTRUCTION. THESE PRACTICES WILL BE IN ACCORDANCE WITH THE CODES SET FORTH IN THE NEW YORK STATE DEPT. OF ENVIRONMENTAL CONSERVATION PUBLICATION TITLED "NEW YORK STANDARDS AND SPECIFICATIONS FOR EROSION AND SEDIMENT CONTROL".
2. CONTRACTOR SHALL PERFORM HIS OPERATIONS TO MINIMIZE AREAS OF DISTURBANCE. ALL DISTURBED AREAS SHALL BE FULLY RESTORED TO THE ORIGINAL CONDITION. THE COST TO PERFORM THIS WORK SHALL BE INCLUDED IN VARIOUS ITEMS THROUGHOUT THIS CONTRACT. NO SEPARATE PAYMENT WILL BE MADE FOR RESTORATION WORK.
3. IT IS THE RESPONSIBILITY OF THE CONTRACTOR TO PROVIDE A SAFE AND FIRM EXCAVATION FOR THE SUBSTRUCTURE REMOVAL AND INSTALLATION. THE COST OF ANY GRADING, CONNECTIONS, MATERIALS, DEWATERING, AND OTHER EQUIPMENT OR OPERATIONS NECESSARY TO CREATE AND/OR MAINTAIN THESE CONDITIONS SHALL BE INCLUDED IN THE COST OF THE VARIOUS ITEMS IN THE CONTRACT.
4. CONTRACTOR TO SUBMIT DEWATERING AND EROSION AND SEDIMENT CONTROL PLANS TO BE APPROVED BY ENGINEER PRIOR TO START OF WORK.
5. EROSION CONTROL MEASURES ARE TO BE INSTALLED PRIOR TO ANY GROUND DISTURBANCE AND SHALL INCLUDE ALL NECESSARY ITEMS: SILT FENCE, STRAW BALE DICS, TURBIDITY CURTAIN, DIVERSION SWALES/DIKES AND ANY OTHER TEMPORARY EROSION CONTROL MEASURES NECESSARY TO PREVENT EROSION AND SEDIMENTATION OF THE PROJECT AREA. SEE STREAM RESTORATION PLAN SHEET 13 OF 16 FOR APPROXIMATE LOCATION OF SILT FENCE. SILT FENCE TO BE PAID FOR UNDER ITEM 205.13. OTHER ITEMS NECESSARY FOR EROSION CONTROL TO BE INCLUDED IN THE COST OF VARIOUS ITEMS IN THE CONTRACT.
6. SILT FENCE SHALL BE INSTALLED ON DOWNSLOPE EDGE OF SOIL DISTURBED BY THIS PROJECT. UPON FINAL GRADING THE DISTURBED SOIL WILL BE SEEDDED AND MULCHED, AND THE MULCH WILL BE MAINTAINED UNTIL SOIL IS FULLY VEGETATED.
7. CONTRACTOR SHALL TAKE ALL PRECAUTIONS TO AVOID CONTAMINATION OF THE STREAM BY FRESH CONCRETE AND CONCRETE LEACHATE.
8. DEBRIS AND EXCESS MATERIALS FROM CONSTRUCTION SHALL BE COMPLETELY REMOVED FROM THE BED AND BANKS OF THE STREAM.
9. CONTRACTOR SHALL PLACE RIPRAP AS SHOWN ON THE PLANS AT THE DIRECTION OF THE ENGINEER.

CONSTRUCTION NOTES

1. SILT FENCE OR SEDIMENT FILTER LOGS SHALL BE INSTALLED ON A LINE OF EQUAL ELEVATION (CONTOUR). IT MAY BE INSTALLED AT INTERMEDIATE POINTS UP SLOPES AS WELL AS AT THE BOTTOM.
2. FOR LOCATIONS THAT WARRANT PLACEMENT OF SILT FENCE OR SEDIMENT FILTER LOGS AT THE BASE OF SLOPES, SILT FENCE OR SEDIMENT FILTER LOGS SHALL BE PLACED A MINIMUM OF 10 FEET FROM THE TOE OF THE SLOPE, TO PROVIDE ADEQUATE AREA FOR SEDIMENT STORAGE AND FACILITATE MAINTENANCE OF THE SEDIMENT CONTAINMENT AREA.
3. THE ENDS OF A ROW OF SILT FENCE OR SEDIMENT FILTER LOGS SHALL BE ANGLED UP SLOPE TO PREVENT CHANNELIZED FLOW FROM BEING CONVEYED PAST THE ENDS OF THE FENCE. A SECTION OF SILT FENCE OR SEDIMENT FILTER LOGS SHOULD NOT EXCEED 100 FEET IN LENGTH.
4. WOOD POSTS FOR SILT FENCE SHALL HAVE A CROSS-SECTION AREA OF 3.5 SQUARE INCHES OR STEEL POSTS SHALL BE "1" OR "1/2" SHAPE AND 13 POUNDS/FEET (MINIMUM) FOR STEEL. SPACING FOR THE PROVIDED SILT FENCE LOGS SHALL BE AS DESIGNATED ON THE DEPARTMENT APPROVED LIST. THE LENGTH OF SILT FENCE POSTS SHALL BE 40 INCHES. WOOD POSTS FOR SEDIMENT FILTER LOGS SHALL BE NOMINAL 2x2. THE LENGTH OF FILTER LOG POSTS SHALL BE 1" GREATER THAN THE DIAMETER OF THE LOG.
5. THE BOTTOM EDGE OF SILT FENCE SHALL BE BURIED A MINIMUM OF 6" BELOW GROUND. THE FENCE SHALL BE INSTALLED WITH THE POSTS ON THE DOWNSLOPE SIDE OF THE FABRIC.
6. WHERE ENDS OF GEOTEXTILE FABRIC COME TOGETHER, THEY SHALL BE OVERLAPPED AND FOLDED AND STAPLED TO PREVENT SEDIMENT BYPASS, OR THE ENDS POSTS OF TWO SECTIONS SHALL BE WRAPPED AS SHOWN IN THE DETAIL FOR SILT FENCE END WRAPPING.
7. SEDIMENT SHALL BE REMOVED WHEN ACCUMULATION REACHES ONE-HALF OF THE ABOVE GROUND HEIGHT OR WHEN BULGES DEVELOP IN THE FABRIC. SEDIMENT SHALL BE DISPOSED OF AS UNSUITABLE MATERIAL.
8. THE FOLLOWING ARE MAXIMUM SLOPE LENGTHS (DISTANCE BETWEEN ROWS) FOR SILT FENCE INSTALLATION:

SLOPE	STEEPNESS	STANDARD**	REINFORCE
*5-10%	20:1 TO 10:1	125	250
10-20%	10:1 TO 5:1	100	150
20-33%	5:1 TO 3:1	60	80
33-50%	3:1 TO 2:1	40	70
>50%	> 2:1	20	30


* FOR SLOPES LESS THAN 5% SILT FENCE IS NOT REQUIRED UNLESS IN SENSITIVE AREAS OR HIGHLY ERODIBLE SOILS.

** STANDARD SILT FENCE IS FABRIC ROLLS STAPLED TO WOODEN POSTS DRIVEN 18 INCHES INTO THE GROUND.

*** REINFORCED SILT FENCE IS FABRIC PLACED AGAINST WELDED WIRE MESH WITH ANCHORED STEEL POSTS DRIVEN 18 INCHES INTO THE GROUND.

9. INSTALLATION OF SILT FENCE OR SEDIMENT LOG, INCLUDING EXCAVATION, BACKFILL, AND COMPACTION OF SOIL SHALL BE INCLUDED IN THE UNIT PRICE BID FOR ITEM.
10. SEDIMENT FILTER LOG POSTS SHALL BE SPACED NO MORE THAN 10 FEET APART. ENDS OF LOGS SHALL BE OVERLAPPED BY 24 INCHES AND STAKED SIDE BY SIDE. THE MAXIMUM SLOPE LENGTH (DISTANCE BETWEEN ROWS) SHALL NOT EXCEED THE FOLLOWING LIMITS:

SEDIMENT FILTER LOG MAX SLOPE LENGTH (FEET)						
DIA. (IN.)	SLOPE %					
	2	5	10	20	25	33
12	250	225	125	65	50	40
18	275	250	150	70	55	45
24	350	275	200	130	100	60

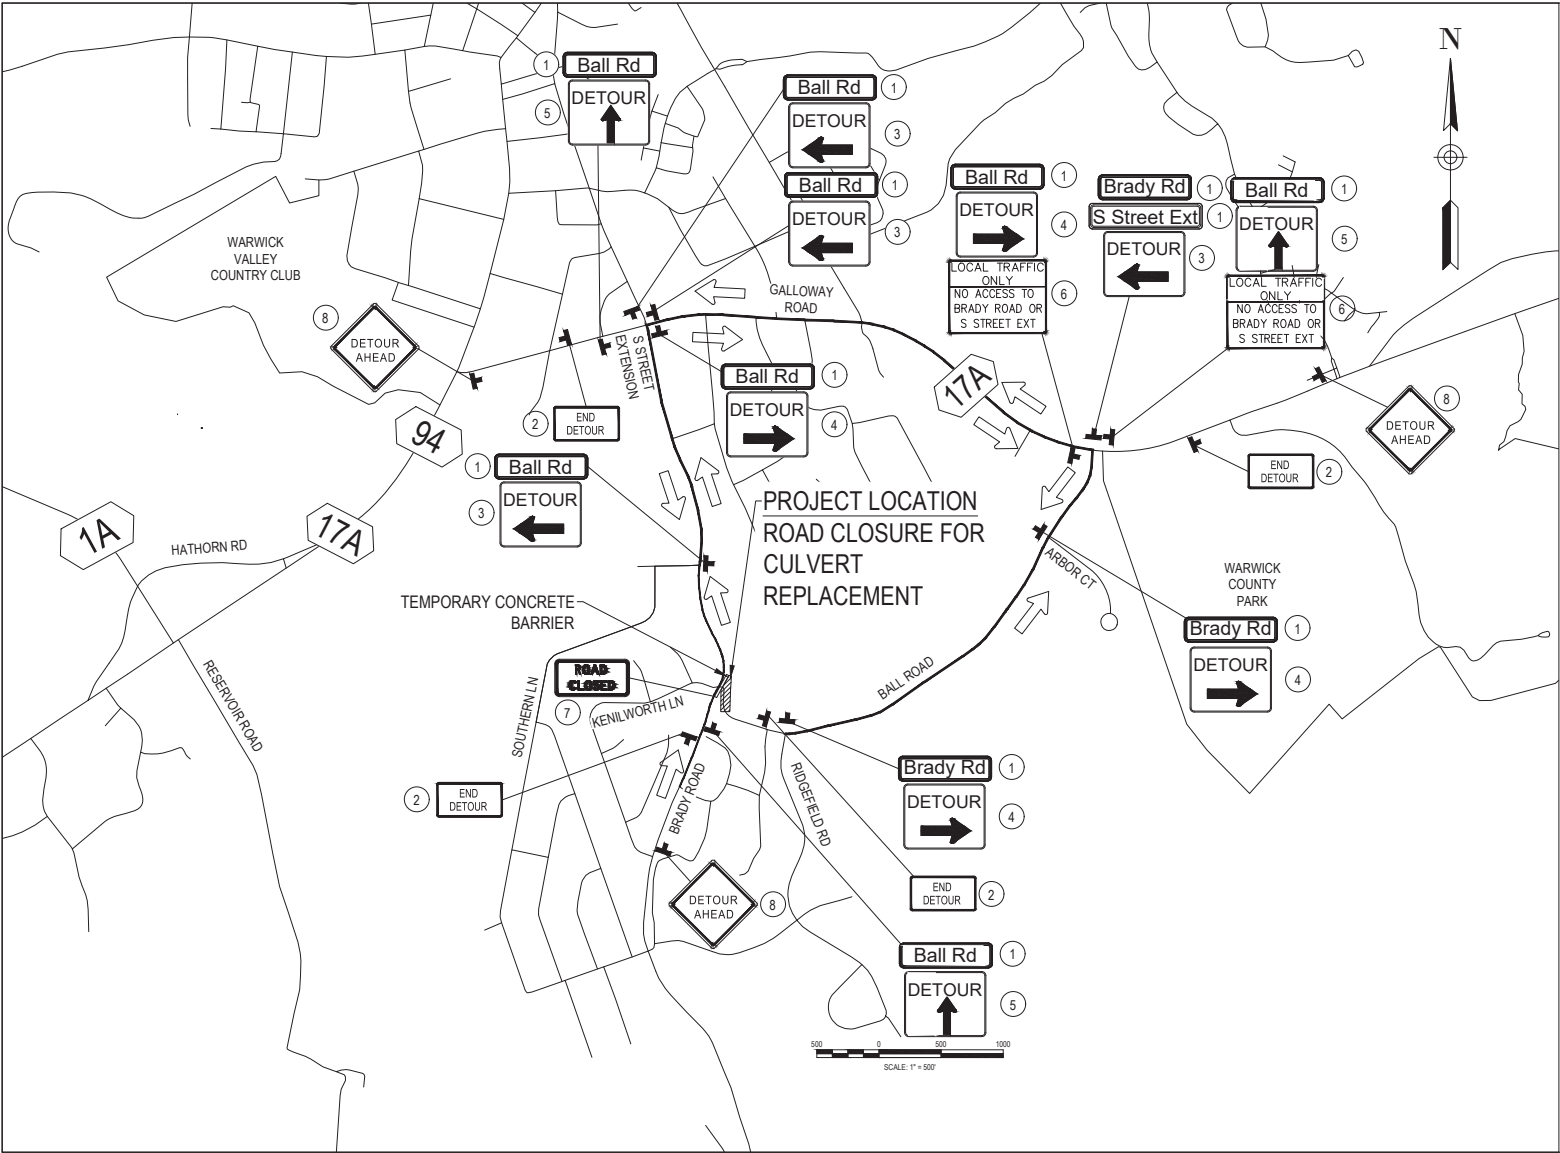

- MAINTENANCE AND PROTECTION OF TRAFFIC NOTES:**
1. MAINTENANCE AND PROTECTION OF TRAFFIC SHALL BE COMPLIED WITH THROUGHOUT THE LENGTH AND DURATION OF THE CONTRACT IN ACCORDANCE WITH "THE NEW YORK STATE MANUAL OF UNIFORM TRAFFIC CONTROL DEVICES" AND THE CONTRACT DOCUMENTS.
 2. DISTANCES SHOWN ARE APPROXIMATE ONLY AND MAY BE REVISED BY THE ENGINEER TO MEET FIELD CONDITIONS (DRIVEWAYS, HIGHWAY ALIGNMENT, ETC.)
 3. THE SIGNING SHOWN IS A MINIMUM ONLY, ADDITIONAL SIGNING MAY BE REQUIRED TO MEET TRAFFIC AND/OR FIELD CONDITIONS. ANY ADDITIONAL SIGNS UP TO 6, TO BE PROVIDED AT NO ADDITIONAL COST.
 4. DURING NON-WORKING HOURS, ALL CONSTRUCTION EQUIPMENT AND MATERIALS SHALL BE STORED IN THE CLOSED PORTION OF THE ROADWAY BEHIND THE CONCRETE BARRIERS.
 5. WORK ZONE TRAFFIC CONTROL, INCLUDING NECESSARY SIGNS, ETC. AND REMOVAL, STORAGE AND REINSTALLING EXISTING SIGNS PAID FOR UNDER ITEM 619.01.
 6. NO ADDITIONAL PAYMENT WILL BE MADE FOR MOVEMENT OF TEMPORARY CONCRETE BARRIERS AFTER INITIAL PLACEMENT. COST FOR MOVEMENT OF EXISTING TEMPORARY CONCRETE BARRIERS SHALL BE CONSIDERED AS PART OF THE MOBILIZATION COST.
 7. TYPE B FLASHERS SHALL BE MOUNTED ON SIGN TYPE 6 AND MAINTAINED FOR THE DURATION OF THE ROAD CLOSURE, TO BE INCLUDED IN ITEM 619.01.

LEGEND:

→ DETOUR ROUTE DIRECTIONS

— DETOUR ROUTE

SIGN	NO. REQ'D.	SIGN NO.	TEXT	SIZE
1	8	D3-1a	Ball Rd	VARIABLES" X 12"
1	3	D3-1a	Brady Rd	VARIABLES" X 12"
1	1	D3-1a	S Street Ext	VARIABLES" X 12"
2	4	M4-8a	END DETOUR	30" X 24"
3	3	M4-8L	DETOUR	30" X 24"
3	5	M4-8R	DETOUR	30" X 24"
3	3	M4-8S	DETOUR	30" X 24"
6	2	R2-10F	LOCAL TRAFFIC ONLY NO ACCESS TO BRADY ROAD OR S STREET EXT	48" X 36"
7	1	R11-2	ROAD CLOSED	48" X 30"
8	3	W25-2	DETOUR AHEAD	36" X 36"



ISSUE	DATE	DESCRIPTION
1	1-15-25	ISSUED FOR PERMITTING


PROJECT MANAGER	LAURA BARCA
PROJECT NUMBER	10400319



TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS


DETOUR PLAN
BALL ROAD

SHEET
01C-1.09

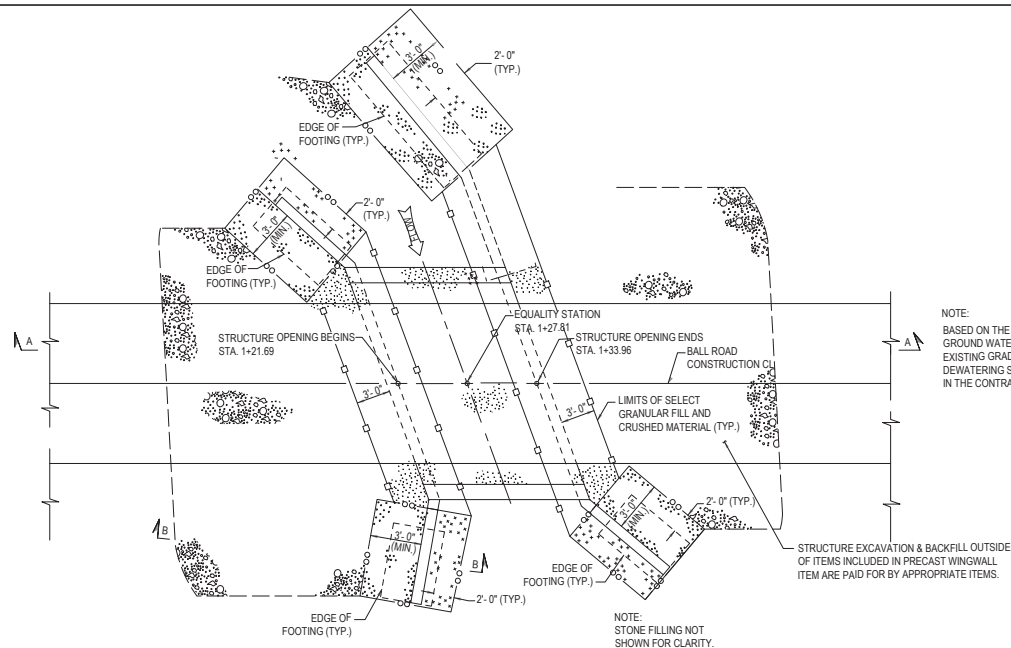


PLAN
NOT TO SCALE

EARTHWORK DETAILS ARE GENERIC VIEWS OF STRUCTURE.
SEE SHEETS 01S-1.02 TO 01S-1.04 FOR CULVERT DIMENSIONS
AND DETAILS.

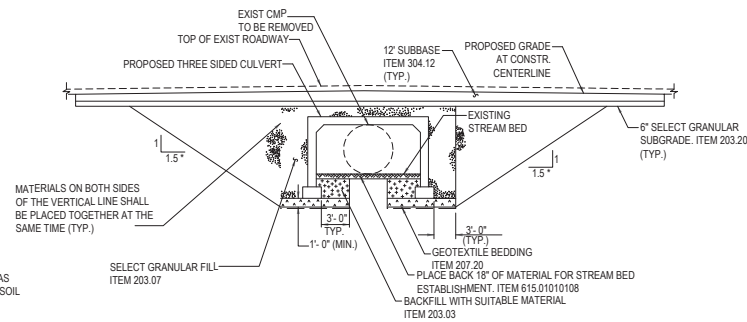

SECTION A-A

NOT TO SCALE

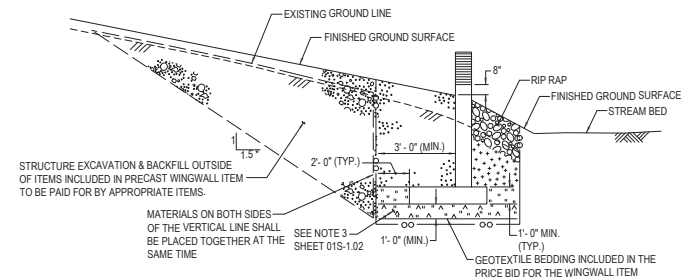

SECTION B-B
PRECAST CANTILEVER WINGWALL

NOT TO SCALE




			PROJECT NUMBER	
1	5-15-25	ISSUED FOR PERMITTING		
ISSUE	DATE	DESCRIPTION	PROJECT NUMBER	10400319



TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

CULVERT EARTHWORK DETAILS
BALL ROAD

SHEET
01S-1.01

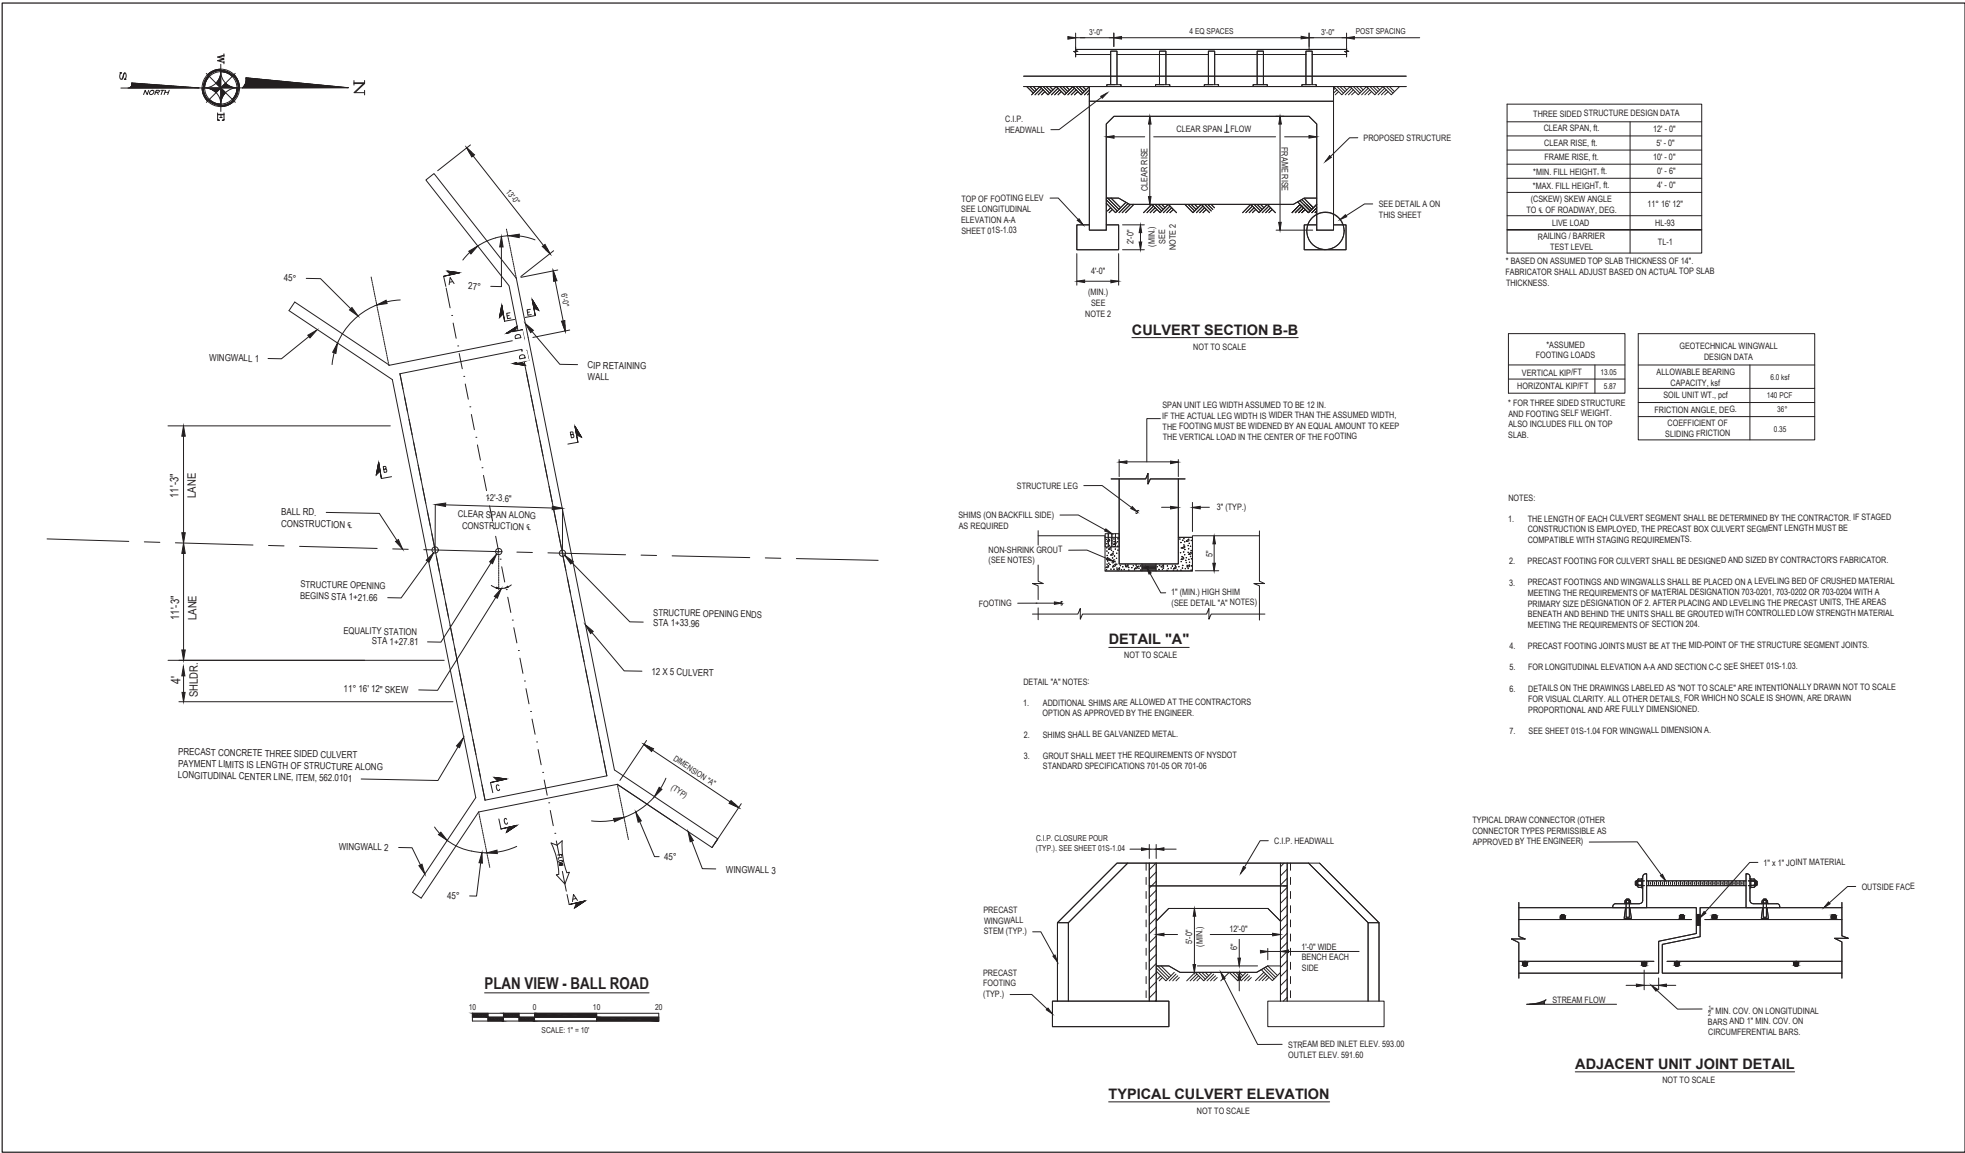

1	1-15-25	ISSUED FOR PERMITTING
2		
3		
4		
5		
6		
7		
8		
9		
10		

Laura Barca



TOWN OF WARWICK
DEPARTMENT OF PUBLIC WORKS

PRECAST CULVERT PLAN
AND ELEVATION
BALL ROAD

SHEET
01S-1.02

Nationwide Permit 3 - Maintenance

Effective Date: February 25, 2022; Expiration Date: March 14, 2026
(NWP Final Notice, 86 FR 73522)

Nationwide Permit 3 - Maintenance. (a) The repair, rehabilitation, or replacement of any previously authorized, currently serviceable structure or fill, or of any currently serviceable structure or fill authorized by 33 CFR 330.3, provided that the structure or fill is not to be put to uses differing from those uses specified or contemplated for it in the original permit or the most recently authorized modification. Minor deviations in the structure's configuration or filled area, including those due to changes in materials, construction techniques, requirements of other regulatory agencies, or current construction codes or safety standards that are necessary to make the repair, rehabilitation, or replacement are authorized. This NWP also authorizes the removal of previously authorized structures or fills. Any stream channel modification is limited to the minimum necessary for the repair, rehabilitation, or replacement of the structure or fill; such modifications, including the removal of material from the stream channel, must be immediately adjacent to the project. This NWP also authorizes the removal of accumulated sediment and debris within, and in the immediate vicinity of, the structure or fill. This NWP also authorizes the repair, rehabilitation, or replacement of those structures or fills destroyed or damaged by storms, floods, fire or other discrete events, provided the repair, rehabilitation, or replacement is commenced, or is under contract to commence, within two years of the date of their destruction or damage. In cases of catastrophic events, such as hurricanes or tornadoes, this two-year limit may be waived by the district engineer, provided the permittee can demonstrate funding, contract, or other similar delays.

(b) This NWP also authorizes the removal of accumulated sediments and debris outside the immediate vicinity of existing structures (e.g., bridges, culverted road crossings, water intake structures, etc.). The removal of sediment is limited to the minimum necessary to restore the waterway in the vicinity of the structure to the approximate dimensions that existed when the structure was built, but cannot extend farther than 200 feet in any direction from the structure. This 200 foot limit does not apply to maintenance dredging to remove accumulated sediments blocking or restricting outfall and intake structures or to maintenance dredging to remove accumulated sediments from canals associated with outfall and intake structures. All dredged or excavated materials must be deposited and retained in an area that has no waters of the United States unless otherwise specifically approved by the district engineer under separate authorization.

(c) This NWP also authorizes temporary structures, fills, and work, including the use of temporary mats, necessary to conduct the maintenance activity. Appropriate measures must be taken to maintain normal downstream flows and minimize flooding to the maximum extent practicable, when temporary structures, work, and discharges of dredged or fill material, including cofferdams, are necessary for construction activities, access fills, or dewatering of construction sites. Temporary fills must consist of materials, and be placed in a manner, that will not be eroded by expected high flows.

After conducting the maintenance activity, temporary fills must be removed in their entirety and the affected areas returned to pre-construction elevations. The areas affected by temporary fills must be revegetated, as appropriate.

(d) This NWP does not authorize maintenance dredging for the primary purpose of navigation. This NWP does not authorize beach restoration. This NWP does not authorize new stream channelization or stream relocation projects.

Notification: For activities authorized by paragraph (b) of this NWP, the permittee must submit a pre-construction notification to the district engineer prior to commencing the activity (see general condition 32). The pre-construction notification must include information regarding the original design capacities and configurations of the outfalls, intakes, small impoundments, and canals. (Authorities: Section 10 of the Rivers and Harbors Act of 1899 and Section 404 of the Clean Water Act (Sections 10 and 404))

Note: This NWP authorizes the repair, rehabilitation, or replacement of any previously authorized structure or fill that does not qualify for the Clean Water Act Section 404(f) exemption for maintenance.

2021 Nationwide Permit General Conditions

Note: To qualify for NWP authorization, the prospective permittee must comply with the following general conditions, as applicable, in addition to any regional or case-specific conditions imposed by the division engineer or district engineer. Prospective permittees should contact the appropriate Corps district office to determine if regional conditions have been imposed on an NWP. Prospective permittees should also contact the appropriate Corps district office to determine the status of Clean Water Act Section 401 water quality certification and/or Coastal Zone Management Act consistency for an NWP. Every person who may wish to obtain permit authorization under one or more NWPs, or who is currently relying on an existing or prior permit authorization under one or more NWPs, has been and is on notice that all of the provisions of 33 CFR 330.1 through 330.6 apply to every NWP authorization. Note especially 33 CFR 330.5 relating to the modification, suspension, or revocation of any NWP authorization.

1. **Navigation**. (a) No activity may cause more than a minimal adverse effect on navigation.

(b) Any safety lights and signals prescribed by the U.S. Coast Guard, through regulations or otherwise, must be installed and maintained at the permittee's expense on authorized facilities in navigable waters of the United States.

(c) The permittee understands and agrees that, if future operations by the United States require the removal, relocation, or other alteration, of the structure or work herein authorized, or if, in the opinion of the Secretary of the Army or his or her authorized representative, said structure or work shall cause unreasonable obstruction to the free navigation of the navigable waters, the permittee will be required, upon due notice from

the Corps of Engineers, to remove, relocate, or alter the structural work or obstructions caused thereby, without expense to the United States. No claim shall be made against the United States on account of any such removal or alteration.

2. **Aquatic Life Movements**. No activity may substantially disrupt the necessary life cycle movements of those species of aquatic life indigenous to the waterbody, including those species that normally migrate through the area, unless the activity's primary purpose is to impound water. All permanent and temporary crossings of waterbodies shall be suitably culverted, bridged, or otherwise designed and constructed to maintain low flows to sustain the movement of those aquatic species. If a bottomless culvert cannot be used, then the crossing should be designed and constructed to minimize adverse effects to aquatic life movements.

3. **Spawning Areas**. Activities in spawning areas during spawning seasons must be avoided to the maximum extent practicable. Activities that result in the physical destruction (e.g., through excavation, fill, or downstream smothering by substantial turbidity) of an important spawning area are not authorized.

4. **Migratory Bird Breeding Areas**. Activities in waters of the United States that serve as breeding areas for migratory birds must be avoided to the maximum extent practicable.

5. **Shellfish Beds**. No activity may occur in areas of concentrated shellfish populations, unless the activity is directly related to a shellfish harvesting activity authorized by NWP 4 and 48, or is a shellfish seeding or habitat restoration activity authorized by NWP 27.

6. **Suitable Material**. No activity may use unsuitable material (e.g., trash, debris, car bodies, asphalt, etc.). Material used for construction or discharged must be free from toxic pollutants in toxic amounts (see section 307 of the Clean Water Act).

7. **Water Supply Intakes**. No activity may occur in the proximity of a public water supply intake, except where the activity is for the repair or improvement of public water supply intake structures or adjacent bank stabilization.

8. **Adverse Effects From Impoundments**. If the activity creates an impoundment of water, adverse effects to the aquatic system due to accelerating the passage of water, and/or restricting its flow must be minimized to the maximum extent practicable.

9. **Management of Water Flows**. To the maximum extent practicable, the pre-construction course, condition, capacity, and location of open waters must be maintained for each activity, including stream channelization, storm water management activities, and temporary and permanent road crossings, except as provided below. The activity must be constructed to withstand expected high flows. The activity must not restrict or impede the passage of normal or high flows, unless the primary purpose of the activity is to impound water or manage high flows. The activity may alter the pre-

construction course, condition, capacity, and location of open waters if it benefits the aquatic environment (e.g., stream restoration or relocation activities).

10. **Fills Within 100-Year Floodplains.** The activity must comply with applicable FEMA-approved state or local floodplain management requirements.

11. **Equipment.** Heavy equipment working in wetlands or mudflats must be placed on mats, or other measures must be taken to minimize soil disturbance.

12. **Soil Erosion and Sediment Controls.** Appropriate soil erosion and sediment controls must be used and maintained in effective operating condition during construction, and all exposed soil and other fills, as well as any work below the ordinary high water mark or high tide line, must be permanently stabilized at the earliest practicable date. Permittees are encouraged to perform work within waters of the United States during periods of low-flow or no-flow, or during low tides.

13. **Removal of Temporary Structures and Fills.** Temporary structures must be removed, to the maximum extent practicable, after their use has been discontinued. Temporary fills must be removed in their entirety and the affected areas returned to pre-construction elevations. The affected areas must be revegetated, as appropriate.

14. **Proper Maintenance.** Any authorized structure or fill shall be properly maintained, including maintenance to ensure public safety and compliance with applicable NWP general conditions, as well as any activity-specific conditions added by the district engineer to an NWP authorization.

15. **Single and Complete Project.** The activity must be a single and complete project. The same NWP cannot be used more than once for the same single and complete project.

16. **Wild and Scenic Rivers.** (a) No NWP activity may occur in a component of the National Wild and Scenic River System, or in a river officially designated by Congress as a “study river” for possible inclusion in the system while the river is in an official study status, unless the appropriate Federal agency with direct management responsibility for such river, has determined in writing that the proposed activity will not adversely affect the Wild and Scenic River designation or study status.

(b) If a proposed NWP activity will occur in a component of the National Wild and Scenic River System, or in a river officially designated by Congress as a “study river” for possible inclusion in the system while the river is in an official study status, the permittee must submit a pre-construction notification (see general condition 32). The district engineer will coordinate the PCN with the Federal agency with direct management responsibility for that river. Permittees shall not begin the NWP activity until notified by the district engineer that the Federal agency with direct management responsibility for that river has determined in writing that the proposed NWP activity will not adversely affect the Wild and Scenic River designation or study status.

(c) Information on Wild and Scenic Rivers may be obtained from the appropriate Federal land management agency responsible for the designated Wild and Scenic River or study river (e.g., National Park Service, U.S. Forest Service, Bureau of Land Management, U.S. Fish and Wildlife Service). Information on these rivers is also available at: <http://www.rivers.gov/>.

17. **Tribal Rights**. No activity or its operation may impair reserved tribal rights, including, but not limited to, reserved water rights and treaty fishing and hunting rights.

18. **Endangered Species**. (a) No activity is authorized under any NWP which is likely to directly or indirectly jeopardize the continued existence of a threatened or endangered species or a species proposed for such designation, as identified under the Federal Endangered Species Act (ESA), or which will directly or indirectly destroy or adversely modify designated critical habitat or critical habitat proposed for such designation. No activity is authorized under any NWP which “may affect” a listed species or critical habitat, unless ESA section 7 consultation addressing the consequences of the proposed activity on listed species or critical habitat has been completed. See 50 CFR 402.02 for the definition of “effects of the action” for the purposes of ESA section 7 consultation, as well as 50 CFR 402.17, which provides further explanation under ESA section 7 regarding “activities that are reasonably certain to occur” and “consequences caused by the proposed action.”

(b) Federal agencies should follow their own procedures for complying with the requirements of the ESA (see 33 CFR 330.4(f)(1)). If pre-construction notification is required for the proposed activity, the Federal permittee must provide the district engineer with the appropriate documentation to demonstrate compliance with those requirements. The district engineer will verify that the appropriate documentation has been submitted. If the appropriate documentation has not been submitted, additional ESA section 7 consultation may be necessary for the activity and the respective federal agency would be responsible for fulfilling its obligation under section 7 of the ESA.

(c) Non-federal permittees must submit a pre-construction notification to the district engineer if any listed species (or species proposed for listing) or designated critical habitat (or critical habitat proposed such designation) might be affected or is in the vicinity of the activity, or if the activity is located in designated critical habitat or critical habitat proposed for such designation, and shall not begin work on the activity until notified by the district engineer that the requirements of the ESA have been satisfied and that the activity is authorized. For activities that might affect Federally-listed endangered or threatened species (or species proposed for listing) or designated critical habitat (or critical habitat proposed for such designation), the pre-construction notification must include the name(s) of the endangered or threatened species (or species proposed for listing) that might be affected by the proposed activity or that utilize the designated critical habitat (or critical habitat proposed for such designation) that might be affected by the proposed activity. The district engineer will determine whether the proposed activity “may affect” or will have “no effect” to listed species and

designated critical habitat and will notify the non-Federal applicant of the Corps' determination within 45 days of receipt of a complete pre-construction notification. For activities where the non-Federal applicant has identified listed species (or species proposed for listing) or designated critical habitat (or critical habitat proposed for such designation) that might be affected or is in the vicinity of the activity, and has so notified the Corps, the applicant shall not begin work until the Corps has provided notification that the proposed activity will have "no effect" on listed species (or species proposed for listing or designated critical habitat (or critical habitat proposed for such designation), or until ESA section 7 consultation or conference has been completed. If the non-Federal applicant has not heard back from the Corps within 45 days, the applicant must still wait for notification from the Corps.

(d) As a result of formal or informal consultation or conference with the FWS or NMFS the district engineer may add species-specific permit conditions to the NWP.

(e) Authorization of an activity by an NWP does not authorize the "take" of a threatened or endangered species as defined under the ESA. In the absence of separate authorization (e.g., an ESA Section 10 Permit, a Biological Opinion with "incidental take" provisions, etc.) from the FWS or the NMFS, the Endangered Species Act prohibits any person subject to the jurisdiction of the United States to take a listed species, where "take" means to harass, harm, pursue, hunt, shoot, wound, kill, trap, capture, or collect, or to attempt to engage in any such conduct. The word "harm" in the definition of "take" means an act which actually kills or injures wildlife. Such an act may include significant habitat modification or degradation where it actually kills or injures wildlife by significantly impairing essential behavioral patterns, including breeding, feeding or sheltering.

(f) If the non-federal permittee has a valid ESA section 10(a)(1)(B) incidental take permit with an approved Habitat Conservation Plan for a project or a group of projects that includes the proposed NWP activity, the non-federal applicant should provide a copy of that ESA section 10(a)(1)(B) permit with the PCN required by paragraph (c) of this general condition. The district engineer will coordinate with the agency that issued the ESA section 10(a)(1)(B) permit to determine whether the proposed NWP activity and the associated incidental take were considered in the internal ESA section 7 consultation conducted for the ESA section 10(a)(1)(B) permit. If that coordination results in concurrence from the agency that the proposed NWP activity and the associated incidental take were considered in the internal ESA section 7 consultation for the ESA section 10(a)(1)(B) permit, the district engineer does not need to conduct a separate ESA section 7 consultation for the proposed NWP activity. The district engineer will notify the non-federal applicant within 45 days of receipt of a complete pre-construction notification whether the ESA section 10(a)(1)(B) permit covers the proposed NWP activity or whether additional ESA section 7 consultation is required.

(g) Information on the location of threatened and endangered species and their critical habitat can be obtained directly from the offices of the FWS and NMFS or their world

wide web pages at <http://www.fws.gov/> or <http://www.fws.gov/ipac> and <http://www.nmfs.noaa.gov/pr/species/esa/> respectively.

19. **Migratory Birds and Bald and Golden Eagles.** The permittee is responsible for ensuring that an action authorized by an NWP complies with the Migratory Bird Treaty Act and the Bald and Golden Eagle Protection Act. The permittee is responsible for contacting the appropriate local office of the U.S. Fish and Wildlife Service to determine what measures, if any, are necessary or appropriate to reduce adverse effects to migratory birds or eagles, including whether "incidental take" permits are necessary and available under the Migratory Bird Treaty Act or Bald and Golden Eagle Protection Act for a particular activity.

20. **Historic Properties.** (a) No activity is authorized under any NWP which may have the potential to cause effects to properties listed, or eligible for listing, in the National Register of Historic Places until the requirements of Section 106 of the National Historic Preservation Act (NHPA) have been satisfied.

(b) Federal permittees should follow their own procedures for complying with the requirements of section 106 of the National Historic Preservation Act (see 33 CFR 330.4(g)(1)). If pre-construction notification is required for the proposed NWP activity, the Federal permittee must provide the district engineer with the appropriate documentation to demonstrate compliance with those requirements. The district engineer will verify that the appropriate documentation has been submitted. If the appropriate documentation is not submitted, then additional consultation under section 106 may be necessary. The respective federal agency is responsible for fulfilling its obligation to comply with section 106.

(c) Non-federal permittees must submit a pre-construction notification to the district engineer if the NWP activity might have the potential to cause effects to any historic properties listed on, determined to be eligible for listing on, or potentially eligible for listing on the National Register of Historic Places, including previously unidentified properties. For such activities, the pre-construction notification must state which historic properties might have the potential to be affected by the proposed NWP activity or include a vicinity map indicating the location of the historic properties or the potential for the presence of historic properties. Assistance regarding information on the location of, or potential for, the presence of historic properties can be sought from the State Historic Preservation Officer, Tribal Historic Preservation Officer, or designated tribal representative, as appropriate, and the National Register of Historic Places (see 33 CFR 330.4(g)). When reviewing pre-construction notifications, district engineers will comply with the current procedures for addressing the requirements of section 106 of the National Historic Preservation Act. The district engineer shall make a reasonable and good faith effort to carry out appropriate identification efforts commensurate with potential impacts, which may include background research, consultation, oral history interviews, sample field investigation, and/or field survey. Based on the information submitted in the PCN and these identification efforts, the district engineer shall determine whether the proposed NWP activity has the potential to cause effects on the

historic properties. Section 106 consultation is not required when the district engineer determines that the activity does not have the potential to cause effects on historic properties (see 36 CFR 800.3(a)). Section 106 consultation is required when the district engineer determines that the activity has the potential to cause effects on historic properties. The district engineer will conduct consultation with consulting parties identified under 36 CFR 800.2(c) when he or she makes any of the following effect determinations for the purposes of section 106 of the NHPA: no historic properties affected, no adverse effect, or adverse effect.

(d) Where the non-Federal applicant has identified historic properties on which the proposed NWP activity might have the potential to cause effects and has so notified the Corps, the non-Federal applicant shall not begin the activity until notified by the district engineer either that the activity has no potential to cause effects to historic properties or that NHPA section 106 consultation has been completed. For non-federal permittees, the district engineer will notify the prospective permittee within 45 days of receipt of a complete pre-construction notification whether NHPA section 106 consultation is required. If NHPA section 106 consultation is required, the district engineer will notify the non-Federal applicant that he or she cannot begin the activity until section 106 consultation is completed. If the non-Federal applicant has not heard back from the Corps within 45 days, the applicant must still wait for notification from the Corps.

(e) Prospective permittees should be aware that section 110k of the NHPA (54 U.S.C. 306113) prevents the Corps from granting a permit or other assistance to an applicant who, with intent to avoid the requirements of section 106 of the NHPA, has intentionally significantly adversely affected a historic property to which the permit would relate, or having legal power to prevent it, allowed such significant adverse effect to occur, unless the Corps, after consultation with the Advisory Council on Historic Preservation (ACHP), determines that circumstances justify granting such assistance despite the adverse effect created or permitted by the applicant. If circumstances justify granting the assistance, the Corps is required to notify the ACHP and provide documentation specifying the circumstances, the degree of damage to the integrity of any historic properties affected, and proposed mitigation. This documentation must include any views obtained from the applicant, SHPO/THPO, appropriate Indian tribes if the undertaking occurs on or affects historic properties on tribal lands or affects properties of interest to those tribes, and other parties known to have a legitimate interest in the impacts to the permitted activity on historic properties.

21. Discovery of Previously Unknown Remains and Artifacts. Permittees that discover any previously unknown historic, cultural or archeological remains and artifacts while accomplishing the activity authorized by an NWP, they must immediately notify the district engineer of what they have found, and to the maximum extent practicable, avoid construction activities that may affect the remains and artifacts until the required coordination has been completed. The district engineer will initiate the Federal, Tribal, and state coordination required to determine if the items or remains warrant a recovery effort or if the site is eligible for listing in the National Register of Historic Places.

22. Designated Critical Resource Waters. Critical resource waters include, NOAA-managed marine sanctuaries and marine monuments, and National Estuarine Research Reserves. The district engineer may designate, after notice and opportunity for public comment, additional waters officially designated by a state as having particular environmental or ecological significance, such as outstanding national resource waters or state natural heritage sites. The district engineer may also designate additional critical resource waters after notice and opportunity for public comment.

(a) Discharges of dredged or fill material into waters of the United States are not authorized by NWPs 7, 12, 14, 16, 17, 21, 29, 31, 35, 39, 40, 42, 43, 44, 49, 50, 51, 52, 57 and 58 for any activity within, or directly affecting, critical resource waters, including wetlands adjacent to such waters.

(b) For NWPs 3, 8, 10, 13, 15, 18, 19, 22, 23, 25, 27, 28, 30, 33, 34, 36, 37, 38, and 54, notification is required in accordance with general condition 32, for any activity proposed by permittees in the designated critical resource waters including wetlands adjacent to those waters. The district engineer may authorize activities under these NWPs only after she or he determines that the impacts to the critical resource waters will be no more than minimal.

23. Mitigation. The district engineer will consider the following factors when determining appropriate and practicable mitigation necessary to ensure that the individual and cumulative adverse environmental effects are no more than minimal:

(a) The activity must be designed and constructed to avoid and minimize adverse effects, both temporary and permanent, to waters of the United States to the maximum extent practicable at the project site (i.e., on site).

(b) Mitigation in all its forms (avoiding, minimizing, rectifying, reducing, or compensating for resource losses) will be required to the extent necessary to ensure that the individual and cumulative adverse environmental effects are no more than minimal.

(c) Compensatory mitigation at a minimum one-for-one ratio will be required for all wetland losses that exceed 1/10-acre and require pre-construction notification, unless the district engineer determines in writing that either some other form of mitigation would be more environmentally appropriate or the adverse environmental effects of the proposed activity are no more than minimal, and provides an activity-specific waiver of this requirement. For wetland losses of 1/10-acre or less that require pre-construction notification, the district engineer may determine on a case-by-case basis that compensatory mitigation is required to ensure that the activity results in only minimal adverse environmental effects.

(d) Compensatory mitigation at a minimum one-for-one ratio will be required for all losses of stream bed that exceed 3/100-acre and require pre-construction notification, unless the district engineer determines in writing that either some other form of mitigation would be more environmentally appropriate or the adverse environmental

effects of the proposed activity are no more than minimal, and provides an activity-specific waiver of this requirement. This compensatory mitigation requirement may be satisfied through the restoration or enhancement of riparian areas next to streams in accordance with paragraph (e) of this general condition. For losses of stream bed of 3/100-acre or less that require pre-construction notification, the district engineer may determine on a case-by-case basis that compensatory mitigation is required to ensure that the activity results in only minimal adverse environmental effects. Compensatory mitigation for losses of streams should be provided, if practicable, through stream rehabilitation, enhancement, or preservation, since streams are difficult-to-replace resources (see 33 CFR 332.3(e)(3)).

(e) Compensatory mitigation plans for NWP activities in or near streams or other open waters will normally include a requirement for the restoration or enhancement, maintenance, and legal protection (e.g., conservation easements) of riparian areas next to open waters. In some cases, the restoration or maintenance/protection of riparian areas may be the only compensatory mitigation required. If restoring riparian areas involves planting vegetation, only native species should be planted. The width of the required riparian area will address documented water quality or aquatic habitat loss concerns. Normally, the riparian area will be 25 to 50 feet wide on each side of the stream, but the district engineer may require slightly wider riparian areas to address documented water quality or habitat loss concerns. If it is not possible to restore or maintain/protect a riparian area on both sides of a stream, or if the waterbody is a lake or coastal waters, then restoring or maintaining/protecting a riparian area along a single bank or shoreline may be sufficient. Where both wetlands and open waters exist on the project site, the district engineer will determine the appropriate compensatory mitigation (e.g., riparian areas and/or wetlands compensation) based on what is best for the aquatic environment on a watershed basis. In cases where riparian areas are determined to be the most appropriate form of minimization or compensatory mitigation, the district engineer may waive or reduce the requirement to provide wetland compensatory mitigation for wetland losses.

(f) Compensatory mitigation projects provided to offset losses of aquatic resources must comply with the applicable provisions of 33 CFR part 332.

(1) The prospective permittee is responsible for proposing an appropriate compensatory mitigation option if compensatory mitigation is necessary to ensure that the activity results in no more than minimal adverse environmental effects. For the NWPs, the preferred mechanism for providing compensatory mitigation is mitigation bank credits or in-lieu fee program credits (see 33 CFR 332.3(b)(2) and (3)). However, if an appropriate number and type of mitigation bank or in-lieu credits are not available at the time the PCN is submitted to the district engineer, the district engineer may approve the use of permittee-responsible mitigation.

(2) The amount of compensatory mitigation required by the district engineer must be sufficient to ensure that the authorized activity results in no more than minimal individual

and cumulative adverse environmental effects (see 33 CFR 330.1(e)(3)). (See also 33 CFR 332.3(f).)

(3) Since the likelihood of success is greater and the impacts to potentially valuable uplands are reduced, aquatic resource restoration should be the first compensatory mitigation option considered for permittee-responsible mitigation.

(4) If permittee-responsible mitigation is the proposed option, the prospective permittee is responsible for submitting a mitigation plan. A conceptual or detailed mitigation plan may be used by the district engineer to make the decision on the NWP verification request, but a final mitigation plan that addresses the applicable requirements of 33 CFR 332.4(c)(2) through (14) must be approved by the district engineer before the permittee begins work in waters of the United States, unless the district engineer determines that prior approval of the final mitigation plan is not practicable or not necessary to ensure timely completion of the required compensatory mitigation (see 33 CFR 332.3(k)(3)). If permittee-responsible mitigation is the proposed option, and the proposed compensatory mitigation site is located on land in which another federal agency holds an easement, the district engineer will coordinate with that federal agency to determine if proposed compensatory mitigation project is compatible with the terms of the easement.

(5) If mitigation bank or in-lieu fee program credits are the proposed option, the mitigation plan needs to address only the baseline conditions at the impact site and the number of credits to be provided (see 33 CFR 332.4(c)(1)(ii)).

(6) Compensatory mitigation requirements (e.g., resource type and amount to be provided as compensatory mitigation, site protection, ecological performance standards, monitoring requirements) may be addressed through conditions added to the NWP authorization, instead of components of a compensatory mitigation plan (see 33 CFR 332.4(c)(1)(ii)).

(g) Compensatory mitigation will not be used to increase the acreage losses allowed by the acreage limits of the NWPs. For example, if an NWP has an acreage limit of 1/2-acre, it cannot be used to authorize any NWP activity resulting in the loss of greater than 1/2-acre of waters of the United States, even if compensatory mitigation is provided that replaces or restores some of the lost waters. However, compensatory mitigation can and should be used, as necessary, to ensure that an NWP activity already meeting the established acreage limits also satisfies the no more than minimal impact requirement for the NWPs.

(h) Permittees may propose the use of mitigation banks, in-lieu fee programs, or permittee-responsible mitigation. When developing a compensatory mitigation proposal, the permittee must consider appropriate and practicable options consistent with the framework at 33 CFR 332.3(b). For activities resulting in the loss of marine or estuarine resources, permittee-responsible mitigation may be environmentally preferable if there are no mitigation banks or in-lieu fee programs in the area that have marine or estuarine

coastal zone management consistency concurrence or presumption of concurrence in order for the activity to be authorized by an NWP. The district engineer or a state may require additional measures to ensure that the authorized activity is consistent with state coastal zone management requirements.

27. **Regional and Case-By-Case Conditions.** The activity must comply with any regional conditions that may have been added by the Division Engineer (see 33 CFR 330.4(e)) and with any case specific conditions added by the Corps or by the state, Indian Tribe, or U.S. EPA in its CWA section 401 Water Quality Certification, or by the state in its Coastal Zone Management Act consistency determination.

28. **Use of Multiple Nationwide Permits.** The use of more than one NWP for a single and complete project is authorized, subject to the following restrictions:

(a) If only one of the NWPs used to authorize the single and complete project has a specified acreage limit, the acreage loss of waters of the United States cannot exceed the acreage limit of the NWP with the highest specified acreage limit. For example, if a road crossing over tidal waters is constructed under NWP 14, with associated bank stabilization authorized by NWP 13, the maximum acreage loss of waters of the United States for the total project cannot exceed 1/3-acre.

(b) If one or more of the NWPs used to authorize the single and complete project has specified acreage limits, the acreage loss of waters of the United States authorized by those NWPs cannot exceed their respective specified acreage limits. For example, if a commercial development is constructed under NWP 39, and the single and complete project includes the filling of an upland ditch authorized by NWP 46, the maximum acreage loss of waters of the United States for the commercial development under NWP 39 cannot exceed 1/2-acre, and the total acreage loss of waters of United States due to the NWP 39 and 46 activities cannot exceed 1 acre.

29. **Transfer of Nationwide Permit Verifications.** If the permittee sells the property associated with a nationwide permit verification, the permittee may transfer the nationwide permit verification to the new owner by submitting a letter to the appropriate Corps district office to validate the transfer. A copy of the nationwide permit verification must be attached to the letter, and the letter must contain the following statement and signature:

“When the structures or work authorized by this nationwide permit are still in existence at the time the property is transferred, the terms and conditions of this nationwide permit, including any special conditions, will continue to be binding on the new owner(s) of the property. To validate the transfer of this nationwide permit and the associated liabilities associated with compliance with its terms and conditions, have the transferee sign and date below.”

(Transferee)

(Date)

30. **Compliance Certification.** Each permittee who receives an NWP verification letter from the Corps must provide a signed certification documenting completion of the authorized activity and implementation of any required compensatory mitigation. The success of any required permittee-responsible mitigation, including the achievement of ecological performance standards, will be addressed separately by the district engineer. The Corps will provide the permittee the certification document with the NWP verification letter. The certification document will include:

- (a) A statement that the authorized activity was done in accordance with the NWP authorization, including any general, regional, or activity-specific conditions;
- (b) A statement that the implementation of any required compensatory mitigation was completed in accordance with the permit conditions. If credits from a mitigation bank or in-lieu fee program are used to satisfy the compensatory mitigation requirements, the certification must include the documentation required by 33 CFR 332.3(l)(3) to confirm that the permittee secured the appropriate number and resource type of credits; and
- (c) The signature of the permittee certifying the completion of the activity and mitigation.

The completed certification document must be submitted to the district engineer within 30 days of completion of the authorized activity or the implementation of any required compensatory mitigation, whichever occurs later.

31. **Activities Affecting Structures or Works Built by the United States.** If an NWP activity also requires review by, or permission from, the Corps pursuant to 33 U.S.C. 408 because it will alter or temporarily or permanently occupy or use a U.S. Army Corps of Engineers (USACE) federally authorized Civil Works project (a “USACE project”), the prospective permittee must submit a pre-construction notification. See paragraph (b)(10) of general condition 32. An activity that requires section 408 permission and/or review is not authorized by an NWP until the appropriate Corps office issues the section 408 permission or completes its review to alter, occupy, or use the USACE project, and the district engineer issues a written NWP verification.

32. **Pre-Construction Notification.** (a) *Timing.* Where required by the terms of the NWP, the prospective permittee must notify the district engineer by submitting a pre-construction notification (PCN) as early as possible. The district engineer must determine if the PCN is complete within 30 calendar days of the date of receipt and, if the PCN is determined to be incomplete, notify the prospective permittee within that 30 day period to request the additional information necessary to make the PCN complete.

The request must specify the information needed to make the PCN complete. As a general rule, district engineers will request additional information necessary to make the PCN complete only once. However, if the prospective permittee does not provide all of the requested information, then the district engineer will notify the prospective permittee that the PCN is still incomplete and the PCN review process will not commence until all of the requested information has been received by the district engineer. The prospective permittee shall not begin the activity until either:

(1) He or she is notified in writing by the district engineer that the activity may proceed under the NWP with any special conditions imposed by the district or division engineer; or

(2) 45 calendar days have passed from the district engineer's receipt of the complete PCN and the prospective permittee has not received written notice from the district or division engineer. However, if the permittee was required to notify the Corps pursuant to general condition 18 that listed species or critical habitat might be affected or are in the vicinity of the activity, or to notify the Corps pursuant to general condition 20 that the activity might have the potential to cause effects to historic properties, the permittee cannot begin the activity until receiving written notification from the Corps that there is "no effect" on listed species or "no potential to cause effects" on historic properties, or that any consultation required under Section 7 of the Endangered Species Act (see 33 CFR 330.4(f)) and/or section 106 of the National Historic Preservation Act (see 33 CFR 330.4(g)) has been completed. If the proposed activity requires a written waiver to exceed specified limits of an NWP, the permittee may not begin the activity until the district engineer issues the waiver. If the district or division engineer notifies the permittee in writing that an individual permit is required within 45 calendar days of receipt of a complete PCN, the permittee cannot begin the activity until an individual permit has been obtained. Subsequently, the permittee's right to proceed under the NWP may be modified, suspended, or revoked only in accordance with the procedure set forth in 33 CFR 330.5(d)(2).

(b) *Contents of Pre-Construction Notification:* The PCN must be in writing and include the following information:

(1) Name, address and telephone numbers of the prospective permittee;

(2) Location of the proposed activity;

(3) Identify the specific NWP or NWP(s) the prospective permittee wants to use to authorize the proposed activity;

(4) (i) A description of the proposed activity; the activity's purpose; direct and indirect adverse environmental effects the activity would cause, including the anticipated amount of loss of wetlands, other special aquatic sites, and other waters expected to result from the NWP activity, in acres, linear feet, or other appropriate unit of measure; a description of any proposed mitigation measures intended to reduce the adverse

(3) When agency coordination is required, the district engineer will immediately provide (e.g., via e-mail, facsimile transmission, overnight mail, or other expeditious manner) a copy of the complete PCN to the appropriate Federal or state offices (FWS, state natural resource or water quality agency, EPA, and, if appropriate, the NMFS). With the exception of NWP 37, these agencies will have 10 calendar days from the date the material is transmitted to notify the district engineer via telephone, facsimile transmission, or e-mail that they intend to provide substantive, site-specific comments. The comments must explain why the agency believes the adverse environmental effects will be more than minimal. If so contacted by an agency, the district engineer will wait an additional 15 calendar days before making a decision on the pre-construction notification. The district engineer will fully consider agency comments received within the specified time frame concerning the proposed activity's compliance with the terms and conditions of the NWPs, including the need for mitigation to ensure that the net adverse environmental effects of the proposed activity are no more than minimal. The district engineer will provide no response to the resource agency, except as provided below. The district engineer will indicate in the administrative record associated with each pre-construction notification that the resource agencies' concerns were considered. For NWP 37, the emergency watershed protection and rehabilitation activity may proceed immediately in cases where there is an unacceptable hazard to life or a significant loss of property or economic hardship will occur. The district engineer will consider any comments received to decide whether the NWP 37 authorization should be modified, suspended, or revoked in accordance with the procedures at 33 CFR 330.5.

(4) In cases of where the prospective permittee is not a Federal agency, the district engineer will provide a response to NMFS within 30 calendar days of receipt of any Essential Fish Habitat conservation recommendations, as required by section 305(b)(4)(B) of the Magnuson-Stevens Fishery Conservation and Management Act.

(5) Applicants are encouraged to provide the Corps with either electronic files or multiple copies of pre-construction notifications to expedite agency coordination.

2021 District Engineer's Decision

1. In reviewing the PCN for the proposed activity, the district engineer will determine whether the activity authorized by the NWP will result in more than minimal individual or cumulative adverse environmental effects or may be contrary to the public interest. If a project proponent requests authorization by a specific NWP, the district engineer should issue the NWP verification for that activity if it meets the terms and conditions of that NWP, unless he or she determines, after considering mitigation, that the proposed activity will result in more than minimal individual and cumulative adverse effects on the aquatic environment and other aspects of the public interest and exercises discretionary authority to require an individual permit for the proposed activity. For a linear project, this determination will include an evaluation of the single and complete crossings of waters of the United States that require PCNs to determine whether they individually

satisfy the terms and conditions of the NWP(s), as well as the cumulative effects caused by all of the crossings of waters of the United States authorized by an NWP. If an applicant requests a waiver of an applicable limit, as provided for in NWPs 13, 36, or 54, the district engineer will only grant the waiver upon a written determination that the NWP activity will result in only minimal individual and cumulative adverse environmental effects.

2. When making minimal adverse environmental effects determinations the district engineer will consider the direct and indirect effects caused by the NWP activity. He or she will also consider the cumulative adverse environmental effects caused by activities authorized by an NWP and whether those cumulative adverse environmental effects are no more than minimal. The district engineer will also consider site specific factors, such as the environmental setting in the vicinity of the NWP activity, the type of resource that will be affected by the NWP activity, the functions provided by the aquatic resources that will be affected by the NWP activity, the degree or magnitude to which the aquatic resources perform those functions, the extent that aquatic resource functions will be lost as a result of the NWP activity (e.g., partial or complete loss), the duration of the adverse effects (temporary or permanent), the importance of the aquatic resource functions to the region (e.g., watershed or ecoregion), and mitigation required by the district engineer. If an appropriate functional or condition assessment method is available and practicable to use, that assessment method may be used by the district engineer to assist in the minimal adverse environmental effects determination. The district engineer may add case-specific special conditions to the NWP authorization to address site-specific environmental concerns.

3. If the proposed activity requires a PCN and will result in a loss of greater than 1/10-acre of wetlands or 3/100-acre of stream bed, the prospective permittee should submit a mitigation proposal with the PCN. Applicants may also propose compensatory mitigation for NWP activities with smaller impacts, or for impacts to other types of waters. The district engineer will consider any proposed compensatory mitigation or other mitigation measures the applicant has included in the proposal in determining whether the net adverse environmental effects of the proposed activity are no more than minimal. The compensatory mitigation proposal may be either conceptual or detailed. If the district engineer determines that the activity complies with the terms and conditions of the NWP and that the adverse environmental effects are no more than minimal, after considering mitigation, the district engineer will notify the permittee and include any activity-specific conditions in the NWP verification the district engineer deems necessary. Conditions for compensatory mitigation requirements must comply with the appropriate provisions at 33 CFR 332.3(k). The district engineer must approve the final mitigation plan before the permittee commences work in waters of the United States, unless the district engineer determines that prior approval of the final mitigation plan is not practicable or not necessary to ensure timely completion of the required compensatory mitigation. If the prospective permittee elects to submit a compensatory mitigation plan with the PCN, the district engineer will expeditiously review the proposed compensatory mitigation plan. The district engineer must review the proposed compensatory mitigation plan within 45 calendar days of receiving a complete PCN and determine whether the proposed

mitigation would ensure that the NWP activity results in no more than minimal adverse environmental effects. If the net adverse environmental effects of the NWP activity (after consideration of the mitigation proposal) are determined by the district engineer to be no more than minimal, the district engineer will provide a timely written response to the applicant. The response will state that the NWP activity can proceed under the terms and conditions of the NWP, including any activity-specific conditions added to the NWP authorization by the district engineer.

4. If the district engineer determines that the adverse environmental effects of the proposed activity are more than minimal, then the district engineer will notify the applicant either: (a) that the activity does not qualify for authorization under the NWP and instruct the applicant on the procedures to seek authorization under an individual permit; (b) that the activity is authorized under the NWP subject to the applicant's submission of a mitigation plan that would reduce the adverse environmental effects so that they are no more than minimal; or (c) that the activity is authorized under the NWP with specific modifications or conditions. Where the district engineer determines that mitigation is required to ensure no more than minimal adverse environmental effects, the activity will be authorized within the 45-day PCN period (unless additional time is required to comply with general conditions 18, 20, and/or 31), with activity-specific conditions that state the mitigation requirements. The authorization will include the necessary conceptual or detailed mitigation plan or a requirement that the applicant submit a mitigation plan that would reduce the adverse environmental effects so that they are no more than minimal. When compensatory mitigation is required, no work in waters of the United States may occur until the district engineer has approved a specific mitigation plan or has determined that prior approval of a final mitigation plan is not practicable or not necessary to ensure timely completion of the required compensatory mitigation.

2021 Further Information

1. District engineers have authority to determine if an activity complies with the terms and conditions of an NWP.
2. NWPs do not obviate the need to obtain other federal, state, or local permits, approvals, or authorizations required by law.
3. NWPs do not grant any property rights or exclusive privileges.
4. NWPs do not authorize any injury to the property or rights of others.
5. NWPs do not authorize interference with any existing or proposed Federal project (see general condition 31).

2021 Nationwide Permit Definitions

Best management practices (BMPs): Policies, practices, procedures, or structures implemented to mitigate the adverse environmental effects on surface water quality resulting from development. BMPs are categorized as structural or non-structural.

Compensatory mitigation: The restoration (re-establishment or rehabilitation), establishment (creation), enhancement, and/or in certain circumstances preservation of aquatic resources for the purposes of offsetting unavoidable adverse impacts which remain after all appropriate and practicable avoidance and minimization has been achieved.

Currently serviceable: Useable as is or with some maintenance, but not so degraded as to essentially require reconstruction.

Direct effects: Effects that are caused by the activity and occur at the same time and place.

Discharge: The term “discharge” means any discharge of dredged or fill material into waters of the United States.

Ecological reference: A model used to plan and design an aquatic habitat and riparian area restoration, enhancement, or establishment activity under NWP 27. An ecological reference may be based on the structure, functions, and dynamics of an aquatic habitat type or a riparian area type that currently exists in the region where the proposed NWP 27 activity is located. Alternatively, an ecological reference may be based on a conceptual model for the aquatic habitat type or riparian area type to be restored, enhanced, or established as a result of the proposed NWP 27 activity. An ecological reference takes into account the range of variation of the aquatic habitat type or riparian area type in the region.

Enhancement: The manipulation of the physical, chemical, or biological characteristics of an aquatic resource to heighten, intensify, or improve a specific aquatic resource function(s). Enhancement results in the gain of selected aquatic resource function(s), but may also lead to a decline in other aquatic resource function(s). Enhancement does not result in a gain in aquatic resource area.

Establishment (creation): The manipulation of the physical, chemical, or biological characteristics present to develop an aquatic resource that did not previously exist at an upland site. Establishment results in a gain in aquatic resource area.

High Tide Line: The line of intersection of the land with the water’s surface at the maximum height reached by a rising tide. The high tide line may be determined, in the absence of actual data, by a line of oil or scum along shore objects, a more or less continuous deposit of fine shell or debris on the foreshore or berm, other physical markings or characteristics, vegetation lines, tidal gages, or other suitable means that delineate the general height reached by a rising tide. The line encompasses spring high tides and other high tides that occur with periodic frequency but does not include storm

Open water: For purposes of the NWP, an open water is any area that in a year with normal patterns of precipitation has water flowing or standing above ground to the extent that an ordinary high water mark can be determined. Aquatic vegetation within the area of flowing or standing water is either non-emergent, sparse, or absent. Vegetated shallows are considered to be open waters. Examples of “open waters” include rivers, streams, lakes, and ponds.

Ordinary High Water Mark: The term ordinary high water mark means that line on the shore established by the fluctuations of water and indicated by physical characteristics such as a clear, natural line impressed on the bank, shelving, changes in the character of soil, destruction of terrestrial vegetation, the presence of litter and debris, or other appropriate means that consider the characteristics of the surrounding areas.

Perennial stream: A perennial stream has surface water flowing continuously year-round during a typical year.

Practicable: Available and capable of being done after taking into consideration cost, existing technology, and logistics in light of overall project purposes.

Pre-construction notification: A request submitted by the project proponent to the Corps for confirmation that a particular activity is authorized by nationwide permit. The request may be a permit application, letter, or similar document that includes information about the proposed work and its anticipated environmental effects. Pre-construction notification may be required by the terms and conditions of a nationwide permit, or by regional conditions. A pre-construction notification may be voluntarily submitted in cases where pre-construction notification is not required and the project proponent wants confirmation that the activity is authorized by nationwide permit.

Preservation: The removal of a threat to, or preventing the decline of, aquatic resources by an action in or near those aquatic resources. This term includes activities commonly associated with the protection and maintenance of aquatic resources through the implementation of appropriate legal and physical mechanisms. Preservation does not result in a gain of aquatic resource area or functions.

Re-establishment: The manipulation of the physical, chemical, or biological characteristics of a site with the goal of returning natural/historic functions to a former aquatic resource. Re-establishment results in rebuilding a former aquatic resource and results in a gain in aquatic resource area and functions.

Rehabilitation: The manipulation of the physical, chemical, or biological characteristics of a site with the goal of repairing natural/historic functions to a degraded aquatic resource. Rehabilitation results in a gain in aquatic resource function, but does not result in a gain in aquatic resource area.

Stormwater management: Stormwater management is the mechanism for controlling stormwater runoff for the purposes of reducing downstream erosion, water quality degradation, and flooding and mitigating the adverse effects of changes in land use on the aquatic environment.

Stormwater management facilities: Stormwater management facilities are those facilities, including but not limited to, stormwater retention and detention ponds and best management practices, which retain water for a period of time to control runoff and/or improve the quality (i.e., by reducing the concentration of nutrients, sediments, hazardous substances and other pollutants) of stormwater runoff.

Stream bed: The substrate of the stream channel between the ordinary high water marks. The substrate may be bedrock or inorganic particles that range in size from clay to boulders. Wetlands contiguous to the stream bed, but outside of the ordinary high water marks, are not considered part of the stream bed.

Stream channelization: The manipulation of a stream's course, condition, capacity, or location that causes more than minimal interruption of normal stream processes. A channelized jurisdictional stream remains a water of the United States.

Structure: An object that is arranged in a definite pattern of organization. Examples of structures include, without limitation, any pier, boat dock, boat ramp, wharf, dolphin, weir, boom, breakwater, bulkhead, revetment, riprap, jetty, artificial island, artificial reef, permanent mooring structure, power transmission line, permanently moored floating vessel, piling, aid to navigation, or any other manmade obstacle or obstruction.

Tidal wetland: A tidal wetland is a jurisdictional wetland that is inundated by tidal waters. Tidal waters rise and fall in a predictable and measurable rhythm or cycle due to the gravitational pulls of the moon and sun. Tidal waters end where the rise and fall of the water surface can no longer be practically measured in a predictable rhythm due to masking by other waters, wind, or other effects. Tidal wetlands are located channelward of the high tide line.

Tribal lands: Any lands title to which is either: 1) held in trust by the United States for the benefit of any Indian tribe or individual; or 2) held by any Indian tribe or individual subject to restrictions by the United States against alienation.

Tribal rights: Those rights legally accruing to a tribe or tribes by virtue of inherent sovereign authority, unextinguished aboriginal title, treaty, statute, judicial decisions, executive order or agreement, and that give rise to legally enforceable remedies.

Vegetated shallows: Vegetated shallows are special aquatic sites under the 404(b)(1) Guidelines. They are areas that are permanently inundated and under normal circumstances have rooted aquatic vegetation, such as seagrasses in marine and estuarine systems and a variety of vascular rooted plants in freshwater systems.

Waterbody: For purposes of the NWP, a waterbody is a “water of the United States.” If a wetland is adjacent to a waterbody determined to be a water of the United States, that waterbody and any adjacent wetlands are considered together as a single aquatic unit (see 33 CFR 328.4(c)(2)).

ADDITIONAL INFORMATION

Information about the U.S. Army Corps of Engineers Regulatory Program, including nationwide permits, may also be accessed at
<http://www.swt.usace.army.mil/Missions/Regulatory.aspx> or
<http://www.usace.army.mil/Missions/CivilWorks/RegulatoryProgramandPermits.aspx>

